

Baghdad Proposal


Urban railway and Iraqi manufacturing
Future national development

OpenSourceRail · Planning baseline 2026-10-04

Complete proposal, detailed schedules and technical evidence annexes

Prepared for the prospective Iraqi sponsor, Baghdad authorities, operating organisation and financing partners.

Baghdad finance only. National expansion is a separate future development programme. Construction and operating approval remain pending.

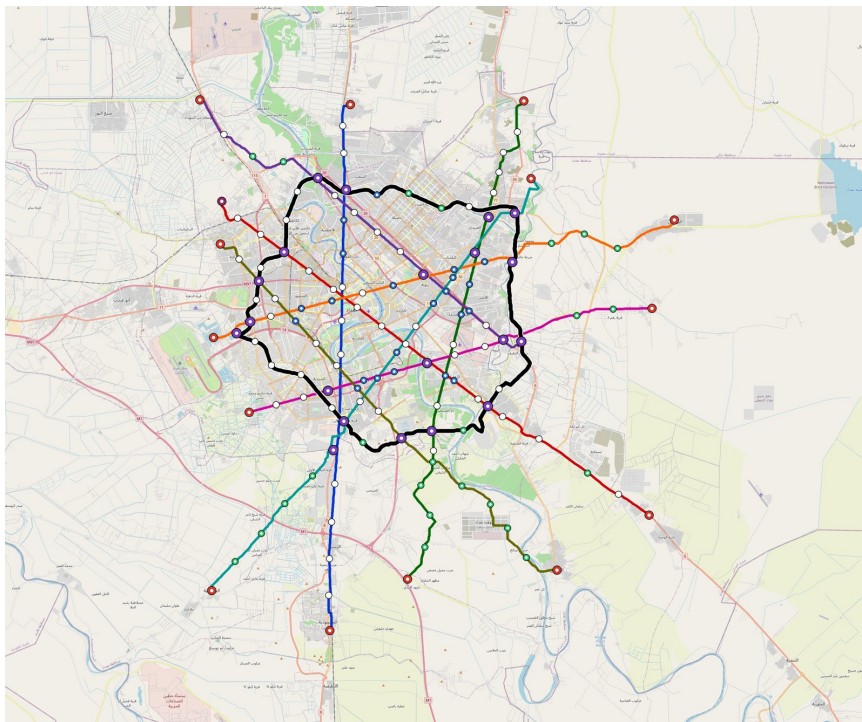

Baghdad planning network

Contents

Baghdad Proposal	5
Baghdad detailed schedules	24
Baghdad detailed engineering and Iraqi manufacturing plan	33
Baghdad – Urban Rail Network	39
Baghdad Planning OSR-ALN Package	43
Baghdad organisation and design work	44
Baghdad line-local depot and stabling quantity package	56
Baghdad delivery estimate and scope reconciliation	57
Baghdad comparable opening fleet and corridor requirements	58
Baghdad chronological charging-energy and cost screen	59
Baghdad delivery reconciliation – 4 October 2026	60
Rental delivery allocation sensitivities	61
Baghdad controlled six-car planning product	62
Baghdad workload, recruitment and competence pilot	63
Comparable standalone opening corridors	65
Nine depot/storage design studies and Iraqi slab manufacture	66
Development leadership and training mobilisation	67
Field investigations, quotations and actual appointments	68
Delivery-cost financial reconciliation	69
Task-derived maintenance and reserve cash	71
Baghdad remaining-work delivery packages	72
Chronological site-limited energy and installed upgrades	73
Six-car child parts and procurement/qualification work	74
Workforce, practical training and a rest-limited pilot	75

Baghdad frozen-resource delivery and funding study	76
Baghdad deployment gaps	79
baghdad depot scope reconciliation	80
Baghdad detailed component register	81
Baghdad mixed joint-stock holding and ordinary-equity study	85
Baghdad factory sized to the city programme	90
Baghdad – Iraq funding appraisal	93
Baghdad financing reconciliation and six-month placement programme	97
Baghdad financing redesign – 2026-10-04	105
Baghdad programme recalculation	108
Baghdad qualification, funding gates and first operating section	111
Baghdad operations cross-check	115
Baghdad civil soil screening	116
Station and depot overnight allocation	117
Baghdad survey-control processing	130
Baghdad drainage and ground-design gate	131
Baghdad field-evidence brief	132
Baghdad surveyed-ground-model gate	136
Baghdad route and station fit gate	137
Baghdad structural-release gate	138
Baghdad surveyed-alignment gate	139
Baghdad manufactured-viaduct comparison	140
Baghdad retained under-viaduct rental portfolio – 2026-10-04	142
Baghdad Acceptance And Accreditation Evidence Basis	145
Baghdad-only funding programme	147

Iraq National OpenSourceRail Strategy	154
RFC 0033 — TACS runtime and committed resource control	156
Distributed Onboard Control Profile	160
Rolling-stock top-down / bottom-up design system	162
RFC 0011 — Civil Infrastructure Design Standard	164
RFC 0014 — Depot Design Standard	172
RFC 0013 — Operations Rulebook	179
Reproducible city operating twins	183
Deployment Planning Reference	186
Ballastless Slab Trackform Designs	189
OSR Rapid Viaduct Kit — Design Basis	192
Viaduct Bearing And Movement Schedule	194
Viaduct Transport And Erection Envelope	195
Viaduct First-Article Test Plan	196
Repository Artifact Policy	197
Current Baghdad delivery review — 4 October 2026	199
Baghdad continuation: physical packages and revised financial conclusion	200
Baghdad review follow-up: controls, CI and deliverable-service sensitivity	202
Baghdad manufactured viaduct and cost review	204
Baghdad scope and industrial review — 4 October 2026	205

Baghdad Proposal

Source: cities/catalogue/west-asia/Iraq/Baghdad/BAGHDAD-PROPOSAL.md

OpenSourceRail proposes an owner led feasibility and front end engineering programme for Baghdad, with Iraqi train manufacture and local infrastructure delivery. This proposal brings the Baghdad network, railway systems, operating organisation, delivery evidence and financing together, and sets out a separate path for future national development. It is addressed to the prospective Iraqi public sponsor, Baghdad authorities, operating organisation and financing partners; no appointment or financing commitment is asserted.

The latest [programme recalculation](#) sizes 3,430 permanent operating FTE and 9 line-local depots for all 762 six-car trainsets. With completed components bought, revised capital is USD 8.250bn. The unquoted positive-margin local-production option gives USD 8.145bn, imported invoice exposure of USD 1.942bn and 23.84% USD capital intensity. It records IQD 0.000tn residual unourced support after assumed facilities and retains IQD 9.966tn total debt at the horizon. Current indexed fares and additional-income assumptions do not repay this scope. Mezzanine defers cash pressure but leaves unpaid balloons; it is a sensitivity, not a recommended solution.

The earlier [delivery-cost continuation](#) remains a comparator: USD 7.679bn capital, before still-unpriced scope, and IQD 3.253tn unpaid gap debt. The original financial schedules below likewise remain controlled reference cases. Debt clearance in an older reference is not the current feasibility conclusion; higher fares and conditional additional funding are tested separately, with no adopted tariff or lender commitment.

The current planning network is 9 lines, 474.2 km of double track route, 164 stations and 762 six car trainsets. Original reference capital, including one final-assembly plant and its EPC, was USD 7.515 billion equivalent; it does not include the latest scope replacement. The direct government capital contribution remains 25% of each revised case. Imports are financed 50% government USD cash and 50% proposed Chinese USD credit; all remaining capital cash, bonds and bank debt are IQD.

The immediate decision proposed is to establish a sponsor, commission survey and demand work, develop the first operable line and plant packages, qualify suppliers and obtain executable financing terms. Construction and operating release require the recorded physical and approval gates. The current resource constrained plan reaches first line revenue in month 40 and full operation in month 76 after financial close. That long schedule is a material design and delivery problem to resolve; this proposal does not substitute a five year promise.

How to read the proposal

The first part states the integrated proposal and the decisions it needs. The next part prints the detailed network registers and six month financing schedules. The technical appendices reproduce every current Baghdad Markdown report, the national brief and selected shared standards. The supporting ZIP preserves the full controlled Baghdad files, every Baghdad financing spreadsheet, the operations payload, national city design inputs and the cited shared references. The source inventory and manifest identify exact file bytes.

Baghdad is the only financed city. National expansion is a future strategic option with its own budgets and approvals. The national totals and generic city pages retain original catalogue assumptions; the latest Baghdad study does not silently reprice or finance other cities. Procurement origin, loan currency and reporting currency are different measures. USD equivalents use the historical model anchor of IQD 1,300/USD; this is not a current execution quote. All prices, demand, debt terms and rights proceeds remain planning assumptions. Older generic foreign turnkey examples reproduced in source appendices are separate from the historical 148 km comparison and the scheduled Baghdad financing cases.

Latest scope, local production and matched funding cases

The 164 stations have two concurrent staff during two normal eight-hour shifts, giving 656 daily shift assignments. The retained 20.5-hour railway also funds 4.5 hours of late cover. Weekly/leave/training/sickness cover gives 1620 station FTE, included in the 3430 permanent railway FTE. Loaded annual payroll is IQD 80.292bn before subsequent OPEX inflation. The general pay floor is IQD 1,175,455/month: 1.5 times the 2021 employee median indexed to 2026 at an assumed 5% a year. Technical/supervisor/senior/director grades use 2.25/3/4/5 times the same proxy. This is not a newly observed national median and does not change the fare-income denominator.

Each line has one depot; all spare/reserve trains are included. Storage uses the actual 111 m train plus 10 m clearance; workshop bays follow bay-hour workload separately. The nine sites total USD 247.790m and replace the old USD 8m allowance once. Itemised storage/workshop/access tracks, points, civil shells, process equipment, services, wash plants, wheel lathes, stores, rescue/isolation and retained energy stock are costed. Land/title, utilities, actual foundations and installed charging/grid upgrades remain open; launch/throat conflicts need an operating replay.

The order requires 9,144 bogies, 9,144 motor/inverter sets, 4,572 battery packs (1.029 GWh gross), 18,288 door cassettes and 27,432 window cassettes. Final assembly employs 1273 production and 191 support FTE for 55 scheduled paid months.

Upstream facilities are sized to the train factory rate and price imported process machinery, local buildings/materials, residual imported inputs, qualification and their full paid establishment. Selected processes (bogie fabrication, battery-pack assembly, door manufacture) have positive whole-order margins under the unquoted assumptions. The remaining processes (motor assembly, window manufacture) stay bought in this case; their Baghdad-only whole-order margins are shown in the make/buy register. Imported cells/BMS, inverters, wheels/axles/bearings and other safety parts remain; no cell gigafactory or future national sales credit is assumed.

The main design uses the reworked central elevated routes and 54.86% elevated track across Baghdad. Further outer civil alternatives permit up to 65% elevated and screen 7.015 km of additional at-grade conversion around exceptional curves, reaching 56.34% elevated. These outer candidate intervals are not adopted or surveyed. Elevation alone removes no horizontal bend. Added viaduct and hypothetical 0/25/50% routing-penalty removal are priced separately; no hypothetical penalty removal is adopted as a saving.

Matched case	CAPEX USD bn	USD intensity	Unsourced support IQD tn	Terminal all debt IQD tn	Defaulted junior vintages
construction_wage_content_stress	8.702	23.30%	0.603	10.744	0
grade-separation-penalty-0pct	8.202	23.77%	0.000	10.131	0
grade-separation-penalty-25pct	8.087	23.91%	0.000	9.799	0
grade-separation-penalty-50pct	7.972	24.05%	0.000	9.467	0
local_all	8.152	23.05%	0.000	10.018	0
local_positive	8.145	23.84%	0.000	9.966	0
local_positive_commercial_gap	8.145	23.84%	19.487	13.000	0
local_positive_mezzanine	8.145	23.84%	0.000	15.906	79
local_positive_mezzanine_stress	8.145	23.84%	17.741	40.960	79
local_positive_raw_price_stress	8.218	24.19%	0.000	10.157	0
local_positive_supplier_delay	8.145	23.84%	0.000	9.942	0
revised_scope_buy	8.250	26.71%	0.000	10.200	0

All twelve cases have invoice-level capital registers, monthly native-currency cash/principal ledgers and six-month bond/loan placement schedules in the [latest study](#) and supporting archive. Government is 25% of total capital, with USD machinery/input downpayments on actual invoice dates and the balance allocated as local IQD appropriation. Only Chinese credit is USD debt; bonds, senior bank/gap debt and mezzanine are IQD. Six months of senior service are reserved from the first draw, with three months of OPEX and industrial working capital. This reserve policy differs from the older reference; matched cases are the valid comparison.

The following capital-only source table is for the latest positive-margin local-production senior case. Fees, interest, reserve funding and gap facilities are separate cashflows; this table reconciles to capital uses only. Ordinary and green bonds are separate placements within the same total funding requirement.


Latest capital source	Currency	Native amount	USD equivalent m
Government import cash	USD	970,909,383	970.909
Government local cash	IQD	1,384,956,400,257	1,065.351
Chinese capital credit	USD	970,909,383	970.909
Ordinary capital bonds	IQD	3,944,816,429,415	3,034.474
Green capital bonds	IQD	1,040,233,767,709	800.180
Senior bank capital credit	IQD	1,661,683,399,041	1,278.218
Conditional climate capital grant	IQD	32,500,000,000	25.000

The proposed IQD mezzanine replaces 10% of residual domestic capital borrowing, with 6% cash coupon, 4% PIK, 2% fee and a 15-year balloon. Cash coupons require senior DSCR of 1.20, funded reserves and genuine residual cash. Deferred coupons and PIK are debt. Unpaid balloons become overdue balances with separately disclosed simple-interest sensitivity, without automatic refinancing, conversion or interest-on-arrears. The case leaves IQD 15.906tn total debt and 79 defaulted draw vintages. It does not improve the unlevered company NPV of USD -4.678bn at the assumed discount rate. Grants, net development-rights receipts, green terms and concessional gap funding are uncommitted; an 8% gap-rate case exposes this dependency. Fares, fare/OPEX inflation, advertising, kiosk/rental receipts and inherited additional income are already included.

Baghdad network and population access

The design retains a planning population of 9,780,429. The 38.9% anchor weighted coverage proxy represents 3,804,586 residents under the model. It is not measured population within an 800 m walking network, nor the number of unique passengers. River crossings, actual entrances, walking barriers and feeders need a surveyed population and access model. A larger network provides a scope to evaluate; it does not prove higher coverage than another proposal.

Line	Shape	Route km	Stations	Peak fleet	Total fleet	Opening month
line-1	radial	49.068	17	78	86	40
line-2	radial	52.851	18	91	101	45
line-3	radial	49.496	19	88	97	50
line-4	radial	42.068	15	72	80	55
line-5	radial	47.321	16	78	86	59
line-6	radial	52.503	17	90	100	65
line-7	radial	39.957	15	71	79	69
line-8	radial	47.849	16	81	90	74
line-9	ring	93.067	31	39	43	76

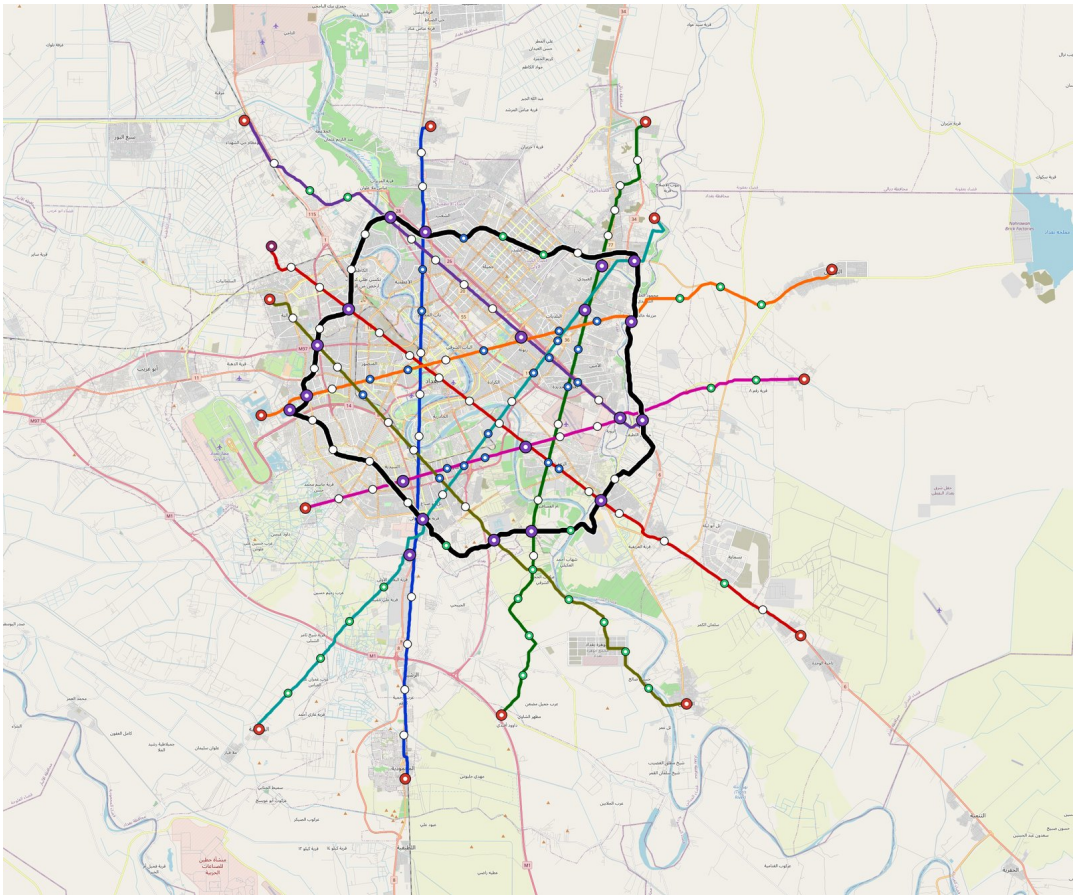


Baghdad network

Line names are controlled design identifiers. Public station names, route brands and final termini require owner approval. Chainages, coordinates, interchange platforms and fleet roles are printed in the network registers and regenerated from the adopted core corridor concept.

The service concept operates 05:30 to 02:00 with a three minute protected peak headway. The current scheduled journeys and fleet sizing are capacity led; accepted junction/authority capacity, ridership, a timetable, station crowding and degraded recovery need operating review. The 762 trainsets comprise peak, spare and cold reserve roles documented in the annex.

City-centre alignment rework

Within the controlled core rectangle (33.22–33.42°N, 44.28–44.53°E), radial corridors use straight tangents and ring connections use broad circular planning fillets. Core land sections are elevated; water crossings retain bridge classification. The analytical core routes shorten from 301.468 to 238.172 km. This is the main design used by the updated station, fleet, civil, energy, depot, staffing, delivery and financing calculations. The earlier extra-viaduct cost-only case did not change geometry.

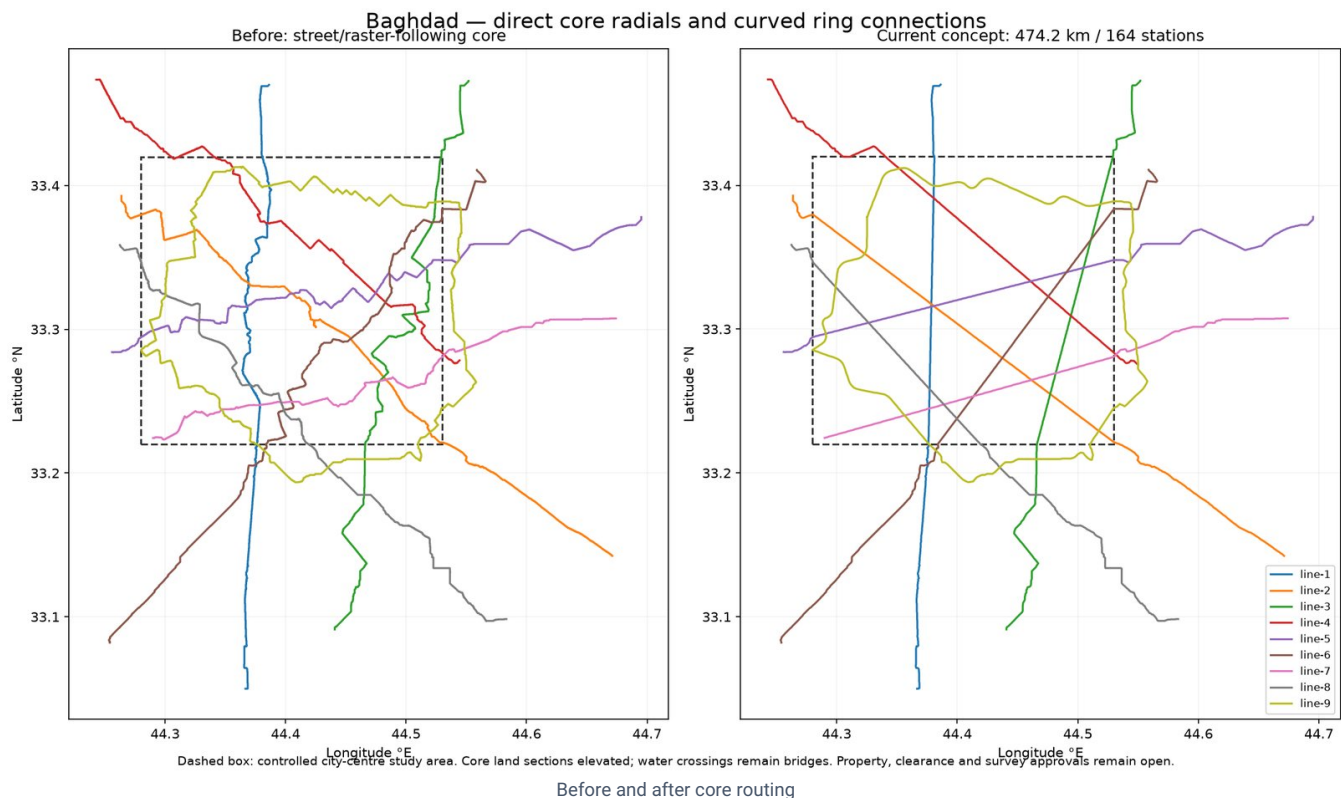

These corridors reserve no property or air rights. Obstacles, heritage/security constraints, surveyed clearances, pier access, utilities, transition curves, cant, vertical geometry and foundations require engineering and owner review. Outer approaches retain bends and exceptional elevated products. The coverage proxy must be measured before selecting the faster/straighter layout as an access solution; no old coverage score is carried forward.

Trains and imported component strategy

The Baghdad profile is metro 6car: 6 cars, 111 m body length, 720 passengers at nominal planning load including 120 seats, and 960 at short duration crush load. Each train has 1,350 kWh nameplate / 1,080 kWh usable LFP battery capacity, 12 traction controllers, 3,600 kW peak traction and a 50 C design ambient. These are reference profiles requiring supplier and physical qualification, not delivered fleet performance.

The original industrial scope is train assembly, body modules, fit out, wiring, coatings, inspection, testing and maintenance, with completed bogies, batteries, windows and doors bought. The latest positive-margin local-production option replaces selected completed imports with Chinese process machinery and residual inputs for Iraqi fabrication/assembly. Solar equipment, glazing and critical component inputs retain imports. Chinese supplier origin and export lender eligibility need evidence for every financed item; the entire imported basket is currently an unqualified scenario. Candidate CRRC equipment remains subject to competitive supplier selection, interface and safety qualification. There is no established CRRC partnership, quotation or endorsement.

Shared LM3 fabrication and first article documentation is reference process evidence for a three car platform. It does not qualify Baghdad's six car consist. The national programme should qualify the shared modules and then validate each consist and its interfaces, rather than treating a shared drawing as an accepted Baghdad train.

Civil infrastructure and stations

The civil screen contains 999 segments: 191.8 km at-grade, 260.1 km elevated, 22.2 km bridge. Route kilometres describe double track corridors; they are not track kilometres or a measurement of all sidings. Station products, 20 interchange complexes and 6 junction records are bound to the generated layout.

The proposed civil programme starts with survey control, utilities, property and access, geotechnical investigation, flood/drainage levels, alignment and station fit. Desktop soil inputs contain 7,287 sample locations and 65 missing profiles; they do not supply foundation bearing capacity, groundwater or deep stratigraphy. Structural calculations, spans, erection, movements and independent checking must follow route specific evidence. Generated alignment exports have unfitted curves, placeholder vertical profiles and undesigned cant.

Stations require accessible approaches, platforms, passenger information, fire and evacuation design, fare equipment, retail and advertising layouts, security, sanitation and maintenance access. Platform and station access standards must be

checked against the final six car envelope and passenger demand. Equipment and architecture references do not establish installed compliance.

The original USD 8m depot allowance is replaced by the nine full-fleet line depots in the latest recalculation above. Surveyed land, foundation/electrical interfaces, fire/security release and supplier quotations remain open. Workshop bays cannot be counted as overnight train parking. The earlier reference policy proposed two revenue trains at selected powered stations and line-local storage for remaining fleet; the latest study gives no capacity credit to station parking. Usable tracks, charging, protected morning release, evening repositioning and repeated-day replay still require acceptance. The depot and stabling appendices retain these failures explicitly.

Manufactured viaduct alternatives and installed cost

The [manufactured-viaduct comparison](#) covers Pi20 and Pi25 with two bearing/connection schemes, plus an OSR-US constrained-access option. Baghdad's infrastructure load seed now explicitly requires the complete 24-axle, 111 m six-car train, with supplier axle positions and loaded distribution still unresolved. A link slab retains independent girder-end bearings; shared bearings require a checked structural continuity connection and staged load path.

Every one of the 497 elevated segments, including 16 exceptional segments, has a comparison record. The original elevated model separates USD 2.536bn standard-rate allowance from USD 0.431bn routing penalties. Penalties discourage difficult routing; they are not supplier-priced structures or savings available merely by deletion. Realignment, station movements, ground/utility investigations and installed whole-life alternatives remain unaccepted.

Retaining simple-span bearings changes the existing periodic cost index from USD 9.748m/km to USD 10.198m/km. The USD 117.066m uniform whole-elevated-network difference is an unadopted rate illustration; Pi bearing quantities are not transferred to OSR-US/special designs. The lower existing rate remains conditional on an unaccepted structural scheme.

The separate financed sensitivity applies only to 249.785 km of standard Pi25, adding USD 112.403m direct and incremental EPC once. It gives USD 7.799bn capital and IQD 3.602tn terminal gap debt, with monthly/six-month financing recalculated under the same 25% government and USD/IQD rules. Existing civil invoice dates and origin proportions are inherited assumptions. Connection, finite end effects, foundations, actual import eligibility and other consequential costs remain unpriced; the original full-fleet case is preserved as a comparator.

Finite supports, unknown foundation lengths, complete member/hook mass gates, configured erection bids, per-item invoice currencies and eight production fronts are included in the supporting data. Installed-price totals remain unknown while scope is unpriced. Accepted complete double-track bays/week, first beam/pier/connection trials and independent design release must precede programme and budget selection. No literature savings or 30 m product is assumed.

Energy and desert operation

The current duty model schedules 3,952 one way journeys and about 217,090 train km per day, with 2,053.8 GWh annual traction demand. It assigns 52.1 MW station/depot PV, 354.0 MWh site storage, 316.0 MW connected charging and 934.2 MW dedicated solar. The design's zero annual residual grid/PPA import is an energy accounting result; it does not establish uninterrupted operation or installed grid independence.

Storage endurance, adverse weather, PV land, heat/dust derating, losses, supplier fire separation, actual charging duty, protection and backup import need a time resolved operating appraisal. Snapshot solver passes and grid only diagnostics do not close these gates. Battery protection and cabin/battery thermal separation must be qualified at the declared ambient and duty. No claimed unlimited battery autonomy or accepted solar islanding is used to close financing.



Engineering map

Train control and operational safety

The current architecture reference is RFC 0033, TACS runtime and committed resource control. RFC 0032's separate authority/protection prototype is superseded. The design retains committed resource ownership in the interlocking, ordered consensus decisions, onboard movement authority, automatic train protection, station departure gates and final brake requests. OCC supplies service intentions and observations; ERP and supervision cannot bypass railway authority or clear protection latches.

The reference uses three static consensus voters and two logical protection channels. Hardware placement, independent power/network domains, sensing, brake outputs and common cause analysis need assessment. Two software channels do not establish independent safety hardware. Lost required permissions, stale/invalid evidence and missing physical proving retain restrictive protection. The runtime is a synthetic process reference and not a deployed Baghdad control system or safety certificate. Existing Baghdad timetable simulations do not constitute RFC 0033 physical acceptance.

Iraqi manufacture and local economic benefit

The Baghdad plant is sized from 4,572 vehicle modules. Its base allowance is USD 323.874m plus USD 22.671m EPC, counted once outside city CAPEX. The current plant construction assumption is 390 working days before train production. Factory siting, freight access, utilities, tooling, staff, production rate, quality capacity and six car qualification require their own approved business and delivery plan.


The original procurement allocation assigns USD 5.831bn equivalent locally. This is potential local expenditure, not payroll, GDP added or a guaranteed Iraqi content ratio. Local train and infrastructure work can retain skills, supplier income, repair capacity and spares knowledge. The latest process appraisal above includes whole-order labour, factory support/maintenance and make/buy margins; manufacturing sales to other customers still need a separate business case. No multiplier, tax recovery or future national plant profit is booked as project cash without evidence. Imported machinery and residual inputs retain foreign exchange and supply-chain exposure.

Operating organisation and digital management

The latest operating establishment is 3,430 FTE with IQD 80.292bn annual loaded payroll, replacing the original 3,217 FTE / IQD 47.044bn allowance. It includes OCC/remote assistance, fleet maintenance, infrastructure/energy, stations, passenger service, administration and training. It remains a planning workload/roster model; legal duties, appointments and competence require acceptance. Construction and factory populations are priced separately as explained above, with measured work hours, crew mixes and throughput still required.

Operating role	Required FTE	Wage grade
occ-lead	5	supervisor
dispatcher	45	technical
remote-assist	428	technical
station-lead	88	supervisor
platform-assistance	810	general
customer-service	810	general
station-cleaning	122	general
workshop-lead	27	supervisor
fleet-mechanical	245	technical
fleet-electrical	166	technical
fleet-finish-cleaning	371	general
infrastructure-lead	18	supervisor
civil-track	105	technical
solar-storage	61	technical
wayside-comms	47	technical
city-director	1	director
chief-engineer	1	senior
quality-safety	23	senior
training	25	senior
procurement-stores	19	technical
finance-people	13	technical

The Baghdad operating package contains 1,680 assets, 7,311 manufacturing/verification tasks, 14,323 material/procurement rows, 9,804 maintenance tasks and 6,098 QA actions. These are generated planning records. Actual purchase orders, execution, measurements and accountable release evidence remain distinct. The project twin, ERPNext/Frappe integration, supervision, QR identities, maintenance and advisory AI support business work; they do not issue movement or safety release authority.

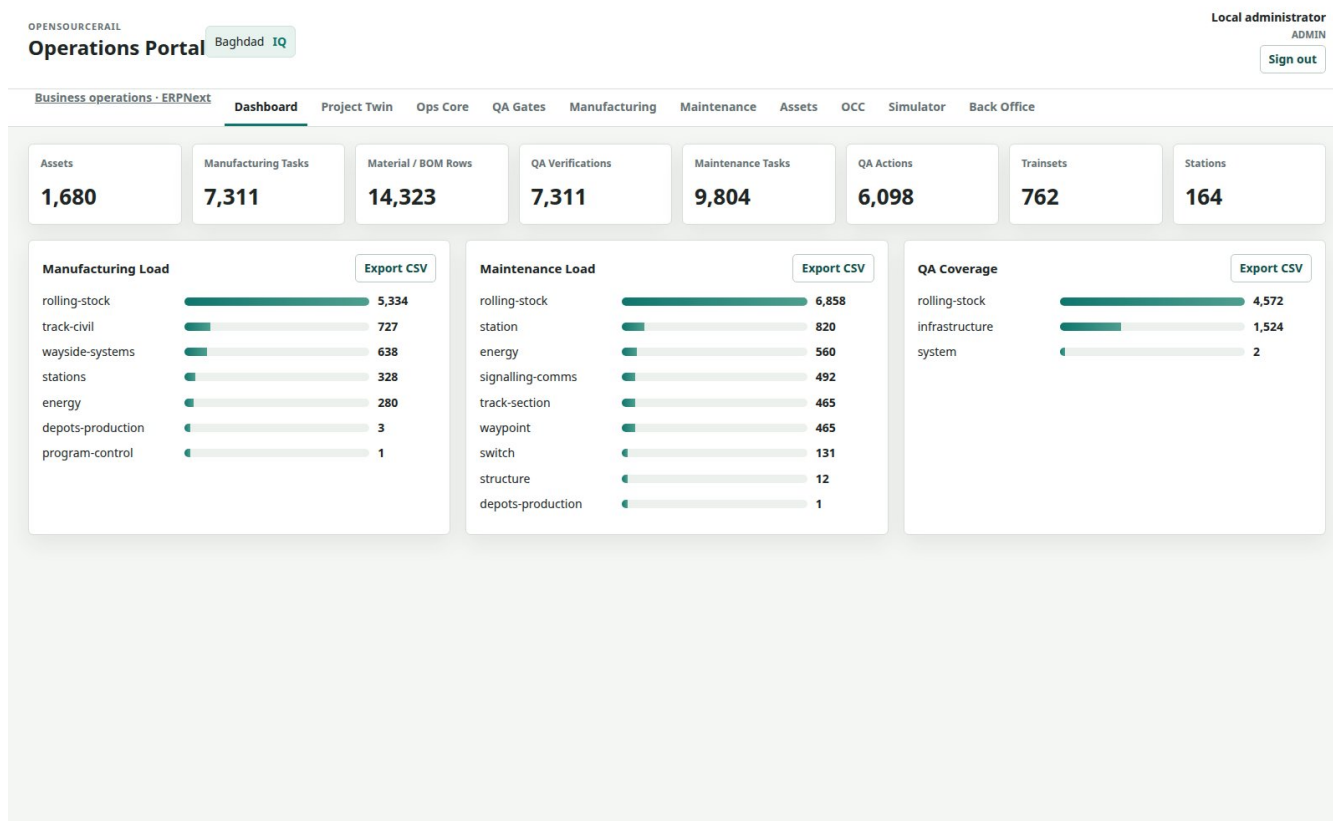

Delivery and commissioning sequence

First obtain survey and demand inputs, freeze a viable first line and plant scope, and reconcile depot and energy duties. Qualify long lead components and the first six car train, then deliver infrastructure, energy, station systems and trained operating staff in accepted phases. Each line needs its own operating and safety acceptance before fare revenue is realised.

The city-sized plant becomes available after 18 months from NTP, followed by first-article qualification and finite six-car production cells. All 762 trains remain in scope. The calculated full fleet finishes alongside the overall infrastructure programme. Civil work and invoice milestones are rephased within the existing crew lanes and dependency graph. Line 1's infrastructure moves from day 196 to 668, reducing its fleet wait from 562 to 90 working days. Resources, durations and opening dates are preserved. Survey, land, utility, permit and contract approval remain necessary before deferring work. See the [physical factory sizing, crews, test paths and capital reconciliation](#).

Current capital milestones span 78 months, based on 260 working days/year and 30 pre NTP working days. Conditional first/full network opening is month 40/76, including the separate three-month line commissioning allowance. Opening-weighted demand and the 25% fixed / 75% variable OPEX proxy require a surveyed phase-specific plan. Factory sizing and its explicit capital increase are included in the new monthly and six-month financing schedules; rates, physical qualification and delivery risk remain open.

The factory's final fleet margin is only 8 working days; test-path throughput margin is 47.90%. The [frozen-resource delivery and financing study](#) separates civil productivity from investment timing: a 1.0 cycle multiplier preserves the complete baseline schedule, faster cycles retain the rephased start floors, and earliest construction is a separate comparison. Removing spending delays at unchanged productivity must not be called a productivity financing penalty.

Recovery options price extra structural/electrical/composite or coordinated production shifts, hiring/training, supplier expediting and testing, with unchanged cell counts and indexed incremental payroll/nonlabour costs. Testing alone does not improve the 75% availability opening dates; upstream production still limits them. A separate temporary first-article facility sensitivity adds USD 37.450m capital plus support staffing and tests first opening in month 36; permanent acceptance paths, first-article qualification and full line fleets remain required. These options are unquoted deterministic comparisons, not adopted delivery commitments.

Shift compression now excludes fixed curing/bonding/inspection holds and the additional 60-day first-article qualification. The [industrial qualification and funding-gate package](#) adds a metric temporary-site layout, cell tooling/transfer interfaces, quantity-based RFQs reconciled inside the existing USD 35m direct allowance, and ten ERPNext evidence tasks with source-bound measurement templates and authenticated independent result verification. Named owners, measurements, quotations and signatures remain pending.

Funding interruptions halt procurement/construction/production and defer invoices, adding local remobilisation and carrying/prolongation costs. Recovered domestic placement and delayed export credit are conditional on re-placement; permanent refusal has no opening or debt-clearance date, and is never filled by an automatic government or gap-loan replacement. The separate first-section study uses 14.034 km and five actual line-1 stations, 16 already-planned six-car trains at six-minute headways, independent turnbacks/charging/maintenance and USD 29.96m extra capital. Conditional section service is month 36, with surveyed demand and physical acceptance still required; the full 762-train baseline remains unchanged. Earlier small-section fares alone do not establish better finance: the study includes advanced invoices, additional support costs, phase demand deducted from later full-line receipts, and native-currency reserves/debt.

Combined delay-cost cases add extended staffing, supervision, carrying, storage/insurance and construction prolongation allowances without buying baseline crew-months twice. The financial downside ladder tests 30% fewer paid trips, 25% lower retail/advertising receipts, 5% annual invoice escalation, 7% rail OPEX growth, no assumed green/grant/rights enhancements, core rates two percentage points higher and an 8% IQD gap facility limited to IQD 4tn. The joint case leaves IQD 27.732tn cumulative uncovered cash and IQD 4.000tn terminal gap debt. Uncovered cash is a missing funding requirement; it is not an additional government contribution or secured credit. Reported repayment in such a case is conditional on filling that gap. The [physical qualification register](#) remains entirely not demonstrated; no model run supplies measured production/civil evidence or lender commitments.

Scenario	First/full month	Peak IQD gap tn	Interest/fees USD eq bn	Debt cleared month
Baseline	40/76	4.371	4.906	303
Faster civil; retained starts	40/76	4.375	4.907	303
Earliest civil; original cycles	40/76	4.741	5.040	305
Earliest civil; faster cycles	40/76	5.025	5.147	307
75% availability, costed	42/83	4.587	4.971	306
75% availability + test shift	42/83	4.600	4.977	307
75% availability + all stages	40/76	4.495	4.958	305
Temporary first-article facility	36/76	4.323	4.926	302

Scenario	First/full month	Peak IQD gap tn	Interest/fees USD eq bn	Debt cleared month
Combined delays, costed	53/97	5.057	5.080	314
Joint downside	53/97	4.000	14.810	Unfunded

OPENSOURCERAIL

Operations Portal

Baghdad IQ

Local administrator
ADMIN
Sign out

Business operations - ERPNext

Dashboard

Project Twin

Ops Core

QA Gates

Manufacturing

Maintenance

Assets

OCC

Simulator

Back Office

Programme days
1551

Critical work
1032

Order candidates
14323

Pre-NTP actions
49

Planned CAPEX
\$7,168,534,161

ERP submitted / draft POs
Snapshot unavailable

Critical Path and Project Baseline

Revision
twin-55263103a9db1172

Status
planning-digital-twin-not-construction-release

Scheduler
earliest-feasible ready-task dispatch with finite-resource lanes followed by CPM forward/backward pass

Critical tasks
1032

External gates
None unresolved in template graph

ERP task progress
Select or export the matching operating baseline

Export Work

ERP observation
No unambiguous matching snapshot
[Explore city operating twins and ERP execution ...](#)

Schedule-linked Cash Requirements

Export Cashflow

Month	Project days	Requirement	Local	Imported	Cumulative
0	-30--9	\$3,301,107	\$2,805,941	\$495,166	\$3,301,107
1	-8-13	\$8,402,818	\$7,142,395	\$1,260,423	\$11,703,925
2	14-34	\$31,135,442	\$26,465,126	\$4,670,316	\$42,839,368

Baghdad project twin

Original reference capital and procurement origin

Capital scope	USD eq m	Imported USD m	Local USD eq m
civil	3,889.522	583.428	3,306.093
stations	741.900	148.380	593.520
depots	8.000	2.000	6.000
rolling stock	1,280.160	448.056	832.104
solar plant	747.367	336.315	411.052
signalling	23.709	11.854	11.854
charging microgrid	57.800	23.120	34.680
epc overhead	420.076	63.011	357.065
Baghdad plant	323.874	64.775	259.099
Plant EPC	22.671	3.401	19.270
Total Baghdad capital	7,515.079	1,684.341	5,830.738

The city and plant total includes the plant EPC once. Budgets are unquoted planning estimates; land, utilities, taxes/duties, escalation, contingency and accepted depot/site scope require closure. Loan principal repaid later is a financing cashflow, not additional construction CAPEX. Origin shares do not establish citizenship of vendors, employment or lender eligibility.

Original reference financing in USD and Iraqi dinars

Capital source	Currency	Native amount	USD equivalent m
bank credit	IQD	1,558,095,156,281	1,198.535
chinese export credit	USD	842,170,427	842.170
domestic bonds	IQD	4,674,285,468,843	3,595.604
government import cash	USD	842,170,427	842.170
government local cash	IQD	1,347,579,171,993	1,036.599

Government cash totals USD 1.879bn equivalent, exactly 25% of capital. Its USD 842.170m import cash is inside that limit. The same amount of Chinese USD debt covers the other half of imports. Remaining capital sources are IQD. Combined USD capital funding is USD 1.684bn (22.41%); IQD is 77.59%. Only Chinese credit is USD debt, while government also needs USD

cash for downpayments.

Facility	Currency	Rate assumption	Grace months per draw	Amortisation months	Arrangement fee
chinese export credit	USD	5%	48	180	1.0%
domestic bonds	IQD	8%	24	180	0.5%
bank credit	IQD	9%	0	84	1.0%

Bond and bank capital split the residual after government and Chinese credit 75:25. Interest, fees and reserve deposits are funded separately in the cash forecast. A direct 25% capital contribution does not cap sovereign bond liabilities, guarantees or all lifetime public risk. Ministry of Finance issuance powers, sponsor structure, investor mandates, IQD placement capacity, draw availability and creditor consent for city/plant pooling need confirmation. Chinese supplier and lender qualification remains pending. Terms are sensitivities, not loan offers or an approved appropriation.

The capital source table above is the reference allocation. The conditional blended/early repayment case below replaces part of those ordinary bonds with green bonds and adds a climate grant that reduces domestic borrowing. It is a separate capital mix with the same total uses, government cash and Chinese credit; the two tables must not be added together.

Conditional blended capital source	Currency	Native amount	USD equivalent m
government import cash	USD	842,170,427	842.170
government local cash	IQD	1,347,579,171,993	1,036.599
Chinese export credit	USD	842,170,427	842.170
Ordinary IQD bonds	IQD	3,543,041,964,449	2,725.417
Green IQD bonds	IQD	1,106,868,504,393	851.437
Bank capital credit	IQD	1,549,970,156,281	1,192.285
Conditional climate capital grant	IQD	32,500,000,000	25.000

The conditional capital grant replaces USD 25m equivalent of domestic borrowing. Additional development rights and new local operating receipts enter later project cash and are not counted as construction capital a second time. Supplemental gap draws pay financing/OPEX/reserve cash needs and are separate from both capital tables.

Delivery estimate, physical scope and operating establishment

The published original USD 7.515079bn equivalent remains a planning base with 12 explicit unpriced scope categories, not the amount proved sufficient to deliver service. The [delivery reconciliation](#) records quantity/rate/source/currency/price-date/inclusions/exclusions/estimator/uncertainty, depot/storage alternatives, six-car BOM/mass/axle/interfaces/labour/qualification, hourly energy, demand-led fleet requirements and workload/competence. Quotations, price dates and actual accountable appointments remain pending. Existing EPC, factory contingency, training/qualification and train QA/labour are not added twice. Uncalibrated correlated cost/delay quantiles remain separate sensitivities, not approved risk budgets.

The original USD 8m depot allowance does not fund the full current fleet, line-local storage and maintenance requirements. Quantity-based alternatives price storage tracks, points, drainage/access, workshop shells/equipment, line-local inspection/rescue/isolation/quarantine and full depot PV/storage. Gross reference budgets are USD 161.006m for workload bays and USD 168.982m retaining declared bays; land, foundations, utility diversion, installation and overlap with charging/EPC remain open. Their replacement illustrations remove the old allowance once, and neither is adopted into loans or original government funding. The existing failed morning-direction/stabling and conflict-aware access gates remain open.

Annual energy netting supplies no firm hourly charging guarantee. The synthetic hourly owned-solar reference requires 860.2 GWh purchases / USD 86.024m per year, before separately priced wheeling, balancing and connection. It also exposes 2.664 GWh unmet charging, so the assumed service is not fully delivered even with aggregate pooling. Weather, charger queues, feeder rights/outages, storage ageing and actual tariffs require measured per-site replay; these are sensitivity values, not a forecast or silently updated finance allowance. Owned, contracted and hybrid options use the same duty and no export income.

Reference workload cover totals 2,826 operating FTE / USD 37.323m loaded annual pay equivalent, against the original catalogue payroll allowance. Local pay, employer/rest terms and measured task hours remain unaccepted. Recruitment cohorts work backwards through joining, practical assessment/repeats and supervised authorisation; factory production payroll and temporary commissioning are separate. The real pilot roster has zero appointed workers and blocks every slot. Native HR/training/maintenance/manufacturing mappings and the read-only task eligibility preview preserve human work-release authority. Six additional 90-day evidence Tasks carry accountable functions, unquoted closure work budgets and independent exit criteria.

Opening fleet comparisons reduce service supply and require calibrated OD/access/fares and usable corridor/dependency evidence. They do not retain unchanged fares or announce an earlier opening from fewer trains alone. The continuation now reconciles these assumptions into explicit unquoted monthly cash sensitivities. [Current review](#) supersedes the historical 347-month figures; [clean-checkout test bootstrap](#) restores the exact archived operations input.

Latest per-site energy, funding and fare reconciliation

The [new monthly and six-month funding ledgers](#) replace allowances once and preserve the original financing reconstruction exactly. The full-fleet sensitivity has peak supplemental debt IQD 9.517tn, company cash NPV before finance USD -4.376bn, and no debt-clear month. Government is 25% of scenario capital; a separate case fixes its original absolute contribution. Imports retain 50% government USD / 50% Chinese USD loan, with bonds, bank/gap credit and receipts in IQD. Conditional grants, rights receipts, local income and cheap gap lending remain uncommitted; removing the additional income exposes unfunded cash.

Per-site reference energy requires 860.5 GWh imports, exposes 9.2 GWh unserved charging, and prices firm energy services/owned-plant maintenance at USD 128.510m/year. Physical grid and charger upgrades remain unpriced. Buying shortage energy in the financial sensitivity does not provide a physical connection or an accepted timetable. Depot layouts label individual tracks/slots; Iraqi yard-slab mould capacity meets cumulative installation dates at assumed cycles, while plant cost and actual curing/qualification remain open. The 23 child part RFQs sit inside the eight parent allocations; all 26 maintenance intervals, practical lesson cards and rest-limited anonymous slots retain their actual evidence gates.

Battery reserve contributions are already in rolling maintenance. Separate monthly restricted-cash ledgers add only inflation shortfalls at replacement, including in the reduced-fleet opening case, and prohibit spending reserve cash on early bond/loan repayment. Reduced fleet procurement also reduces service receipts; contracted solar moves plant capital to a provider whose resource costs remain visible.

[Installed-site shortage diagnostics](#) separate local PV from wheeled generation and trace every constrained hour. The installed energy/charger throughput case reduces fare and commercial receipts; it is an upper bound until actual charging events and timetable feasibility are accepted. [Development and training mobilisation](#) funds interim authorities from NTP, schedules external teachers, assessors and mentors before opening, and retains absent real appointments and equipment as explicit gates. The reduced-fleet factory replay removes deferred orders and rebuilds finite production queues, preserving expansion-capable plant/depot capital. Opening dates use the later of civil readiness and replayed fleet acceptance, with later dates propagated into all operating cashflows. No earlier receipts or cheaper factory are invented. All integrated sensitivities retain zero dividends; terminal project cash is not audited distributable profit.

Initial base fare IQD	Paid-demand multiplier	44-trip income share	Debt-clear month	Terminal gap IQD tn	Before-finance cash NPV USD bn
1500	0.962	13.4%	405	0.000	-4.076
1750	0.918	15.6%	340	0.000	-3.683
2000	0.882	17.8%	297	0.000	-3.306
2500	0.825	22.3%	244	0.000	-2.590
3000	0.781	26.7%	211	0.000	-1.916

These fare sensitivities retain annual 5% fare/OPEX/income increases and variable pricing, with the existing uncalibrated price elasticity. Debt clearance is conditional on funding placement; a negative company cash NPV persists across these trials. The affordability share uses the historical income proxy, not disposable-income surveys. No higher fare, commercial first-corridor rank, operational release or accepted lease/loan is created by the calculation.

Early deficits and additional financing

The independent flat price reconstruction requires USD 5.963bn gross early additional cash and retains USD 3.662bn later. Their difference is USD 2300.383m net nominal deficit before pricing gap finance. These figures cannot be added to construction capital as though they were new infrastructure. Later revenue cannot fund an earlier payment without a priced and available facility.

The candidate replaces eligible ordinary capital bonds with IQD green debt at 4% plus arrangement and 0.5% annual guarantee charges; it also tests an uncommitted USD 25m equivalent climate grant, USD 300m equivalent net development rights and USD 25m equivalent annual additional net local receipts. A green label alone changes no coupon. Grants replace eligible domestic capital borrowing; guarantees enhance credit rather than provide cash. Supplemental IQD credit at 2% and a 0.5% draw fee is capped at IQD 13tn outstanding, not treated as proven market capacity. All these conditional sources require legal, donor, investor and valuation evidence.

Additional routes to qualify include climate/renewable energy grants or concessional finance, guaranteed IQD on lending, phased green bonds/sukuk, development rights and station land leases, telecom/fibre leases, naming rights, sponsorship, employer travel contracts and carefully priced concessions. Carbon receipts remain unbooked contingent upside. Upfront lease receipts cannot be added while the same future rents remain in revenue. Keep net proceeds after costs and any transferred liabilities; foreign development finance needs confirmed IQD on lending or a priced hedge to preserve the currency structure.

Financing and pricing sensitivity	Peak gap IQD tn	Uncovered IQD tn	Terminal gap IQD tn
blended candidate	7.784	0.000	5.091

Financing and pricing sensitivity	Peak gap IQD tn	Uncovered IQD tn	Terminal gap IQD tn
commercial gap credit	13.000	17.914	13.000
concessional gap credit	9.950	0.000	7.934
fare 5pct flat costs elastic	3.837	0.000	0.000
fare 5pct flat costs fixed demand	3.178	0.000	0.000
fare 5pct opex 5pct	4.256	0.000	0.000
fare 5pct opex 5pct income 2pct	5.439	0.000	0.000
fare 5pct opex 5pct rents indexed	4.071	0.000	0.000
fare 5pct opex 7pct	5.786	0.000	0.000
fixed fare 5pct opex	13.000	9.741	13.000
green concessional only	9.085	0.000	7.363
green label only	0.000	7.751	0.000
unfunded reference	0.000	7.751	0.000
variable fare 5pct opex 5pct	4.028	0.000	0.000
zero cost liquidity bound	7.751	0.000	2.990

Rail, property, energy and industrial financing redesign

The [twelve-case financing redesign](#) tests opening-linked principal, longer civil amortisation, a 15-year total insured green tenor and USD 1bn-equivalent total station rights replacing USD 300m, plus three retained viaduct-rental variants. Separate rail, solar, factory and developer monthly/native-currency accounts cancel PPA payments, train invoices, plant capacity fees and rights transfers on consolidation. The rental variants add a fifth borrower with zero extra operating-gap cap and no unapproved transfers to rail. Six-month placement envelopes and loan-vintage dates accompany every borrower. Fares/kiosks/advertising remain included; no future national order, surplus-power sale or unawarded climate grant services the integrated case.

The integrated sensitivity leaves peak aggregate IQD liquidity of IQD 7.929tn, cumulative missing funding IQD 0.000tn, and resource NPV USD -2.906bn, or USD -3.372bn after unverified public-land opportunity cost. Company cash balances and an assumed credit cap cannot establish bankability. Longer grace still pays interest, and changing finance terms leaves the core unlevered NPV unchanged.

Government remains 25% of the original rail/energy/factory capital. Import cash/Chinese credit still split 50:50 in USD; other credit, equity, fares, rights and payments are IQD. Private property construction is an additional explicitly priced scope, with its own IQD debt and equity. Optional indexed availability payments add public obligations outside the 25% capital limit; resource NPV cancels those government transfers. The combined downside retains delayed openings, weaker fare/nonfare demand, inflation and restricted financing, and adds weaker property sales/rights: IQD 46.788tn remains missing. Fifteen station candidates and six 90-day evidence workstreams have no invented title, valuation, investor term or named owner.

Iraqi mixed joint-stock holding and staged ordinary equity

The [eighteen-case ordinary-equity study](#) proposes a holding company with 100%-owned rail, energy, factory and station-development businesses, including retained viaduct premises. It replaces the prior subsidiary private equity rather than adding it twice. Government's original USD 1.970bn-equivalent cash remains 25% of original capital; converting it into shares creates zero new money. Same-price private subscriptions of USD 500m/1bn/2bn equivalent leave government ownership of 79.0%/65.3%/48.4%. IQD subscriptions, paid share registers, premium/dilution and fees are explicit. A secondary government share sale gives cash to the seller and zero to the company.

The \$1bn primary sensitivity requests six founder calls and a conditional later issue at month 60, with 2% fees. Monthly paid state capital constrains actual settlement; listing at that date is unproven. Against a matched tax-stressed holding reference, peak IQD liquidity falls from 5.404tn to 2.525tn. Domestic principal waits for full-network opening. Subscription failure cannot silently expand agreed six-month capital-credit placements or draw operating rescue for construction: the next unfunded invoice is withheld and no opening is reported. Whole-programme subscription delay and joint downside have separate cash/debt ledgers. Government's USD cash and Chinese USD credit remain the import split; other money remains IQD.

The \$1bn case's illustrative private equity return is 2.75% nominal IRR, below the assumed 15% hurdle, with first dividend at month 323. Dividends require profit, cleared debt, intact reserves and no missing cash; shares have no guaranteed redemption. Tax, depreciation, property inventory, factory impairment, retained earnings and internal-charge eliminations reconcile in pro-forma accounts. The base tax sensitivity avoids assumed group loss relief; a separate aggregate-profit proxy is explicitly unqualified. Resource NPV after land remains USD -3.372bn; changing financing does not create additional resources or financial feasibility.

Current Iraqi corporate/admission rules require an accepted mandate, legal/capital approvals, eligible audited business/accounts and actual investors. The 2019 liabilities restriction also needs entity-level assessment: the consolidated screening proxy flags 209 months in the \$1bn sensitivity. The structure therefore needs capitalisation/legal resolution before

execution. Incorporated status, listing approval, public-land equity valuation and independent audit are all absent. Six additional source-bound ERP evidence packages cover legal/tax, mandate, subscriptions, accounts, governance and admission. Open licences are retained; no exclusive design valuation, national train order or uncontracted export income is assumed.

Retained premises beneath suitable viaducts

The [commercial-space register](#), [open unit plan](#), [pilot and rental model](#) links 497 elevated segments / 260.1474 km to civil chainage, planning coordinates and existing track assets. A preliminary 25 m bay screen reserves approaches, support inspection zones and independent access, suggesting 873,810 m². Confirmed eligible area remains zero: surveyed height/footprint, ownership, street/utility access, fire/flood/impact protection and station-sale overlap are unaccepted. The 200,000 m² illustration has 0 m² unmapped and supplies no integrated lease cash. A 30-unit draft pilot and reusable independent 30 m² enclosure have no invented tenant, permit or live contract.

The medium 100,000 m² scenario adds USD 87.523m equivalent of indexed fit-out capital. Leasing follows civil/rail readiness, rent-free periods, occupancy ramp, tenant turnover and arrears. Occupied/vacant maintenance, insurance, 12-year refurbishment, depreciation and tax are visible. Security deposits are liabilities backed by restricted cash; they supply no revenue, capital or dividends. Existing kiosks are unchanged and station buildings assumed sold cannot also generate rent. Additional under-viaduct land/rights cost is unverified; no free land value is asserted.

Before-tax incremental rental resource NPV is USD 19.166m, with the lower-rent/prolonged-vacancy case USD -38.539m. In the wholly owned \$1bn holding case, medium rents give private nominal IRR 3.00%, first dividend month 323 and peak IQD liquidity 2.555tn. Recurring rent adds value only after its resources/costs; it does not close the multibillion-dollar financial deficit.

The independent lender-policy comparison allows annual dividends with at least 1.30 historical/projected debt coverage, positive profit, completed capital, intact operating/tax/forward-service/renewal reserves and conservative leverage. These terms are unapproved and do not produce earlier distributions under the current tested assumptions: the non-rental first dividend remains month 323. A separately labelled final-cash diagnostic leaves actual accounts unchanged: proportional unrestricted terminal cash raises the original \$1bn private IRR from 2.75% to 4.07%, with no guaranteed redemption, unvalued asset sale or quoted share-exit price.

Each pilot unit carries lease/meter/inspection/use fields, civil-parent links and five common physical hazard paths. Tenant fire, flooding, impact, blocked bearing/inspection access and utility faults can affect piers, spans and railway operation; controller redundancy provides no mitigation for these hazards. Six additional native ERP evidence drafts require actual site, civil/fire, market, quote, maintenance/lease and finance evidence before occupancy or construction release.

Passenger fares and other operating income

Base model average paid trip yield is IQD 1,317. At full steady operation, existing fares contribute IQD 547.335bn/year, shops/kiosks IQD 11.542bn and advertising IQD 17.932bn. These already reduce the funding gap. Rental occupancy is 88%, advertising 85%; prices, collection and customer demand are not verified Baghdad lease quotations. Commercial figures are gross receipts, with dedicated concession costs requiring appraisal.

Low capacity use assumes 1,138,320 paid trips/day, not unique travellers or a demand survey. The proposed fare design should evaluate concession funding, student and low income access, commuter caps, transfer integration, peak/off peak tiers and collection costs before adopting a tariff. Neither a fare increase nor future kiosk rent places the early financing by itself.

The base full network operating allowance totals USD 192.579m/year equivalent, before the separate inflation sensitivities. Existing maintenance includes a battery renewal reserve on a 12 year reference cycle and fixed asset renewal allowances; it is not an accepted lifecycle replacement plan. Do not add the same battery reserve as new CAPEX. Condition based renewal quantities, inflation, dedicated concession costs, tax and supplier maintenance terms need qualification.


Base steady annual OPEX	USD equivalent m
civil station depot maintenance	92.788
labour	36.188
residual grid energy	0.000
rolling stock maintenance including battery renewal reserve	51.206
signalling maintenance	1.185
solar plant maintenance	11.211

Annual ticket increases and OPEX inflation

The requested paired sensitivity indexes fares, OPEX and income 5% annually from financial close. No tickets are sold before opening. Nominal average fares are IQD 1,525 at first opening and IQD 1,765 at full opening. With 5% income growth, 44 trips remain 11.7% of the income proxy. With only 2% income growth that burden reaches 13.96% at full opening and the assumed real price elasticity reduces paid trips.

Variable pricing tests 40% of baseline trips at 1.25 times the standard fare and 60% at 0.90 times it, with separate demand response and the same capacity limit. If OPEX grows 7% while fares/income grow 5%, the model leaves IQD 0.000tn uncovered cash and IQD 0.000tn terminal unpaid gap debt. This sensitivity still needs additional financing before later surpluses; repayment remains conditional on that funding being available. Existing rent is flat unless the rental indexation sensitivity is chosen; new net rights/receipt targets are held nominal.

The paired case's unlevered NPV is USD -3.262bn at 13.4% nominal discount, excluding new grant/rights/net income targets and with un-escalated capital. Paying debt under a nominal model is not evidence of positive discounted project value. CAPEX escalation, renewal inflation, future FX, floating rates and surveyed demand remain material appraisal work.

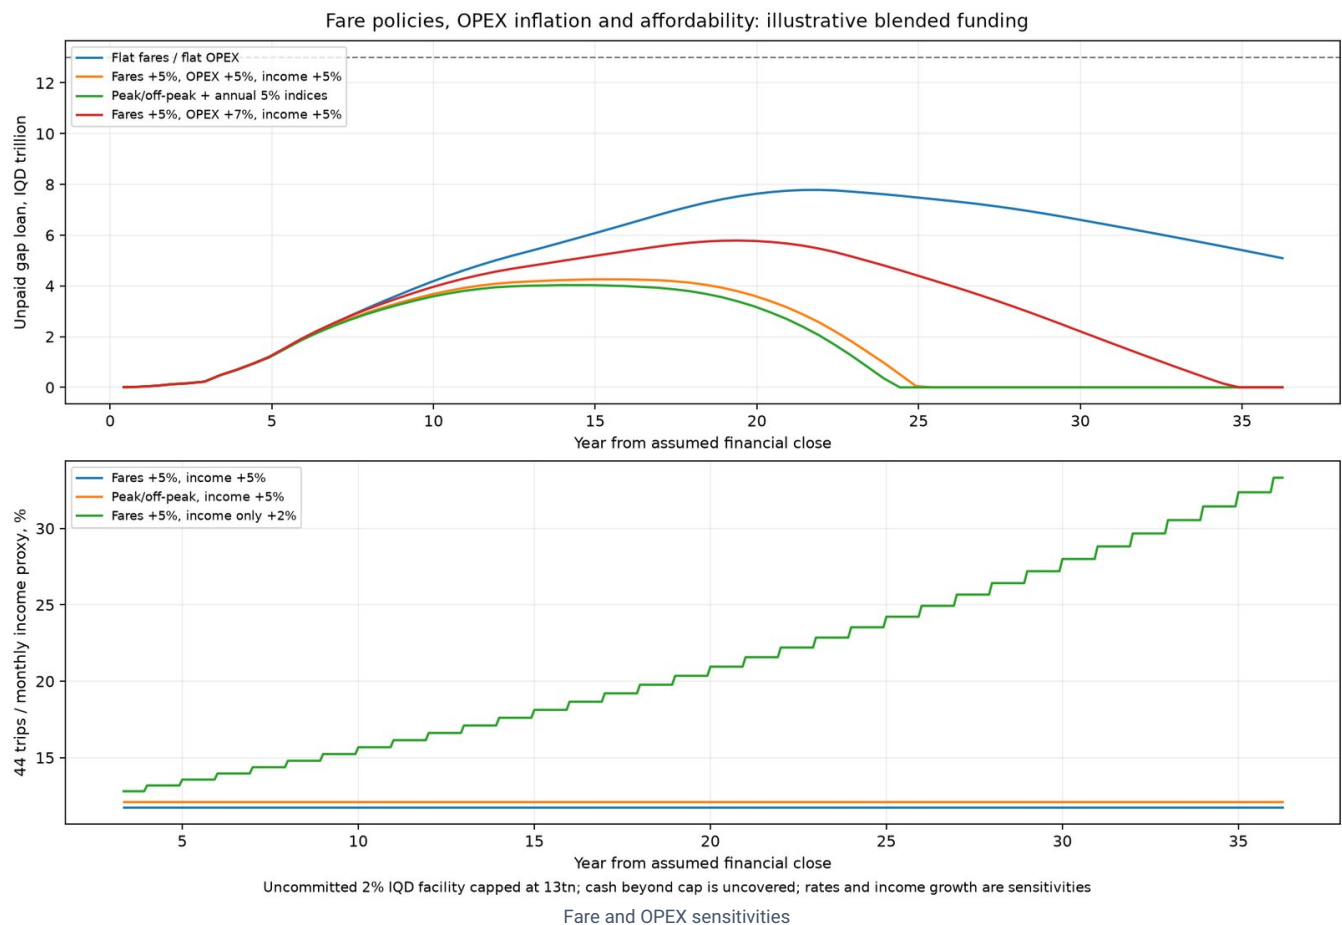

Surplus cash and early debt retirement


Surplus first pays OPEX, scheduled principal, interest and fees, then debt service reserves and three months of current OPEX. Voluntary payments cannot be funded by a new gap draw or uncovered cash in the same month. All comparisons below use the same buffers and 5% fare/OPEX/income inputs. Scheduled and voluntary principal are deducted once from native balances.

Repayment policy	All debt cleared month	Net saving vs buffered gap only USD eq m	Premium USD eq m
cost priority	303	168.132	21.169
cost priority noncallable bonds	365	71.442	4.683
cost priority zero premium	303	195.771	0.000
gap only buffered	365	0.000	0.000
gap then core	306	9.839	1.572
loans then bonds	305	81.916	6.310

Cost priority retires bank credit, ordinary bonds, Chinese credit, green bonds, then cheaper gap credit. Under assumed contractual rights it saves USD 168.132m equivalent after premiums and clears debt in month 303 versus 365 for buffered

gap only. Loans first saves USD 81.916m. All retain IQD 0.362tn operating buffer at the horizon.


Premiums assume 1% bank/Chinese/green and 2% ordinary bonds, with minimum draw ages 6/12/24 months respectively. Eligible vintages are oldest first, retaining instalments and shortening maturity. Calls, notice, compensation, tax and market buyback prices need actual terms. The noncallable case makes no early bond payments; cost ordering is a heuristic rather than a globally best solution. Savings are nominal finance costs, not principal savings or present value wealth. Month numbers run from financial close, with no calendar commencement date assumed.

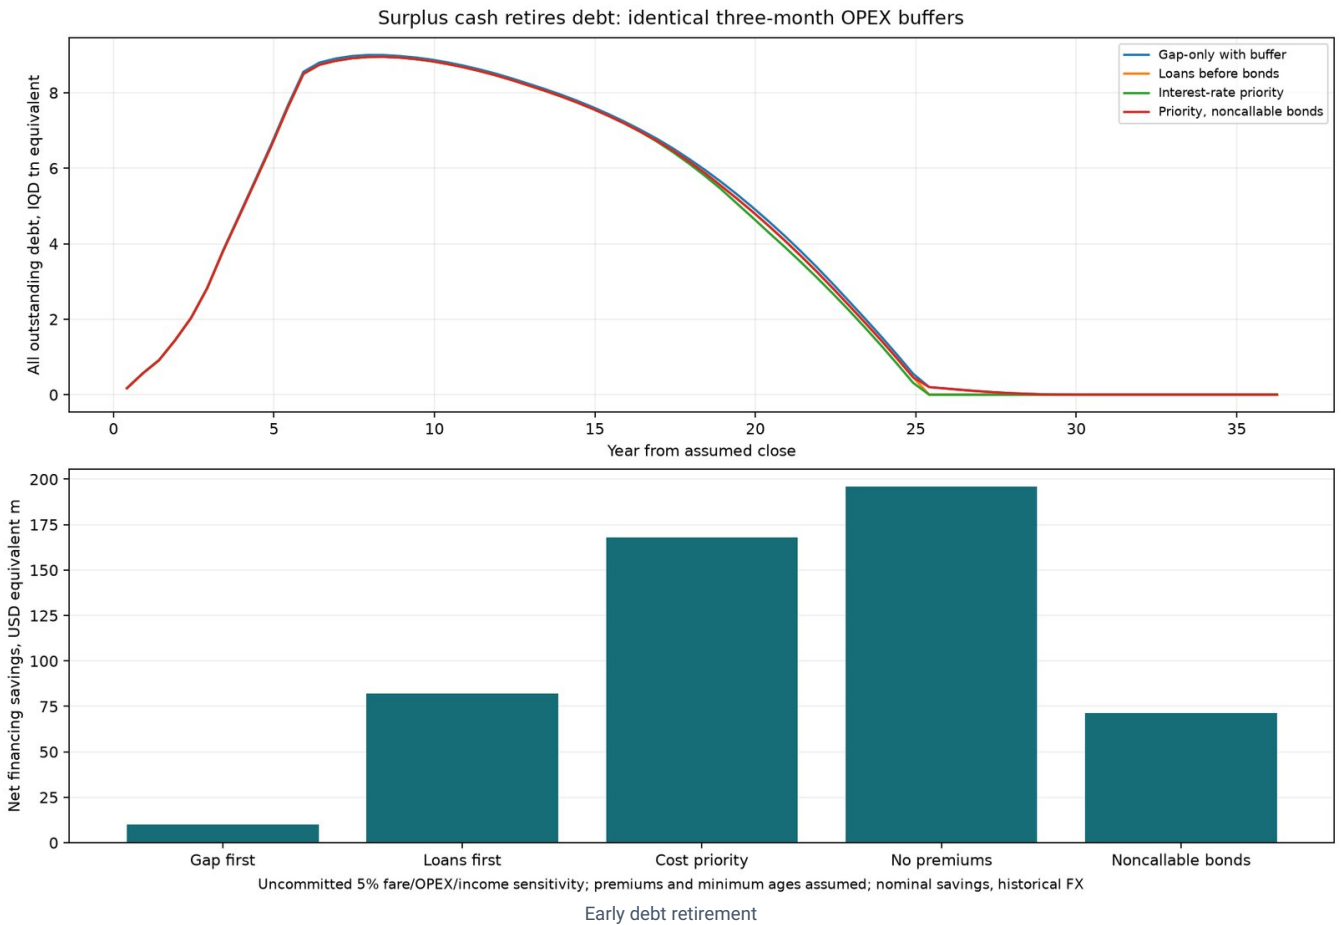

Historical Baghdad metro comparison

Measure	Latest positive-margin local-production Baghdad study	Historical proposal or requested comparator
Route km	474.2	148
Lines / stations	9 / 164	7 / 64
Capital USD equivalent bn	8.145	18.000 reported
Capital USD equivalent m / route km	17.18	121.62
USD capital funding bn	1.942	18.000 requested all USD scenario
Chinese USD debt bn	0.971	Final debt and government split unverified

The July 2024 reported estimate is a historical 148 km, USD 18bn scope. An entirely USD foreign loan/government cash basis is the requested comparator, not a verified financing contract. Under that assumption the latest study's USD capital requirement is 89.2% lower. Distinct scope, price date, tunnelling/structures, land, utilities, qualification and schedule prevent a like for like bid saving claim. Third party fares, actual financing and comparable population access are not established. Its Iraqi labour share cannot be assumed zero. The following retained figure illustrates the original reference allocation; the table above uses the revised study.

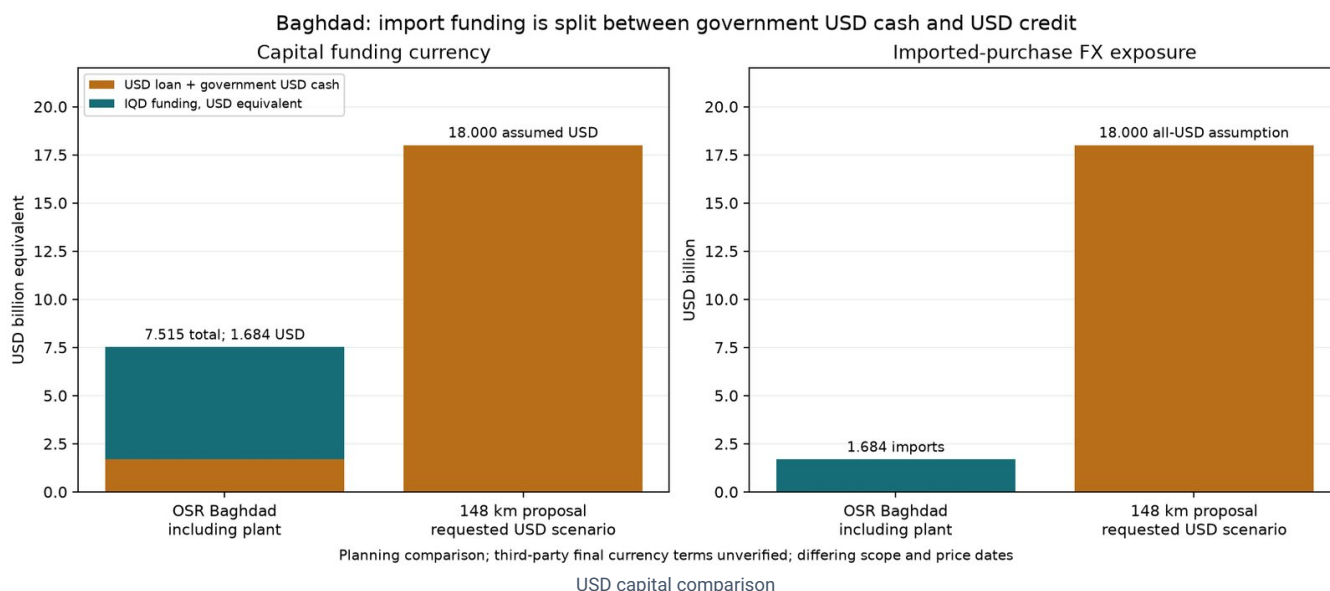

Future national development

Baghdad can establish manufacturing, maintenance, training, procurement and digital delivery capacity that later Iraqi cities can reuse. The existing catalogue contains 18 cities representing 29,491,199 planning residents, 3,652 trainsets and 15,530 vehicle modules across several standard families. These are proposed urban networks; national intercity rail and freight connections are a future feasibility topic, without routes, budgets, revenues or approvals in these totals.

Future catalogue city	Planning population	Fleet family	Route km	Trainsets	City CAPEX USD eq m
Baghdad	9,780,429	metro-6car	474.2	762	7,168.534
Basra	3,955,000	metro-6car	268.0	396	4,733.790
Sulaymaniyah	2,150,000	metro-4car	106.0	121	1,631.553
Erbil	1,952,000	metro-4car	119.2	198	1,661.148
Mosul	1,940,000	metro-4car	190.4	246	3,106.334
Kirkuk	1,780,000	metro-4car	128.0	151	1,968.390
Najaf	1,540,000	metro-4car	140.2	196	2,169.549
Karbala	1,390,000	metro-4car	154.0	188	3,310.017
Nasiriyah	705,000	light-metro-3car	43.0	136	830.408
Hillah	700,000	light-metro-3car	52.3	161	809.252
Amarah	660,000	light-metro-3car	40.9	130	817.343
Ramadi	525,000	light-metro-3car	37.7	118	683.366
Baqubah	470,000	light-metro-3car	52.6	164	850.661
Diwaniyah	440,000	light-metro-3car	38.8	120	653.229
Kut	410,000	light-metro-3car	41.9	131	793.032
Samawah	373,770	light-metro-3car	41.7	133	690.584
Duhok	360,000	light-metro-3car	51.6	162	789.021
Fallujah	360,000	light-metro-3car	43.9	139	697.337

Current catalogue city capital totals sum to USD 33.364bn. Adding one shared factory at USD 769.581m and its EPC at USD 53.871m produces USD 34.187bn equivalent nationally on the catalogue basis. The Baghdad funding reference already contains USD 323.874m of plant and USD 22.671m of plant EPC. The national allowance uses the larger city-order envelope or module allowance. Future scope beyond that Baghdad reference totals USD 26.672bn, including only USD 476.906m of additional shared-plant/EPC allowance, with no second full plant added. Other cities now use current depot and staffing calculations; Baghdad's optional upstream plants remain separate sensitivities. Imported/local procurement in the generic national origin model is USD 7.046bn / USD 27.141bn; this is procurement composition, not a national loan programme.

The additional national plant allowance is an unquoted planning envelope; the actual expansion, renewal and concurrent production programme remain unpriced. Intercity connections, research/training institutions, shared governance and capital acceleration also require separate budgets. Independent city-order factory plans do not prove simultaneous national throughput. The 18 city aggregate is not a five year delivery commitment. Future orders require a throughput/renewal study, scheduled allocation and separate appropriations; no national revenue or profit services Baghdad debt in this proposal.

National industrial and institutional programme

Create common interface standards and supplier quality processes; qualify body, interior and infrastructure suppliers in Iraq; develop local module assembly, battery service, tools, spares and repair capability. A shared apprenticeship and technician programme should cover fabrication, concrete/precast, rail installation, power electronics, charging, software, accessibility and accountable inspection. Set competency outcomes and measured hours before assigning job numbers or training budgets.

Establish a national asset and evidence framework with separate city ownership, budgets, installed configuration and operating approval. Shared procurement and maintenance standards may reduce duplicated development, but each city still needs its own survey, demand, fiscal powers, financial close and safety acceptance. National development should coordinate with existing railways, freight access and universities where feasible; institutional appointments and agreements remain proposed.

Conditional national sequence

Stage	Proposed work	Decision before investment
Baghdad foundation	Sponsor, surveyed first line, plant and six car qualification	Accepted scope, executable finance and physical evidence
Demonstration and repeatability	Prove operating and industrial outcomes; maintain Mosul and Samawah as planning examples	Evidence of safe service, actual cost, production and affordable demand
Next city feasibility	Evaluate regional demand, access, land, energy and local implementation capacity	City specific business case and legal/financial approval
Broader urban rollout	Allocate shared factory output by accepted opening dates; qualify family differences	Priced capacity expansion, renewal and approved city finance
Intercity and national services	Study railway interfaces, freight/logistics, training and shared standards	New scope, environmental approvals and independently funded appraisal

Mosul and Samawah are useful reference packages; their inclusion here is not a selected construction order. Basra, Erbil, Sulaymaniyah and the other cities require transparent prioritisation from actual need and readiness. Future national borrowing shares and USD/IQD exposure must be recalculated from each qualified import basket. Baghdad's 25% contribution and 50:50 import split are not silently imposed on future city budgets.

Ownership and decisions requested

The proposed public sponsor should establish the legal project vehicle and accountable budget authority. The city/operator should own demand, fares, service and operating competence. Manufacturing management should own supplier interfaces, tooling, work hours and first article evidence. Independent survey, civil, energy and safety assessors should control their acceptance evidence. Lenders and placement advisers should validate rights, currency, timing, fees and investor capacity. These are proposed functions, not appointments.

Commission a phased Baghdad feasibility package that closes the route, station, depot and energy scope, independently verifies demand and affordable fares, prices capital and lifecycle obligations, and obtains term sheets for the USD import and IQD domestic funding. Review the long production schedule and fund any acceleration explicitly. Present the accepted first phase to the sponsor and competent authorities before construction. Maintain the national chapter as a separately approved development framework.

Current Baghdad deployment gates

Gate	Status	Responsible function	Closure action
soil-desktop-inputs	closed	civil/geotechnical designer	Sample current station and civil geometry from the pinned soilDB source and retain means, uncertainty and nodata.
soil-coverage	open	geotechnical investigator	Fill mapped coverage gaps through local records and targeted sampling; keep estimated and measured records distinct.
control-processing	open	survey team	Receive survey control observations; process and check the project CRS, datum and residuals.
ground-model	open	survey team	Receive and inspect the terrain, point cloud and ground-model deliveries against independent control.
surveyed-alignment	open	alignment designer	Replace or confirm generated geometry with checked survey alignment and platform reconciliation.
route-station-fit	open	civil/station designer	Resolve utilities, land/access, flood levels, station access and construction staging against the current route.
drainage-ground	open	civil/geotechnical designer	Use the soil investigation plan to collect local geotechnics and groundwater, size foundations/treatment, and check drainage with local rainfall and surveyed levels.
structural-release	open	structural designer and checker	Complete route-specific support/span, foundation, movement and erection calculations and close checking comments.
model-timing-comparison	closed	simulation engineer	Reconcile current native reference journey times with SUMO using the same scenario dwells and route.
full-service-validation	closed	simulation engineer	Run current nominal and degraded full-service cases against the current scenario and simulator; retain failures and exact provenance.
operating-release	open	operator	Complete conflict-aware capacity and degraded-operation review and sign the bound operating evidence.
morning-fleet-allocation	open	service planner	Reconcile revenue fleet with required morning departures on each line; retain two station berths and same-line overflow storage.
continuous-stabling-replay	open	simulation engineer	Run the selected line-local station/depot candidate across consecutive evenings and synchronised morning starts.
stabling-physical-fit	open	track/station designer	Locate usable station and line-local depot tracks, shared charging, isolation, inspection access and protected morning release slots.
solar-storage-endurance	open	energy designer	Bind declared station/ROW/dedicated PV to site storage and actual charging duty, reconcile conversion losses and prove replenishment across adverse weather; specify residual backup duty explicitly.
depot-placement-and-budget	open	depot and cost designer	Place the declared PV/storage inventory within the controlled site layout and reconcile itemised installed costs and renewal scope with existing allowances.
workforce-duty-and-workload	open	city operating lead	Reconcile the funded role plan with named shift/leave cover, measured inspection and cleaning workloads, simultaneous service-depot arrivals and actual local employment inputs.

3 checks are closed and 14 deployment gates remain open. Manufacturing, system certification and donor/lender decisions have additional distinct gates. The Baghdad package is complete as a planning example and has operational release false. Synthetic simulation, generated registers and documentary completeness are not physical acceptance.

Detailed schedules and source appendices

The [detailed engineering plan](#) and [component register](#) expand Baghdad's six-car mechanical interfaces, civil works, Iraqi slab manufacture, missing parts, onboard power/wiring, software host allocation and ERP handover. The register carries 69 reference part rows and all 60 Rust software allocations, with unknown prices and supplier identities left open. It corrects the ST6 seat layout and electronics interface errors; it does not release shop drawings or add unpriced components to the accepted finance totals. Local ERP recovery and planning-contract checks are recorded separately from production readiness.

The following proposal annex prints every station, interchange, fleet role, energy site and the complete cost priority six month draw/repayment schedule. Civil segment chainages and junction details are in the attached registers and design. Full monthly

and alternative case ledgers remain in the supporting archive and repository. Technical annexes reproduce the city survey, ground, alignment, depot, stabling, delivery, deployment, finance and acceptance reports, followed by the current shared architecture and engineering references.

[Source inventory](#) and [publication manifest](#) identify exact inputs and outputs. [Supporting data archive](#) includes the controlled files and complete operations payload. The editable proposal, PDF and appendix source list can be regenerated with the repository's proposal builder.

External instrument and historical sources are retained from the financing baseline. Source retrieval attempts on 3 October 2026 for China Exim, the GCF Iraq page and the NIC notice returned a timeout or access denial; this proposal does not claim a new source verification or a new lending commitment. Detailed financing reports retain the original source URLs and their stated evidence limits.

Baghdad detailed schedules

Source: <cities/catalogue/west-asia/Iraq/Baghdad/DETAILED-SCHEDULES.md>

Station register

Coordinates and chainages are planning inputs. IDs are controlled; anchor names remain in the UTF-8 CSV rather than being adopted as public station names. Latitude/longitude are WGS84 degrees.

Station ID	Line	Chainage km	Latitude	Longitude	Platform m
line-1-2500-0775-s000000	line-1	0.000	33.049995	44.366651	121.0
line-1-2343-0771-s003515	line-1	3.515	33.078249	44.365791	121.0
line-1-2180-0774-s007014	line-1	7.014	33.107584	44.366436	121.0
line-1-2017-0784-s010529	line-1	10.529	33.136918	44.368585	121.0
line-1-1848-0797-s014034	line-1	14.034	33.167333	44.371379	121.0
line-1-1702-0808-s017045	line-1	17.045	33.193608	44.373743	121.0
line-1-1553-0819-s020413	line-1	20.413	33.220423	44.376106	121.0
line-1-1422-0822-s023058	line-1	23.058	33.243998	44.376751	121.0
line-1-1273-0825-s026063	line-1	26.063	33.270813	44.377396	121.0
line-1-1124-0828-s029068	line-1	29.068	33.297628	44.378040	121.0
line-1-0975-0831-s032084	line-1	32.084	33.324443	44.378685	121.0
line-1-0826-0834-s035089	line-1	35.089	33.351258	44.379330	121.0
line-1-0677-0837-s038094	line-1	38.094	33.378073	44.379975	121.0
line-1-0528-0840-s041099	line-1	41.099	33.404888	44.380619	121.0
line-1-0382-0837-s044110	line-1	44.110	33.431163	44.379975	121.0
line-1-0260-0833-s046583	line-1	46.583	33.453119	44.379115	121.0
line-1-0166-0866-s049067	line-1	49.068	33.470036	44.386206	121.0
line-2-1987-2192-s000000	line-2	0.000	33.142317	44.671157	121.0
line-2-1895-2056-s003494	line-2	3.494	33.158874	44.641931	121.0
line-2-1800-1920-s007001	line-2	7.001	33.175971	44.612706	117.0
line-2-1648-1703-s012612	line-2	12.612	33.203326	44.566074	121.0
line-2-1550-1543-s017049	line-2	17.049	33.220962	44.531690	121.0
line-2-1504-1477-s018832	line-2	18.832	33.229241	44.517507	121.0
line-2-1471-1434-s020071	line-2	20.071	33.235180	44.508267	121.0
line-2-1390-1326-s023089	line-2	23.090	33.249757	44.485058	121.0
line-2-1310-1220-s026095	line-2	26.095	33.264154	44.462279	121.0
line-2-1228-1112-s029098	line-2	29.098	33.278912	44.439071	121.0
line-2-1147-1006-s032100	line-2	32.100	33.293489	44.416292	121.0
line-2-1065-0897-s035123	line-2	35.123	33.308246	44.392868	121.0
line-2-0985-0791-s038129	line-2	38.129	33.322643	44.370089	121.0
line-2-0903-0683-s041132	line-2	41.132	33.337401	44.346881	121.0
line-2-0819-0573-s044239	line-2	44.239	33.352518	44.323242	121.0
line-2-0741-0469-s047164	line-2	47.164	33.366555	44.300893	121.0
line-2-0670-0367-s050001	line-2	50.001	33.379333	44.278974	121.0
line-2-0595-0296-s052851	line-2	52.851	33.392830	44.263716	121.0
line-3-2271-1120-s000000	line-3	0.000	33.091207	44.440790	121.0
line-3-2129-1197-s003513	line-3	3.513	33.116762	44.457337	117.0
line-3-1987-1220-s007007	line-3	7.007	33.142317	44.462279	117.0
line-3-1854-1179-s010503	line-3	10.503	33.166253	44.453469	117.0
line-3-1702-1235-s014007	line-3	14.007	33.193608	44.465503	121.0
line-3-1613-1236-s015796	line-3	15.796	33.209625	44.465718	121.0
line-3-1502-1252-s018148	line-3	18.148	33.229601	44.469156	121.0
line-3-1367-1288-s021170	line-3	21.170	33.253896	44.476892	121.0
line-3-1231-1323-s024180	line-3	24.180	33.278372	44.484413	121.0
line-3-1096-1359-s027190	line-3	27.190	33.302667	44.492150	121.0
line-3-0962-1395-s030191	line-3	30.191	33.326783	44.499886	121.0
line-3-0827-1430-s033205	line-3	33.205	33.351078	44.507407	121.0
line-3-0691-1466-s036223	line-3	36.223	33.375553	44.515143	121.0
line-3-0628-1483-s037624	line-3	37.624	33.386891	44.518797	121.0
line-3-0556-1502-s039233	line-3	39.233	33.399849	44.522880	121.0
line-3-0465-1526-s041263	line-3	41.264	33.416226	44.528037	121.0
line-3-0378-1545-s043281	line-3	43.281	33.431883	44.532120	121.0
line-3-0288-1607-s046283	line-3	46.282	33.448080	44.545444	121.0
line-3-0151-1637-s049496	line-3	49.496	33.472735	44.551890	121.0

Station ID	Line	Chainage km	Latitude	Longitude	Platform m
line-4-0146-0199-s000000	line-4	0.000	33.473635	44.242872	121.0
line-4-0298-0305-s004261	line-4	4.261	33.446280	44.265650	121.0
line-4-0395-0433-s007765	line-4	7.765	33.428823	44.293157	117.0
line-4-0420-0570-s011272	line-4	11.272	33.424324	44.322598	117.0
line-4-0491-0706-s015030	line-4	15.030	33.411547	44.351823	121.0
line-4-0569-0798-s017763	line-4	17.763	33.397509	44.371594	121.0
line-4-0644-0884-s020327	line-4	20.326	33.384012	44.390075	121.0
line-4-0731-0987-s023342	line-4	23.341	33.368355	44.412209	121.0
line-4-0818-1088-s026352	line-4	26.352	33.352698	44.433913	121.0
line-4-0906-1190-s029379	line-4	29.378	33.336861	44.455832	121.0
line-4-0993-1292-s032385	line-4	32.385	33.321204	44.477752	121.0
line-4-1080-1393-s035395	line-4	35.395	33.305547	44.499456	121.0
line-4-1144-1468-s037613	line-4	37.613	33.294029	44.515573	121.0
line-4-1210-1544-s039856	line-4	39.856	33.282151	44.531905	121.0
line-4-1246-1628-s042068	line-4	42.068	33.275672	44.549956	121.0
line-5-1199-0260-s000000	line-5	0.000	33.284131	44.255980	121.0
line-5-1170-0351-s002077	line-5	2.077	33.289350	44.275536	121.0
line-5-1128-0422-s003974	line-5	3.974	33.296908	44.290793	121.0
line-5-1105-0514-s006016	line-5	6.016	33.301047	44.310563	121.0
line-5-1070-0649-s009029	line-5	9.029	33.307346	44.339574	121.0
line-5-1036-0785-s012031	line-5	12.031	33.313465	44.368800	121.0
line-5-1001-0920-s015033	line-5	15.033	33.319764	44.397811	121.0
line-5-0967-1056-s018034	line-5	18.034	33.325883	44.427037	121.0
line-5-0932-1191-s021036	line-5	21.036	33.332182	44.456047	121.0
line-5-0897-1326-s024049	line-5	24.049	33.338480	44.485058	121.0
line-5-0863-1462-s027063	line-5	27.063	33.344599	44.514284	121.0
line-5-0853-1593-s029915	line-5	29.915	33.346399	44.542435	121.0
line-5-0781-1759-s034077	line-5	34.077	33.359356	44.578108	117.0
line-5-0740-1905-s037585	line-5	37.585	33.366735	44.609482	117.0
line-5-0803-2052-s041080	line-5	41.080	33.355397	44.641072	117.0
line-5-0677-2304-s047321	line-5	47.321	33.378073	44.695225	121.0
line-6-2322-0251-s000000	line-6	0.000	33.082029	44.254046	121.0
line-6-2194-0355-s003511	line-6	3.511	33.105064	44.276395	117.0
line-6-2069-0472-s007016	line-6	7.016	33.127560	44.301538	117.0
line-6-1936-0575-s010529	line-6	10.529	33.151496	44.323672	117.0
line-6-1813-0699-s014028	line-6	14.028	33.173631	44.350319	117.0
line-6-1694-0774-s017029	line-6	17.029	33.195047	44.366436	121.0
line-6-1580-0848-s020342	line-6	20.342	33.215563	44.382338	121.0
line-6-1483-0909-s023078	line-6	23.078	33.233020	44.395447	121.0
line-6-1379-0987-s026086	line-6	26.086	33.251737	44.412209	121.0
line-6-1264-1073-s029098	line-6	29.098	33.272433	44.430690	121.0
line-6-1150-1158-s032106	line-6	32.106	33.292949	44.448956	121.0
line-6-1047-1235-s035108	line-6	35.108	33.311485	44.465503	121.0
line-6-0932-1321-s038132	line-6	38.132	33.332182	44.483984	121.0
line-6-0817-1407-s041145	line-6	41.145	33.352878	44.502465	121.0
line-6-0713-1485-s044164	line-6	44.164	33.371594	44.519226	121.0
line-6-0647-1587-s047165	line-6	47.166	33.383472	44.541146	121.0
line-6-0495-1669-s052503	line-6	52.503	33.410827	44.558767	121.0
line-7-1069-2206-s000000	line-7	0.000	33.307526	44.674166	121.0
line-7-1073-2033-s003493	line-7	3.493	33.306806	44.636989	117.0
line-7-1102-1872-s007005	line-7	7.005	33.301587	44.602391	117.0
line-7-1185-1622-s012693	line-7	12.693	33.286650	44.548667	121.0
line-7-1206-1546-s014599	line-7	14.599	33.282871	44.532335	121.0
line-7-1238-1464-s016516	line-7	16.516	33.277112	44.514714	121.0
line-7-1276-1329-s019531	line-7	19.531	33.270273	44.485703	121.0
line-7-1313-1195-s022541	line-7	22.541	33.263614	44.456907	121.0
line-7-1351-1061-s025559	line-7	25.559	33.256776	44.428111	121.0
line-7-1389-0926-s028574	line-7	28.574	33.249937	44.399100	121.0
line-7-1426-0792-s031584	line-7	31.584	33.243278	44.370304	121.0
line-7-1444-0727-s033033	line-7	33.033	33.240039	44.356336	121.0
line-7-1464-0658-s034590	line-7	34.590	33.236440	44.341508	121.0
line-7-1497-0538-s037275	line-7	37.275	33.230501	44.315721	121.0
line-7-1531-0418-s039957	line-7	39.957	33.224382	44.289934	121.0

Station ID	Line	Chainage km	Latitude	Longitude	Platform m
line-8-2231-1783-s000000	line-8	0.000	33.098405	44.583265	121.0
line-8-2175-1647-s003504	line-8	3.504	33.108484	44.554039	117.0
line-8-2045-1565-s007016	line-8	7.016	33.131879	44.536418	117.0
line-8-1940-1488-s010527	line-8	10.527	33.150776	44.519871	117.0
line-8-1857-1362-s014032	line-8	14.032	33.165713	44.492794	117.0
line-8-1751-1233-s017689	line-8	17.689	33.184789	44.465073	117.0
line-8-1645-1094-s021347	line-8	21.347	33.203866	44.435203	121.0
line-8-1525-0991-s024765	line-8	24.765	33.225462	44.413068	121.0
line-8-1423-0898-s027774	line-8	27.774	33.243818	44.393083	121.0
line-8-1323-0806-s030783	line-8	30.782	33.261815	44.373313	121.0
line-8-1224-0715-s033798	line-8	33.798	33.279631	44.353757	121.0
line-8-1125-0623-s036821	line-8	36.821	33.297448	44.333987	121.0
line-8-1026-0532-s039824	line-8	39.824	33.315265	44.314432	121.0
line-8-0948-0460-s042156	line-8	42.156	33.329302	44.298959	121.0
line-8-0851-0373-s045009	line-8	45.010	33.346759	44.280263	121.0
line-8-0785-0290-s047849	line-8	47.849	33.358637	44.262427	121.0
line-9-0678-0582-s000000	line-9	0.000	33.377893	44.325176	121.0
line-9-0552-0632-s003005	line-9	3.005	33.400569	44.335921	121.0
line-9-0492-0740-s006009	line-9	6.009	33.411367	44.359130	121.0
line-9-0558-0854-s009023	line-9	9.023	33.399489	44.383628	121.0
line-9-0566-0985-s012040	line-9	12.040	33.398049	44.411779	121.0
line-9-0559-1126-s015544	line-9	15.544	33.399309	44.442079	117.0
line-9-0625-1270-s019041	line-9	19.041	33.387431	44.473024	117.0
line-9-0619-1393-s022049	line-9	22.049	33.388511	44.499456	121.0
line-9-0628-1483-s024068	line-9	24.068	33.386891	44.518797	121.0
line-9-0647-1607-s027110	line-9	27.110	33.383472	44.545444	121.0
line-9-0875-1578-s032071	line-9	32.071	33.342440	44.539212	121.0
line-9-1185-1622-s039062	line-9	39.062	33.286650	44.548667	121.0
line-9-1246-1628-s040331	line-9	40.331	33.275672	44.549956	121.0
line-9-1427-1526-s046095	line-9	46.095	33.243098	44.528037	121.0
line-9-1503-1477-s048127	line-9	48.127	33.229421	44.517507	121.0
line-9-1611-1368-s053112	line-9	53.112	33.209985	44.494084	117.0
line-9-1613-1218-s056128	line-9	56.128	33.209625	44.461849	121.0
line-9-1645-1094-s058873	line-9	58.873	33.203866	44.435203	121.0
line-9-1664-0923-s063151	line-9	63.151	33.200446	44.398455	117.0
line-9-1580-0848-s065621	line-9	65.621	33.215563	44.382338	121.0
line-9-1512-0785-s067632	line-9	67.632	33.227801	44.368800	121.0
line-9-1444-0727-s069624	line-9	69.624	33.240039	44.356336	121.0
line-9-1363-0647-s072200	line-9	72.200	33.254616	44.339144	121.0
line-9-1322-0517-s075210	line-9	75.210	33.261995	44.311208	121.0
line-9-1217-0443-s078216	line-9	78.216	33.280891	44.295306	121.0
line-9-1190-0372-s079883	line-9	79.883	33.285750	44.280048	121.0
line-9-1128-0422-s081781	line-9	81.781	33.296908	44.290793	121.0
line-9-1032-0449-s084241	line-9	84.241	33.314185	44.296595	121.0
line-9-0948-0460-s086012	line-9	86.012	33.329302	44.298959	121.0
line-9-0889-0468-s087258	line-9	87.258	33.339920	44.300678	121.0
line-9-0819-0573-s090161	line-9	90.161	33.352518	44.323242	121.0

Interchange register

Interchange	Lines	Latitude	Longitude
interchange-000	line-1, line-6	33.194327	44.370089
interchange-001	line-1, line-7, line-9	33.241839	44.364932
interchange-002	line-1, line-9	33.402188	44.382123
interchange-003	line-2, line-9	33.229331	44.517507
interchange-004	line-2, line-7	33.263884	44.459593
interchange-005	line-2, line-9	33.352518	44.323242
interchange-006	line-3, line-9	33.209625	44.463784
interchange-007	line-3, line-6	33.351978	44.504936
interchange-008	line-3, line-6, line-9	33.380233	44.517991
interchange-009	line-4, line-9	33.411457	44.355476
interchange-010	line-4, line-5	33.334521	44.455940
interchange-011	line-4, line-7	33.282511	44.532120
interchange-012	line-4, line-7, line-9	33.281161	44.549312
interchange-013	line-5, line-9	33.287550	44.277792
interchange-014	line-5, line-9	33.296908	44.290793
interchange-015	line-5, line-9	33.344419	44.540823
interchange-016	line-1, line-6, line-9	33.217183	44.380261
interchange-017	line-6, line-9	33.383472	44.543295
interchange-018	line-8, line-9	33.203866	44.435203
interchange-019	line-8, line-9	33.329302	44.298959

Fleet roles

Line	Peak	Rotation	Spare	Cold reserve	Total
line-1	78	0	7	1	86
line-2	91	0	9	1	101
line-3	88	0	8	1	97
line-4	72	0	7	1	80
line-5	78	0	7	1	86
line-6	90	0	9	1	100
line-7	71	0	7	1	79
line-8	81	0	8	1	90
line-9	39	0	3	1	43

Energy site register

Site station	Tier	PV kW	Storage kWh	Grid import kW	Charger kW
line-1-2500-0775-s000000	terminal	300.0	2000.0	3200.0	2000.0
line-1-2343-0771-s003515	standard	300.0	2000.0	2000.0	2000.0
line-1-2180-0774-s007014	standard	300.0	2000.0	2000.0	2000.0
line-1-2017-0784-s010529	standard	300.0	2000.0	2000.0	2000.0
line-1-1848-0797-s014034	standard	300.0	2000.0	2000.0	2000.0
line-1-1702-0808-s017045	interchange	300.0	2000.0	2400.0	2000.0
line-1-1553-0819-s020413	interchange	300.0	2000.0	2400.0	2000.0
line-1-1422-0822-s023058	interchange	300.0	2000.0	2400.0	2000.0
line-1-1273-0825-s026063	standard	300.0	2000.0	2000.0	2000.0
line-1-1124-0828-s029068	standard	300.0	2000.0	2000.0	2000.0
line-1-0975-0831-s032084	standard	300.0	2000.0	2000.0	2000.0
line-1-0826-0834-s035089	major	300.0	2000.0	2400.0	2000.0
line-1-0677-0837-s038094	major	300.0	2000.0	2400.0	2000.0
line-1-0528-0840-s041099	interchange	300.0	2000.0	2400.0	2000.0
line-1-0382-0837-s044110	standard	300.0	2000.0	2000.0	2000.0
line-1-0260-0833-s046583	standard	300.0	2000.0	2000.0	2000.0
line-1-0166-0866-s049067	terminal	300.0	2000.0	3200.0	2000.0
line-2-1987-2192-s000000	terminal	300.0	2000.0	3200.0	2000.0
line-2-1895-2056-s003494	standard	300.0	2000.0	2000.0	2000.0
line-2-1648-1703-s012612	standard	300.0	2000.0	2000.0	2000.0
line-2-1550-1543-s017049	standard	300.0	2000.0	2000.0	2000.0
line-2-1504-1477-s018832	interchange	300.0	2000.0	2400.0	2000.0
line-2-1471-1434-s020071	standard	300.0	2000.0	2000.0	2000.0
line-2-1390-1326-s023089	major	300.0	2000.0	2400.0	2000.0
line-2-1310-1220-s026095	interchange	300.0	2000.0	2400.0	2000.0
line-2-1228-1112-s029098	standard	300.0	2000.0	2000.0	2000.0
line-2-1147-1006-s032100	standard	300.0	2000.0	2000.0	2000.0
line-2-1065-0897-s035123	standard	300.0	2000.0	2000.0	2000.0
line-2-0985-0791-s038129	standard	300.0	2000.0	2000.0	2000.0
line-2-0903-0683-s041132	standard	300.0	2000.0	2000.0	2000.0
line-2-0819-0573-s044239	interchange	300.0	2000.0	2400.0	2000.0
line-2-0741-0469-s047164	standard	300.0	2000.0	2000.0	2000.0
line-2-0670-0367-s050001	standard	300.0	2000.0	2000.0	2000.0
line-2-0595-0296-s052851	depot-main	5000.0	40000.0	12000.0	2000.0
line-3-2271-1120-s000000	terminal	300.0	2000.0	3200.0	2000.0
line-3-1702-1235-s014007	standard	300.0	2000.0	2000.0	2000.0
line-3-1613-1236-s015796	interchange	300.0	2000.0	2400.0	2000.0
line-3-1502-1252-s018148	standard	300.0	2000.0	2000.0	2000.0
line-3-1367-1288-s021170	major	300.0	2000.0	2400.0	2000.0
line-3-1231-1323-s024180	standard	300.0	2000.0	2000.0	2000.0
line-3-1096-1359-s027190	major	300.0	2000.0	2400.0	2000.0
line-3-0962-1395-s030191	major	300.0	2000.0	2400.0	2000.0
line-3-0827-1430-s033205	interchange	300.0	2000.0	2400.0	2000.0
line-3-0691-1466-s036223	interchange	300.0	2000.0	2400.0	2000.0
line-3-0628-1483-s037624	interchange	300.0	2000.0	2400.0	2000.0
line-3-0556-1502-s039233	standard	300.0	2000.0	2000.0	2000.0
line-3-0465-1526-s041263	standard	300.0	2000.0	2000.0	2000.0
line-3-0378-1545-s043281	standard	300.0	2000.0	2000.0	2000.0
line-3-0288-1607-s046283	standard	300.0	2000.0	2000.0	2000.0
line-3-0151-1637-s049496	terminal	300.0	2000.0	3200.0	2000.0
line-4-0146-0199-s000000	terminal	300.0	2000.0	3200.0	2000.0
line-4-0298-0305-s004261	standard	300.0	2000.0	2000.0	2000.0
line-4-0491-0706-s015030	interchange	300.0	2000.0	2400.0	2000.0
line-4-0569-0798-s017763	standard	300.0	2000.0	2000.0	2000.0
line-4-0644-0884-s020327	standard	300.0	2000.0	2000.0	2000.0
line-4-0731-0987-s023342	standard	300.0	2000.0	2000.0	2000.0
line-4-0818-1088-s026352	standard	300.0	2000.0	2000.0	2000.0
line-4-0906-1190-s029379	interchange	300.0	2000.0	2400.0	2000.0
line-4-0993-1292-s032385	major	300.0	2000.0	2400.0	2000.0
line-4-1080-1393-s035395	major	300.0	2000.0	2400.0	2000.0
line-4-1144-1468-s037613	standard	300.0	2000.0	2000.0	2000.0

Site station	Tier	PV kW	Storage kWh	Grid import kW	Charger kW
line-4-1210-1544-s039856	interchange	300.0	2000.0	2400.0	2000.0
line-4-1246-1628-s042068	terminal	300.0	2000.0	3200.0	2000.0
line-5-1199-0260-s000000	terminal	300.0	2000.0	3200.0	2000.0
line-5-1170-0351-s002077	interchange	300.0	2000.0	2400.0	2000.0
line-5-1128-0422-s003974	interchange	300.0	2000.0	2400.0	2000.0
line-5-1105-0514-s006016	standard	300.0	2000.0	2000.0	2000.0
line-5-1070-0649-s009029	major	300.0	2000.0	2400.0	2000.0
line-5-1036-0785-s012031	major	300.0	2000.0	2400.0	2000.0
line-5-1001-0920-s015033	standard	300.0	2000.0	2000.0	2000.0
line-5-0967-1056-s018034	major	300.0	2000.0	2400.0	2000.0
line-5-0932-1191-s021036	interchange	300.0	2000.0	2400.0	2000.0
line-5-0897-1326-s024049	major	300.0	2000.0	2400.0	2000.0
line-5-0863-1462-s027063	major	300.0	2000.0	2400.0	2000.0
line-5-0853-1593-s029915	interchange	300.0	2000.0	2400.0	2000.0
line-5-0677-2304-s047321	terminal	300.0	2000.0	3200.0	2000.0
line-6-2322-0251-s000000	terminal	300.0	2000.0	3200.0	2000.0
line-6-1694-0774-s017029	interchange	300.0	2000.0	2400.0	2000.0
line-6-1580-0848-s020342	interchange	300.0	2000.0	2400.0	2000.0
line-6-1483-0909-s023078	standard	300.0	2000.0	2000.0	2000.0
line-6-1379-0987-s026086	major	300.0	2000.0	2400.0	2000.0
line-6-1264-1073-s029098	major	300.0	2000.0	2400.0	2000.0
line-6-1150-1158-s032106	standard	300.0	2000.0	2000.0	2000.0
line-6-1047-1235-s035108	major	300.0	2000.0	2400.0	2000.0
line-6-0932-1321-s038132	major	300.0	2000.0	2400.0	2000.0
line-6-0817-1407-s041145	interchange	300.0	2000.0	2400.0	2000.0
line-6-0713-1485-s044164	interchange	300.0	2000.0	2400.0	2000.0
line-6-0647-1587-s047165	interchange	300.0	2000.0	2400.0	2000.0
line-6-0495-1669-s052503	terminal	300.0	2000.0	3200.0	2000.0
line-7-1069-2206-s000000	terminal	300.0	2000.0	3200.0	2000.0
line-7-1185-1622-s012693	interchange	300.0	2000.0	2400.0	2000.0
line-7-1206-1546-s014599	interchange	300.0	2000.0	2400.0	2000.0
line-7-1238-1464-s016516	standard	300.0	2000.0	2000.0	2000.0
line-7-1276-1329-s019531	standard	300.0	2000.0	2000.0	2000.0
line-7-1313-1195-s022541	interchange	300.0	2000.0	2400.0	2000.0
line-7-1351-1061-s025559	major	300.0	2000.0	2400.0	2000.0
line-7-1389-0926-s028574	major	300.0	2000.0	2400.0	2000.0
line-7-1426-0792-s031584	interchange	300.0	2000.0	2400.0	2000.0
line-7-1444-0727-s033033	interchange	300.0	2000.0	2400.0	2000.0
line-7-1464-0658-s034590	standard	300.0	2000.0	2000.0	2000.0
line-7-1497-0538-s037275	standard	300.0	2000.0	2000.0	2000.0
line-7-1531-0418-s039957	terminal	300.0	2000.0	3200.0	2000.0
line-8-2231-1783-s000000	terminal	300.0	2000.0	3200.0	2000.0
line-8-1645-1094-s021347	interchange	300.0	2000.0	2400.0	2000.0
line-8-1525-0991-s024765	standard	300.0	2000.0	2000.0	2000.0
line-8-1423-0898-s027774	major	300.0	2000.0	2400.0	2000.0
line-8-1323-0806-s030783	standard	300.0	2000.0	2000.0	2000.0
line-8-1224-0715-s033798	standard	300.0	2000.0	2000.0	2000.0
line-8-1125-0623-s036821	major	300.0	2000.0	2400.0	2000.0
line-8-1026-0532-s039824	standard	300.0	2000.0	2000.0	2000.0
line-8-0948-0460-s042156	interchange	300.0	2000.0	2400.0	2000.0
line-8-0851-0373-s045009	standard	300.0	2000.0	2000.0	2000.0
line-8-0785-0290-s047849	terminal	300.0	2000.0	3200.0	2000.0
line-9-0678-0582-s000000	standard	300.0	2000.0	2000.0	2000.0
line-9-0552-0632-s003005	standard	300.0	2000.0	2000.0	2000.0
line-9-0492-0740-s006009	interchange	300.0	2000.0	2400.0	2000.0
line-9-0558-0854-s009023	interchange	300.0	2000.0	2400.0	2000.0
line-9-0566-0985-s012040	major	300.0	2000.0	2400.0	2000.0
line-9-0619-1393-s022049	standard	300.0	2000.0	2000.0	2000.0
line-9-0628-1483-s024068	interchange	300.0	2000.0	2400.0	2000.0
line-9-0647-1607-s027110	interchange	300.0	2000.0	2400.0	2000.0
line-9-0875-1578-s032071	interchange	300.0	2000.0	2400.0	2000.0
line-9-1185-1622-s039062	interchange	300.0	2000.0	2400.0	2000.0
line-9-1246-1628-s040331	interchange	300.0	2000.0	2400.0	2000.0

Site station	Tier	PV kW	Storage kWh	Grid import kW	Charger kW
line-9-1427-1526-s046095	standard	300.0	2000.0	2000.0	2000.0
line-9-1503-1477-s048127	interchange	300.0	2000.0	2400.0	2000.0
line-9-1613-1218-s056128	interchange	300.0	2000.0	2400.0	2000.0
line-9-1645-1094-s058873	interchange	300.0	2000.0	2400.0	2000.0
line-9-1580-0848-s065621	interchange	300.0	2000.0	2400.0	2000.0
line-9-1512-0785-s067632	standard	300.0	2000.0	2000.0	2000.0
line-9-1444-0727-s069624	interchange	300.0	2000.0	2400.0	2000.0
line-9-1363-0647-s072200	standard	300.0	2000.0	2000.0	2000.0
line-9-1322-0517-s075210	standard	300.0	2000.0	2000.0	2000.0
line-9-1217-0443-s078216	standard	300.0	2000.0	2000.0	2000.0
line-9-1190-0372-s079883	interchange	300.0	2000.0	2400.0	2000.0
line-9-1128-0422-s081781	interchange	300.0	2000.0	2400.0	2000.0
line-9-1032-0449-s084241	standard	300.0	2000.0	2000.0	2000.0
line-9-0948-0460-s086012	interchange	300.0	2000.0	2400.0	2000.0
line-9-0889-0468-s087258	standard	300.0	2000.0	2000.0	2000.0
line-9-0819-0573-s090161	interchange	300.0	2000.0	2400.0	2000.0

Six month capital and supplemental draw requirements

Cost priority with identical three month operating buffers. Settlement is monthly; six month rows are envelopes, not advance placements. Unrounded CSV values reconcile; displayed amounts are rounded. Tranches continue through the entire model horizon.

Months	Gov USD m	Gov IQD bn	China USD m	Ordinary bond IQD bn	Green IQD bn	Bank IQD bn	Gap IQD bn
0 to 5	13.66	37.91	13.66	111.93	0.00	37.31	5.25
6 to 11	33.85	83.24	33.85	253.29	0.00	84.43	18.39
12 to 17	24.72	73.41	24.72	213.37	0.00	71.12	37.55
18 to 23	41.27	105.74	41.27	316.56	1.82	106.13	61.35
24 to 29	63.11	110.25	63.11	307.47	62.31	123.26	72.37
30 to 35	93.45	131.93	93.45	332.13	143.77	158.63	103.40
36 to 41	95.67	132.94	95.67	328.83	153.47	160.77	301.91
42 to 47	96.39	134.48	96.39	332.29	154.82	162.37	217.87
48 to 53	95.10	132.99	95.10	328.05	153.23	160.43	243.17
54 to 59	95.57	133.12	95.57	329.20	153.29	160.83	262.50
60 to 65	94.87	131.37	94.87	325.05	152.18	159.08	328.80
66 to 71	84.17	126.31	84.17	326.91	118.81	148.57	327.96
72 to 77	10.35	13.88	10.35	37.96	13.17	17.04	293.59
78 to 83	0.00	0.00	0.00	0.00	0.00	0.00	251.75
84 to 89	0.00	0.00	0.00	0.00	0.00	0.00	234.85
90 to 95	0.00	0.00	0.00	0.00	0.00	0.00	219.89
96 to 101	0.00	0.00	0.00	0.00	0.00	0.00	206.23
102 to 107	0.00	0.00	0.00	0.00	0.00	0.00	194.74
108 to 113	0.00	0.00	0.00	0.00	0.00	0.00	179.11
114 to 119	0.00	0.00	0.00	0.00	0.00	0.00	163.21
120 to 125	0.00	0.00	0.00	0.00	0.00	0.00	140.74
126 to 131	0.00	0.00	0.00	0.00	0.00	0.00	120.85
132 to 137	0.00	0.00	0.00	0.00	0.00	0.00	99.32
138 to 143	0.00	0.00	0.00	0.00	0.00	0.00	79.07
144 to 149	0.00	0.00	0.00	0.00	0.00	0.00	57.01
150 to 155	0.00	0.00	0.00	0.00	0.00	0.00	37.48
156 to 161	0.00	0.00	0.00	0.00	0.00	0.00	31.99
162 to 167	0.00	0.00	0.00	0.00	0.00	0.00	29.75
168 to 173	0.00	0.00	0.00	0.00	0.00	0.00	21.85
174 to 179	0.00	0.00	0.00	0.00	0.00	0.00	16.02
180 to 185	0.00	0.00	0.00	0.00	0.00	0.00	7.56
186 to 191	0.00	0.00	0.00	0.00	0.00	0.00	1.29
192 to 197	0.00	0.00	0.00	0.00	0.00	0.00	4.17
198 to 203	0.00	0.00	0.00	0.00	0.00	0.00	0.00
204 to 209	0.00	0.00	0.00	0.00	0.00	0.00	0.00
210 to 215	0.00	0.00	0.00	0.00	0.00	0.00	0.00
216 to 221	0.00	0.00	0.00	0.00	0.00	0.00	0.00
222 to 227	0.00	0.00	0.00	0.00	0.00	0.00	0.00

Months	Gov USD m	Gov IQD bn	China USD m	Ordinary bond IQD bn	Green IQD bn	Bank IQD bn	Gap IQD bn
228 to 233	0.00	0.00	0.00	0.00	0.00	0.00	0.00
234 to 239	0.00	0.00	0.00	0.00	0.00	0.00	0.00
240 to 245	0.00	0.00	0.00	0.00	0.00	0.00	0.00
246 to 251	0.00	0.00	0.00	0.00	0.00	0.00	0.00
252 to 257	0.00	0.00	0.00	0.00	0.00	0.00	0.00
258 to 263	0.00	0.00	0.00	0.00	0.00	0.00	0.00
264 to 269	0.00	0.00	0.00	0.00	0.00	0.00	0.00
270 to 275	0.00	0.00	0.00	0.00	0.00	0.00	0.00
276 to 281	0.00	0.00	0.00	0.00	0.00	0.00	0.00
282 to 287	0.00	0.00	0.00	0.00	0.00	0.00	0.00
288 to 293	0.00	0.00	0.00	0.00	0.00	0.00	0.00
294 to 299	0.00	0.00	0.00	0.00	0.00	0.00	0.00
300 to 305	0.00	0.00	0.00	0.00	0.00	0.00	0.00
306 to 311	0.00	0.00	0.00	0.00	0.00	0.00	0.00
312 to 317	0.00	0.00	0.00	0.00	0.00	0.00	0.00
318 to 323	0.00	0.00	0.00	0.00	0.00	0.00	0.00
324 to 329	0.00	0.00	0.00	0.00	0.00	0.00	0.00
330 to 335	0.00	0.00	0.00	0.00	0.00	0.00	0.00
336 to 341	0.00	0.00	0.00	0.00	0.00	0.00	0.00
342 to 347	0.00	0.00	0.00	0.00	0.00	0.00	0.00
348 to 353	0.00	0.00	0.00	0.00	0.00	0.00	0.00
354 to 359	0.00	0.00	0.00	0.00	0.00	0.00	0.00
360 to 365	0.00	0.00	0.00	0.00	0.00	0.00	0.00
366 to 371	0.00	0.00	0.00	0.00	0.00	0.00	0.00
372 to 377	0.00	0.00	0.00	0.00	0.00	0.00	0.00
378 to 383	0.00	0.00	0.00	0.00	0.00	0.00	0.00
384 to 389	0.00	0.00	0.00	0.00	0.00	0.00	0.00
390 to 395	0.00	0.00	0.00	0.00	0.00	0.00	0.00
396 to 401	0.00	0.00	0.00	0.00	0.00	0.00	0.00
402 to 407	0.00	0.00	0.00	0.00	0.00	0.00	0.00
408 to 413	0.00	0.00	0.00	0.00	0.00	0.00	0.00
414 to 419	0.00	0.00	0.00	0.00	0.00	0.00	0.00
420 to 425	0.00	0.00	0.00	0.00	0.00	0.00	0.00
426 to 431	0.00	0.00	0.00	0.00	0.00	0.00	0.00
432 to 435	0.00	0.00	0.00	0.00	0.00	0.00	0.00

Six month early repayments and closing balances

Early principal is additional to the scheduled principal separately retained in the full ledger. Outstanding debt uses the final month of each period. USD equivalent aggregates convert Chinese native debt at the historical IQD 1,300 anchor. Premiums and operating buffers are distinct from principal.

Months	Core early principal USD eq m	Premium USD eq m	Gap principal IQD bn	All debt closing IQD tn eq	Cash closing IQD tn	OPEX buffer IQD bn
0 to 5	0.00	0.00	0.00	0.171	0.000	0.000
6 to 11	0.00	0.00	0.00	0.568	0.000	0.000
12 to 17	0.00	0.00	0.00	0.915	0.000	0.000
18 to 23	0.00	0.00	0.00	1.441	0.000	0.000
24 to 29	27.00	0.27	0.00	2.035	0.000	0.000
30 to 35	36.27	0.36	0.00	2.819	0.000	0.000
36 to 41	31.44	0.31	0.00	3.810	0.000	24.246
42 to 47	18.69	0.19	0.00	4.730	0.000	31.449
48 to 53	13.51	0.14	0.00	5.658	0.000	40.284
54 to 59	11.55	0.12	0.00	6.593	0.000	52.714
60 to 65	0.00	0.00	0.00	7.584	0.000	63.212
66 to 71	0.00	0.00	0.00	8.500	0.000	69.423
72 to 77	0.00	0.00	0.00	8.742	0.000	83.874
78 to 83	0.00	0.00	0.00	8.844	0.000	83.874
84 to 89	0.00	0.00	0.00	8.912	0.000	88.068
90 to 95	0.00	0.00	0.00	8.947	0.000	88.068
96 to 101	0.00	0.00	0.00	8.951	0.000	92.471
102 to 107	0.00	0.00	0.00	8.932	0.000	92.471
108 to 113	0.00	0.00	0.00	8.891	0.000	97.095

Months	Core early principal USD eq m	Premium USD eq m	Gap principal IQD bn	All debt closing IQD tn eq	Cash closing IQD tn	OPEX buffer IQD bn
114 to 119	0.00	0.00	0.00	8.835	0.000	97.095
120 to 125	0.00	0.00	0.00	8.760	0.000	101.949
126 to 131	0.00	0.00	0.00	8.673	0.000	101.949
132 to 137	0.00	0.00	0.00	8.573	0.000	107.047
138 to 143	0.00	0.00	0.00	8.460	0.000	107.047
144 to 149	0.00	0.00	0.00	8.334	0.000	112.399
150 to 155	0.00	0.00	0.00	8.198	0.000	112.399
156 to 161	0.00	0.00	0.00	8.059	0.000	118.019
162 to 167	0.00	0.00	0.00	7.912	0.000	118.019
168 to 173	0.00	0.00	0.00	7.751	0.000	123.920
174 to 179	0.00	0.00	0.00	7.578	0.000	123.920
180 to 185	0.00	0.00	0.00	7.390	0.000	130.116
186 to 191	0.00	0.00	0.00	7.189	0.000	130.116
192 to 197	16.92	0.34	0.00	6.964	0.000	136.622
198 to 203	35.61	0.71	0.00	6.714	0.000	136.622
204 to 209	70.33	1.41	0.00	6.436	0.000	143.453
210 to 215	107.58	2.15	0.00	6.133	0.000	143.453
216 to 221	147.90	2.96	0.00	5.806	0.000	150.626
222 to 227	187.59	3.75	0.00	5.457	0.000	150.626
228 to 233	244.73	3.35	0.00	5.071	0.000	158.157
234 to 239	272.75	2.73	0.00	4.689	0.000	158.157
240 to 245	238.80	2.39	74.78	4.296	0.000	166.065
246 to 251	0.00	0.00	383.61	3.913	0.000	166.065
252 to 257	0.00	0.00	398.87	3.514	0.000	174.368
258 to 263	0.00	0.00	411.25	3.102	0.000	174.368
264 to 269	0.00	0.00	427.36	2.675	0.000	183.087
270 to 275	0.00	0.00	440.44	2.235	0.000	183.087
276 to 281	0.00	0.00	457.44	1.777	0.000	192.241
282 to 287	0.00	0.00	471.27	1.306	0.000	192.241
288 to 293	0.00	0.00	489.21	0.817	0.000	201.853
294 to 299	0.00	0.00	503.81	0.313	0.000	201.853
300 to 305	0.00	0.00	312.96	0.000	0.210	211.946
306 to 311	0.00	0.00	0.00	0.000	0.743	211.946
312 to 317	0.00	0.00	0.00	0.000	1.292	222.543
318 to 323	0.00	0.00	0.00	0.000	1.851	222.543
324 to 329	0.00	0.00	0.00	0.000	2.425	233.670
330 to 335	0.00	0.00	0.00	0.000	3.010	233.670
336 to 341	0.00	0.00	0.00	0.000	3.612	245.354
342 to 347	0.00	0.00	0.00	0.000	4.225	245.354
348 to 353	0.00	0.00	0.00	0.000	4.855	257.621
354 to 359	0.00	0.00	0.00	0.000	5.497	257.621
360 to 365	0.00	0.00	0.00	0.000	6.157	270.502
366 to 371	0.00	0.00	0.00	0.000	6.830	270.502
372 to 377	0.00	0.00	0.00	0.000	7.521	284.027
378 to 383	0.00	0.00	0.00	0.000	8.226	284.027
384 to 389	0.00	0.00	0.00	0.000	8.950	298.229
390 to 395	0.00	0.00	0.00	0.000	9.689	298.229
396 to 401	0.00	0.00	0.00	0.000	10.448	313.140
402 to 407	0.00	0.00	0.00	0.000	11.222	313.140
408 to 413	0.00	0.00	0.00	0.000	12.017	328.797
414 to 419	0.00	0.00	0.00	0.000	12.828	328.797
420 to 425	0.00	0.00	0.00	0.000	13.662	345.237
426 to 431	0.00	0.00	0.00	0.000	14.512	345.237
432 to 435	0.00	0.00	0.00	0.000	15.088	362.499

[Complete civil chainages](#) · [station names and attributes](#) · [junction records](#) · [complete repayment ledger](#)

Baghdad detailed engineering and Iraqi manufacturing plan

Source: cities/catalogue/west-asia/Iraq/Baghdad/DETAILED-ENGINEERING.md

Baghdad uses a six-car, 111 m metro family. The next design stage retains ballastless slab track and expands the civil, mechanical, electronics and software packages into controlled interfaces, parts and manufacturing operations. The [component register](#), [parts CSV](#) and [source-bound JSON](#) contain the calculated city quantities and open supplier positions. These are engineering references; production drawings, surveys, qualified suppliers and operational approvals remain required.

The current city allocation, six-car trainsets, cars, stations, energy sites, bogies and wheelsets are regenerated in the [quantity register](#) from the main design and scenario. Wheelsets are children of complete bogies, not extra purchases. Doors, cooling loops, fixtures, harnesses and equipment repeats are reference allocations that must pass the six-car family review. The detailed three-car LM3 manufacturing package is useful process evidence; it is not a released Baghdad production package and cannot be doubled to obtain qualified six-car interfaces.

Reference architecture and drawing package

The mechanical load path is wheelset to suspension/axlebox to bogie frame to secondary suspension/pivot to car underframe to coupler and body structure. Cladding attaches to the structural frame through controlled service rails and retention features; FRP panels do not replace the primary crash structure. Keep longitudinal crash loads, recovery loads, passenger fixture loads and equipment retention as separate calculation cases with a common drawing revision.

The electrical path is protected charging contact to traction battery/HV junction to inverters/motors and protected auxiliary DC/DC branches. Battery, inverter and motor cooling circuits require a coordinated heat balance. The nominal traction bus is 675 V and normal maximum 740 V; “800 V class” describes a component class, not the normal bus voltage. Coordination must include abnormal/transient limits, insulation monitoring, HV interlocks, precharge, discharge, isolation and emergency disconnect.

Controlled drawing	Required content	Reference data available	Release owner / remaining evidence
BG-M-001 Trainset arrangement	Six-car positions, couplers, gangways, swept and evacuation envelopes	111 m train envelope; six cars; five intercar interfaces; two ends	Rolling-stock authority: exact end/coupler lengths, curve sweep and tolerance stack
BG-M-002 Car structure	Underframe/side/roof members, joints, datums, lift/recovery points	18.5 m average module allocation; geometry is not a cut list	Structures: stress/fatigue/crash, weld map, material thicknesses, distortion and NDT
BG-M-003 Bogie interface	Pivots, spring/air attachments, wheel profile, brake/motor clearances	One powered and one trailer bogie per car reference	Supplier + dynamics authority: axle loads, suspension rates, hunting, curves and brake duty
BG-M-004 Battery and HV bay	Racks, crash retention, isolation, vent paths and removable pack access	225 kWh gross allocation per car; 1,350 gross / 1,080 usable per train	HV/battery authority: actual pack mass/dimensions, fault current, thermal propagation and retention
BG-M-005 Cooling and HVAC	Chiller/radiator/pump, hoses, expansion/bleed, ducts and condensate	Hot-desert 50 °C design ambient	Thermal authority: traction/aux duty, degraded operation, dust and heat rejection
BG-M-006 Door/glazing	Openings, leaves, locks, seals, glazing retention and maintenance access	Two double-leaf openings per side/car reference	Body + accessibility authority: family-specific layout, loading, escape and obstruction
BG-M-007 Harness and connector	Wire/terminal IDs, cavity views, cut lengths, routing, clamps and separation	HV/LV/data service zones; reference host counts	Electrical authority: current/voltage drop, insulation, EMC, connector and supplier pin freeze
BG-M-008 Interior/accessibility	Seats, rails, ramps/steps, lighting, fire barriers and service panels	720 nominal passengers, 120 seats, 960 crush per train	Interior authority: fixture loads, fire/smoke, accessibility and passenger evacuation
BG-C-001 ST6 and slipform section	Concrete geometry, cage, inserts, rail seats, drainage and transitions	Six-metre panel geometry and 20 seats	Track/civil authority: reinforcement, support stiffness, shrinkage, fasteners and actual geotechnical zones
BG-C-002 Viaduct and bridge interfaces	Pi20/Pi25, foundations, bearings, joints, CWR and walkway interfaces	Standard 20/25 m spans; bridge-specific exceptions	Structures: permanent/variable/thermal/seismic/braking, fatigue, scour and foundation release
BG-E-001 End electronics cabinet	Rails, protection, output chain, harness, thermal and enclosure	Corrected T-OBS capacity and exposed Pico bench pins	Electronics authority: actual vendor BOM, schematic, HAL, EMC and injected faults

Use train longitudinal datum X, track centre Y and surveyed rail datum Z for integration. Each supplier drawing must state its own mating datum and tolerance contribution. The track reference gauge is 1,435 mm between the running faces; rail-head width and inclination are needed to convert this into rail-centre/baseplate coordinates. Existing simplified CAD rail-line positions must not be used as drilling coordinates. A platform step/gap or bogie pivot offset copied from LM3 is an unresolved six-car interface until reviewed.

Mechanical manufacturing and missing kit content

Local work can cover steel structure fabrication, service rails, FRP moulding/trim, interiors, mounts, battery enclosures, harness manufacture, pipework and final integration. Initially import complete qualified bogies, motor/inverter packages, cells/qualified packs, safety glazing, doors and electronics where local process and product qualification is absent. A later local-content decision needs supplier drawings/licences, process capability, acceptance tests and economics; local fabrication is not evidence that a safety-critical design is accepted.

Work package	Make/buy and production route	Child content that must be explicit	Verification / hold point
Car frame	Iraqi cut/form/machine/fixture/weld	Plates/sections, brackets, joint preparation, isolation, drains and finish	Released datum/fixture, WPS, weld/NDT, dimensional and load inspection
FRP skin	Iraqi mould/layout/cure/trim/fit	Resin/fibre/core, inserts, retention clips, edge seals and fire-compatible finish	Laminate/fire/smoke, cure coupon, insert pullout and panel retention
Bogie	Complete supplier package first	Wheels/axles, bearings, suspension, dampers, brakes, grounding and guards	Family axle-load/dynamics/brake qualification and complete serial records
Battery/HV	Import qualified core; locally integrate after approval	Rack, fuses, contactors, precharge, disconnect, HVIL, BMS, sensors, vent/containment and service lift	Supplier duty, propagation, isolation, fault-current and retention tests
Thermal	Local formed tube/hose/brackets with sourced pumps/chillers	Fluid, filters, manifolds, isolation valves, drains, bleed/expansion and leak detection	Pressure/cleanliness, heat balance at hot ambient and failure response
Brake	Supplier-controlled complete design	Compressor, dryer, reservoir, valve blocks, parking brake, hoses and sensors	Pressure/leak, stop distance, adhesion/degraded modes and rescue
Doors/glass	Qualified sourced units with local frame/fitting	Lock/detection/obstruction, emergency release, drainage, seals, adhesive and retainers	Opening alignment, force/leak/retention and interlock to safety host
Wiring	Iraqi formboard/cut/crimp/test	Cable, contacts, mating halves, seals, glands, shielding, clamps and labels	Calibrated crimp/pull, cavity checks, continuity and insulation
Final vehicle	Local installation and configuration	Torque evidence, fluids, firmware, mass/CG, identification and handover records	Weighted family vehicle, static brake/door tests, route acceptance and traceability

The existing small-component standard, factory release, tooling, inspection and mass-closure modules remain useful. Their product IDs and drawing seeds must be cross-referenced to a Baghdad family-specific EBOM/MBOM before ERP Work Orders are released. No exact bolt torque, weld size, laminate layup or heat-exchanger area is invented here. Those values must close the applicable load, thermal or supplier calculation.

Slab track decision

Choose ballastless slab track as the reference permanent way. Use continuous slipforming for long, open, machine-accessible at-grade sections; use Iraqi-made OSR-ST6 single-track precast panels in constrained streets, utility/transition zones, short possessions, station/depot interfaces and replaceable sections. On standard elevated Pi20/Pi25 structures, use direct-fixation plinths above the structural flange with a thin alignment layer only where needed. Floating track is a location-specific vibration treatment, not a blanket addition.

Slab track is selected for the design package because it supports controlled alignment, modular installation and local concrete work. Lifecycle value must be tested against settlement risk, access, reparability, construction traffic, drainage and noise. It is not inherently cheaper on weak or uninvestigated ground. Keep ballasted/special transition arrangements available as engineered exceptions where life-cycle, geotechnical or depot requirements justify them.

ST6 single-track reference	Value / quantity
Dimensions	6,000 × 2,900 mm; 250 mm base; two 380 × 160 mm plinths
Double track	Two independently manufactured rows on 3,500 mm centres
Concrete, base and plinths	5.0796 m³ per panel; excludes service-trough envelope, bedding and steel
Bare concrete planning mass	12.699 t at 2,500 kg/m³; steel, inserts and lifting rig add weight
Reinforcement allowance	761.94 kg at 150 kg/m³; not a released bar schedule
Rail seats	20 per panel; 10 per rail, at $X = 300 + 600 \times i$ mm, $i = 0 \dots 9$
Repeated-module seat pitch	600 mm including the panel joint; maximum reference spacing remains 650 mm
Complete seat child allocation	One pad/baseplate kit, two clips, two lateral insulators, two anchor assemblies and one adjustment kit; supplier pattern to freeze
Bedding illustration	30 mm over 17.4 m² = 0.522 m³; actual support/grout design required
Lifting illustration	Four engineered anchors; supplier load sharing, strength, angle and rigging required

The previous CAD placed the first baseplate centre at the concrete edge, extending its 260 mm footprint beyond the panel. The corrected layout centres seats inside the module and keeps uniform pitch across repeated joints. Continuous-run planning quantities still use the existing 650 mm basis; precast method zones need their own 20-seat-per-panel schedule. Do not apply a single rounded per-km seat allowance as a fabrication order for every six-metre panel.

A complete track seat needs the matched rail, baseplate, resilient pad/layer, clips, insulators, anchors, shim/adjustment and tested fastening system. The legacy sleeper/clip CAD remains a ballasted alternative; it is not the default slab-track MBOM.

Source proprietary/safety-critical elastic parts and qualified anchors initially; manufacture concrete/cages, ducts/covers, moulds, jigs and appropriate metalwork locally. Local clip or pad manufacture requires licensing/material/process/fatigue and insulation qualification, not just matching the rendered shape.

Pandrol's published direct-fixation system provides an example of adjustable, resilient fastening for slab structures with system-specific performance and testing. This supports the architecture; it does not select Pandrol, approve an equivalent, transfer the vendor stiffness/adjustment values to OSR or establish Iraq pricing. [Pandrol technical sheet](#).

Iraqi slab manufacturing line

Add a dedicated slab line alongside the shared Baghdad plant or a route-adjacent civil yard after a haulage/capacity comparison. Do not consume the same Pi-beam moulds, crane shifts or curing spaces twice in the production programme. A mould row must record mould ID, cycle, available shifts, crane allocation, rejected pieces and actual release strength. The previous 24-hour mould-cycle target remains a trial target; use the existing 48-hour planning basis until hot-weather trials substantiate an alternative.

- 1 Release panel/cage/insert drawings, supplier fastener pattern, concrete mix/exposure class and prototype inspection plan.
- 2 Qualify Iraqi cement, aggregate, water and admixtures for the site sulfate/chloride exposure. Check shrinkage, creep and curing rather than assuming a higher concrete grade solves durability.
- 3 Build surveyed reusable steel moulds, cage/weld jigs and insert/rail-seat gauges. Fit engineered lifting sockets, bonding/drain sleeves and unique panel identity.
- 4 Inspect cage cover, insert positions, cleanliness and mould dimensions before casting. Record supplier/batch and mixing conditions.
- 5 Place/vibrate the approved mix or use qualified self-compacting concrete. Protect from heat/wind, control moisture and record maturity against strength tests.
- 6 Release lifting only at the calculated strength. Survey rail-seat datums, flatness, geometry and cracks; record repair/rejection decisions against panel serials.
- 7 Transport with designed support points and route clearance; inspect after transport. Install on accepted formation/bed, grout under the released procedure and survey rail alignment.
- 8 Install the matched fastening system, complete CWR welding/stress management, verify gauge/cant/height and inspect bonding/insulation/drainage. Record the as-installed rail/fastener/panel configuration.
- 9 Perform proof loading/ride/geometry and monitored settlement trials before series deployment. Retain replaceability and maintenance-access demonstrations.

The line requires batching/aggregate handling, controlled curing, slab moulds, cage jigs, insert fixtures, maturity/strength testing, survey gear, lifting frames, certified rigging and loading/storage space. Iraqi labour can fabricate cages/moulds and operate casting, survey, installation and maintenance; specialist training, qualified lifting/welding and independent inspection need funded work packages. No construction-job count or local-content percentage is asserted without a priced resource and origin schedule.

A quantity example for one kilometre of double track wholly assigned to ST6 is 334 full panels = $2 \times \text{ceil}(1,000/6)$, 6,680 seats and 1,696.5864 m³ of base/plinth concrete. These cover 1,002 m per track with end trimming/interface treatment unresolved. It is an example, not Baghdad's method allocation. If the surveyed constrained length is L on each of the two tracks, use $2 \times \text{ceil}(L/6)$ and separately schedule short end pieces; do not infer L from all at-grade kilometres.

Civil interfaces that need completion

Interface	Required design information	Acceptance and cost implication
Formation/slab	Ground zones, groundwater, modulus, settlement, sulfate exposure, utility trenches	Settlement and transition design; preparation/ground improvement measured by zone
Drainage/flood	Catchments, design storm, outlet levels, maintenance access, debris and scour	Cable routes separated from wet channels; outfalls/attenuation/pumps counted where required
Viaduct/slab/CWR	Thermal range, neutral rail temperature, braking, deck movement and restraint	Rail–structure interaction analysis; no automatic expansion device at every deck gap
Bearings/continuity	Unit lengths, pier stiffness, seismic/thermal restraints, replacement/lift access	Supplier bearing envelope and certified reactions; quantity schedule by actual support
River/highway bridges	Survey/navigation, scour, traffic/diversion, foundations and special spans	Separate bridge design; standard Pi spans do not release major crossings
Elevated evacuation	Walkway/barrier loads, clear width, station access and rescue route	Outer 1 m cassette reference checked against obstruction and fire/evacuation rules
Station boarding	Six-car swept envelope, floor height, tolerance and accessibility	Surveyed step/gap and dwell/evacuation capacity; LM3 offsets cannot be copied blindly
Depot/stabling	Full-fleet circulation and storage, workshop equipment, wash/drainage/recovery	One depot per line is priced by fleet and workload in the current programme ; workshop bays are not parking
Plant/logistics	Crane charts, rig loads, haul route, curing, power/water/waste and laydown	12.699 t concrete panel is not the certified shipping/lift weight; steel/rigging included

Keep the existing construction-method and foundation catalogs. Their “actual length and cost required” gates prevent generic deep-pile lengths from being adopted as surveyed Baghdad foundations. Release each geotechnical zone and map it to the alignment segments before recalculating quantities and installed costs.

Onboard electronics corrections

The revised [T-OBS bench design](#) and [integration JSON](#) close erroneous interface assumptions and add missing power, watchdog, relay-feedback, harness and external-controller blocks. They do not release a production board or pretend that a driver exists because its crate appears in the workspace.

Issue identified	Corrected design treatment
HDR-60-24 treated as 24 V to 5/12 V	It is AC/high-voltage DC input to 24 V output; use appropriately protected DC/DC branches onboard
USB isolator used as SPI / Pico device-to-device link	Use directionally correct SPI isolation with one controller and one peripheral
TPS3701 called dual heartbeat watchdog	Voltage detector only; separate channel heartbeat watchdogs and hardware inhibition
Pico GP30–39, ADC at GP14–17, native CAN/RMII	Exposed Pico pins and supported functions only; custom chip pinout separately frozen; external CAN/Ethernet controllers
ATECC608B driven through SPI	Selected breakout uses I2C; provisioning and exact variant confirmed
Digital ultrasonic echo sampled through ADS1115	Timed digital capture with voltage-level conversion; raw piezo requires an AFE/driver design
Radar said to ship M12 / USB-C	AWR1843BOOST EVM uses vendor J3 CAN, micro USB and 5 V barrel; add qualified adapter/harness
HAP claimed Gigabit/12 V PoE	Select HAP TX 100BASE-TX; vendor 9–18 V power separately; T1 interface differs
Ultrasonic face hidden behind radome	Separate acoustic apertures and tested radar/optical windows
Under-20-W host and 1-A input protection	71.5 W simultaneous output sizing envelope; 79.44 W at 90% efficiency; 99.31 W with 25% margin; 100 W reference capacity
Two relays asserted “always safe”	Require end-to-end polarity, feedback, welded-contact/driver faults and common-cause analysis

Capacity is not measured average power. Do not inflate train OPEX from a 100 W converter nameplate or retain a 40 W allowance as if it covers the updated candidate assembly. Production sensor and firmware selection must provide a measured duty cycle for the auxiliary energy/thermal model. Exact wire gauge, fuse, supply voltage range, bus topology, PCB layout, heat spreader and relay remain design-owned.

Primary specifications checked 3 October 2026: [Mean Well](#), [TI voltage detector](#), [TI radar](#), [Livox](#), [Raspberry Pi carrier](#), [Pico 2](#), [Microchip secure element](#). Candidate lifecycle/price and rail suitability are not implied by a working datasheet link.

Software and hardware integration work

The component register verifies all 60 Rust workspace packages against deployment/components.toml. Existing control, diagnostics, AFC, CBM, station, supervision and identity software is retained. RFC0033 TACS runtime/resource control remains a process reference; it is not installed Baghdad protection equipment. A logical redundant process cannot substitute for independent power, I/O, sensing and qualified timing.

Work package	Required binding / acceptance
Device HAL	Board-revision ADC/timer/PIO, external CAN/Ethernet, GPIO defaults, watchdog and relay feedback; mock tests plus actual bench traces
Sensor ingress	Vendor framing, calibration, timestamps/sequence/CRC, data age, malformed frames, packet loss and common sensor faults

Work package	Required binding / acceptance
Protection output	Complete boot/reset/timeout/permission truth table and hardware watchdog inhibition; braking and traction supplier interfaces
Runtime deployment	Qualified host composition, task/WCET budgets, fault containment, resource authority, committed resource state and degraded recovery
Clock/network	Actual timestamp accuracy, redundant routes/switches, PTP loss, CAN termination, bandwidth and shared-path failure analysis
Target images	Reproducible signed build, configuration/board hash, driver versions, SBOM, secure boot/update/rollback and release evidence
Operations integration	Event provenance, CBM/Issue triage, maintenance states, trusted operator decisions and reporting; ERP/FUXA remain outside the safety authority
Ticketing/revenue	Actual validators/payment/acquirer contracts, offline/replay/refund behaviour, Arabic UX, tariff versions and daily settlement reconciliation
Cybersecurity/service	Key provisioning/revocation, account/role access, logs/storage limits, patch ownership and restore drills

The image cookbook explicitly records that production SD images are absent. Leave that fact visible. Add real driver/board work against each package and evidence gate; do not create empty drivers or announce “complete onboard firmware” from successful host-library tests. Hardware-in-loop must test a full protected output path using representative I/O and faults.

ERP recheck and detail handover

The city component compiler, city configuration validator and supervision asset validator pass for all 266 cities; supervision covers 249,114 equipment records. This proves reusable planning/asset contracts. Baghdad’s enabled reusable profile currently contains the induction training programme; it does not automatically create production, purchasing, quality or maintenance documents.

The local ERP MariaDB service was repeatedly failing on 3 October 2026 because it could not create temporary InnoDB files under /tmp. The compose definition now gives the database a writable, bounded 512 MiB temporary filesystem with mode 1777. The database was recreated against its existing persistent volume; it became healthy and the ERP ping API returned HTTP 200. No city assets, Work Orders, stock movements or loan records were fabricated during this repair. Health does not replace backup/restore or load testing.

ERP handover	Existing capability	Inputs needed to activate the detailed package
Engineering parts / Item / BOM	Native Items, nested BOMs and version exposure/disposition	Exact family part/revision, UOM, make/buy, supplier alternatives, child content and approved production BOM
Production	Draft Work Orders and native execution/Job Cards	Approved BOM, city source/WIP/FG warehouses, workstations, routing, actual hours, dated capacity and operator permissions
Procurement / stock	Project material requests, purchasing, receipts, replenishment	Landed freight/duty/tax, lead time, MOQ, safety stock, serial/batch and warehouse availability; no invented stock
Quality	Draft native Quality Inspections and evidence references	Released characteristics, sampling and limits, gauges/calibration, inspector, receipt line and retained actual results
Maintenance / CBM	Asset Maintenance, Issue-driven repair preview and controlled draft repair	Commissioned serial asset, approved interval/team/date, spares and handback acceptance
Training	Reusable programme and native events	Competence criteria, assessor, actual attendance and role authorisation
Finance	Native currency/accounting and project budgets; proposal cashflow remains a separate planning model	Iraqi legal company, fiscal year, IQD chart/accounts, USD-import clearing, actual bank/loan/bond terms, treasury schedule and approvals
Lifecycle	Version/evidence/disposition and physical identity templates	Real HTTPS resolver, physical serial binding and verified evidence before printable deployment labels

Use the 69 engineering rows as reference requirements first. They are not automatically posted as live ERP Items or added to existing priced city materials; complete assemblies and their child content need a nested MBOM to avoid double counting. The generic ERP manufacturing/quality/maintenance contracts should remain disabled until actual approved inputs exist.

For Baghdad finance, keep the previously selected government share 25%, imported component cash/Chinese-credit split 50/50 and all other cash/debt/bonds in IQD. Confirm company currency IQD, actual FX conversion dates and USD exposures when live treasury accounting is configured. Imported procurement is not automatically all Chinese-origin credit-eligible; rails, fastening hardware, safety electronics and tooling need actual origin/loan-eligibility schedules. Foreign climate money is not IQD financing unless an on-lender or a priced hedge provides that currency structure.

Cost and release reconciliation

The parts register does not reprice individual civil or vehicle components. The separate [city-sized factory calculation](#) now replaces the four-slot production assumption with physical six-car cells, crews, tooling and test paths, with facility readiness at 18 months from NTP. Its larger physical plant allowance and EPC are included once in the Baghdad funding programme. It adds no second plant or future national-city debt. Existing civil and vehicle allowances already contain planning permanent-way and equipment scope; the component breakdowns clarify what a complete package must contain. Unknown detailed unit costs remain null/open, not zero or a claim that all omissions are covered. The depot, civil manufacturing line, full control-electronics integration, spares, qualification and measured auxiliary duty need RFQs and scope reconciliation before the current financing model becomes a tender-grade model.

For each priced assembly, mark child lines as included, separately payable or excluded; bind quantities, installed rates and origin to one revision. Compare the detail subtotal with its current allowance, update CAPEX/import split/EPC only for an accepted scope delta, then regenerate the Baghdad cashflow, tranche and debt sweep outputs together. A prototype/localisation plan must not be treated as an agreed Chinese loan, grant or bond subscription.

Release sequence: surveyed alignment/ground/utility zones to family and track interface freeze to priced complete BOM/MBOM to local manufacturing trials to hardware/software integration and fault tests to independent review to approved construction/production documents to field acceptance. This makes missing components actionable without marking them as manufactured or qualified.

Baghdad – Urban Rail Network


Source: [cities/catalogue/west-asia/Iraq/Baghdad/README.md](https://cities.catalogue/west-asia/Iraq/Baghdad/README.md)

Country: IQ · Population: 9,780,429 · [Original national catalogue](#)

Current planning basis: 2026-10-04 [programme recalculation](#), local_positive conditional local-production case. The main route is the reworked city-centre elevated planning alignment; service remains a capacity-led assumption. Revised scope is unquoted and uncommitted; this is not a construction design or an operating release.

Programme capital is USD 8.145bn, including line-local depots, final assembly and selected upstream component plants. Assumed facilities cover the modelled cash deficits; their placement is uncommitted, and the case retains IQD 9.966tn terminal debt. Older catalogue financial passes establish arithmetic for their own assumptions, not viability of this revised scope.

Network

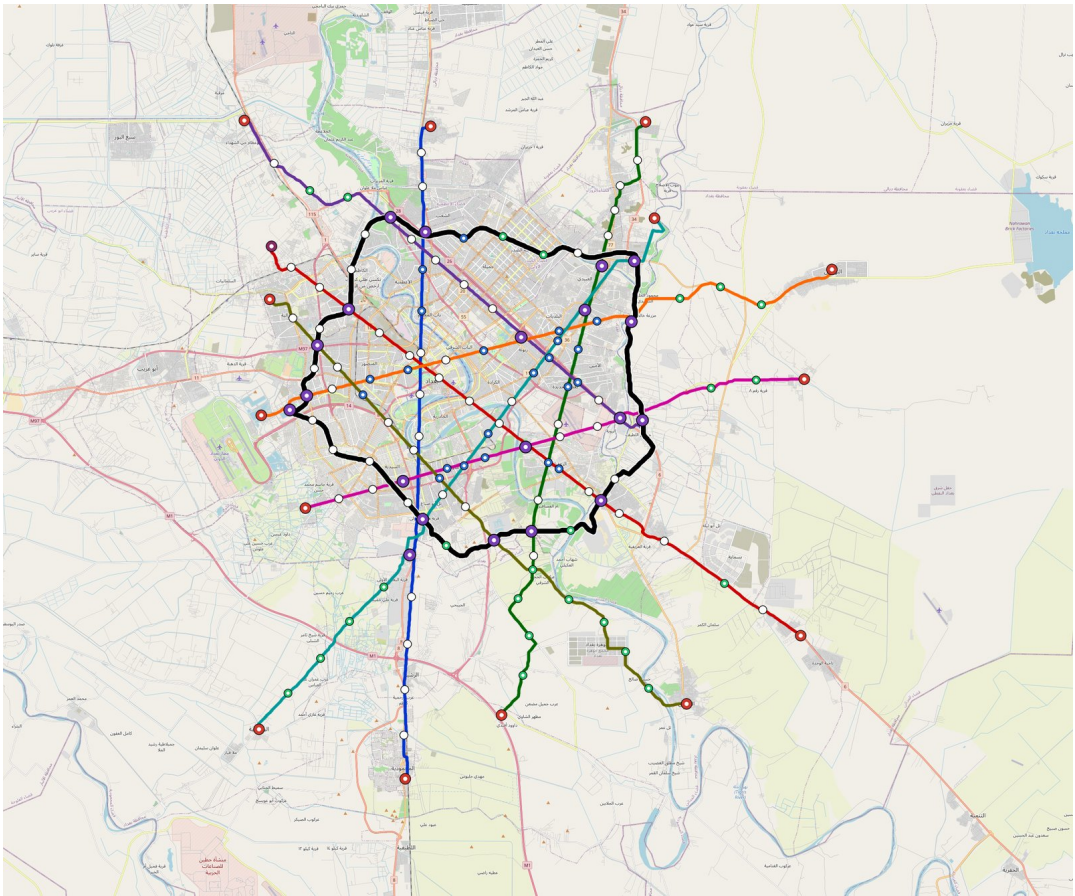

Baghdad rail network on OpenStreetMap

Local measure	Value
Lines / unique stations / interchanges	9 / 164 / 20
Route length	474.2 km double track
Coverage / transfer reachability	38.9% / 39%
Estimated station catchment	3,804,586 residents
Service span / peak headway	05:30–02:00 / 3 min
Fleet	762 × 6-car metro-6car trainsets (688 peak revenue)
Peak network throughput	259,200 passengers/hour
Practical service capacity	2,276,640 passenger-trips/day
Annual paid-trip planning range	415.5–664.8 M

Lines

Line	Length	Stations	Trainsets	Termini
line-1	49.1 km	17	86	S Outer N Outer
line-2	52.9 km	18	101	SE Outer NW Outer
line-3	49.5 km	19	97	S Outer NE Outer
line-4	42.1 km	15	80	NW Outer E Mid
line-5	47.3 km	16	86	W Mid E Outer
line-6	52.5 km	17	100	SW Outer NE Mid
line-7	40.0 km	15	79	E Outer SW Mid
line-8	47.8 km	16	90	SE Outer NW Mid
line-9	93.1 km	31	43	NW Mid NW Mid
Total	474.2 km	164 unique	762	

Coverage is an anchor-weighted planning proxy, not measured pedestrian access. Straighter core routes change station catchments; OD counts, walk/feeder access and property clearance require review.

Energy

Local measure	Value
Scheduled service	3,952 one-way journeys / 198,855 train-km/day
Annual traction demand	1,881.3 GWh
Station/depot PV / storage	46.7 MW / 318.0 MWh
Aggregate charging power	280.0 MW
Dedicated solar plant	934.2 MW
Residual grid/PPA import	0.0 GWh/yr
Worst powered-stop gap	line-8: 21.3 km / 344 kWh
Lowest traversal charging margin	line-8: 229 kWh

These energy quantities describe the current regenerated scenario. Zero annual residual grid import is an accounting balance, not accepted hourly autonomy. Depot charging/grid upgrades, duty and launch conflicts remain open.

Current capital and operating people

Revised capital scope	USD equivalent million
Civil and bearing allowance	4,001.925
Stations and core elevated access	983.810
Rolling stock	1,189.779
Final assembly and component plants	408.902
Line-local depots	247.790
Solar and charging	805.167
Signalling and programme overhead	507.669
Total programme	8,145.042

There are 9 depots, one per line, with 762 storage slots for all 111 m six-car trains plus clearance. Depot reference capital is USD 247.790m, replacing the old USD 8m once. Workshop bays are sized separately by workload. The current case gives no capacity credit to station stabling. Actual land, foundations, connected access, installed charging and morning launch acceptance remain open. [Depot quantities](#) · [Items](#).

The operating establishment is 3,430 FTE, including 1,620 station-cover FTE. Two staff per station and two normal eight-hour shifts give 656 daily shift assignments; retained 20.5-hour service also funds late cover and weekly/leave/training/sickness relief. Loaded annual payroll is IQD 80.292bn, with subsequent OPEX inflation. General pay starts at IQD 1,175,455/month, 50% above the historical employee median indexed to 2026. Technical/supervisor/senior/director grades are separate; this is not a newly measured median. [Roles and wages](#). Final assembly has 1273 production and 191 support FTE; selected upstream plants add 229 production and 35 support FTE. Their 55 paid production months are separate from permanent railway jobs. [Construction crew screen](#) is incomplete; contractor labour is already inside contract rates.

Iraqi manufacture and USD capital exposure

Product	Network quantity	Current case
bogie	9144	Local process option
motor-inverter-set	9144	Bought component
battery-225kwh-pack	4572	Local process option
door-cassette	18288	Local process option
window-cassette	27432	Bought component

Imported process machinery supports the selected Iraqi fabrication and assembly options shown above. Cells/BMS, wheels/axles/bearings, inverters and other critical inputs retain imports. Products with negative Baghdad-only whole-order margins remain bought in this case. Plant readiness/qualification within 18 months is assumed, not demonstrated. [Make/buy appraisal](#).

Compared with the matched bought-component case, capital changes from USD 8.250bn to USD 8.145bn; imported invoice exposure changes from USD 2.204bn (26.71%) to USD 1.942bn (23.84%). The historical 148 km / USD 18bn proposal has a different scope and assumed all-USD funding; it is not a matched tender saving.

Current funding and cashflows

Government capital is exactly 25%. Imports use 50% government USD cash / 50% proposed Chinese USD credit. Only Chinese debt is USD; the rest of government cash, bonds, bank/gap credit and mezzanine is IQD. Government invoice downpayments are scheduled within the total 25% contribution. FX is the historical planning anchor of IQD 1,300/USD.


Capital-only source	Currency	Native amount
Government import cash	USD	970,909,383
Government local cash	IQD	1,384,956,400,257
Chinese capital credit	USD	970,909,383
Ordinary capital bonds	IQD	3,944,816,429,415
Green capital bonds	IQD	1,040,233,767,709
Senior bank capital credit	IQD	1,661,683,399,041
Conditional climate grant	IQD	32,500,000,000

Interest/fees, reserve cash, OPEX and gap facilities are additional cashflows, not capital added twice. Fares, kiosks, advertising, additional receipts and fare/OPEX indexation are included. Green/grant/rights terms and concessional gap credit remain uncommitted. Conditional first/full line revenue is month 40 / 76; physical and financing gates are open.

The tested IQD mezzanine leaves 79 defaulted draw vintages and increases terminal debt to IQD 15.906tn. It does not cure the operating deficit. [Monthly cashflow](#) · [Six-month bond/loan placements](#) · [All twelve cases](#).

City-centre elevated alignment

The main design uses straight core radial tangents and broad curved ring connections inside the explicit 33.22–33.42°N / 44.28–44.53°E study area. Land sections there are elevated; water crossings remain bridges. The core analytical routes shorten from 301.468 km to 238.172 km. The main network is 474.180 route km, with 54.86% elevated across the whole system. Maps, station placement, fleet, civil quantities, staff and finance use that reworked design. [Analytical controls and limitations](#).

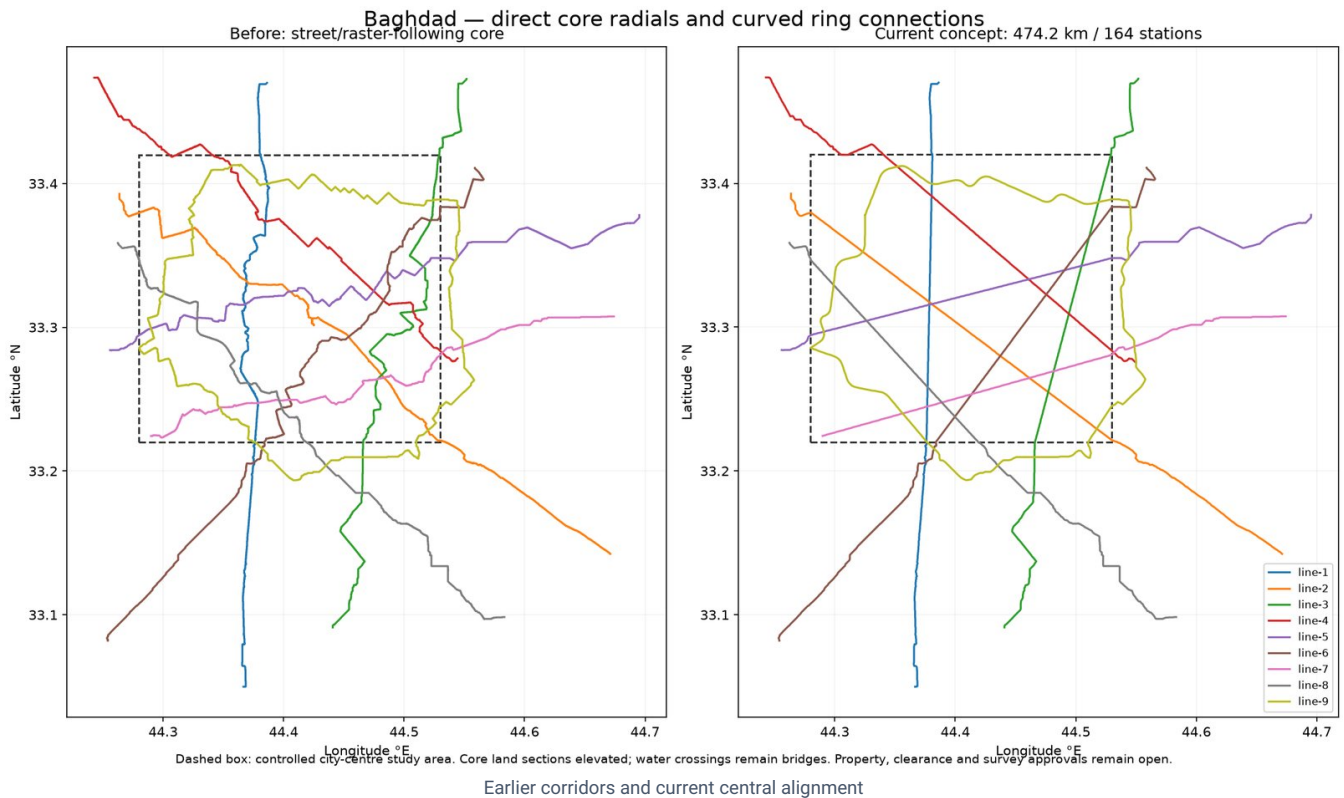

Property/air rights, obstacles, protected sites, surveyed heights, utilities, piers, foundations, transition curves and vertical alignment remain open. Existing outer approaches retain street/raster bends; exceptional geometry still requires realignment or special products. Additional outer grade-separation sensitivities add 7.015 km and retain current dates; they are not the adopted core geometry or an achieved routing-penalty saving.

Evidence, original references and regeneration

[Complete proposal PDF](#) · [Editable proposal](#) · [Supporting data](#) · [Planning-only ERP drafts](#) · [Original catalogue finance](#) · [Original depot/stabling screen](#). Simulation, energy and asset evidence uses the current reworked geometry; the new staffing/depot/factory plans do not create accepted sites, appointed employees or operational assets.

Auto-planned by the OpenSourceRail design pipeline. Shared assumptions are in the [deployment planning reference](#). Inputs: [design](#), [scenario](#), [map](#), [package evidence](#). City-local [simulation](#), [energy](#), [GIS](#), [operations](#) and [delivery](#) retain their recorded planning/release gates.

For presentation-only updates, run `.venv/bin/python tools/automation/publish-city-summary.py`; add `- -check` to detect drift. The city regeneration pipeline uses this publisher. A stale scope study stops publication rather than silently restoring the original cost headline. Publication provenance is in [publication-manifest.json](#).

Baghdad Planning OSR-ALN Package

Source: [cities/catalogue/west-asia/Iraq/Baghdad/engineering/alignment/README.md](https://github.com/OpenSourceRail/Baghdad/blob/master/cities/catalogue/west-asia/Iraq/Baghdad/engineering/alignment/README.md)

Deterministic alignment exports for every line in the current generated network.

File	Design line	Length	Stations
baghdad-line1.aln.toml	line-1	49,067.5 m	17
baghdad-line2.aln.toml	line-2	52,850.6 m	18
baghdad-line3.aln.toml	line-3	49,496.5 m	19
baghdad-line4.aln.toml	line-4	42,067.8 m	15
baghdad-line5.aln.toml	line-5	47,321.3 m	16
baghdad-line6.aln.toml	line-6	52,503.4 m	17
baghdad-line7.aln.toml	line-7	39,957.0 m	15
baghdad-line8.aln.toml	line-8	47,848.5 m	16
baghdad-line9.aln.toml	line-9	93,067.1 m	31

Status

These files are planning-only and not for construction. Horizontal control comes from the current WGS84 corridor and is projected to the local UTM zone. Circular curves and transitions are not fitted, the vertical profile is a zero-datum placeholder, and cant has not been designed. Survey, curve-fit, vertical-profile, cant, geotechnical, utility, property, drainage, and structural release gates therefore remain open.

Each OSR-ALN file records the SHA-256 hashes of `../design.toml` and the city corridor GeoJSON used to generate it.

Baghdad organisation and design work

Source: cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery/README.md

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

3217 indicative operating FTE, including management; annual labour allowance \$36,188,046. Group totals reconcile to the existing finance model. Individual role shares are editable planning allocations, not measured workload or an accepted duty roster.

GoA 4 control and remote assistance; local station batteries supply train top-ups. Two revenue trainsets per selected station with same-line depot overflow. Shared domestic design/software/factory capability serves city teams.

City operating organisation

Function	FTE	Reports to	Skills	Tasks
City accountable lead	1	Local owner board	Local operating governance; budget and emergency accountability	Own city delivery and operations; coordinate shared domestic capabilities
Engineering authority	4	City director	Systems integration; configuration and design checking	Own interfaces and technical concessions; commission competent discipline checks
Quality and safety assurance	7	Local owner board (independent escalation)	Independent inspection; hazard review; traceability	Audit evidence; raise stop-work/hold points independently of production
Training and competence assessors	6	City director	Practical assessment; instruction; competence records	Train local recruits and apprentices; witness competence before unsupervised work
Procurement and stores	8	City director	BOM traceability; repairable spares; supplier quality	Purchase controlled common parts; manage local repair loops and critical stock
Finance and people administration	7	City director	Payroll; cost control; roster and employment administration	Maintain local pay/leave inputs; reconcile labour budget and workload
Fleet workshop supervision	50	Chief engineer	Isolation authority; work planning; calibrated tooling	Allocate same-line workshop slots; control defect and release records
Mechanical technicians	171	Workshop lead	Wheels/brakes; joint inspection; controlled fastener assembly	Inspect bogies and brakes; replace modules; record torque/preload evidence
Electrical and battery technicians	147	Workshop lead	HV isolation; LFP diagnostics; controls and harness repair	Diagnose packs, HVAC and controllers; verify protective interlocks
Vehicle cleaning and finish repair	122	Workshop lead	GFRP/EPDM compatibility; coating preparation; controlled washing	Turnaround clean; inspect seals; repair finish damage under qualified process
Infrastructure work supervision	38	Chief engineer	Track access; lifting and electrical isolation coordination	Plan possessions; check civil and energy defect closure
Track and civil technicians	147	Infrastructure lead	Survey checks; track geometry; bearing/joint inspection	Inspect settlement, track, deck joints, drainage and walkways
Solar and station storage technicians	129	Infrastructure lead	PV DC safety; storage BMS; charger and protection testing	Maintain PV/storage/top-up equipment; measure soiling and energy balance
Wayside and communications technicians	56	Infrastructure lead	Fail-restrictive controls; networking; configuration control	Maintain point/crossing equipment where installed; test communications and recovery
Shift leadership and degraded-operation authority	72	City director	GoA 4 incident command; dispatch competence	Own service start; coordinate recovery and same-line depot releases
Line dispatch and control	191	OCC lead	Timetable supervision; protected movement authority	Monitor headways and station berths; authorise line-local recovery
Remote assistance	215	OCC lead	Vehicle fault diagnosis; passenger emergency response	Resolve remote-assist requests; coordinate on-site responders
Passenger service and fare support	127	City director	Accessible communication; fare-system support	Resolve passenger queries; verify fare equipment and complaints
Station cleaning and waste	104	Station lead	Product compatibility; wet-floor control; waste segregation	Clean measured public areas; record defects and wash-water disposal
Station team coordination	243	OCC lead	Accessible evacuation; platform protection	Allocate mobile teams; inspect opening and closing readiness
Platform and accessibility assistance	1372	Station lead	Accessibility assistance; crowd management; first aid	Assist boarding; manage obstructions and platform incidents

Recruit and apprentice locally; assess practical task competence, isolate/hold/release authority and refresher needs. Training duration follows the demonstrated skills gap, not a universal weeks-to-qualification claim.

Quality and safety staff can escalate holds directly to the local owner board. Functions can be combined where competence and cover permit. Management allocations are already inside the operating totals.

Roster closure: named duty and leave roster including service-depot turnaround crews; measured cleaning/inspection person-minutes and simultaneous arrivals; country/local pay and actual grade costs; local employment/rest requirements and night emergency cover.

Construction and domestic manufacturing work

Concurrent crews/workstations below come from the existing dated work orders, with inclusive finish days. Worker headcount awaits an explicit crew mix; named skills are not assumed to mean one person each. Factory capacity is shared across city orders. Peaks from different work centres need not occur together.

Work centre	Peak resources (unknown if unsized)	Peak task slots	First peak day	Resource-days	Skills/tasks
Baghdad six-car body installation	unknown	3	601	unknown	body-cell lead; composite fitter; quality technician / rs-25-clip-on-body
Baghdad six-car composite kits	unknown	11	597	unknown	composite cell lead; laminator; quality technician; trim technician / rs-23-moulded-body-modules
Baghdad six-car electrical integration	unknown	21	625	unknown	battery technician; electrical lead; quality technician; software technician / rs-30-traction-battery-control
Baghdad six-car fitout and static test	unknown	17	644	unknown	HVAC technician; door technician; fit-out lead; quality technician / rs-40-fitout-static-test
Baghdad six-car structural assembly	unknown	25	584	unknown	bogie technician; brake technician; fabrication lead; weld inspector / rs-20-carbody-bogie
Baghdad trainset acceptance bays	unknown	13	659	unknown	commissioning lead; quality manager; software technician; test operator / rs-50-dynamic-commissioning
Baghdad trainset kitting	unknown	4	556	unknown	production planner; quality technician; stores clerk / rs-10-material-kit
corridor civil crew	2	2	5	3042	civil supervisor; drainage technician; permit coordinator; plant operator; quality technician; safety officer; survey lead / trk-10-survey-utility, trk-20-subgrade-drainage
depot works	unknown	1	624	unknown	depot operations lead; depot supervisor; electrical supervisor; quality technician; systems technician; tooling technician / dep-10-building-plant, dep-20-charging-stabling
energy crew	unknown	2	501	unknown	PV technician; battery technician; commissioning lead; electrical supervisor; quality technician; software technician / en-10-energy-build, en-20-energy-commission
project controls	unknown	1	0	unknown	production planner; project controls lead; quality manager; safety assurance lead / sys-00-baseline-freeze
station civil crew	unknown	2	431	unknown	accessibility lead; quality technician; station civil supervisor; steelwork lead / st-10-civil-structure
station systems crew	unknown	2	589	unknown	electrical supervisor; fare-system technician; quality technician; systems technician / st-20-mep-passenger-systems

Work centre	Peak resources (unknown if unsized)	Peak task slots	First peak day	Resource-days	Skills/tasks
track crew	2	2	293	2465	quality technician; rail welder; survey technician; track supervisor / trk-30-trackform-rail
track/switch crew	unknown	2	222	unknown	quality technician; survey technician; switch technician; systems technician; track supervisor / sw-10-turnout-build, sw-20-install-proof
wayside bench	unknown	3	480	unknown	quality technician; software technician; systems technician / wpt-10-cabinet-bench
wayside systems crew	unknown	3	641	unknown	quality technician; radio technician; software technician; systems supervisor / wpt-20-install-c ommission

Civil and mechanical refinements

Climate: hot-desert; 28 °C reference, 50 °C upper ambient. Cold ambient: missing.

Free movement $\alpha L \Delta T$. 8/10/12 microstrain/K are declared sensitivity cases, not measured concrete properties. Reference is the preset annual mean, not installation temperature; sunlit component temperatures and gradients require separate inputs.

Each elevated segment is separate; 25 m catalogue span, up to 4 spans/unit from the shared production/continuity templates, two tracks and two webs. Shared bearings require an unaccepted structural continuity connection; a simple-span link slab retains independent girder-end bearings. Rounded spans are a procurement screen, not surveyed support positions. Deck gaps count the existing catalogue unit interfaces; abutment details remain separate.

Elevated segment	Longest unit m	Bearings	Internal connections	Hot movement mm at 8 / 10 / 12 μ strain/K
line-1 388.3–428.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 488.3–528.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 588.3–676.6 m	100.0	20	3	17.6 / 22.0 / 26.4
line-1 696.6–736.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 956.6–1016.6 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 1336.6–1356.6 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 1829.7–1849.7 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 1909.7–1949.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 2086.3–2146.3 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 2274.6–2334.6 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 3034.6–3114.6 m	100.0	20	3	17.6 / 22.0 / 26.4
line-1 3474.6–3514.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 3602.8–3651.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 4444.3–4464.3 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 4512.5–4532.5 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 4689.1–4709.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 5029.1–5049.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 5237.4–5297.4 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 5905.7–5925.7 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 6425.7–6485.7 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 7014.0–7074.0 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 7154.0–7222.3 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 7242.3–7302.3 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 7522.3–7582.3 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 7642.3–7670.5 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 7690.5–7770.5 m	100.0	20	3	17.6 / 22.0 / 26.4
line-1 8058.8–8118.8 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 8327.1–8347.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 8503.7–8543.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 8623.7–8643.7 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 8892.0–9028.5 m	100.0	32	4	17.6 / 22.0 / 26.4
line-1 9205.1–9225.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 9309.9–9358.2 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 9458.2–9554.8 m	100.0	20	3	17.6 / 22.0 / 26.4

Elevated segment	Longest unit m	Bearings	Internal connections	Hot movement mm at 8 / 10 / 12 µstrain/K
line-1 9859.7–9987.9 m	100.0	32	4	17.6 / 22.0 / 26.4
line-1 10187.9–10256.2 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 10276.2–10364.5 m	100.0	20	3	17.6 / 22.0 / 26.4
line-1 10412.8–10441.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 10609.4–10709.4 m	100.0	20	3	17.6 / 22.0 / 26.4
line-1 10769.4–10857.6 m	100.0	20	3	17.6 / 22.0 / 26.4
line-1 11145.9–11205.9 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 11474.2–11662.5 m	100.0	40	6	17.6 / 22.0 / 26.4
line-1 11830.8–11850.8 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 12259.1–12299.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 14301.9–14321.9 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 15206.8–15275.0 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 15375.0–15475.0 m	100.0	20	3	17.6 / 22.0 / 26.4
line-1 15851.6–15891.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 16059.9–16079.9 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 16736.5–16804.8 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 16824.8–16844.8 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 17084.8–17104.8 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 17144.8–17193.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 17854.5–17874.5 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 17974.5–18034.5 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 18182.7–18202.7 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 18251.0–18299.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 18905.6–18953.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 19627.0–19647.0 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 19735.3–19815.3 m	100.0	20	3	17.6 / 22.0 / 26.4
line-1 20108.4–20128.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 20148.4–20225.0 m	100.0	20	3	17.6 / 22.0 / 26.4
line-1 20245.0–20293.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 20313.3–20373.3 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 20373.3–25214.7 m	100.0	972	145	17.6 / 22.0 / 26.4
line-1 25274.7–25294.7 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 25374.7–25554.7 m	100.0	40	6	17.6 / 22.0 / 26.4
line-1 25614.7–25674.7 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 25743.0–25783.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 25923.0–25963.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 26003.0–26083.0 m	100.0	20	3	17.6 / 22.0 / 26.4
line-1 26103.0–26123.0 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 26203.0–26523.0 m	100.0	68	9	17.6 / 22.0 / 26.4
line-1 26711.3–26871.3 m	100.0	36	5	17.6 / 22.0 / 26.4
line-1 26951.3–26991.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 27071.3–27191.3 m	100.0	28	3	17.6 / 22.0 / 26.4
line-1 27211.3–27271.3 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 27331.3–27391.3 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 27451.3–27739.6 m	100.0	60	9	17.6 / 22.0 / 26.4
line-1 27899.6–29047.8 m	100.0	232	34	17.6 / 22.0 / 26.4
line-1 29127.8–29207.8 m	100.0	20	3	17.6 / 22.0 / 26.4
line-1 29247.8–29287.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 29467.8–29607.8 m	100.0	32	4	17.6 / 22.0 / 26.4
line-1 29676.1–29736.1 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 29776.1–29796.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 29816.1–29936.1 m	100.0	28	3	17.6 / 22.0 / 26.4
line-1 29956.1–30036.1 m	100.0	20	3	17.6 / 22.0 / 26.4
line-1 30076.1–30136.1 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 30156.1–30216.1 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 30624.4–30944.4 m	100.0	68	9	17.6 / 22.0 / 26.4
line-1 30964.4–31344.4 m	100.0	80	12	17.6 / 22.0 / 26.4
line-1 31384.4–31664.4 m	100.0	60	9	17.6 / 22.0 / 26.4
line-1 32004.4–32024.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 32104.4–32184.4 m	100.0	20	3	17.6 / 22.0 / 26.4
line-1 32284.4–32344.4 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 32484.4–32552.7 m	75.0	16	2	13.2 / 16.5 / 19.8

Elevated segment	Longest unit m	Bearings	Internal connections	Hot movement mm at 8 / 10 / 12 µstrain/K
line-1 32572.7–32612.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-1 32732.7–32792.7 m	75.0	16	2	13.2 / 16.5 / 19.8
line-1 33232.7–33252.7 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 33512.7–33761.0 m	100.0	52	7	17.6 / 22.0 / 26.4
line-1 33781.0–33921.0 m	100.0	32	4	17.6 / 22.0 / 26.4
line-1 33981.0–34061.0 m	100.0	20	3	17.6 / 22.0 / 26.4
line-1 34101.0–34121.0 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 34141.0–42795.5 m	100.0	1736	260	17.6 / 22.0 / 26.4
line-1 42948.7–42968.7 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 43177.0–43197.0 m	25.0	8	0	4.4 / 5.5 / 6.6
line-1 44130.1–44150.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-2 2228.8–2285.3 m	75.0	16	2	13.2 / 16.5 / 19.8
line-2 2418.5–2475.0 m	75.0	16	2	13.2 / 16.5 / 19.8
line-2 2579.9–2656.5 m	100.0	20	3	17.6 / 22.0 / 26.4
line-2 4649.3–4705.8 m	75.0	16	2	13.2 / 16.5 / 19.8
line-2 6133.8–6162.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 6694.6–6722.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 9444.2–9472.5 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 9625.6–9673.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 12450.4–12506.9 m	75.0	16	2	13.2 / 16.5 / 19.8
line-2 12924.9–12973.2 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 13001.5–13049.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 13106.4–13214.6 m	100.0	28	3	17.6 / 22.0 / 26.4
line-2 13311.2–13339.5 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 13359.5–13407.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 13447.8–13467.8 m	25.0	8	0	4.4 / 5.5 / 6.6
line-2 13496.1–13516.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-2 13644.3–13692.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 14170.6–14190.6 m	25.0	8	0	4.4 / 5.5 / 6.6
line-2 14360.3–14445.2 m	100.0	20	3	17.6 / 22.0 / 26.4
line-2 14858.3–14934.9 m	100.0	20	3	17.6 / 22.0 / 26.4
line-2 14954.9–15011.5 m	75.0	16	2	13.2 / 16.5 / 19.8
line-2 15144.6–15286.0 m	100.0	32	4	17.6 / 22.0 / 26.4
line-2 15487.4–15544.0 m	75.0	16	2	13.2 / 16.5 / 19.8
line-2 15592.3–15648.9 m	75.0	16	2	13.2 / 16.5 / 19.8
line-2 15773.7–15822.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 15946.8–15975.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 16023.4–16051.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 16120.0–16168.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 16341.4–16369.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 16699.4–16727.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 16747.7–16796.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 16844.2–16864.2 m	25.0	8	0	4.4 / 5.5 / 6.6
line-2 17157.4–17177.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-2 17225.7–19186.7 m	100.0	396	59	17.6 / 22.0 / 26.4
line-2 19275.0–27281.9 m	100.0	1608	240	17.6 / 22.0 / 26.4
line-2 27386.8–27519.9 m	100.0	32	4	17.6 / 22.0 / 26.4
line-2 27757.9–27806.2 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 27967.6–28072.5 m	100.0	28	3	17.6 / 22.0 / 26.4
line-2 28282.2–28475.3 m	100.0	40	6	17.6 / 22.0 / 26.4
line-2 28543.6–28631.9 m	100.0	20	3	17.6 / 22.0 / 26.4
line-2 28660.2–28845.0 m	100.0	40	6	17.6 / 22.0 / 26.4
line-2 28893.3–28921.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 29009.9–29098.2 m	100.0	20	3	17.6 / 22.0 / 26.4
line-2 29154.7–29194.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 29223.0–29243.0 m	25.0	8	0	4.4 / 5.5 / 6.6
line-2 29544.4–29572.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 29592.7–29661.0 m	75.0	16	2	13.2 / 16.5 / 19.8
line-2 29757.6–29777.6 m	25.0	8	0	4.4 / 5.5 / 6.6
line-2 29910.7–29930.7 m	25.0	8	0	4.4 / 5.5 / 6.6
line-2 29959.0–30015.6 m	75.0	16	2	13.2 / 16.5 / 19.8
line-2 30035.6–30063.8 m	50.0	12	1	8.8 / 11.0 / 13.2

Elevated segment	Longest unit m	Bearings	Internal connections	Hot movement mm at 8 / 10 / 12 µstrain/K
line-2 30245.3–30301.8 m	75.0	16	2	13.2 / 16.5 / 19.8
line-2 30350.1–30378.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 30398.4–30418.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-2 30446.7–30495.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 30515.0–30651.5 m	100.0	32	4	17.6 / 22.0 / 26.4
line-2 30679.8–30728.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 30933.0–32845.8 m	100.0	388	57	17.6 / 22.0 / 26.4
line-2 32990.6–33147.2 m	100.0	36	5	17.6 / 22.0 / 26.4
line-2 33195.5–33263.7 m	75.0	16	2	13.2 / 16.5 / 19.8
line-2 33312.0–33360.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 33400.3–33428.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 33456.9–33593.4 m	100.0	32	4	17.6 / 22.0 / 26.4
line-2 33661.7–33778.3 m	100.0	28	3	17.6 / 22.0 / 26.4
line-2 33894.9–34079.7 m	100.0	40	6	17.6 / 22.0 / 26.4
line-2 34196.3–34272.9 m	100.0	20	3	17.6 / 22.0 / 26.4
line-2 34292.9–34361.1 m	75.0	16	2	13.2 / 16.5 / 19.8
line-2 34808.8–34837.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 34885.4–34913.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 34942.0–35046.8 m	100.0	28	3	17.6 / 22.0 / 26.4
line-2 35095.1–35180.0 m	100.0	20	3	17.6 / 22.0 / 26.4
line-2 35506.2–35622.8 m	100.0	28	3	17.6 / 22.0 / 26.4
line-2 35642.8–35739.4 m	100.0	20	3	17.6 / 22.0 / 26.4
line-2 35759.4–35807.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 35855.9–35924.2 m	75.0	16	2	13.2 / 16.5 / 19.8
line-2 35944.2–36109.1 m	100.0	36	5	17.6 / 22.0 / 26.4
line-2 36157.4–36177.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-2 36225.7–36273.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 36410.5–36438.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 36507.1–36555.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 36575.4–36595.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-2 36623.6–36691.9 m	75.0	16	2	13.2 / 16.5 / 19.8
line-2 36711.9–37074.8 m	100.0	76	11	17.6 / 22.0 / 26.4
line-2 37131.3–37517.6 m	100.0	80	12	17.6 / 22.0 / 26.4
line-2 37545.9–37585.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 37614.2–38168.7 m	100.0	116	17	17.6 / 22.0 / 26.4
line-2 38663.3–49904.7 m	100.0	2252	337	17.6 / 22.0 / 26.4
line-2 49904.7–49932.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 49952.9–50001.2 m	50.0	12	1	8.8 / 11.0 / 13.2
line-2 50274.4–50294.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-3 6748.7–6777.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-3 7995.2–8043.5 m	50.0	12	1	8.8 / 11.0 / 13.2
line-3 8100.0–8128.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-3 8689.2–8717.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-3 9278.3–9306.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-3 16972.1–18128.1 m	100.0	236	35	17.6 / 22.0 / 26.4
line-3 18196.4–36732.7 m	100.0	3712	556	17.6 / 22.0 / 26.4
line-3 36929.2–41733.2 m	100.0	968	144	17.6 / 22.0 / 26.4
line-3 42796.0–42816.0 m	25.0	8	0	4.4 / 5.5 / 6.6
line-3 42964.3–43024.3 m	75.0	16	2	13.2 / 16.5 / 19.8
line-3 43144.3–43164.3 m	25.0	8	0	4.4 / 5.5 / 6.6
line-3 44248.6–44268.6 m	25.0	8	0	4.4 / 5.5 / 6.6
line-3 44373.4–44393.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-3 44859.7–44899.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-3 45412.8–45441.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-3 46222.5–46242.5 m	25.0	8	0	4.4 / 5.5 / 6.6
line-3 46262.5–46282.5 m	25.0	8	0	4.4 / 5.5 / 6.6
line-3 46727.4–46787.4 m	75.0	16	2	13.2 / 16.5 / 19.8
line-3 48007.4–48067.4 m	75.0	16	2	13.2 / 16.5 / 19.8
line-3 48127.4–48187.4 m	75.0	16	2	13.2 / 16.5 / 19.8
line-3 48555.7–48595.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 0.0–80.0 m	100.0	20	3	17.6 / 22.0 / 26.4
line-4 140.0–180.0 m	50.0	12	1	8.8 / 11.0 / 13.2

Elevated segment	Longest unit m	Bearings	Internal connections	Hot movement mm at 8 / 10 / 12 µstrain/K
line-4 220.0–296.6 m	100.0	20	3	17.6 / 22.0 / 26.4
line-4 421.4–489.7 m	75.0	16	2	13.2 / 16.5 / 19.8
line-4 546.3–622.8 m	100.0	20	3	17.6 / 22.0 / 26.4
line-4 642.8–731.1 m	100.0	20	3	17.6 / 22.0 / 26.4
line-4 1097.4–1117.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-4 2119.7–2167.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 2292.8–2369.4 m	100.0	20	3	17.6 / 22.0 / 26.4
line-4 2389.4–2437.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 2514.2–2562.5 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 2880.5–2908.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 3524.8–3544.8 m	25.0	8	0	4.4 / 5.5 / 6.6
line-4 3621.3–3641.3 m	25.0	8	0	4.4 / 5.5 / 6.6
line-4 4184.2–4212.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 4547.0–4567.0 m	25.0	8	0	4.4 / 5.5 / 6.6
line-4 4927.0–4947.0 m	25.0	8	0	4.4 / 5.5 / 6.6
line-4 7308.9–7337.2 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 7393.8–7413.8 m	25.0	8	0	4.4 / 5.5 / 6.6
line-4 7918.0–7946.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 8002.9–8031.2 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 8385.7–8414.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 8502.3–8550.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 8827.1–8855.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 9452.8–10041.1 m	100.0	120	18	17.6 / 22.0 / 26.4
line-4 10157.7–10186.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 10748.8–10797.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 10865.4–10885.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-4 11058.5–11098.5 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 11243.4–11271.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 11541.4–11714.5 m	100.0	36	5	17.6 / 22.0 / 26.4
line-4 12032.5–12060.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 12273.9–12302.2 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 13363.9–13412.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 13460.4–13875.0 m	100.0	88	12	17.6 / 22.0 / 26.4
line-4 14048.1–14164.7 m	100.0	28	3	17.6 / 22.0 / 26.4
line-4 14233.0–14261.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 14289.5–14317.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 14386.1–14406.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-4 14627.5–14732.4 m	100.0	28	3	17.6 / 22.0 / 26.4
line-4 14780.7–14962.1 m	100.0	40	6	17.6 / 22.0 / 26.4
line-4 15186.9–15215.2 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 15331.8–15388.4 m	75.0	16	2	13.2 / 16.5 / 19.8
line-4 15416.7–27788.6 m	100.0	2476	371	17.6 / 22.0 / 26.4
line-4 27961.7–28231.4 m	100.0	56	8	17.6 / 22.0 / 26.4
line-4 28452.8–39637.6 m	100.0	2240	336	17.6 / 22.0 / 26.4
line-4 39637.6–39665.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 39722.5–39750.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-4 40416.4–40436.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-4 40884.1–40904.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-4 41129.0–41149.0 m	25.0	8	0	4.4 / 5.5 / 6.6
line-5 0.0–20.0 m	25.0	8	0	4.4 / 5.5 / 6.6
line-5 48.3–156.6 m	100.0	28	3	17.6 / 22.0 / 26.4
line-5 926.3–986.3 m	75.0	16	2	13.2 / 16.5 / 19.8
line-5 2479.7–2539.7 m	75.0	16	2	13.2 / 16.5 / 19.8
line-5 2857.6–12600.6 m	100.0	1952	292	17.6 / 22.0 / 26.4
line-5 12620.6–12757.2 m	100.0	32	4	17.6 / 22.0 / 26.4
line-5 12777.2–12797.2 m	25.0	8	0	4.4 / 5.5 / 6.6
line-5 12845.5–12973.8 m	100.0	32	4	17.6 / 22.0 / 26.4
line-5 13022.1–13170.3 m	100.0	32	4	17.6 / 22.0 / 26.4
line-5 13218.6–13375.2 m	100.0	36	5	17.6 / 22.0 / 26.4
line-5 13415.2–13503.5 m	100.0	20	3	17.6 / 22.0 / 26.4
line-5 13571.8–13620.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-5 13660.0–13728.3 m	75.0	16	2	13.2 / 16.5 / 19.8

Elevated segment	Longest unit m	Bearings	Internal connections	Hot movement mm at 8 / 10 / 12 µstrain/K
line-5 13964.9–13993.2 m	50.0	12	1	8.8 / 11.0 / 13.2
line-5 14149.7–14278.0 m	100.0	32	4	17.6 / 22.0 / 26.4
line-5 14346.3–14366.3 m	25.0	8	0	4.4 / 5.5 / 6.6
line-5 14542.9–14611.2 m	75.0	16	2	13.2 / 16.5 / 19.8
line-5 14807.7–14856.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-5 15100.9–15189.2 m	100.0	20	3	17.6 / 22.0 / 26.4
line-5 15229.2–15365.7 m	100.0	32	4	17.6 / 22.0 / 26.4
line-5 15474.0–15562.3 m	100.0	20	3	17.6 / 22.0 / 26.4
line-5 15787.1–15895.4 m	100.0	28	3	17.6 / 22.0 / 26.4
line-5 16023.7–28700.1 m	100.0	2540	381	17.6 / 22.0 / 26.4
line-5 28980.1–29000.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-5 29300.1–29360.1 m	75.0	16	2	13.2 / 16.5 / 19.8
line-5 29604.9–29681.5 m	100.0	20	3	17.6 / 22.0 / 26.4
line-5 36271.4–36319.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-5 36516.2–36536.2 m	25.0	8	0	4.4 / 5.5 / 6.6
line-5 39045.6–39073.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-5 39926.4–39946.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-5 42607.5–42655.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-5 44903.1–44931.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-5 44979.7–44999.7 m	25.0	8	0	4.4 / 5.5 / 6.6
line-5 46199.1–46239.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 0.0–173.1 m	100.0	36	5	17.6 / 22.0 / 26.4
line-6 664.3–749.1 m	100.0	20	3	17.6 / 22.0 / 26.4
line-6 1552.8–1581.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 1657.6–1685.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 2982.2–3010.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 3038.7–3067.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 4117.0–4145.2 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 4278.4–4306.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 4617.8–4646.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 4807.5–4835.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 4864.1–4892.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 11462.3–11490.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 13745.1–13773.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 15723.6–15751.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 15820.1–15840.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-6 15888.4–15908.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-6 16599.5–17760.4 m	100.0	236	35	17.6 / 22.0 / 26.4
line-6 18373.5–18461.8 m	100.0	20	3	17.6 / 22.0 / 26.4
line-6 18481.8–18521.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 18641.8–18718.4 m	100.0	20	3	17.6 / 22.0 / 26.4
line-6 20490.3–20546.9 m	75.0	16	2	13.2 / 16.5 / 19.8
line-6 20980.0–27525.3 m	100.0	1312	196	17.6 / 22.0 / 26.4
line-6 27553.5–27630.1 m	100.0	20	3	17.6 / 22.0 / 26.4
line-6 28545.5–28573.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 28650.4–28726.9 m	100.0	20	3	17.6 / 22.0 / 26.4
line-6 28783.5–28936.6 m	100.0	36	5	17.6 / 22.0 / 26.4
line-6 28964.9–28993.2 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 29013.2–29041.5 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 29069.8–29098.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 29174.6–29202.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 29251.2–29279.5 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 29384.3–29517.5 m	100.0	32	4	17.6 / 22.0 / 26.4
line-6 29537.5–29642.3 m	100.0	28	3	17.6 / 22.0 / 26.4
line-6 29747.2–29832.0 m	100.0	20	3	17.6 / 22.0 / 26.4
line-6 30271.4–30328.0 m	75.0	16	2	13.2 / 16.5 / 19.8
line-6 30404.6–30509.4 m	100.0	28	3	17.6 / 22.0 / 26.4
line-6 30566.0–30670.8 m	100.0	28	3	17.6 / 22.0 / 26.4
line-6 30719.1–30824.0 m	100.0	28	3	17.6 / 22.0 / 26.4
line-6 30880.6–30900.6 m	25.0	8	0	4.4 / 5.5 / 6.6
line-6 30928.8–30957.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-6 30985.4–31376.5 m	100.0	80	12	17.6 / 22.0 / 26.4

Elevated segment	Longest unit m	Bearings	Internal connections	Hot movement mm at 8 / 10 / 12 µstrain/K
line-6 31558.0–45184.7 m	100.0	2732	409	17.6 / 22.0 / 26.4
line-6 45212.9–46137.2 m	100.0	188	27	17.6 / 22.0 / 26.4
line-6 46277.2–46297.2 m	25.0	8	0	4.4 / 5.5 / 6.6
line-6 47585.5–47605.5 m	25.0	8	0	4.4 / 5.5 / 6.6
line-7 0.0–20.0 m	25.0	8	0	4.4 / 5.5 / 6.6
line-7 3153.1–3173.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-7 3493.1–3513.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-7 5093.1–5113.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-7 9310.8–9339.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-7 11202.2–11222.2 m	25.0	8	0	4.4 / 5.5 / 6.6
line-7 12467.8–12487.8 m	25.0	8	0	4.4 / 5.5 / 6.6
line-7 12516.1–12564.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-7 12644.4–12672.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-7 13002.4–13022.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-7 13227.2–13315.5 m	100.0	20	3	17.6 / 22.0 / 26.4
line-7 13432.1–13452.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-7 13548.7–13605.2 m	75.0	16	2	13.2 / 16.5 / 19.8
line-7 13918.4–13938.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-7 14046.7–14930.3 m	100.0	180	27	17.6 / 22.0 / 26.4
line-7 14930.3–15243.5 m	100.0	68	9	17.6 / 22.0 / 26.4
line-7 15331.8–23098.8 m	100.0	1556	233	17.6 / 22.0 / 26.4
line-7 23118.8–23323.6 m	100.0	48	6	17.6 / 22.0 / 26.4
line-7 23793.3–23841.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-7 24283.0–24567.9 m	100.0	60	9	17.6 / 22.0 / 26.4
line-7 24784.4–24872.7 m	100.0	20	3	17.6 / 22.0 / 26.4
line-7 25021.0–25089.3 m	75.0	16	2	13.2 / 16.5 / 19.8
line-7 25157.6–25197.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-7 25265.9–25285.9 m	25.0	8	0	4.4 / 5.5 / 6.6
line-7 25354.2–25402.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-7 25599.0–39957.0 m	100.0	2876	431	17.6 / 22.0 / 26.4
line-8 1198.0–1298.0 m	100.0	20	3	17.6 / 22.0 / 26.4
line-8 2029.1–2057.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 2114.0–2170.5 m	75.0	16	2	13.2 / 16.5 / 19.8
line-8 2661.7–2746.5 m	100.0	20	3	17.6 / 22.0 / 26.4
line-8 2843.1–2871.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 3370.8–3390.8 m	25.0	8	0	4.4 / 5.5 / 6.6
line-8 3943.3–3971.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 4402.7–4431.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 4471.0–4499.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 4519.3–4615.9 m	100.0	20	3	17.6 / 22.0 / 26.4
line-8 6159.0–6199.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 6259.0–6279.0 m	25.0	8	0	4.4 / 5.5 / 6.6
line-8 6339.0–6379.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 7483.8–7523.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 7723.8–7803.8 m	100.0	20	3	17.6 / 22.0 / 26.4
line-8 8223.8–8283.8 m	75.0	16	2	13.2 / 16.5 / 19.8
line-8 10971.5–11019.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 11684.1–11732.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 11760.6–11780.6 m	25.0	8	0	4.4 / 5.5 / 6.6
line-8 12002.1–12050.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 12146.9–12175.2 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 12561.5–12609.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 12629.7–12678.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 12706.3–12726.3 m	25.0	8	0	4.4 / 5.5 / 6.6
line-8 12996.0–13044.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 13112.6–13152.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 13765.7–13822.3 m	75.0	16	2	13.2 / 16.5 / 19.8
line-8 13878.9–13907.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 14012.0–14052.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 14248.6–14305.1 m	75.0	16	2	13.2 / 16.5 / 19.8
line-8 14325.1–14353.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 14551.4–14599.7 m	50.0	12	1	8.8 / 11.0 / 13.2

Elevated segment	Longest unit m	Bearings	Internal connections	Hot movement mm at 8 / 10 / 12 µstrain/K
line-8 14668.0–14696.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 14999.1–15027.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 15084.0–15124.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 15144.0–15240.5 m	100.0	20	3	17.6 / 22.0 / 26.4
line-8 15317.1–15365.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 15425.4–15510.2 m	100.0	20	3	17.6 / 22.0 / 26.4
line-8 15595.1–15623.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 16102.8–16131.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 16405.6–16433.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 16462.2–16490.5 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 16575.3–16603.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 17549.3–17569.3 m	25.0	8	0	4.4 / 5.5 / 6.6
line-8 17669.3–17689.3 m	25.0	8	0	4.4 / 5.5 / 6.6
line-8 20555.5–20583.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 22429.1–22457.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 23874.2–45066.0 m	100.0	4240	636	17.6 / 22.0 / 26.4
line-8 45150.9–45199.2 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 45275.7–45304.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 45465.4–45485.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-8 45573.7–45602.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 45806.9–45826.9 m	25.0	8	0	4.4 / 5.5 / 6.6
line-8 45903.4–45923.4 m	25.0	8	0	4.4 / 5.5 / 6.6
line-8 45951.7–45971.7 m	25.0	8	0	4.4 / 5.5 / 6.6
line-8 46000.0–46108.3 m	100.0	28	3	17.6 / 22.0 / 26.4
line-8 46128.3–46196.6 m	75.0	16	2	13.2 / 16.5 / 19.8
line-8 46321.4–46349.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 46369.7–46409.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 46566.3–46626.3 m	75.0	16	2	13.2 / 16.5 / 19.8
line-8 46686.3–46754.6 m	75.0	16	2	13.2 / 16.5 / 19.8
line-8 47051.1–47091.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-8 47703.7–47732.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 0.0–1445.7 m	100.0	292	43	17.6 / 22.0 / 26.4
line-9 1602.3–1730.5 m	100.0	32	4	17.6 / 22.0 / 26.4
line-9 1895.4–1963.7 m	75.0	16	2	13.2 / 16.5 / 19.8
line-9 2108.5–2373.4 m	100.0	56	8	17.6 / 22.0 / 26.4
line-9 2489.9–2509.9 m	25.0	8	0	4.4 / 5.5 / 6.6
line-9 2558.2–2606.5 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 2654.8–2674.8 m	25.0	8	0	4.4 / 5.5 / 6.6
line-9 2723.1–2743.1 m	25.0	8	0	4.4 / 5.5 / 6.6
line-9 4130.2–4408.2 m	100.0	60	9	17.6 / 22.0 / 26.4
line-9 4456.5–4476.5 m	25.0	8	0	4.4 / 5.5 / 6.6
line-9 4613.0–4701.3 m	100.0	20	3	17.6 / 22.0 / 26.4
line-9 4769.6–4917.9 m	100.0	32	4	17.6 / 22.0 / 26.4
line-9 5114.5–5162.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 5359.3–5447.6 m	100.0	20	3	17.6 / 22.0 / 26.4
line-9 5515.9–21514.4 m	100.0	3200	480	17.6 / 22.0 / 26.4
line-9 21779.3–25230.6 m	100.0	696	104	17.6 / 22.0 / 26.4
line-9 26275.5–26315.5 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 26335.5–27430.0 m	100.0	220	33	17.6 / 22.0 / 26.4
line-9 29051.5–29148.0 m	100.0	20	3	17.6 / 22.0 / 26.4
line-9 29216.3–29332.9 m	100.0	28	3	17.6 / 22.0 / 26.4
line-9 30555.7–30584.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 30948.9–32167.7 m	100.0	248	36	17.6 / 22.0 / 26.4
line-9 35029.3–35057.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 35479.0–35575.6 m	100.0	20	3	17.6 / 22.0 / 26.4
line-9 35603.9–35643.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 35663.9–35752.2 m	100.0	20	3	17.6 / 22.0 / 26.4
line-9 38993.3–39013.3 m	25.0	8	0	4.4 / 5.5 / 6.6
line-9 40961.0–40989.2 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 41876.3–41952.9 m	100.0	20	3	17.6 / 22.0 / 26.4
line-9 42154.3–42182.6 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 43171.2–43199.4 m	50.0	12	1	8.8 / 11.0 / 13.2

Elevated segment	Longest unit m	Bearings	Internal connections	Hot movement mm at 8 / 10 / 12 µstrain/K
line-9 43247.7–43276.0 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 43352.6–43409.1 m	75.0	16	2	13.2 / 16.5 / 19.8
line-9 45362.8–45391.1 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 45749.0–46231.9 m	100.0	100	15	17.6 / 22.0 / 26.4
line-9 46996.1–47044.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 47064.4–49538.6 m	100.0	496	74	17.6 / 22.0 / 26.4
line-9 49798.6–49846.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 50569.8–50722.9 m	100.0	36	5	17.6 / 22.0 / 26.4
line-9 50771.2–50791.2 m	25.0	8	0	4.4 / 5.5 / 6.6
line-9 50811.2–50947.8 m	100.0	32	4	17.6 / 22.0 / 26.4
line-9 50996.0–51282.3 m	100.0	60	9	17.6 / 22.0 / 26.4
line-9 51823.2–51871.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 52201.1–52269.4 m	75.0	16	2	13.2 / 16.5 / 19.8
line-9 52326.0–52354.3 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 52975.1–53031.7 m	75.0	16	2	13.2 / 16.5 / 19.8
line-9 53131.7–53171.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 53191.7–53291.7 m	100.0	20	3	17.6 / 22.0 / 26.4
line-9 53471.7–53491.7 m	25.0	8	0	4.4 / 5.5 / 6.6
line-9 55268.2–56288.2 m	100.0	208	30	17.6 / 22.0 / 26.4
line-9 58207.7–59592.2 m	100.0	280	42	17.6 / 22.0 / 26.4
line-9 60590.2–60618.4 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 61036.4–61064.7 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 61695.8–61775.8 m	100.0	20	3	17.6 / 22.0 / 26.4
line-9 61815.8–61855.8 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 61984.1–62040.7 m	75.0	16	2	13.2 / 16.5 / 19.8
line-9 64778.6–64798.6 m	25.0	8	0	4.4 / 5.5 / 6.6
line-9 64826.9–64866.9 m	50.0	12	1	8.8 / 11.0 / 13.2
line-9 66283.1–66339.7 m	75.0	16	2	13.2 / 16.5 / 19.8
line-9 66367.9–93067.1 m	100.0	5340	801	17.6 / 22.0 / 26.4

Mapped soil has 63 incomplete profiles. Prioritise investigation and settlement/drainage monitoring; mapped pH/texture do not determine bearing resistance, pile depth, sulfate/chloride exposure or a coating category.

[Location-specific soil investigation plan](#). Flag counts: {"coverage-gap": 63, "fine-soil-plasticity-and-shrink-swell-tests": 3228, "granular-density-and-groundwater-tests": 1828, "silt-moisture-frost-and-erosion-review": 2005}.

Joints, paints, finishes and cleaning

Steel, GFRP body and roof finish zones retain their shared qualified process. Protect electrical bond lands, seals, drains, PV glass and inspection areas. Radiative paint remains a trial option; no unverified cooling benefit enters the energy model.

Work package	Asset-level tasks generated
rs-finish-seal-joint	762
rs-controlled-wash	762
civil-joint-drain-finish	325
energy-soiling-cleaning	140

The operations bundle carries these inspection/cleaning triggers, owners and required work-order evidence. Cleaning intervals follow measured condition and access; material compatibility and wash-water handling must be qualified locally.

Release inputs still required:

- civil movement: complete deployment train axle positions and loaded distribution; component temperature extremes and erection temperature; measured concrete CTE/shrinkage/creep; selected connection load path, construction stages and bearing restraint; rail interaction, seismic and foundation movement; surveyed supports and abutment movement details.
- fasteners: joint loads and fatigue spectrum; fastener grade and proof load; actual finish/lubrication torque-tension trial; preload loss, slip/separation, bearing and thread checks.
- seals: supplier qualified compression range and ageing; actual thickness, land gap and tolerances; module thermal mismatch and vibration; water-ingress test after assembly and cleaning.
- finishes: local exposure and substrate preparation qualification; approved product system and batch TDS limits; DFT/adhesion/cure and fire/UV/wash qualification; masking, repair and inspection records.

- cleaning: measured washable area by material, not canopy area; trial person-minutes, water and safe access windows; detergent/nozzle/material compatibility; wash-water collection and local disposal route.

[Structured report](#) · [Workforce spreadsheet](#) · [Deployment gates](#)

Baghdad line-local depot and stabling quantity package

Source: cities/catalogue/west-asia/iraq/baghdad/engineering/delivery-baseline/DEPOT-PACKAGE.md

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

The original allocation remains 265 station trains + 497 depot/storage trains = 762 and its morning-direction check remains failed. The 4 missing directional starts require an operating/stabling revision with conflict-aware evening returns, morning launches, recovery and degraded charging. This package does not turn storage capacity arithmetic into a physically accepted allocation.

Line	Station storage ID	Storage positions	Usable track m	Tracks / turnouts	Declared / workload bays
line-1	line-1-0166-0866-s049067	52	6,292	18 / 20	0 / 12
line-2	line-2-0595-0296-s052851	67	8,107	23 / 25	115 / 14
line-3	line-3-0151-1637-s049496	65	7,865	22 / 24	0 / 14
line-4	line-4-1246-1628-s042068	54	6,534	18 / 20	0 / 11
line-5	line-5-0677-2304-s047321	60	7,260	20 / 22	0 / 12
line-6	line-6-0495-1669-s052503	74	8,954	25 / 27	0 / 14
line-7	line-7-1531-0418-s039957	53	6,413	18 / 20	0 / 11
line-8	line-8-0785-0290-s047849	68	8,228	23 / 25	0 / 13
line-9	line-9-0819-0573-s090161	4	484	2 / 4	0 / 6

The planning arrangement uses at most three 121 m usable train slots per storage track, separate fan/throat turnouts and 5 m track spacing, with a 1.8 access/land multiplier. Track metres are single-track storage lengths, not route-km or workshop bays. Yard geometry is not located on a surveyed parcel. Storage charging shares existing powered sites; connecting tracks, peak chargers/feeders, protection, rescue access and quarantine need site engineering.

One alternative retains the declared 125 main-depot bays and zero workshop bays at eight line-local sites. Another derives line-local bays from an explicit 400 bay-hours/train/year sensitivity, 260 days/year, 16 hours/day and 70% bay availability. Neither is a released maintenance requirement. Bogie changes, heavy inspections, isolation, lifting, wash/cleaning, tools, stores and travel must establish actual bay occupation; person-hours are not bay-hours. The second alternative avoids assuming an unestablished interline move to the main workshop. Both price line-local inspection, rescue/isolation, quarantine, storage track/points, drainage/access, workshop shells/equipment and full depot PV/storage equipment quantities.

[Detailed items](#) show reference quantities and unquoted rates. The existing energy report's USD 5.93m increment above the catalogue equipment and 33,333 m² PV module requirement versus 4,000 m² canopy remain open. This package prices full 5 MW PV / 40 MWh equipment once; it does not also add the USD 5.93m delta. Equipment is not installed plant cost. PV placement, foundations/soil, battery fire spacing, DC protection, racking, utility connection and renewals are unpriced. Signed overlap decisions must reconcile the USD 8m depot and USD 67.6m charging allowances before adopting any replacement budget.

Baghdad delivery estimate and scope reconciliation

Source: <cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-baseline/ESTIMATE.md>

The published USD 7.515079bn equivalent is a base planning estimate, not a complete delivery budget. City subtotal is USD 7.168534bn and the one Baghdad factory including its EPC is USD 346.545m. [Scope register](#) retains quantity, implied rate, currency/source quality, inclusions, exclusions, estimator role and uncertainty. Every actual price date, quotation and named estimator remains unknown. Category implied rates reconcile the baseline; they are not surveyed rates.

Baseline WBS	Quantity	USD m equivalent	Evidence
civil	474.180	3,889.522	category-planning-estimate
stations	164.000	741.900	category-planning-estimate
depots	1.000	8.000	category-planning-estimate
rolling_stock	762.000	1,280.160	category-planning-estimate
solar_plant	934,208.924	747.367	category-planning-estimate
signalling	474.180	23.709	category-planning-estimate
charging_microgrid	1.000	57.800	category-planning-estimate
epc_overhead	1.000	420.076	category-planning-estimate
factory-direct	1.000	323.874	factory-sizing-allowance
factory-epc	1.000	22.671	factory-sizing-allowance

12 additional scope records retain null costs, not zero: land/title, utility diversions, duties/tax, owner costs, pre-opening people, six-car qualification, installed control/HIL, initial spares, working capital, civil/station investigations, task-derived maintenance and cyber deployment. Each requires a signed inclusion/quotation decision before financing is recalculated. Surveyed grade separation, foundations, standard spans, temporary works/erection, passenger access/evacuation, road interfaces and station functions must be investigated by corridor; civil and station standards alone do not resolve them.

EPC has [identified delivery obligations](#), with individual priced contracts still null. Their sum cannot be asserted from the existing percentage. Factory contingency USD 53.979m, factory design/training/qualification USD 20.0m, routine train QA/labour/logistics and factory EPC are already embedded and must not be added twice. Initial stock, battery renewal cash dates, labour/maintenance contracts and working-capital reserves need account-level reconciliation.

Depot alternative	Gross priced reference USD m	Provisional replacement total USD bn
retained_declared_bays	168.982	7.676062
workload_bays	161.006	7.668086

Replacement illustrations subtract the old depot allowance once, then add the gross quantity-based reference. They remain incomplete: charging/PV/EPC overlaps and unpriced work are unresolved. No alternative is adopted into the published funding programme; government/import shares, loans and opening dates remain conditional on the original scope. Retained property additions remain their existing separate scenarios, not automatically added to this base.

The seeded [correlated cost-and-delay sensitivity](#) combines a shared risk quantile with idiosyncratic cost events and delay escalation. Illustrative known-scope P50 is USD 9.320bn and P80 USD 10.041bn. These are uncalibrated distributions, not an approved probabilistic budget. Unpriced scope is excluded rather than priced at zero; existing contingencies remain embedded; stress outputs are alternatives and cannot be added to the base. Calibrate from investigations, contract evidence, event-level dependencies and actual invoice dates. [GAO estimating guidance](#) supports technical baseline, WBS, data, alternatives, risk analysis and updates; it does not validate OSR's rates. Reference checked 4 October 2026.

Baghdad comparable opening fleet and corridor requirements

Source: <cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-baseline/FIRST-PHASE.md>

Demand is capacity-led in the existing model; population coverage is an access proxy. This [line-specific supply comparison](#) tests 6-minute opening peak service, 12-minute off-peak and 15-minute late service, 10% spares and retained cold reserves. Cycle time is inferred from the current peak fleet x minimum headway, not independently proved junction/turnback occupancy. Each line retains its published conditional full-line opening date.

Line	Opening month	Full fleet	Opening fleet	Deferred trains	Opening daily capacity
line-1	40	86	44	42	172,800
line-2	45	101	52	49	172,800
line-3	50	97	50	47	172,800
line-4	55	80	41	39	172,800
line-5	59	86	44	42	172,800
line-6	65	100	51	49	172,800
line-7	69	79	41	38	172,800
line-8	74	90	47	43	172,800
line-9	76	43	44	0	167,400

The reference opening fleet is 414 versus 762, deferring 349 trains / USD 586.320m gross equivalent, while requiring 1 extra train / USD 1.680m to meet the rounded spare policy on line 9. Net reduction is 348 trains at the current planning unit price. This is deferred procurement, not a validated saving or adopted service cut. Train-km and directional capacity fall with the new service; unchanged fares/revenue are never assumed. Expansion requires measured peak demand above 70% for 90 days, conflict-aware capacity, accepted spares and a newly financed delivery tranche.

Commercial corridor ranks, OD, access population and paid trips remain null. Compare actual origins/destinations/time, transfers vs paid boardings, accessibility/feeder catchments, fares, useful interchanges and standalone OPEX before choosing a first corridor. The existing 14.034 km outer-line demonstrator remains unproven commercially. Shared factory/civil/utility/control dependencies, accepted vehicles, staffing and operating release must accompany any opening. No earlier date or factory resize is asserted from vehicle subtraction alone. Existing acceleration/recovery cost-NPV trade-offs remain unchanged.

Baghdad chronological charging-energy and cost screen

Source: cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-baseline/HOURLY-ENERGY.md

The base traction intensity and timetable imply 1,881.3 GWh/year. The dedicated plant is 934.2 MW, plus existing on-site PV and 318 MWh storage. The base model's annual generation netting is not firm delivered charging. Ten percent of traction purchased at USD 0.10/kWh is USD 18.813m/year, an arithmetic sensitivity, not a forecast.

Hourly CSVs contain three 8,760-hour synthetic representative weather/age years for each of owned solar, contracted solar and additional hybrid storage. They use the same timetable-derived service duty, with overnight schedules split across midnight; charger loss, PV performance/wheeling loss, storage charge/discharge losses, SoC floor, age degradation, import limits and curtailment are explicit. A seven-day poor-production spell is included. Initial storage sits at its protected floor, supplying no free energy. End storage is recorded and not sold.

Synthetic case	Grid GWh	Unservd GWh	Annual energy USD m	Extra hybrid equipment USD m
synthetic_reference:owned_solar	860.2	2.664	126.296	0.0
synthetic_reference:contracted_solar	860.2	2.664	187.585	0.0
synthetic_reference:hybrid_storage	398.4	2.664	80.115	180.0
synthetic_poor_year:owned_solar	978.5	2.818	134.092	0.0
synthetic_poor_year:contracted_solar	978.5	2.818	177.257	0.0
synthetic_poor_year:hybrid_storage	744.4	2.818	110.683	180.0
synthetic_aged_year_10:owned_solar	878.0	2.664	128.077	0.0
synthetic_aged_year_10:contracted_solar	878.0	2.664	189.366	0.0
synthetic_aged_year_10:hybrid_storage	454.3	2.664	85.699	180.0

Electricity purchase, wheeling, balancing, capacity connection and owned-plant maintenance / contracted-solar payment are separate. PPA pays generated output even if curtailed; no surplus power sale is booked. The contracted case removes dedicated solar ownership capital and O&M, not existing station equipment. Hybrid storage adds its priced equipment once, with installed compound/protection, disposal and replacement costs still unquoted. Twenty-year indexed discounted cost is a partial comparison, not lifecycle bankability; no contract or tariffs are accepted. Unserved demand means the assumed service is unmet: no unchanged fares are credited to that service.

Aggregate connection and storage pooling are optimistic and unestablished. This screen does not supply site-specific wheeling rights or instantaneous charger arrival/queue proof. Measured multi-year weather/soiling, per-site feeder/charger duty, auxiliary loads, storage cycling/degradation, grid outages and binding backup contracts must be replayed before changing the funding programme's electricity allowance or selecting an ownership option.

Baghdad delivery reconciliation — 4 October 2026

Source: [cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-baseline/README.md](https://github.com/OpenSourceRail/cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-baseline/README.md)

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

The original Baghdad estimate is USD 7.515079bn equivalent, with an incomplete delivery scope. This package turns the attached review into reproducible quantity/cost/workload comparisons and six budgeted evidence workstreams. It adds no assumed passengers, leases, supplier quotes, appointments or approval, and does not replace the published finance case before scope is accepted.

- [Base estimate, exclusions, EPC and correlated cost/schedule sensitivity](#)
- [Line-local storage/depot quantities and alternative workshop scopes](#)
- [Six-car BOM, mass/axle ledger, interfaces, labour and qualification](#)
- [Chronological generation/charging/storage and ownership comparisons](#)
- [Opening fleet and first-corridor demand requirements](#)
- [Workload establishment, recruitment, curricula and eligibility pilot](#)
- [Baghdad-specific governance instance](#)
- [Six 90-day evidence workstreams and budgets](#)

The governance instance is tailored to Baghdad with accountable functions and closure work, while 0/13 appointments, 0/11 systems and 0/8 gates remain ready/accepted. Names, appointment/competence evidence, legal entity and delegations remain pending. Role allocation is not a real appointment. Native ERP evidence Tasks remain open and do not approve budgets, manufacture or operation. Cybersecurity identity/secrets/updates/recovery/incident ownership and observation-only supervision boundaries retain their existing deployment gates.

Fresh-checkout validation: install the existing project test/render dependencies, then run `.venv/bin/python tools/automation/bootstrap_baghdad_tests.py` before the Baghdad tests. It selectively restores the exact ignored operations input from the tracked, hash-bound proposal archive, rejects drift/duplicate entries and preserves any differing workspace payload. It does not resynthesise the city or change controlled station IDs. Run the bootstrap with `--check` to verify only.

Regenerate `.venv/bin/python tools/automation/baghdad_delivery_base_line.py`, then the proposal. `--check` verifies all input/output hashes. None of the calculated alternatives has been accepted as an investment-ready budget.

- [Rental fit-out allocation and inspection-interruption comparison](#)

Rental delivery allocation sensitivities

Source: [cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-baseline/RENTAL-DELIVERY.md](#)

The existing medium portfolio retains identical physical fit-out and timing. These unquoted arrangements allocate costs and receipts; they create no extra funding, accepted tenant demand or macroeconomic saving.

Option	Landlord capital USD m	Partner capital USD m	Landlord before-tax NPV USD m	Partner value NPV USD m	Combined value NPV USD m
landlord_funded	87.523	0.000	18.132	0.000	18.132
tenant_funded_shell	52.514	35.009	19.783	-1.651	18.132
developer_concession	0.000	87.523	29.816	-11.684	18.132

Tenant-funded shells assume tenants pay 40% of fit-out/refurbishment for a 20% rent discount; their value column is avoided rent minus costs, not cash receipts or trading profit. The developer concession allocates 35% of collected rent and 20% of routine costs to the landlord; the developer funds fit-out/refurbishment. No concessions or subscriptions are signed.

All options lose two months of proportional rent every ten years after each cohort handover for structural inspection access. Routine costs continue. Maintenance work, compensation, tax, actual interruption dates and contract terms remain unpriced. [Monthly ledgers and limitations](#) keep each party and combined value separate. The existing property/finance cases remain unchanged. Actual market enquiries and a small accepted pilot must determine selection.

Baghdad controlled six-car planning product

Source: [cities/catalogue/west-asia/iraq/baghdad/engineering/delivery-baseline/SIX-CAR-BASELINE.md](#)

Configuration M6-A-DRAFT, family metro-6car, covers 762 consists / 4572 cars at 111 m, 204 t controlled tare, 720 passengers / 960 crush, 1,350 kWh gross / 1,080 usable battery, 675 V nominal and 50 C HVAC ambient. [Family BOM](#) and [interface/qualification register](#) are separate from LM3's detailed 120-product manufacturing reference. Every quote, supplier part, mass evidence, production BOM and acceptance remains null/unaccepted. Common architectural ideas do not grant six-car applicability.

Six-car cost/mass category	Count / unit	Mass kg/consist	Allocated USD/consist
M6-carbody-structure	6 car	78,000	420,000
M6-bogie-running-gear	12 bogie	45,000	300,000
M6-traction-controls	12 controller	13,200	180,000
M6-battery-modules	6 225 kWh gross module	8,700	270,000
M6-interior-doors-glazing	6 car kit	42,000	240,000
M6-thermal-roof-services	6 car kit	12,000	90,000
M6-trainline-couplers	1 six-car system	1,500	70,000
M6-assembly-qa-logistics	1 consist	0	110,000

Cost allocations sum to the existing USD 1,680,000/train. These are a control allocation of the price ceiling, not supplier estimates. The category mass subtotal is 200,400 kg and unallocated controlled-tare reserve 3,600 kg; no weighed closure is claimed. There are 24 reference axles: average tare load 8.50 t and crush load 11.50 t using an explicit 75 kg/passenger assumption. Individual axle/bogie imbalance, payload distribution and structural limits require calculations and weighing. The system schedule has 24 door cassettes and 36 window cassettes. Five inter-car interfaces, trainline/brake propagation, accessible platform/door interfaces, redundant controls, HV/charging, thermal/fire/EMC/harness interfaces each carry an acceptance requirement.

[Labour routes](#) use the actual Baghdad factory stages, reference crew and cycle days. None is a measured six-car cycle. Rework, supplier queues and the current test-path throughput margin need trials; scaling an LM3 cycle is not evidence. Factory production payroll stays within train procurement, separate from railway operating payroll and factory capital. Work Order / Job Card references remain null until production BOMs, method revisions, calibrated tools, qualified operators and independent inspections exist.

The first-article qualification work breakdown has a USD 12.0m unquoted reference. Its incremental funding is null because overlap with the factory's USD 20.0m design/training/qualification allowance remains unresolved. No automatic extra qualification or train premium is added. Supplier quotes, a detailed child-part BOM, structural/braking/trainline/thermal testing, acceptance labour and series-release authority must replace the planning controls before manufacture.

Baghdad workload, recruitment and competence pilot

Source: <cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-baseline/WORKFORCE-COMPETENCE.md>

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

The prior 3,217 FTE / USD 36.188m/year allowance is USD 937.42/person/month. The existing 21-role weighted split remains a budget allocation, not shift cover. This separate [establishment](#) derives posts/task hours, 1520 productive hours per FTE after leave, training, sickness and travel/handovers, integer cover and editable grade pay with employer/overtime allowances.

Function	Annual workload h	Concurrent posts	Reference FTE	Loaded annual IQD m
occ-lead	7,482	1	5	157.9
dispatcher	67,342	9	45	947.7
remote-assist	643,495	86	428	9,013.7
station-lead	127,202	17	88	2,779.9
platform-assistance	1,227,130	164	810	10,235.2
customer-service	306,782	41	206	2,603.0
station-cleaning	179,580	0	122	1,541.6
workshop-lead	37,440	9	27	852.9
fleet-mechanical	365,760	0	245	5,159.7
fleet-electrical	243,840	0	166	3,496.0
fleet-finish-cleaning	556,260	0	371	4,688.0
infrastructure-lead	18,720	9	18	568.6
civil-track	151,738	0	105	2,211.3
solar-storage	84,000	0	61	1,284.7
wayside-comms	65,600	0	47	989.8
city-director	1,520	1	1	31.6
chief-engineer	1,520	1	1	31.6
quality-safety	34,207	0	23	726.6
training	37,040	0	25	526.5
procurement-stores	27,780	0	19	400.1
finance-people	18,520	0	13	273.8

Reference total is 2,826 operating FTE, loaded payroll USD 37.323m/year equivalent. Quantities are explicit task-hour/post assumptions, not measured local work or accepted Iraqi pay/rest terms. Higher overtime, emergency cover, queues, simultaneous faults and actual maintenance could change them. The dedicated solar plant specialist workload is unpriced. Maintenance contracts and payroll must be reconciled to avoid adding contractor labour twice to existing envelopes. No revised OPEX is silently adopted.

Factory 1,094 direct staffed-shift positions are separate; their production payroll is already in train procurement. Construction crew counts remain unknown and separate, rather than scheduled task slots called people. Temporary commissioning has its own cash requirement.

[Recruitment cohorts](#) work backwards from each conditional line opening through requisition, selection, joining, training, first/repeated assessment and supervised experience. Offers allow 15% pre-join attrition and 80% first-pass / 75% repeat-pass assumptions. Hiring alone provides zero authorised productive capacity. Paid pre-opening training plus trainer/assessor reference cash is IQD 33.252bn; additional three-month commissioning payroll is IQD 0.853bn. These are distinct pre-opening uses, with overlap against EPC still unverified; rigs, agency fees and local terms remain unquoted. No trained/appointed person is invented.

[Seven controlled curriculum drafts](#) cover induction, OCC, stations/accessibility, fleet, civil/energy, factory and supervisors/assessors. Each lists prerequisites, method revision, equipment, practical exercises, critical assessment criteria, assessor requirements and retraining triggers. [Arabic glossary](#) is a draft requiring native technical review; full Arabic lessons are pending. Attendance, practical competence and scoped task authorisation are separate records.

The [seven-day first-corridor OCC roster](#) contains actual service-hour coverage requirements and zero named workers. Every slot is blocked pending appointments and task-specific authorisation. The executable [eligibility evaluator](#) checks worker record, assessed task/asset-family/location/method scope, validity, suspension, skill fade, availability, checked rest, access, permits, tools/materials, competent supervision and independent verification. Evaluate both at planning and task start; changed or expired evidence blocks eligibility. It creates no assignment or operational release.

Department owns outcomes/budget/risk; unit owns assets/backlog; crew owns executable access-window work; worker owns a scoped method/evidence; verifier owns independent acceptance/handback. [Native ERP mappings](#) retain Staffing

Plan/recruitment/Employee/onboarding/training/shift records, manufacturing Work Order/Job Card and maintenance Asset Maintenance/Asset Repair, with Project/Task for programme evidence. Dashboards track accepted output, blocks, competence expiry, shortages, overdue hazards and forecast cost; attendance or Task closure never counts as physical acceptance. Deploy permissions/recovery/rest rules against actual records before enabling assignment.

[Frappe staffing documentation](#) supports administrative records. [ORR competence guidance](#) is a useful reference for assessment/monitoring/reassessment, not Iraqi legal approval. References checked 4 October 2026.

Comparable standalone opening corridors

Source: <cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-closure/CORRIDOR-COMPARISON.md>

Each corridor pays for its own workload/shift cover including central leadership, existing maintenance/solar shares and per-site energy service assumptions. The price test uses the same current fare, 20% capacity-use sensitivity and existing station commercial revenue allocation. Debt, tax, land, parcel-specific works, interchange effects and grid upgrades remain outside this operating-only break-even. OD and access evidence remain null, so no commercial rank or first-corridor selection is fabricated.

Line	Fleet	FTE	OPEX USD m/year	Operating-neutral paid trips m/year	Neutral capacity use	Fare at 20% use IQD
line-1	44	250	23.120	20.497	32.5%	2140
line-2	52	269	25.151	22.364	35.5%	2336
line-3	50	272	23.993	21.085	33.4%	2202
line-4	41	225	20.308	17.995	28.5%	1879
line-5	44	237	22.552	20.073	31.8%	2096
line-6	51	263	25.220	22.569	35.8%	2357
line-7	41	225	19.560	17.256	27.4%	1802
line-8	47	244	23.133	20.645	32.7%	2156
line-9	44	373	39.134	34.390	56.3%	3707

[Detailed cases and investigation forms](#) retain fares, affordability, OD/transfers, paid demand, pedestrian/feeder catchments, interchange and standalone debt-service fields. The affordability column prices 44 monthly trips against the historical model income proxy; it is not surveyed disposable income. Lower vehicle procurement reduces service/capacity; unchanged receipts and earlier openings are not assumed. Surveyed ground, utilities, foundations, drainage, erection/temporary works, evacuation/access and actual shared dependencies must accompany selection. A 10% civil opportunity is not claimed as a saving.

Nine depot/storage design studies and Iraqi slab manufacture

Source: [cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-closure/DEPOTS-SLAB-MANUFACTURE.md](#)

[Located track and slot register](#) identifies 497 storage positions, 169 tracks, 60,137 usable track metres, 120,274 rail metres and 200,464 reference fixation-seat kits. 50,912.0 m³ concrete is a geometric reference for yard slabs, excluding foundations, reinforcement, grout/stray-current systems and point panels. Existing track/package costs are not supplemented by these quantities a second time.


Line	Slots	Storage tracks	Workshop bays	Layout
line-1	52	18	12	SVG
line-2	67	23	14	SVG
line-3	65	22	14	SVG
line-4	54	18	11	SVG
line-5	60	20	12	SVG
line-6	74	25	14	SVG
line-7	53	18	11	SVG
line-8	68	23	13	SVG
line-9	4	2	6	SVG

Drawings use local planning coordinates and distinguish storage slots from workshop bays. Rectangular packing can include unused end positions; it creates no acquired parcel or released alignment. Throat radii, bypass/escape tracks, drainage/outfalls, road/fire/evacuation access, utilities, lifting/inspection/rescue/quarantine areas and grid connection need actual surveys and supplier footprints. Line 6 requires about 33,333m² PV module area; no 4,000m² canopy is credited as adequate.


The yard-only slab production study requires 12 parallel mould cells at a one-working-day cycle/75% utilisation, ready month 18 and delivering two months before each opening. Its [prefix-capacity programme](#) includes cut/end panels and never casts beyond usable lengths. Moulds, curing/QA, batching, reinforcement, transport, lifting and installation require quantities/quotes and measured cycles. Factory CAPEX is null, not free. Main-line slab manufacture is a different existing production requirement; these cells cannot be represented as its total capacity. Iraqi casting/assembly remains a proposed procurement route, not a qualified plant.

Baghdad line-6: storage and workshop planning study

Local coordinates only. NOT a surveyed, structurally released or operationally authorised layout.



Workshop packing; internal track access unresolved



25 storage tracks / 74 slots / 8954 usable track m

Yard packing envelope 363 x 225 m; access/point/land geometry unresolved

Workshop: 14 bays; shell packing 605 x 30 m

Inspection, rescue, battery quarantine, PV/BESS, drainage outfall and fire access require located design.

Green blocks: 111 m trains + 10 m slot clearance. Actual train assignments and charger circuits remain empty.

No drawing footprint is credited as acquired land or accepted turnout geometry.

Line 6 storage and workshop packing study

[Startup alternatives](#) compare the existing revenue fleet with the frozen original dispatch-point set, including 4 missing line-9 directions. Holding that set fixed requires 4 extra revenue trains and 2 extra spares: USD 10.08m vehicle reference, before consequential costs. Adding trains must not silently expand dispatch-point selection. Reserving fewer start points or buying trains requires a separate selected-start, cycle, turnback, depot/charging and funding replay; neither changes the baseline nor closes the existing failed gate.

Development leadership and training mobilisation

Source: <cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-closure/DEVELOPMENT-TRAINING.md>

Interim function	Start month	Operating handover month	Loaded IQD/month
city-director	0	40	2,632,500
chief-engineer	0	40	2,632,500
development-training-head	18	40	1,755,000

Interim development authorities begin at NTP. The training head mobilises at month 18; rigs must be ready by month 24, before operating cohorts join. [Cohort lesson schedules and all operating roles](#) distinguish teaching, initial/repeat assessment, supervised experience and handover. Named incumbents/successors, qualified assessors, equipment and signed handovers remain absent.

[Monthly capacity and cash](#) buys the existing contracted teaching/assessment allowance once. New interim leadership and external supervision add IQD 2.381bn before inflation, explicitly included in the integrated financing cases. Operating trainees supply zero qualified teaching/assessor/mentor capacity. These hour-derived minimum posts require actual competence, rig availability, observation ratios and daily/rest schedules; they do not establish an operating roster. The OCC pilot remains an anonymous rest-constrained example; all 21 roles have coverage and lesson requirements, with actual full rosters still unaccepted.

The native Employee attachment preview validates a controlled snapshot only. It returns `snapshot_eligible` for those assertions, keeps `eligible` and `live_start_check` false, and does not resolve current authoritative revocation. Real task start requires current permits, calibration, stock release, competence, availability and human work-release authority.

Field investigations, quotations and actual appointments

Source: [cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-closure/FIELD-WORK-PACKETS.md](#)

[Scope inclusion forms](#), [supplier requests](#), [corridor investigations](#) and [six work packages](#) turn unresolved items into defined data collection and independent exit criteria. No external contact has been made. Existing USD 360,000 estimator-work budget is an unquoted closure allowance with EPC overlap unknown, not committed funding or priced boreholes/equipment tests.

Repository artifacts are prepared; all six native evidence Tasks remain open, preserving actual owner/project/dates/status. Actual survey, qualified suppliers, OD/tenant enquiries, Iraqi appointments/approvals, signed finance and subscriptions remain pending. Honest nulls must be replaced by independently accepted evidence before those workstreams can close. [GAO estimating guidance](#) supports technical scope, WBS, data, alternatives/risk and actual-cost updates; it does not validate these rates or release the scheme.

Delivery-cost financial reconciliation

Source: [cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-closure/FINANCE-RECONCILIATION.md](#)

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

These executable sensitivities preserve the original reference, then replace the original depot allowance once and replace labour/solar OPEX once. Incremental EPC is an explicit 7% allowance; qualification credit against the existing factory allowance is explicit. Paid training/assessment/supervised experience and additional commissioning specialists are separate pre-opening cash; no factory production wages are duplicated. Battery top-ups add only the shortfall above reserve contributions already in maintenance. Land, duties, utility diversions, spare inclusion, actual owner insurance and grid/charger upgrade capital remain unpriced.

Case	Capital USD bn	Government USD bn equivalent	Peak gap debt IQD tn	Unfunded support IQD tn	Debt clear without unfunded cash month	Company before-finance cash NPV USD bn
reference	7.515	1.879	4.371	0.000	303	-3.262
reconciled_full_fleet	7.679	1.920	9.517	0.000	None	-4.376
reconciled_fixed_origin al_government	7.679	1.879	9.625	0.000	None	-4.376
reconciled_without_uncommitted_income	7.679	1.920	11.721	0.000	None	-4.376
opening_fleet_supply_scaled	7.094	1.774	13.000	3.965	None	-4.762
contracted_solar	6.931	1.733	11.974	0.000	None	-4.430
installed_energy_supply_bound	7.679	1.920	13.000	0.520	None	-4.844
simple_span_bearing_index	7.799	1.950	9.773	0.000	None	-4.457

The fixed-government case retains the original absolute government contribution and reallocates its USD downpayment within that ceiling. Other cases use 25% of their own capital; increased appropriation is not committed. In every case imports are funded 50% government USD/50% proposed Chinese USD credit; ordinary/green bonds, bank and gap credit remain IQD. All debt/reserve/buffer/principal/cash residuals reconcile. Six-month bond units are placement requirements, not subscriptions. Climate/rights/additional local income remain uncommitted in conditional cases; the dedicated case removes all these targets and green pricing benefits.

Opening-fleet procurement follows the selected supply case and its extra spare. Factory cost/capacity is retained, and opening dates follow the later of civil readiness and replayed fleet acceptance; paid receipts scale with reduced timetable supply and ramps. Future expansion dates and funding remain null. Contracted solar removes city-owned plant CAPEX but keeps provider plant resources visible and charges generation; a private provider, rights, prices and firm deliverability are not established. Company cash NPVs are not like-for-like complete resource NPVs.

[Summary and source-bound cases](#) include full monthly native-currency ledgers, six-month bond/loan sale and repayment schedules, fees, grace, early principal, buffers and terminal debt/cash. Only genuine surplus after all obligations and buffers can fund contractual voluntary repayment; uncovered support cannot fund it. No new public subsidy or tariff adoption is claimed. Baseline fares and OPEX retain 5% growth and the existing elasticity/income assumptions.

[Opening factory replay](#) manufactures exactly 414 planned trains, including the extra line-9 spare, with rebuilt finite factory queues. Dropped orders are removed from manufacturing and invoice cash; original expansion-capable factory CAPEX is retained. Openings are the later of civil readiness and replayed fleet acceptance; later dates flow through receipts, payroll, reserves and the operating horizon. Depots retain full eventual-network capacity; staffing, maintenance, reserve and site energy follow the lower supply. All sensitivities retain zero modelled dividends; retained cash is not distributable profit without taxes, covenants and approvals.

The `simple_span_bearing_index` sensitivity removes the bearing reduction only from existing standard Pi25 length, then adds the declared incremental EPC once. It inherits original civil invoice dates and procurement-origin proportions as assumptions, keeps government at 25%, splits assumed imports 50% USD government cash / 50% Chinese USD credit, and retains all other funding in IQD. Monthly/six-month ledgers, interest, fees, reserves and early repayment are recalculated. This is an unquoted index counterfactual, not a bearing supplier offer; finite end effects, connection costs, actual import eligibility and consequential foundations remain unpriced. OSR-US and special segments do not inherit Pi25 bearing quantities.

Fare/demand/affordability sensitivities

Base fare IQD	Paid-demand multiplier	44-trip income share	Debt-clear month	Terminal gap IQD tn	Before-finance cash NPV USD bn
1500	0.962	13.4%	405	0.000	-4.076
1750	0.918	15.6%	340	0.000	-3.683
2000	0.882	17.8%	297	0.000	-3.306
2500	0.825	22.3%	244	0.000	-2.590
3000	0.781	26.7%	211	0.000	-1.916

[Full results](#) change the base fare once, retain existing peak/off-peak pricing and 5% annual fare/OPEX/income growth, reduce paid trips with the existing uncalibrated elasticity, and scale existing station commercial receipts with demand. Debt clearance and cash NPV are different tests. Conditional green/grant/rights/local-income targets and cheap IQD gap credit remain uncommitted. An assumed higher fare is not a sustainable tariff until OD, distributional affordability and actual service/credit conditions are accepted. The 44-trip share uses the historical income proxy and base fare before variable-price weighting, not measured disposable income.

Task-derived maintenance and reserve cash

Source: [cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-closure/MAINTENANCE-RENEWALS.md](#)

[Task workload](#) covers daily/weekly/monthly inspections, every-roundtrip safety/diagnostic checks, wheel reprofile at 150,000km, bogie overhaul at 600,000km and body overhaul at ten years. Six-car quantities are 24 wheelsets and 12 bogies/train. Reference workload is 347,138 mechanical and 185,446 electrical person-hours/year, compared with existing workload allowances 365,760 / 243,840. Durations, defects, access queues, equipment, parts and non-fleet tasks remain unmeasured; lower reference hours do not authorise staff reductions.

Battery replacement stays on the existing 12-year cycle. Reference annual reserve is USD 17.145m within the existing USD 51.206m rolling maintenance envelope. [Monthly reserve ledger](#) separates indexed contributions, replacement withdrawals, required top-ups and closing restricted cash. At 5% inflation/zero reserve interest, reference top-ups total USD 305.318m nominal; terminal restricted cash is USD 603.332m. It cannot repay loans/bonds or become terminal sale income. The replacement bill is not added to annual reserve spending a second time.

Initial 2% battery-spare stock is USD 4.115m reference; existing allowance inclusion is unknown. Serial-specific service/mileage/cell-health dates must replace line-opening proxies. Native Asset Maintenance/Asset Repair, calibration/parts and independent handback records remain required. No actual asset, spare, Work Order or accepted Job Card is invented.

[All 26 controlled interval records](#) also retain station, civil/track/structures, energy, wayside, tooling, finish/joint/wash and soiling work. Condition-based tasks have no invented frequency or labour cost. [Opening-fleet reserve cash](#) uses 414 trainsets and adds its own indexed shortfalls to the reduced-supply financing case.

Baghdad remaining-work delivery packages

Source: [cities/catalogue/west-asia/iraq/Baghdad/engineering/delivery-closure/README.md](#)

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

This continuation completes repository calculations, concept layouts, RFQ/field forms, financial sensitivities and competence/recovery checks. It does not complete surveys, obtain quotes, appoint people, sign leases/loans or release a railway. The original financing and engineering examples remain their controlled baseline. All alternatives are unquoted/uncommitted and retain unknown costs.

- [Depot track/slot layout and yard slab production](#)
- [Six-car child parts, interfaces and supplier request forms](#)
- [Per-site hourly energy and upgrade requirements](#)
- [Maintenance tasks, renewal dates and restricted reserve cash](#)
- [Comparable standalone corridor break-even and field investigations](#)
- [Reconciled monthly funding, six-month bonds/loans and repayment](#)
- [Practical training, department/unit allocation and rest-limited roster](#)
- [Remaining evidence and six native ERP work packages](#)

Run `.venv/bin/python tools/automation/baghdad_delivery_closure.py`, then rebuild the proposal. - - check rejects source/output drift. Existing `bootstrap_baghdad_tests.py` restores the exact test input. Native personal records and recovery receipts remain private in `var/erpnext/`.

Chronological site-limited energy and installed upgrades

Source: [cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-closure/SITE-ENERGY.md](#)

Each station retains its own storage capacity/power and grid limit. Timetable train-km allocate duty between lines; installed charger kW allocate duty within a line. This is a synthetic allocation, not measured charger events or a queue/feeder acceptance test. The utility plant is allocated by duty, on-site PV has no wheeling loss, and utility PV has the explicit loss/charge. Each node conserves hourly energy and preserves losses, curtailment, shortages and SoC.

Weather	Imports GWh	Unserved GWh	Firm energy services USD m/year	Required grid upgrade MW	Charger overload MW
reference	860.5	9.2	128.510	123.406	169.138
poor	968.9	18.7	136.313	126.921	169.138
aged10	875.7	9.5	130.067	123.406	169.138

The firm-service cash sensitivity buys unmet energy and pays the increased connection charges. It requires physical connection and charger upgrades whose capital is unpriced. It does not claim a trip can be served by paying a bill. [Site totals](#) and reference line-hourly ledgers expose every node requirement. Whole-grid pooling is removed; within-line duty allocation, site transformer/feeder limits, rights/outages, charging times, installed storage ageing and weather still need measurements. Original annual-netting finance remains unchanged, with no export income or energy ownership proceeds invented.

[All 28 aggregate shortage hours](#) remain an explicit pooled comparator. [Site-specific shortage hours](#) expose grid/charger limits, opening/closing stored energy, local PV and remote generation before wheeling. Local PV never incurs remote wheeling losses/charges. The installed-throughput case reduces fare, station and additional commercial receipts; it is an energy upper bound, not a validated achieved timetable.

Six-car child parts and procurement/qualification work

Source: [cities/catalogue/west-asia/iraq/baghdad/engineering/delivery-closure/SIX-CAR-PROCUREMENT.md](#)

Child parts expand the eight parent allocations without duplicating their USD 1,680,000/train budget. Body modules, 12 bogies, 24 wheelsets/48 wheels, battery interfaces, traction controllers, doors/windows, mounting rails, lighting and thermal/trainline interfaces derive from the actual six-car system counts. Harnesses, protection, braking, redundant control and installed sensing quantities remain null where the supplier/design schedule is absent. Price, mass, drawing and applicability are not inferred from the LM3 reference.

Supplier RFQ forms require drawing/revision, interface, price/currency/date, country/invoice origin, delivery, duties, warranty, payment terms, local labour and actual Chinese-credit eligibility. None has been sent or answered. **Qualification work packages** retain the existing USD 12m unquoted reference and unresolved overlap with the factory's USD 20m design/training allowance. Routine assembly/QA wages already in train procurement are not added to OPEX. Software/runtime/bench evidence remains observation/reference evidence until the target family and installed interfaces are qualified.

Workforce, practical training and a rest-limited pilot

Source: [cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-closure/WORKFORCE-PILOT.md](#)

The [seven lesson cards](#) provide practical scenarios, prerequisites/apparatus, critical observations, assessor authority, retraining and Arabic draft instructions. Attendance, practical assessment and task/asset/location authorisation stay separate. All actual candidate/assessor outcomes and native Arabic review remain null. The draft must not become an operational rulebook through generation.

[Pilot schedule](#) covers 143.5 OCC hours over seven days with 5 unnamed planning positions, maximum 8-hour shifts, minimum 11-hour rest and maximum 40 hours per rolling seven days. These are editable scheduling assumptions, not accepted Iraqi employment terms. No worker identity is invented; every slot remains ineligible until real Employee/assessment/authorisation/resources and a fresh start check exist. Leave/sickness/annual relief, supervised staffing, tools/permits and independent checks remain necessary.

Department/unit/role budgets, recruitment cohorts, task workload and native HR/Work Order/Job Card/Asset Maintenance/Asset Repair records remain linked to the existing workload package. Read-only administrative previews require native role/document permissions and a baseline-bound private employee packet; human work-release authority remains separate. [Frappe staffing documentation](#) describes the native administration; it does not appoint Baghdad staff.

Baghdad frozen-resource delivery and funding study

Source: cities/catalogue/west-asia/Iraq/Baghdad/engineering/delivery-risk/README.md

These are deterministic disturbances, not P80/P90 dates or measured failure rates. All planned six-car trains must pass acceptance before their line opens. Selected stage cells, civil crew lanes and dispatch order remain fixed in every stress. No stress calls the capacity-sizing search.

The explicit segregated-path calendar books 16 exclusive running hours per train at the case availability, inside acceptance-bay occupation, with setup and clearance. This adds a conservative calendar audit to the published average-throughput check. Baseline lane order is preserved; a replanned optimal dispatch might recover some delay. Financial-close months include 30 pre-NTP working days and three commissioning months.

Case	First/full month	Peak IQD gap debt, tn	Interest/fees USD eq, bn	Debt cleared month
calendar_baseline	40/76	4.371	4.906	303
factory_delay_6months	46/82	4.575	4.956	306
supplier_shortage_6months	46/82	4.575	4.957	306
half_staff_late_12months	44/80	4.527	4.945	306
rework_10pct	41/80	4.528	4.954	305
one_test_path_outage_6months	40/76	4.371	4.906	303
civil_access_6months	42/82	4.327	4.885	303
availability_75pct	42/83	4.566	4.964	306
availability_65pct	44/91	4.787	5.017	309
combined	53/97	4.968	5.051	313
combined_second_test_shift	53/97	4.983	5.058	313
availability_75pct_second_test_shift	42/83	4.579	4.970	306
civil_cycles_20pct_faster	40/76	4.375	4.907	303
civil_earliest_unchanged_cycles	40/76	4.741	5.040	305
civil_earliest_20pct_faster	40/76	5.025	5.147	307
availability_75pct_costed	42/83	4.587	4.971	306
availability_75pct_test_shift_costed	42/83	4.600	4.977	307
hiring_ramp_costed	44/80	4.539	4.949	306
supplier_shortage_costed	46/82	4.593	4.963	307
availability_75pct_structural_shift	41/82	4.607	4.978	307
availability_75pct_electrical_shift	41/82	4.575	4.966	306
availability_75pct_composite_shift	41/82	4.573	4.964	306
availability_75pct_all_stage_shifts	40/76	4.495	4.958	305
recruitment_training_recovery	40/76	4.381	4.912	303
supplier_expedite_recovery	43/79	4.490	4.912	305
temporary_first_article	36/76	4.323	4.926	302
combined_delay_costs	53/97	5.057	5.080	314
combined_lower_demand	53/97	9.412	7.360	Unpaid
combined_escalation	53/97	7.348	6.661	351
combined_finance_downside	53/97	4.000	10.248	Unfunded
joint_downside	53/97	4.000	14.810	Unfunded
domestic_placement_interrupted_recovered	46/82	4.417	4.899	306
export_credit_delayed_recovered	46/82	4.250	4.845	305

Separate productivity from investment timing

The corrected civil_cycles_20pct_faster case retains every rephased start floor and changes only civil occupation durations. A 1.0 multiplier is tested as an exact schedule identity, including running-path reservations and line openings. Civil_earliest_unchanged_cycles removes the spending delays at original durations; civil_earliest_20pct_faster changes both. Their costs must not be attributed to productivity alone. Earlier completion may still advance completion/retention invoices even when mobilisation timing is retained. These are diagnostic cycle assumptions with no added crews or accepted acceleration price.

Recovery comparisons and priced assumptions

Factory cells and dispatch lane order remain fixed. Fixed curing, bonding, inspection and test holds are listed in `baghdad-delivery-risk.toml` as unqualified working-calendar equivalents. Shift compression applies only to the remaining staffed occupation; the additional 60-day first-article qualification is unchanged. At one shift the original schedule is preserved exactly. Cure elapsed hours and batch/test evidence must replace these assumed splits before adoption. The test-only option uses the same selected segregated paths with a second eight-hour test shift: 26 incremental staff and USD 0.75m direct lighting/training per selected path plus 7% EPC, and indexed payroll before and after fares. It does not repair upstream stage throughput. The single structural, electrical and composite options add four staffed hours/day to the named stage at unchanged bay count; the coordinated option applies this to all seven stages and funds the second test shift. Incremental production FTE is half each selected stage crew, paid at a 25% premium, with nonlabour shift costs equal to 25% of added payroll. Each stage adds a USD 1m installation/training allowance and USD 10,000 per added FTE plus EPC. These assumed shift efficiencies, relief and wage premiums need qualification.

Use `availability_75pct_costed`, `hiring_ramp_costed` and `supplier_shortage_costed` as matching delay-cost baselines for their respective recovery options. Recruitment recovery funds USD 10,000 per delayed half of the 1044 production positions plus EPC and tests a six-month rather than twelve-month staffing ramp. Supplier recovery charges an assumed IQD local logistics fee of 2% of city imported invoice value, indexed to payment, and tests a shortage cut from 130 to 65 working days; this is a causal scenario assumption, not a guaranteed delivery improvement. Foreign-currency freight reimbursement and invoice eligibility need quotations. Neither purchases another train nor credits an unspecified subsidy.

The temporary first-article option adds USD 35m direct facility/tooling and 7% EPC, ready at day 260 (12 planning months from NTP), plus 60 incremental support FTE until the permanent plant is ready. Only the already-planned prototype assembles there. Acceptance still waits for permanent bays and running paths at day 390, and series still waits for first-article qualification. All line fleets remain complete at opening. The temporary site and staff must have their own RFQs and acceptance; no shorter passenger section is folded into this option.

Delay costs and combined financial downside

Original delivery-only cases remain lower-bound comparisons. `Combined_delay_costs` additionally prices extended direct production staffing plus 100 support FTE at the existing Iraqi labour proxy; it compares staffed span lengths so a pure start delay does not buy the same crew-months twice. Plant storage/insurance/utilities carrying uses 1% of direct plant capital per extra/idle year excluding wages. Civil prolongation adds 150 supervision FTE and nonlabour site overhead at 0.5% of city capital per year beyond baseline civil completion. All these incremental operating costs are charged monthly at 5% annual indexing; baseline train labour/materials already inside procurement are not repeated. Rework prices 83 affected trains at USD 25,000 each. Monthly incremental-cost files reconcile each allowance to the case OPEX ledger. Contingency, tax and contractor claims remain unquoted; these are not a funded risk reserve.

The downside ladder isolates 30% fewer paid trips plus 25% lower existing retail/advertising receipts, 5% annual capital escalation applied to each invoice at actual payment month from financial close, and weaker financing. Weaker financing removes assumed green enhancement, climate grants, development rights and additional net income, increases core coupons two percentage points, and replaces the 2%/IQD 13tn gap sensitivity with 8% credit at a 1% draw fee and IQD 4tn maximum outstanding. Chinese credit and government import cash remain USD, all domestic credit/bonds/cash IQD; government remains 25% of escalated capital. Separately, `domestic_placement_interrupted_recovered` and `export_credit_delayed_recovered` stop procurement/construction/production for 130 working days and price local remobilisation plus prolongation; repayment is conditional on subsequently placing the refused debt. Permanent refusal has no opening or repayment date: see the [funding gates and evidence execution package](#), including denied amounts, escrow requirements and six-month placement shortfalls. No gap facility is used to conceal a refused core source.

Lower demand with combined delays leaves IQD 2.350tn terminal gap debt. `Joint_downside` applies all of those assumptions together and 7% rail OPEX inflation: IQD 27.732tn cumulative uncovered cash and IQD 4.000tn terminal gap debt. Uncovered support is a balancing requirement, not an extra government appropriation, loan or cash source. Its presence blocks any unconditional repayment claim even if the simulated debt eventually amortizes. Interest totals in such cases also assume the missing cash is supplied; they do not establish an executable financed programme.

Base fare and OPEX sensitivities remain 5% from financial close, with existing kiosks/advertising, separate receipts and each line revenue ramp included. No tickets are sold before opening. Capital escalation is absent from reference cases and explicit in the named escalation cases. Green/grant/rights and all financing availability remain uncommitted. No future national city cashflow supports Baghdad debt.

Evidence needed before adopting a recovery plan

The [qualification register](#) assigns owners, required measurements/RFQs and acceptance rules for production, suppliers, recruitment, civil quantities, depot/site fit, demand, funding and operation. Every row remains not demonstrated. No measurements or quotations were obtained by running this model. The baseline fleet and test-path margins follow the current [factory sizing](#); they require measured cycles and acceptance trials. Shorter passenger sections require a separate route, turnback, charging, depot, fleet duty and safety/operating acceptance study; the present comparisons retain full fleets and existing operating scope.

Regenerate after the city controls, factory plan and Baghdad funding programme are current with `.venv/bin/python tools/automation/baghdad_delivery_stress.py`, then regenerate the proposal. Verify source/output bindings with `--check`.

[Scenario comparison](#) · [Machine-readable assumptions/results](#) · [Baseline half-year funding](#) · [Combined stress half-year funding](#) · [Joint downside half-year funding](#)

Baghdad deployment gaps

Source: [cities/catalogue/west-asia/Iraq/Baghdad/engineering/deployment/README.md](#)

3 closed checks; 14 open gates. Status follows the linked evidence; generating a receipt template does not count as receiving field data.

Soil inputs include a route/station investigation plan.

Gate	Status	Responsible function	Closure work
soil-desktop-inputs	closed	civil/geotechnical designer	Sample current station and civil geometry from the pinned soilDB source and retain means, uncertainty and nodata.
soil-coverage	open	geotechnical investigator	Fill mapped coverage gaps through local records and targeted sampling; keep estimated and measured records distinct.
control-processing	open	survey team	Receive survey control observations; process and check the project CRS, datum and residuals.
ground-model	open	survey team	Receive and inspect the terrain, point cloud and ground-model deliveries against independent control.
surveyed-alignment	open	alignment designer	Replace or confirm generated geometry with checked survey alignment and platform reconciliation.
route-station-fit	open	civil/station designer	Resolve utilities, land/access, flood levels, station access and construction staging against the current route.
drainage-ground	open	civil/geotechnical designer	Use the soil investigation plan to collect local geotechnics and groundwater, size foundations/treatment, and check drainage with local rainfall and surveyed levels.
structural-release	open	structural designer and checker	Complete route-specific support/span, foundation, movement and erection calculations and close checking comments.
model-timing-comparison	closed	simulation engineer	Reconcile current native reference journey times with SUMO using the same scenario dwells and route.
full-service-validation	closed	simulation engineer	Run current nominal and degraded full-service cases against the current scenario and simulator; retain failures and exact provenance.
operating-release	open	operator	Complete conflict-aware capacity and degraded-operation review and sign the bound operating evidence.
morning-fleet-allocation	open	service planner	Reconcile revenue fleet with required morning departures on each line; retain two station berths and same-line overflow storage.
continuous-stabling-replay (evidence missing)	open	simulation engineer	Run the selected line-local station/depot candidate across consecutive evenings and synchronised morning starts.
stabling-physical-fit	open	track/station designer	Locate usable station and line-local depot tracks, shared charging, isolation, inspection access and protected morning release slots.
solar-storage-endurance	open	energy designer	Bind declared station/ROW/dedicated PV to site storage and actual charging duty, reconcile conversion losses and prove replenishment across adverse weather; specify residual backup duty explicitly.
depot-placement-and-budget	open	depot and cost designer	Place the declared PV/storage inventory within the controlled site layout and reconcile itemised installed costs and renewal scope with existing allowances.
workforce-duty-and-workload	open	city operating lead	Reconcile the funded role plan with named shift/leave cover, measured inspection and cleaning workloads, simultaneous service-depot arrivals and actual local employment inputs.

city civil and operating deployment evidence; manufacturing and system certification remain in their own release registers.

baghdad depot scope reconciliation

Source: cities/catalogue/west-asia/Iraq/Baghdad/engineering/depot-scope/README.md

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

Depot energy quantities reconciled: yes. Physical/cost/stabling closure: open.

The policy assigns two revenue trains per selected powered station for coordinated morning starts and the remaining fleet to storage on its own line. Depot storage tracks are sized separately from maintenance bays; see the [station/depot allocation](#). The dispatch table below diagnoses the current simulator initialization; it is not a proposed overnight parking allocation or a requirement for more depots.

Depot station	PV kWp	Storage modules / kWh	Required / reference PV area m²	Additional equipment reference USD
line-2-0595-0296-s052851	5,000	80 / 40,000	33,333.3 / 4,000	5,930,000

The equipment reference is an unapproved sensitivity using existing repository rates. It is not added to CAPEX; allowance inclusion and installed scope remain unverified.

Initial dispatch station	Line	Trainsets	Train-body length m	Slot length with clearance m	Physical slots
line-1-2500-0775-s000000	line-1	43	4,773.0	5,203.0	unverified
line-1-0166-0866-s049067	line-1	43	4,773.0	5,203.0	unverified
line-2-1987-2192-s000000	line-2	51	5,661.0	6,171.0	unverified
line-2-0595-0296-s052851	line-2	50	5,550.0	6,050.0	unverified
line-3-2271-1120-s000000	line-3	49	5,439.0	5,929.0	unverified
line-3-0151-1637-s049496	line-3	48	5,328.0	5,808.0	unverified
line-4-0146-0199-s000000	line-4	40	4,440.0	4,840.0	unverified
line-4-1246-1628-s042068	line-4	40	4,440.0	4,840.0	unverified
line-5-1199-0260-s000000	line-5	43	4,773.0	5,203.0	unverified
line-5-0677-2304-s047321	line-5	43	4,773.0	5,203.0	unverified
line-6-2322-0251-s000000	line-6	50	5,550.0	6,050.0	unverified
line-6-0495-1669-s052503	line-6	50	5,550.0	6,050.0	unverified
line-7-1069-2206-s000000	line-7	40	4,440.0	4,840.0	unverified
line-7-1531-0418-s039957	line-7	39	4,329.0	4,719.0	unverified
line-8-2231-1783-s000000	line-8	45	4,995.0	5,445.0	unverified
line-8-0785-0290-s047849	line-8	45	4,995.0	5,445.0	unverified
line-9-0678-0582-s000000	line-9	22	2,442.0	2,662.0	unverified
line-9-0819-0573-s090161	line-9	21	2,331.0	2,541.0	unverified

- Operating PV/storage capacities are retained assumptions, not validated depot sizing. Reassess depot and station energy duties after distributed overnight placement and charging are represented.
- PV area is module area at the catalogue 0.15 kWp/m2, not gross land area; setbacks, access and packing require layout.
- Battery footprint and separation require supplier/fire-engineering data; no area or approval is invented.
- Dispatch queues are initial simulator placements, not an overnight operating plan. Slot lengths use one train plus 5 m at each end from RFC 0014.
- Workshop bays and passenger platforms are not credited as verified overnight stabling slots.

Required closure records: a supplier equipment/footprint schedule; located PV and battery layout; itemised budget with explicit baseline inclusions; a station-by-station healthy-fleet allocation with track IDs, usable lengths, assigned trainsets, charger sharing, security/isolation and access; and coordinated morning departures with conflict-aware evening/morning repositioning evidence.

Baghdad detailed component register

Source: <cities/catalogue/west-asia/Iraq/Baghdad/engineering/detail/README.md>

Generated from the current city design, six-car profile, engineering parts and software/ERP contracts. Engineering release remains false. Cost and finance rates remain unchanged; unknown unit costs are open rather than zero.

Reference allocation: 762 trainsets, 4,572 cars, 9,144 bogies, 164 stations, 140 energy sites and one shared plant.

See [complete parts CSV](#), [source-bound register](#), [dimensioned ST6 reference](#) and [design and Iraqi manufacturing plan](#). The two-bogie-per-car allocation and repeated mechanical kit quantities are reference architecture, subject to Metro-6car family release. Nested wheelsets, clips and batteries are not extra charges on top of complete bought assemblies.

Track and parts quantities

The rail reference covers net mainline running length only. Actual procurement additionally needs alignment method zones, switches, stabling, depot track and cutting/weld/spares schedules. Slab panel totals remain unassigned until constrained zones are measured; rail-seat child quantities require a seat installation schedule.

ID	Part / assembly	Basis	Per basis	Network reference	Route
TR-01	60E1 reference running rail	route-km (m)	4000	1,896,718.8	import-or-qualified-local-source
TR-02	Resilient direct-fixation complete seat kit	rail-seat (each)	1	Open	import-first-local-assembly-later
TR-03	Elastic clips	rail-seat (each)	2	Open	import-qualified
TR-04	Rail pad / bonded resilient layer	rail-seat (each)	1	Open	import-qualified
TR-05	Lateral rail insulators	rail-seat (each)	2	Open	import-qualified
TR-06	Anchor assembly including insert, bolt and washer	rail-seat (set)	2	Open	local-inserts-after-qualification
TR-07	Vertical/lateral adjustment and levelling kit	rail-seat (set)	1	Open	local-machining-after-qualification
TR-08	OSR-ST6 precast slab panel	slab-panel (each)	1	Open	Iraqi-precast
TR-09	ST6 concrete, base and plinths only	slab-panel (m3)	5.0796	Open	Iraqi-batching
TR-10	ST6 reinforcement planning allowance	slab-panel (kg)	761.94	Open	Iraqi-cage-fabrication
TR-11	ST6 bedding / levelling grout	slab-panel (m3)	0.522	Open	local-qualified-material
TR-12	ST6 lifting sockets / engineered anchors	slab-panel (each)	4	Open	import-qualified-local-install
TR-13	Drainage channel and removable cover	route-km (m)	2000	948,359.4	Iraqi-precast
TR-14	Rail electrical continuity bond / monitored stray-current provision	project (set)	Open	Open	local-harness-import-terminals
TR-15	Turnout slab bearer, point drive, detection and locking kit	project (set)	Open	Open	mixed
TR-16	Rail/deck expansion interface and transition section	project (set)	Open	Open	mixed
TR-17	Utility ducts, draw pits, barriers and fencing	project (set)	Open	Open	Iraqi-manufacture
ME-01	Underframe and load-bearing car structure	car (each)	1	4,572	Iraqi-fabrication
ME-02	Modular FRP cladding, end frames and service rails	car (each)	1	4,572	Iraqi-composite-and-metalwork
ME-03	Powered bogie complete including frame, suspension and brakes	car (each)	1	4,572	import-first
ME-04	Trailer bogie complete including frame, suspension and brakes	car (each)	1	4,572	import-first
ME-05	Wheelset including wheels, axle, bearings and axleboxes	bogie (each)	2	18,288	included-in-bogie-import
ME-06	Motor and traction inverter/controller set	car (each)	2	9,144	import-qualified
ME-07	225 kWh nameplate traction battery allocation	car (each)	1	4,572	import-cells-local-pack-after-qualification
ME-08	Battery support, HV junction box, fuse, contactors and precharge	car (each)	1	4,572	mixed
ME-09	Battery/inverter liquid cooling loop	car (each)	1	4,572	local-assembly-import-pump-and-chiller

ID	Part / assembly	Basis	Per basis	Network reference	Route
ME-10	HV-to-LV DC/DC and battery-backed auxiliary distribution	car (each)	1	4,572	import-qualified-local-harness
ME-11	HVAC unit, ducts, filters, condensate and mounts	car (each)	1	4,572	mixed
ME-12	Passenger door package including leaves, drive, locks and detection	car (each)	4	18,288	import-qualified-local-fitting
ME-13	Side glazing, window frames, seals and adhesives	car (each)	Open	Open	import-glass-local-frame
ME-14	Intercar coupler, gangway, jumper and air/electrical interfaces	trainset (each)	5	3,810	mixed
ME-15	Train-end recovery coupler and sensor cowl	trainset (each)	2	1,524	mixed
ME-16	Brake supply/control and parking brake package	car (each)	1	4,572	mixed
ME-17	Roof PV, MPPT, mounts and protected DC wiring	car (each)	1	4,572	import-panels-local-mounts
ME-18	Interior, seats, grab rails, lighting and accessibility kit	car (each)	1	4,572	Iraqi-assembly
ME-19	Fire detection, alarm, segregation and suppression provisions	car (each)	1	4,572	mixed
ME-20	HV/LV/data harness, connector and clamp schedule	car (each)	1	4,572	Iraqi-harness-production
ME-21	Service consumables, fasteners, fluids and replacement spares	project (each)	Open	Open	mixed
EL-01	T-ECU/S end host assembly	trainset (each)	2	1,524	import-electronics-Iraqi-integration
EL-02	T-ECU/A application end host assembly	trainset (each)	2	1,524	import-electronics-Iraqi-integration
EL-03	T-OBS end host and external sensor assembly	trainset (each)	2	1,524	import-electronics-Iraqi-integration
EL-04	Safety evaluator MCU channel	t-obs (each)	2	3,048	import-electronics-Iraqi-integration
EL-05	Independent hardware heartbeat watchdog	t-obs (each)	2	3,048	import-electronics-Iraqi-integration
EL-06	Channel power conversion and voltage monitoring branch	t-obs (each)	2	3,048	import-electronics-Iraqi-integration
EL-07	Application compute module and carrier	t-obs (each)	1	1,524	import-electronics-Iraqi-integration
EL-08	Radar evaluation assembly and CAN interface adapter	t-obs (each)	1	1,524	import-electronics-Iraqi-integration
EL-09	Lidar HAP TX candidate and data/power harness	t-obs (each)	1	1,524	import-electronics-Iraqi-integration
EL-10	Stereo camera, carrier-compatible flex and rigid calibration bar	t-obs (each)	2	3,048	import-electronics-Iraqi-integration
EL-11	Ultrasonic sensing position	t-obs (each)	4	6,096	import-electronics-Iraqi-integration
EL-12	Isolated peer cross-check SPI link	t-obs (each)	1	1,524	import-electronics-Iraqi-integration
EL-13	Hardware series permission contacts and independent coil drivers	t-obs (each)	1	1,524	import-electronics-Iraqi-integration
EL-14	HV/LV input surge protection and branch fuse assemblies	t-obs (each)	1	1,524	import-electronics-Iraqi-integration
EL-15	Enclosure, heat spreader, glands, vents and grounding hardware	t-obs (each)	1	1,524	import-electronics-Iraqi-integration
EL-16	Train network switch, isolated CAN and external Ethernet controller set	trainset (each)	Open	Open	import-electronics-Iraqi-integration
EL-17	Train-to-ground radios, modem carrier, antennas and surge arresters	trainset (each)	Open	Open	import-electronics-Iraqi-integration
EL-18	W-SBC field cabinet and point/crossing I/O	project (each)	Open	Open	import-electronics-Iraqi-integration
EL-19	S-SBC station host and protected UPS/network enclosure	station (each)	1	164	import-electronics-Iraqi-integration
EL-20	Operator/server cluster, backup and disaster recovery	project (each)	Open	Open	import-electronics-Iraqi-integration

ID	Part / assembly	Basis	Per basis	Network reference	Route
CI-01	Pi20/Pi25 beam, pier cap, column and foundation package	project (each)	Open	Open	Iraqi-precast-and-site
CI-02	Walkway, barrier, cable tray and access cassette	project (each)	Open	Open	Iraqi-fabrication
CI-03	Station accessible platform, ramp/lift/stair and canopy package	station (each)	1	164	Iraqi-civil-and-metalwork
CI-04	Station fire, water, drainage, power and earthing services	station (each)	1	164	mixed
CI-05	Ticket validators, vending, gates and settlement terminals	station (each)	Open	Open	mixed
CI-06	Station PA/PIS, CCTV, help points and telecom cabinet	station (each)	1	164	mixed
CI-07	Charging contact, interlock, protection, DC/DC and site battery	site (each)	1	140	import-core-local-assembly
CI-08	Depot lifts, pits, wheel service, wash and recovery equipment	project (each)	Open	Open	mixed
CI-09	Precast plant moulds, cage jigs, batch/curing and survey tools	plant (each)	1	1	Iraqi-fabrication-import-special-tooling
CI-10	Rail weld/clip/anchor tools and track survey trolley	plant (each)	1	1	mixed
CI-11	Electrical bench, harness formboards and EMC/environmental test access	plant (each)	1	1	mixed

Corrected onboard power envelope

T-OBS simultaneous output allocation is 71.50 W; at 90% efficiency, input is 79.44 W. A 25% sizing margin requires 99.31 W, selecting a 100 W reference capacity. At the assumed 18 V minimum input, envelope current is 4.41 A, or 5.52 A including capacity margin. These are capacity assumptions, not energy-consumption measurements or qualified fuse/converter ratings.

Software host allocation

All 60 workspace packages have exactly one disposition record. This verifies inventory, not physical HAL, sensor driver, firmware timing or operational safety.

Component	Disposition	Hosts
osr-afc	composed-service	s-sbc
osr-afc-backoffice	deployable-endpoint	o-srv
osr-alignment	shared-library	design-tooling
osr-analytics	deployable-endpoint	o-srv
osr-ato	composed-service	t-ecu-a
osr-atp	composed-service	t-ecu-s
osr-aux-power	composed-service	t-ecu-a
osr-balise	composed-service	w-sbc
osr-bms	composed-service	t-ecu-s
osr-brake	composed-service	t-ecu-s
osr-cbm-backend	deployable-endpoint	o-srv
osr-cbm-onboard	composed-service	t-ecu-a
osr-city-studio	tooling	design-tooling
osr-consensus	composed-service	w-sbc, o-srv
osr-core	shared-library	all
osr-crypto	shared-library	all
osr-derailment	composed-service	t-ecu-s
osr-design	tooling	design-tooling
osr-door-control	composed-service	t-ecu-s
osr-energy-site	composed-service	w-sbc
osr-event-recorder	composed-service	t-ecu-a
osr-fire-safety	composed-service	t-ecu-s
osr-gui-shared	shared-library	o-srv, simulation
osr-historian	deployable-endpoint	o-srv
osr-hot-axle	composed-service	t-ecu-a

Component	Disposition	Hosts
osr-hot-axle-wayside	composed-service	w-sbc
osr-hvac	composed-service	t-ecu-a
osr-interlocking	composed-service	w-sbc
osr-intrusion-detect	composed-service	w-sbc
osr-level-crossing	composed-service	w-sbc
osr-lifecycle-identity	shared-library	o-srv, design-tooling
osr-lighting	composed-service	t-ecu-a
osr-obstacle-detect	composed-service	t-obs
osr-onboard-routing	composed-service	t-ecu-s
osr-passenger-assist	composed-service	t-ecu-a
osr-occ	deployable-endpoint	o-srv
osr-occ-gui	deployable-endpoint	o-srv
osr-odometry	composed-service	t-ecu-s
osr-pis-onboard	composed-service	t-ecu-a
osr-pis-station	composed-service	s-sbc
osr-proto	shared-library	all
osr-psd	composed-service	s-sbc
osr-ptp	shared-library	t-ecu-s, t-ecu-a, t-obs, w-sbc, s-sbc
osr-regen	composed-service	t-ecu-a
osr-routing	shared-library	o-srv, design-tooling
osr-safety-case	tooling	assurance-tooling
osr-secbus	shared-library	all
osr-selftest	deployable-endpoint	t-ecu-s, t-ecu-a, t-obs, w-sbc, s-sbc
osr-sim	simulation	simulation
osr-sim-gui	simulation	simulation
osr-station-scada	composed-service	s-sbc
osr-supervision-contract	shared-library	o-srv, simulation
osr-t2g	composed-service	t-ecu-a
osr-tcms	composed-service	t-ecu-a
osr-runtime	shared-library	design-tooling
osr-tcn	shared-library	t-ecu-s, t-ecu-a, t-obs
osr-traction	composed-service	t-ecu-s
osr-trainset-image	deployable-endpoint	t-ecu-s, t-ecu-a, t-obs
osr-tvm	composed-service	s-sbc
osr-wayside-points	composed-service	w-sbc

ERP coverage

Validated workflow contracts: assignment, budget, maintenance, manufacturing, quality, replenishment, service, training.

Enabled profile instances: training/city-induction. Other workflows exist in the app but require real deployment inputs before enablement. A valid reusable profile does not mean that production orders, maintenance assignments or capital budgets have been activated.

Profiles/templates only; legal company, physical bindings, approved schedules, suppliers, stock and production BOMs remain deployment-owned. Reference parts are not auto-created as live ERP Items.

Source hashes bind this report to its exact inputs. Rebuild with `.venv/bin/python engineering/baghdad_detail.py`; verify with `--check`.

Baghdad mixed joint-stock holding and ordinary-equity study

Source: cities/catalogue/west-asia/Iraq/Baghdad/engineering/equity/README.md

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

As of 2026-10-04. This is a proposed Iraqi holding company with 100%-owned rail, station-development, energy and manufacturing subsidiaries, not an incorporated company, offering, approved listing or committed funding. Baghdad alone supplies the order book. Future national projects remain uncontracted and supply zero revenue, collateral and terminal sale proceeds.

Ownership, new money and currencies

Government still provides USD 1.878769790bn equivalent: 25% of the original USD 7.515079159bn rail/energy/factory capital, rather than 25% of shares or of the enlarged property programme. Reclassifying that existing contribution as ordinary equity generates zero additional cash. At the same subscription price, ownership is government cash divided by government plus private subscribed cash. Borrowing earns no ordinary shares.

Transaction	Gross primary USD m eq	Company net primary USD m eq	Final government shares	Final Iraqi ownership	Government secondary sale USD m eq
primary_500m	500.0	490.0	78.98%	93.69%	0.0
primary_1000m	1000.0	980.0	65.26%	89.58%	0.0
primary_2000m	2000.0	1960.0	48.44%	84.53%	0.0
primary_1000m_premium	1000.0	980.0	66.22%	89.87%	0.0
secondary_500m	0.0	0.0	73.39%	92.02%	500.0

The share unit is an illustrative IQD 1 par and IQD 1 subscription price, not an accepted company valuation or legal share denomination. The premium sensitivity prices the later 25% issue at IQD 1.2, recording the difference in share premium and reducing dilution. Private subscriptions are 70% Iraqi and 30% foreign as an explicit scenario. Every paid-capital month observes the model's 25% state floor and 51% Iraqi floor; actual eligibility and beneficial ownership require counsel. Pending private subscriptions wait for sufficient paid government shares instead of treating promised government capital as paid. No shares or cash are credited for undelivered subscriptions. Land/concession/open designs are not priced into paid-up equity.

The government_grant_reference and government_equity_reference have identical debt, cash and physical costs before distributions. Government grants are a separately identified capital reserve without shares; cash-equity contribution is paid-in ordinary equity. Guarantees and public-service appropriations are uncommitted and never booked as subscription cash. A secondary sale transfers existing government shares: the seller receives the price, the company receives zero, and borrowing requirements remain unchanged. The secondary case omits sale fees as an explicit sensitivity; no government sale is authorised.

Original-scope imported parts are USD 1.684340853bn: government USD cash USD 842.170427m and Chinese USD credit USD 842.170427m. Only Chinese credit is USD debt. Remaining government cash, share subscriptions, bonds, bank/gap credit, fares, property proceeds and dividends are IQD. USD figures for those items are reference conversions at 1,300 IQD/USD, without a dollar-indexed obligation or promised conversion. Original-scope USD capital intensity is 22.41%; local procurement prices still require actual imported-content and FX quotes. The additional USD 2.4bn-equivalent property construction is assumed IQD and makes physical group capital USD 9.915079159bn. It does not add government cash beyond the original 25% rule.

Conditional results and investor returns

Case	Actual gross primary USD m eq	Conditional first/full month	Peak IQD gap tn	Missing IQD cash tn	First dividend month	Private annual equity IRR
government_grant_reference	0.0	40/76	5.404	0.000	None	undefined
government_equity_reference	0.0	40/76	5.404	0.000	371	undefined
primary_500m	500.0	40/76	3.786	0.000	347	2.68%
primary_1000m	1000.0	40/76	2.525	0.000	323	2.75%
primary_2000m	2000.0	40/76	1.313	0.000	251	2.92%
primary_1000m_premium	1000.0	40/76	2.525	0.000	323	2.65%
secondary_500m	0.0	40/76	5.404	0.000	371	2.88%
undersubscribed_1000m	58.1	Blocked	0.000	0.000	None	undefined
failed_later_primary	750.0	Blocked	1.425	0.000	None	undefined
delayed_1000m	1000.0	46/82	2.454	0.000	323	3.06%
joint_downside_1000m	1000.0	53/97	4.000	38.763	None	undefined
joint_downside_undersubscribed	58.3	Blocked	0.000	0.000	None	undefined
aggregate_tax_proxy_1000m	1000.0	40/76	1.664	0.000	299	3.32%
coverage_dividends_1000m	1000.0	40/76	2.565	0.000	323	2.74%
rental_small_1000m	1000.0	40/76	2.545	0.000	323	2.77%
rental_medium_1000m	1000.0	40/76	2.555	0.000	323	3.00%
rental_medium_coverage_1000m	1000.0	40/76	2.588	0.000	323	3.00%
rental_medium_downside_1000m	1000.0	40/76	2.695	0.000	335	2.62%

The \$1bn primary case places IQD 1.300tn gross and IQD 1.274tn net after 2% issue fees. Peak IQD liquidity falls from 5.404tn in the matched holding-company equity reference to 2.525tn. These references pool four wholly owned businesses and include a conservative tax stress; they are different from the existing 4.461tn rail planning baseline and the independently financed 8.450tn SPV alternative. The original SPV private subscriptions of IQD 1.389tn are replaced, not added to holding subscriptions.

Private equity IRR for the \$1bn case is 2.75% nominal, with a 15% hurdle NPV of USD -508.624m for the 70% Iraqi private cohort. Its first dividend is month 323; ordinary shares have no guaranteed redemption or principal payment. With 5% general inflation, a roughly 3% nominal return does not establish an attractive real return. Actual ordinary dividends, retained profits, reserve balances, shareholder payments and ownership are exported monthly. IRR is undefined without positive shareholder receipts, or for ambiguous multi-sign cash flows; blocked-case NPV covers only funded investment to suspension and omits unresolved recovery/termination, so it is not a complete investor downside valuation.

Planned unlevered group resource NPV remains USD -2.906bn, or USD -3.372bn after the assumed unverified USD 600m land opportunity cost. It excludes debt/equity transfers, corporation tax and issuance fees and reconciles to the prior consolidated resource case. Debt replacement changes investor cash and finance costs, not this before-financing resource value. Blocked scenarios retain this planned-scope diagnostic while reporting only actual funded-prefix capital; no unbuilt assets or future earnings are presented as delivered. Financial resource NPV excludes wider social/economic benefits such as travel time and local employment, which need separate evidence.

Subscriptions, six-month placements and release gates

Founder/anchor subscriptions request 75% in six equal calls at months 0, 6, 12, 18, 24 and 30. The remaining 25% is a conditional primary issue at month 60, which may be private rather than listed; no admission is assumed. Actual settlements may extend beyond the requested dates to preserve the paid state floor. [primary_1000m-six-months.csv](#) reports actual subscriptions, net fees, restricted capital cash, government USD/IQD cash, native capital-credit draws, dividends and gap requirements every six months. Each monthly row reconciles physical invoices against capital sources; unspent subscription cash is restricted until construction invoices complete.

Net equity displaces the residual 25% bank/75% bond capital basket, bank first in each invoice. Domestic bank principal is amortised over 240 months and bond principal over 216 months, starting no earlier than full-network opening. This group-wide grace is more conservative than per-line cohorts and needs actual facility documents. Reference coupons stay 9%/8%; China retains 5%, 48-month draw grace and 180-month amortisation. Interest is paid throughout construction; arrangement fees, undrawn Chinese commitment charges, prepayment lock-ins/premiums, six months of debt service reserve, three months of OPEX buffer and factory warranty cash are included. The separate IQD 2% gap sensitivity has a 0.5% draw fee and 13tn cap; downside uses 8%, 1% and 4tn. None is committed.

Undersubscription and failed later issues hold the fully subscribed case's six-month capital-debt envelopes fixed. If the missing shares require capital credit beyond that envelope, the next physical invoice is withheld and the case reports no opening. The operating gap facility cannot cover refused capital. Already funded costs and debt remain; there is no forgiveness or assumed rescue. Resumption requires newly executable finance, rephasing, priced hold/restart and physical acceptance; resolution costs are unmodelled. The six-month delay sensitivity instead moves financial-close-to-NTP work and subscriptions together, retains fixed nominal property sales and indexes operations from close; it is a conditional whole-programme deferral, not a priced mid-construction suspension. Joint downside uses the existing 55/106-month physical stress, fare/nonfare shortfall, higher rates/inflation and weaker property sales, without uncontracted extra income.

Retained viaduct rentals, dividend policies and terminal cash

The [civil-linked rental portfolio](#) adds distinct, retained under-viaduct enclosures to the existing station-area sales. No sold parcel also supplies rent; actual title/overlap, height, fire/access and local tenant demand remain unaccepted. The 200,000 m² illustration exceeds the reference geometry screen and is omitted from group funding. Smaller cases include their own IQD fit-out capital, collected rents, rent-free/occupancy ramps, arrears/write-offs, vacant costs, insurance, refurbishment and cohort depreciation. Existing kiosk income is unchanged. Cash corporate tax is calculated once inside the group model; the rental ledger's separate tax diagnostic is not added again. Tenant deposits remain matched restricted cash and liabilities, supplying zero capital or dividends. Government original cash and Chinese USD imports remain unchanged; fit-outs borrow the domestic residual and use the existing parent subscription, with no additional partner cash in this 100%-owned alternative. Rental cases extend the domestic principal gate to the latest fit-out handover if it follows full-network opening; the conditional railway opening dates remain unchanged.

The medium rental case gives peak IQD gap debt 2.555tn, first dividend month 323, private nominal IRR 3.00% and planned before-tax resource NPV after existing station land USD -3.353bn. Additional corridor rights/opportunity cost is unknown, so this is not a complete new-land appraisal. The lower-rent/prolonged-vacancy case retains its costs rather than assuming free premises. Annual rental resource gains and investor gains are separately quantified.

Default ordinary dividends still require full debt repayment. coverage-and-reserves is an unapproved lender-policy sensitivity: annual distributions require 12 actual and 12 projected months of coverage at least 1.30, completed capital, cumulative distributable-profit proxy, no missing cash/current gap draw, restricted capital exhausted, intact OPEX/warranty reserves, six months of forward scheduled debt service and 12 months of upcoming rental refurbishment. CFADS excludes property-sale receipts and adds back their transaction costs; debt coverage includes scheduled interest/principal/fees and gap interest/fees, excluding voluntary principal sweeps. Forecast debt uses actual remaining vintages without future prepayment; forecast tax conservatively assumes no depreciation/interest/loss relief. No upcoming construction draw is permitted by the completion gate. The revolving gap sensitivity has no stated contractual amortisation, so its interest enters coverage and any distribution still needs an actual maturity/covenant agreement.

Up to 50% of cash surplus is held for possible dividends before optional debt sweeps; the balance repays the most expensive eligible credit. Final distributions also preserve cash for accrued tax and a liabilities/book-equity ceiling of 3.0. These are conservative group proxies, not subsidiary upstream permission, a legal reserve calculation or signed lender consent. Compared with the default first dividend at 323, the policy case first pays in month 323, private IRR 2.74%. With medium rentals, its first dividend is 323 and private IRR 3.00%. Monthly ledgers expose the actual coverage numerator/denominator, reserves, profit, dividends and debt balances. Earlier dividends reduce sweeps and can increase future finance costs; they are not new profit.

The original \$1bn default case ends with USD 3.585bn-equivalent unrestricted cash. A separately labelled `terminal_cash_sensitivity` allocates available final cash after nonsecurity debt/tax liabilities, at current proportional shares. It changes no actual dividend, company cash or share count and assumes zero transaction cost as an explicit illustration. Private IRR including this unapproved final cash return is 4.07%, versus 2.75% from dividends alone. Restricted deposits, reserves, unresolved funding, unvalued property/rail/factory assets and quoted share-price appreciation are excluded. Failed/unfunded cases cannot present a completed-horizon cash exit. No redemption, liquidation authority or proceeds are guaranteed; counsel must assess capital reduction, tax, transaction and continuing-service obligations before any distribution of capital. Each case exports both ordinary returns and the independent cash-only diagnostic, avoiding double counting.

Pro-forma accounts and consolidation

The group eliminates PPA, internal train invoices/capacity fees and station-rights charges using [the existing intercompany ledger](#). Factory input cash moves to group train assets at its actual purchase date; original manufacturing payroll/QA/overhead remains counted once. Subsidiary equity is replaced by parent subscriptions. Central treasury access, subsidiary distributions/guarantees and lender consent are assumptions requiring explicit agreements; 100% ownership alone does not permit unrestricted transfers. Business operating records remain separately attributable in [group-resource-monthly.csv](#). These are cash-based pro-forma accounts, not audited statutory statements or proof of admission.

Rail, train, solar and factory assets depreciate over 30, 20, 25 and 20 years respectively, phased into operation; depreciation is a noncash charge. Factory remaining book assets are conservatively impaired at Baghdad backlog/warranty close; there are no later orders or salvage receipts. Property construction is inventory, released once to cost of sales as sold; sold space generates no extra rental revenue. Existing maintenance/battery renewals remain in cash OPEX, plus the earlier explicit solar/caretaker allowance; reserves are not spent twice. Land opportunity cost remains a separate in-kind appraisal exposure, not a cash injection, paid-up shares or free balance-sheet asset.

The 15% corporate rate is the Iraqi GCT headline non-oil rate, not a tax ruling. Base scenarios tax each positive annual business operating-profit proxy after assigned depreciation/COGS, retaining internal business charges solely for a conservative tax stress. They assume no parent-interest deductions, subsidiary loss netting, exemptions, refunds or carryforward relief. This yields IQD 3.168tn lifetime cash tax in the normal case. The separately labelled `aggregate_tax_proxy_1000m` sensitivity taxes positive annual consolidated profit including finance costs; group eligibility is unestablished. Neither is statutory taxable income. Customs, property-transfer taxes, transaction withholding, relief and deductible rates require a priced Iraqi tax opinion before these budgets are investment-ready. [GCT corporate declaration guidance](#).

Annual tax is accrued at year end and paid next month, including final stub settlement. Net assets reconcile against nominal capital, share premium, issue-fee deductions, net retained profit and dividends; cash and book residuals must stay below USD 0.02/0.05. Missing cash is explicitly separate assumed unfunded support, never new government equity. Dividends require cumulative positive distributable-profit proxy, no missing funding, all debt repaid, no unused capital cash and intact OPEX/warranty/DSRA reserves. A further 10% positive-profit retention is contractual sensitivity, not the statutory reserve rule. Audited distributable profit, legal reserves, subsidiary upstreamability and board approval remain additional gates even when the model shows a possible dividend.

Iraqi legal, governance and admission gates

[Companies Law Articles 7 and 7 bis](#) support a mixed company with initial state capital at least 25%, holding subsidiaries and annual consolidated accounts. Mandate, concession, incorporation, capital approvals and enforceable public-service obligations still require the competent Iraqi bodies. Publish ordinary commercial contracts separately from affordability/service subsidies; optional future availability support requires an appropriation outside the 25% construction rule.

The [official 2019 amendment, Articles 12 and 28](#) contains the relevant 51% Iraqi participation condition and a liabilities limit of 300% of capital plus other owners' rights, with adjustment powers. Application, current amendments, foreign-investor exceptions, entity-level calculation and permitted treasury structure require counsel. A consolidated screening proxy flags 209 months above that limit or with insufficient book equity in the \$1bn scenario. It is not a legal compliance certificate; passing a share-floor check does not clear this debt constraint. The model is therefore not an executable capital structure until legal/capitalisation resolution is accepted.

[Regular-market Regulation 6](#) normally requires two years/history and audits, at least 100 shareholders, equity at least paid-up capital, actual business and two years' distributable profit; a discretionary shorter history provision does not constitute admission. [Secondary-market Regulation 15](#) provides a one-year activity/audit route and equity of at least 50% of paid-up capital, alongside approvals and disclosures. Apply the [ISC September 2026 amendments](#) and seek the regulator's current interpretation before fixing any offering date. Actual shareholder count, audits, eligible profits, applications and approvals are absent. All cases set `company_incorporated` and `listing_approved` false; month 60 is a funding assumption, not a listing prediction.

Use an independent board/audit committee, published related-party prices and conflicts policy, minority pre-emption/approval protections, consolidated and subsidiary disclosure, audited capital registers, procurement oversight and an explicit public-service contract. Government control and future retail ownership do not themselves demonstrate these controls. Open licences remain intact: investors own businesses, assets and enforceable contracts, without any valuation premium for exclusive ownership of openly licensed designs. New land/concession contributions require independent valuation, title and separate dilution treatment; none is included here.

ISC's [2025 market report](#) records IQD 531.5485bn share turnover and IQD 23.673365tn market capitalisation. The old IQD 4.461tn planning gap is approximately 8.4 times annual turnover; turnover is not a ceiling on primary subscriptions. The model therefore requires anchor placement evidence for each tranche rather than assumed retail absorption. The \$1bn primary gross IQD 1.3tn is about 2.45 times that turnover, which is a scale comparison, not proof of capacity or incapacity. Sources checked 3 October 2026.

Evidence programme

Six new native ERP work packages require Iraqi corporate/tax counsel, public mandate and capital register, anchor/debt placement proof, audit/consolidation and dividend policy, minority/open-licence controls, and actual admission evidence. Owners, quotes, signatures and approvals remain pending. Due days are relative to an approved programme start. The ERPNext Task import contains draft descriptions and no invented live IDs; local import receipts remain private. Existing ten physical/funding qualification tasks and six financing-redesign tasks continue to apply. Model outputs do not accept any evidence or permit operation. No external investor solicitation, issuance or expenditure is authorised.

Regenerate: `.venv/bin/python tools/automation/baghdad_equity.py`; validate source/output hashes with `--check`. Commitments and accepted physical evidence are required before any construction/opening/dividend decision.

Baghdad factory sized to the city programme

Source: [cities/catalogue/west-asia/Iraq/Baghdad/engineering/factory/README.md](#)

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

One factory is sized for 762 complete six-car trainsets / 4,572 cars, with physical cells, crews and test paths. Facility readiness is 18 months from notice to proceed (working day 390), replacing the old 24-month assumption. Financial close precedes NTP by 30 working days; these are conditional offsets, not dated construction commitments.

The unchanged infrastructure resource model finishes on working day 1550. The sized flow accepts the final train on day 1542, 8 working days earlier. Full-network commissioning therefore follows infrastructure completion, rather than waiting decades for four generic train-production slots. All 762 trains remain in the planned scope; there is no smaller opening-fleet substitution.

Flow and physical capacity

Cycles explicitly represent a whole six-car trainset, with structural, electrical and fit-out allowances doubled from the old generic cycle. One eight-hour shift and 85% productive availability are assumed. Occupation is $\text{ceil}(\text{productive cycle} / \text{availability})$; availability is not deducted again from that output. The first complete train belongs to the 762 and carries an additional 60-working-day qualification allowance. Every remaining material-kit task depends on that first-article acceptance; no series release is assumed before day 556.

Stage	Productive days	Occupied days	Cells/bays	Direct crew
Baghdad trainset kitting	3	4	4	12
Baghdad six-car structural assembly	24	29	25	450
Baghdad six-car composite kits	10	12	11	88
Baghdad six-car body installation	2	3	3	36
Baghdad six-car electrical integration	20	24	21	252
Baghdad six-car fitout and static test	16	19	17	204
Baghdad trainset acceptance bays	12	15	13	52

The limiting steady capacity is 224.1 trainsets / 1345 cars per working year. The resource scheduler simulates each train's linked stages, finite lanes and first-article gate. Cells are calculated from the city's fleet and the remaining infrastructure window, then increased to the first feasible balanced allocation; this is a reproducible capacity design, not a proof of minimum land or minimum cost.

Production bays use a 135 m by 6.5 m envelope for the 111 m consist, not a released building module. Composite and kitting cells have separate floor assumptions. Process and support space totals 112,755 m². The site screen is 43.2 hectares, including circulation/storage and 3 independently segregated 2.0 km test paths. These are site-reservation assumptions pending geometry, braking, fire, access, geotechnical and safe-operation design. Dynamic acceptance bays are not independent running tracks: the separate path calculation permits only 331.5 trainsets/year, based on 16 exclusive track-hours/train and 85% path availability. A shared route cannot be counted twice. The test-path margin above limiting production is only 47.90%; the final fleet has only 8 working days of schedule margin. See the [frozen-resource disruption, costed second-shift recovery and civil acceleration study](#). Those stresses preserve the selected cells rather than resizing them to hide delay.

Direct cell staffing totals 1,094 positions per staffed shift before management, stores, maintenance, relief and shift coverage. It is a proposed resource requirement, not measured job creation. Manufacturing labour and materials are already in train procurement CAPEX; they are not added again to plant CAPEX or railway OPEX.

Line handover and the early-line constraint

Line	Full fleet	Infrastructure day	Fleet day	Opening month
line-1	86	668	758	40
line-2	101	785	875	45
line-3	97	897	987	50
line-4	80	990	1080	55
line-5	86	1090	1180	59
line-6	100	1206	1296	65
line-7	79	1298	1388	69
line-8	90	1402	1492	74
line-9	43	1550	1542	76

The factory completes alongside the overall city civil programme. Full-fleet openings are retained. Noncritical infrastructure now moves within its existing crew lanes and dependency graph towards fleet handover, with a 90-working-day target buffer; critical infrastructure retains its original completion dates. Line 1's infrastructure completion moves from day 196 to day 668, reducing the idle interval before its fleet from 562 to 90 working days. No rolling-stock date, task duration, resource count or opening date changes. This is a conditional investment-timing proposal: surveys, land, utilities, permits and contract dates require approval before deferring site work. [Original and rephased line reconciliation](#) preserves both sets of dates. Line priority follows the original infrastructure requirements, with actual asset identifiers preserved.

The opening calculation retains the separate three-month integrated commissioning allowance after line infrastructure, the full fleet and shared depot/control work. The 60-day first-article allowance and three-month line allowance cover different activities. Required approvals, surveys, physical tests and independent acceptance remain open; neither allowance constitutes accepted safety evidence or an approved construction calendar.

Eighteen-month facility construction sequence

Activity	Working days	Accountable role
Land/access, survey, design and approvals	60	Sponsor and owner engineer
Mobilisation, earthworks, foundations and underground services	70	Local civil contractor
Factory shell, lifting structure and utility backbone	70	Local structural and MEP contractors
Production cells, moulds, cranes and test-track construction	80	Production engineer and equipment suppliers
Equipment installation, calibration, staffing and training	70	Factory operator and quality manager
Factory process proving, safe-work and facility acceptance	40	Owner engineer and independent inspectors

These six sequential planning packages total 390 working days. Long-lead tooling, cranes, battery handling equipment and imported systems must be ordered early enough to install and prove within that window. Land/access and financing availability are required at NTP. A delay to those gates changes the programme; the schedule is not a contractor-backed promise.

Factory capital and cashflow

Physical budget allocation	USD million
buildings	78.929
serviced site	15.116
stage tooling	102.850
test tracks	18.000
shared utilities stores labs logistics	35.000
design training qualification	20.000
contingency	53.979

The physical envelope is USD 323.874 million direct, compared with the old module allowance of USD 274.320 million. The programme budgets the larger amount, USD 323.874 million plus USD 22.671 million EPC, counted once. The resulting capital increase is USD 53.023 million; added bays are not treated as free capacity. Rates and quantities are engineering allocations requiring Iraqi contractor/vendor quotations, not market-verified prices. Actual equipment origin must also reconcile to the programme's imported/local allowances.

Factory payments are re-timed to the 390-day facility programme and city train payments follow the new production tasks. Baghdad's monthly debt, interest, 5% fare/OPEX indexing, liquidity gaps, surplus repayments and six-month bond/loan requirements are recalculated from those dates. Government remains 25% of capital; import cash and Chinese credit retain the 50:50 USD split, with remaining funding in IQD. The existing aggregate plant import allowance remains 20% of direct plant

capital, allocated within tooling/test equipment rather than buildings; supplier origin and the actual equipment mix require RFQs and eligibility checks. EPC retains its separate procurement-origin allowance. Future national cities do not enter this plant's production load or Baghdad cashflow.

Procurement and qualification requirements

Before release, obtain measured six-car labour routes and prototype cycle times; trainset-level supplier delivery schedules; released mould/fixture drawings and duplication plans; lifting/handling and HV/battery fire segregation; stores, quarantine and rework capacity; inspection/calibration capacity; crew recruitment and training; both independent test-path designs; utility availability; and a land/industrial permit package. Composite cells cannot be mistaken for the number of panel moulds: the final panel design and cure/release conditions determine mould duplication. The hypothetical whole-kit cycle must be validated against that tooling count. Existing civil precast/slab yards retain their own production resources and are not assigned to train bays.

The 85% factor is a deterministic allowance for non-productive time, not a quantified programme contingency. Supplier disruption, multi-month qualification, redesign and civil delays need risk scenarios before investment decisions. Expansion beyond Baghdad needs a new demand and capacity assessment; a national module budget is not a promise of parallel national production.

[Cell and tooling register](#) · [762 planned trainset acceptances](#) · [Line handover reconciliation](#) · [Machine-readable calculation](#) · [Factory capacity inputs](#)

Regenerate after operations with `.venv/bin/python tools/automation/generate-factory-plan.py`; validate the same command with `--check`. Status: reference planning engineering, no construction or manufacturing release.

Baghdad — Iraq funding appraisal

Source: <cities/catalogue/west-asia/Iraq/Baghdad/engineering/finance/FUNDING-MODEL.md>

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

Generated from current city CAPEX and procurement milestones. All facilities and appropriations remain uncommitted.

Government capital is 25% of total city CAPEX, before Chinese credit is deducted. The residual after that contribution and proposed Chinese proceeds is split 75% IQD bonds / 25% IQD bank credit. Imported purchases use 50% government USD cash and 50% proposed Chinese credit, assuming full-basket eligibility is later qualified; the remaining government contribution is IQD. Financing fees, construction interest, reserves and operating/debt support are additional funding requirements, not included in the 25% capital contribution. See the [Baghdad-only programme](#) for the uncovered cash requirements if no additional government cash is available.

Construction cash runs through month 78; full-network operations start in month 78 after retention. This conservative rollout follows the current resource-constrained CPM, not a five-year promise.

Capital sources and uses

USD is the comparison unit below. Chinese credit is USD debt; domestic bonds and bank credit are IQD debt. Baghdad imported purchases are funded 50% government USD cash and 50% proposed Chinese loan; the remaining government capital and local cash are IQD. The full Baghdad import basket is assumed eligible pending supplier-origin and lender qualification. Other city appraisals retain their own assumptions. Fares and local operating payments are budgeted in IQD.

Capital source	Contract / cash currency	Native amount at model FX	USD equivalent
chinese export credit	USD	808,082,706.05	808,082,706.05
domestic bonds	IQD	4,454,109,966,999.19	3,426,238,436.15
bank credit	IQD	1,484,703,322,333.06	1,142,079,478.72
government import cash	USD	808,082,706.05	808,082,706.05
government local cash	IQD	1,279,266,084,532.49	984,050,834.26
Total city capital uses	Mixed	—	7,168,534,161.23

Chinese buyer credit is proposed for eligible Chinese component invoices only. Government contributes its configured capital share, including the eligible-invoice downpayment; IQD bonds and bank credit finance the residual. The conditional ledger also calculates cash needed for fees, construction interest, reserves and operating/debt shortfalls. That additional support is uncommitted and is an unfunded requirement if Baghdad public cash is capped at its 25% capital contribution.

Proposed instruments

Instrument	Currency	Rate assumed	Grace from draw	Repayment
chinese export credit	USD	5.0%	48 months	180 months
domestic bonds	IQD	8.0%	24 months	180 months
bank credit	IQD	9.0%	0 months	84 months

Chinese component allocation

These allocations divide existing imported budgets; they are not additional costs, supplier quotes or confirmed origin.

Bucket	Component	Assumed eligible invoice USD
civil	other_imports_pending_lender_and_origin_qualification	583,428,252.90
stations	other_imports_pending_lender_and_origin_qualification	148,380,000.00
depots	other_imports_pending_lender_and_origin_qualification	2,000,000.00
rolling_stock	bogies	179,222,400.00
rolling_stock	traction_batteries	134,416,800.00
rolling_stock	windows	22,402,800.00
rolling_stock	doors	44,805,600.00
rolling_stock	other_imports_pending_lender_and_origin_qualification	67,208,400.00
solar_plant	solar_panels_and_inverters	336,315,212.65
signalling	other_imports_pending_lender_and_origin_qualification	11,854,494.50
charging_microgrid	solar_panels_and_inverters	8,092,000.00
charging_microgrid	station_batteries	9,248,000.00

Bucket	Component	Assumed eligible invoice USD
charging_microgrid	other_imports_pending_lender_and_origin_qualification	5,780,000.00
epc_overhead	other_imports_pending_lender_and_origin_qualification	63,011,452.05

Annual cash requirements

Year 1 begins at assumed financial close; NTP follows 30 working days later. Amounts below are USD millions. DSCR excludes subsidy; public cash includes capital, fees, interest, reserves and support.

Year	CAPEX	Revenue	OPEX	Debt service	Public cash	DSCR before support
1	337.53	0.00	0.00	10.87	97.00	0.00
2	693.86	0.00	0.00	50.58	227.63	0.00
3	1371.39	0.00	0.00	127.63	477.90	0.00
4	1591.10	0.00	0.00	250.57	656.96	0.00
5	1581.50	0.00	0.00	385.19	789.13	0.00
6	1509.05	0.00	0.00	528.61	914.00	0.00
7	84.11	110.92	96.29	619.41	943.99	0.02
8	0.00	277.31	192.58	649.77	577.00	0.13
9	0.00	388.24	192.58	656.08	455.35	0.30
10	0.00	443.70	192.58	634.25	367.27	0.40
11	0.00	443.70	192.58	592.25	317.42	0.42
12	0.00	443.70	192.58	544.08	268.87	0.46
13	0.00	443.70	192.58	496.24	221.74	0.51
14	0.00	443.70	192.58	469.95	216.03	0.53
15	0.00	443.70	192.58	469.60	218.48	0.53
16	0.00	443.70	192.58	469.60	218.48	0.53
17	0.00	443.70	192.58	469.60	218.48	0.53
18	0.00	443.70	192.58	462.02	202.08	0.54
19	0.00	443.70	192.58	432.70	162.19	0.58
20	0.00	443.70	192.58	377.38	89.58	0.67
21	0.00	443.70	192.58	290.77	8.83	0.86
22	0.00	443.70	192.58	195.93	0.00	1.28
23	0.00	443.70	192.58	93.39	0.00	2.69
24	0.00	443.70	192.58	28.36	0.00	8.86
25	0.00	443.70	192.58	9.75	0.00	25.75
26	0.00	443.70	192.58	0.13	0.00	1911.90
27	0.00	443.70	192.58	0.00	0.00	—
28	0.00	443.70	192.58	0.00	0.00	—
29	0.00	443.70	192.58	0.00	0.00	—
30	0.00	443.70	192.58	0.00	0.00	—
31	0.00	443.70	192.58	0.00	0.00	—
32	0.00	443.70	192.58	0.00	0.00	—
33	0.00	443.70	192.58	0.00	0.00	—
34	0.00	443.70	192.58	0.00	0.00	—
35	0.00	443.70	192.58	0.00	0.00	—
36	0.00	443.70	192.58	0.00	0.00	—
37	0.00	221.85	96.29	0.00	0.00	—

Sensitivities

Scenario	Peak annual public cash USD m	Minimum operating DSCR	Peak uncovered monthly capital USD m
base low demand	943.99	0.02	0.00
high capacity use	914.00	0.13	0.00
capex plus 25 percent	1183.64	0.02	0.00
demand minus 40 percent	988.36	-0.05	0.00
iqd depreciation 35 percent	800.33	0.02	0.00
commissioning delay two years	966.08	0.02	0.00
china credit unavailable	874.02	0.03	17.30
four year bullet bonds	1737.14	0.01	0.00
government payment delay six months	1125.32	0.02	14.34
interest plus three points	1134.31	0.02	0.00
combined downside	1202.33	-0.03	0.00

Assumptions and evidence

- Working-day milestones use 260 working days/year and 30 working days before NTP; holidays and an approved local calendar are pending.
- No signed Chinese loan, supplier-origin qualification, guarantee, bond mandate, bank facility, appropriation or tax/duty assessment.
- Chinese origin and lender eligibility remain unqualified proxies. Default advance is 85%; Baghdad assumes all imports can qualify for 50% USD loan / 50% government USD cash. Additional imported categories require lender and supplier approval; neither assumption is a verified lender rule.
- Domestic bonds assume a proposed MoF sovereign IQD programme; municipal borrowing powers and market demand are not assumed.
- Long amortising domestic bonds are an appraisal target; the four-year bullet sensitivity exposes redemption without automatic refinancing.
- Construction cohorts need separately approved facilities. A long rollout does not imply a lender offers decades of draw availability.
- Interest is paid on drawn native balances; mid-month draw convention, monthly repayment, fees paid by government; no interest capitalisation.
- All cash is nominal; no inflation/escalation in base. IQD revenue and OPEX are translated at scenario FX; imported energy/parts OPEX needs a separate currency survey.
- Unquoted CAPEX budgets remain nominal USD planning values. IQD tranches and appropriations convert at draw-date FX; no automatic local supplier price benefit from depreciation is assumed.
- Income used for labour and fares is the retained country-finance planning proxy, not a verified current Iraqi household median or an agreed wage/fare contract.
- Government payment delays and unavailable China credit produce explicit capital cash gaps; no committed bridge credit is assumed.
- Restricted DSRA targets six times current monthly service and uses available project cash before requesting support. Support cash is a required contribution, not a commitment; repayments and reserve balances are conditional on it. Baghdad programme caps government capital at 25% and separately discloses the additional unfunded requirement. Future-service covenant testing is pending.
- Battery renewal reserve remains inside existing rolling-stock maintenance OPEX; no second battery CAPEX is added.
- Demand is capacity-led, not a surveyed forecast. Passing reconciliation does not demonstrate affordability or bankability.

Long construction schedules can leave much of the debt already repaid by government before full-network opening. An operating DSCR above one therefore does not establish self-financing or remove the construction-period public cash burden. Uncovered capital gaps are conditional funding requirements, not actual cash receipts.

See [editable assumptions](#), [monthly cashflow](#), [annual cashflow](#), and [machine-readable model](#).

The [IMF Article IV](#) provides the historical FX anchor. [CBI](#) describes its role as fiscal agent for MoF bonds. [China Exim](#) describes export buyer credit; numeric project terms remain assumptions.

Conditional phased-opening sensitivity

The base above withholds all fares until every capital milestone. This separate sensitivity opens completed lines after the editable commissioning lag and gates every line on shared system/depot work. The city-sized Baghdad production plant is unavailable for its first 390 working days (18 months from NTP), followed by the scheduled first-article qualification gate. Opening also requires actual civil, train, depot, power and safety acceptance, which is not established by this calculation.

Revenue and variable OPEX use each line's share of controlled trainsets. Each line has its own 50% / 75% / 100% revenue ramp. Fixed OPEX is 25% of the full-network annual budget from first opening; remaining OPEX scales with opened fleet. These are explicit uncalibrated sensitivity assumptions, not a ridership survey or verified staffing plan.

First / last planned opening: month 40 / 76 from financial close (month zero). City additional funding requirement: USD 5,509.68 million. The plant remains separate. Future surplus is retained; gross additional support is not net lifetime loss or discounted cost.

Line	Opening month	Revenue / variable OPEX share
line-1	40	11.29%

Line	Opening month	Revenue / variable OPEX share
line-2	45	13.25%
line-3	50	12.73%
line-4	55	10.50%
line-5	59	11.29%
line-6	65	13.12%
line-7	69	10.37%
line-8	74	11.81%
line-9	76	5.64%

[Phased monthly cashflow](#) ·
 [phased annual cashflow](#)

Baghdad financing reconciliation and six-month placement programme

Source: <cities/catalogue/west-asia/Iraq/Baghdad/engineering/finance/FUNDING-RECONCILIATION.md>

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

Scope: Baghdad city and one Baghdad manufacturing plant. Samawah, Mosul and every other city are excluded. Month zero is an assumed financial close, not an approved date. All financing and additional revenues remain uncommitted.

The numbers that must add up

The original capital sources and uses reconcile. The confusion was combining upfront capital, repayment of that same capital debt, gross liquidity injections and later retained cash. The revised schedule also spreads city EPC overhead across direct works instead of paying the entire programme allowance against the initial five-day baseline-freeze task. Capital cost is unchanged. An independent implementation rebuilds every debt vintage, interest charge, principal payment and financing fee from native draws; it does not copy the reported support total.

Capital source	Native currency	Native amount, billion	USD equivalent, million
chinese export credit	USD	0.842170	842.170
government import cash	USD	0.842170	842.170
government local cash	IQD	1,347.579172	1,036.599
domestic bonds	IQD	4,674.285469	3,595.604
bank credit	IQD	1,558.095156	1,198.535
Capital uses / sources	Mixed	—	7,515.079

Government cash remains 25% of capital, with government USD import cash inside that contribution. Imports are financed 50% government USD cash / 50% Chinese USD loan. Every other loan and bond is IQD. An international green lender must provide confirmed IQD on-lending or a priced currency hedge to preserve that strategy. A green label does not supply additional money.

Lifetime operating / finance reconciliation	USD equivalent, million
Fare and existing nonfare receipts	13,644.125
OPEX	6,138.577
Repayment of originally drawn capital principal	5,636.309
Interest on original capital financing	4,129.288
Original financing fees	40.334
Net nominal lifetime liquidity deficit	2,300.383
Gross extra cash required as bills fall due	5,962.665
Later unrestricted cash retained if those requirements are met	3,662.282

USD 5,962.665m gross injections minus USD 3,662.282m retained cash equals USD 2,300.383m net deficit. Capital purchases are already financed by their capital sources; principal repayments belong to the lifetime cash ledger and must not be added to the construction budget again. Net reserve deposits are zero at the end. This is a nominal identity, not discounted viability, and assumes city/plant cash can legally be pooled

A zero-interest, zero-fee revolving bridge is only a mathematical lower bound. Real gap funding must charge interest and fees on the borrowing needed to carry early deficits, repay itself from later surplus and show any terminal debt. Later surplus cannot be counted both as retained cash and as loan repayment.

Tickets, kiosk rents and advertising already included

Full-network steady annual receipts	IQD billion	USD equivalent, million
Passenger tickets	547.335	421.027
Station shops and kiosk leases	11.542	8.878
Advertising space	17.932	13.794
Total existing operating receipts	576.808	443.699

Tickets use 415.49m annual paid trips at IQD 1,317 average yield. This is assumed capacity use, not calibrated demand. Shops/kiosks use 27,656 m² at IQD 39,520/m²/month and 88% occupancy; advertising uses 5,084 boards at IQD 345,800/month and 85% occupancy. Rates derive from the retained income proxy, not Baghdad lease quotes. These are gross

rental/advertising receipts; dedicated concession costs, tenant demand and collection losses require appraisal.

All three receipts enter the existing operating cashflows and therefore already reduce the financing gap. The phased sensitivity scales the combined receipts by opened-fleet share and the separate 50% / 75% / 100% revenue ramp for each line. Retail and advertising demand may follow different ramps in practice. Proposed naming rights, telecom leases, parking, development proceeds or new commercial receipts must be genuinely additional and net of costs; existing rents cannot be booked again or sold upfront while also retained in future revenue.

What gap finance actually does

The illustrative maximum outstanding facility is IQD 13.000 trillion (USD 10.000bn equivalent). This is a size assumption, not proof that the Iraqi banking market can place it. All available surplus after core obligations and reserves is swept to its repayment. No refinancing or debt forgiveness is assumed at the final maturity.

Scenario	Gross new liquidity draws, IQD tn	Peak facility balance, IQD tn	Uncovered cash beyond facility, IQD tn	Terminal unpaid facility, IQD tn
unfunded reference	0.000	0.000	7.751	0.000
green label only	0.000	0.000	7.751	0.000
zero cost liquidity bound	7.751	7.751	0.000	2.990
commercial gap credit	13.000	13.000	17.914	13.000
concessional gap credit	9.950	9.950	0.000	7.934
blended candidate	7.959	7.784	0.000	5.091
green concessional only	9.085	9.085	0.000	7.363

Reference and label-only cases have no gap facility: their uncovered column is the required external cash contribution, not an approved government top-up. With a facility, uncovered cash excludes the separate terminal loan balance; both need a solution. Gross draws can exceed the maximum outstanding commitment when a revolving facility is repaid and redrawn. Conditional ledgers do not establish that an unfunded payment occurred.

Commercial gap credit assumes 8% interest and 1.0% draw fees. Concessional gap credit assumes 2% interest and 0.5% draw fees. Neither is a term sheet or an available GCF line. Funding old debt-service deficits is not automatically eligible green use of proceeds.

Explicit blended sensitivity

Candidate climate expenditure is USD 2,085.33m of electric rolling stock, solar and charging provision, including USD 1,277.84m assigned locally. Climate benefit, supplier qualification and green eligibility require independent review. Candidate green bonds replace only domestic bonds attributable to those expenditures; civil works and unrelated overhead are not automatically relabelled.

The blended sensitivity replaces that eligible bond portion with proposed IQD green bonds/sukuk at 4%, 48 months' grace and 240 months' amortisation, with 0.75% arrangement fees and 0.5%/year enhancement fees on outstanding principal. The lower rate depends on a concessional or guarantee structure; a green label alone retains the original 8% terms and changes no financial outcome.

Additional targets are a USD 25m climate capital grant translated into IQD receipts, replacing domestic borrowing against eligible local capital after month 24; USD 300m net development-rights proceeds in 6 six-month instalments from month 24; and USD 25m/year genuinely new net local receipts at full opening, scaled with the opened fleet. These are editable targets, not appraisals, GCF approvals, developer contracts or statutory levies. Existing rents, advertising and fares cannot be counted again; transaction/development costs and displaced future rents must be deducted. Public land contribution also needs economic valuation.

Solving the model rather than declaring the targets sufficient requires approximately USD 113.94m/year additional NET receipts (IQD 148.13bn/year at full opening) to eliminate both uncovered cash and the terminal facility under the other blended assumptions. This is a break-even funding requirement, not a forecast or a recommended passenger fare increase. Any covenant, inflation, FX or demand change can raise it.

Variable tickets, annual price changes and OPEX inflation

The following cases retain the same conditional blended capital/grant/rights/2% IQD facility assumptions. They change fares, OPEX and income separately. A 5% tariff increase with flat costs is an optimistic sensitivity; the paired 5% OPEX case is the requested inflation comparison. None is an adopted fare, a lender commitment or an Iraqi inflation forecast.

Indices compound in annual steps from financial close, including the years before first opening. No tickets are sold before service starts; the nominal launch price reflects elapsed inflation. Existing retail/advertising are held flat unless the case explicitly indexes those rents. New net income and rights targets remain fixed nominal amounts. CAPEX escalation and future

FX changes still require a separate full nominal appraisal.

Demand responds to fare relative to the indexed income proxy with an illustrative elasticity of -0.30, except the explicitly fixed-demand cases. Income growth is a separate assumption, not evidence that wages will keep pace. Discount-led demand growth is capped at 2.0 times the baseline, within the original practical capacity. There is no calibrated Baghdad peak-switching or household demand model.

Variable tickets assume 40% of baseline trips in a peak tier at 1.25 times the standard fare, and remaining trips at 0.90 times it. Each tier gets its own demand response before revenues are combined. Concessions, commuter caps, integrated transfers and off-peak eligibility require an actual tariff design and funding contract; their costs are not silently waived.


Pricing sensitivity	Fare / OPEX / income growth	Full-opening average fare, IQD	44 trips / income at full opening	Peak facility, IQD tn	Uncovered cash, IQD tn	Terminal debt, IQD tn
fare 5pct flat costs fixed demand	5% / 0% / 0%	1,765	15.7%	3.178	0.000	0.000
fare 5pct flat costs elastic	5% / 0% / 0%	1,765	15.7%	3.837	0.000	0.000
fixed fare 5pct opex	0% / 5% / 5%	1,317	8.8%	13.000	9.741	13.000
fare 5pct opex 5pct	5% / 5% / 5%	1,765	11.7%	4.256	0.000	0.000
fare 5pct opex 7pct	5% / 7% / 5%	1,765	11.7%	5.786	0.000	0.000
fare 5pct opex 5pct income 2pct	5% / 5% / 2%	1,765	14.0%	5.439	0.000	0.000
variable fare 5pct opex 5pct	5% / 5% / 5%	1,822	12.1%	4.028	0.000	0.000
fare 5pct opex 5pct rents indexed	5% / 5% / 5%	1,765	11.7%	4.071	0.000	0.000

In the paired 5% case, the first line's average nominal fare is IQD 1,525 in month 40; at full opening in month 76 it is IQD 1,765. Its maximum supplemental facility is IQD 4.256tn, with IQD 0.000tn uncovered cash and IQD 0.000tn unpaid at the end. Later surplus can repay a priced facility under these assumptions; it does not remove the early borrowing requirement.

At an 5% general-price assumption, the 8% real discount assumption becomes 13.4% nominal. The paired-case unlevered NPV is USD -3.262bn equivalent before grants/new rights/net-income targets and with capital still un-escalated. Large distant nominal balances are not present-value wealth or proof of project viability.

If income rises with fares, the modelled commuting share stays broadly constant. With income rising only 2%, the same ticket policy becomes progressively less affordable and reduces paid trips. If OPEX rises 7% against 5% fares, the tested financing again leaves uncovered requirements and terminal debt. Maintaining an affordable real tariff, collecting revenue and placing the required early IQD facility matter as much as the nominal annual increase.

Fare policies, OPEX inflation and affordability: illustrative blended funding

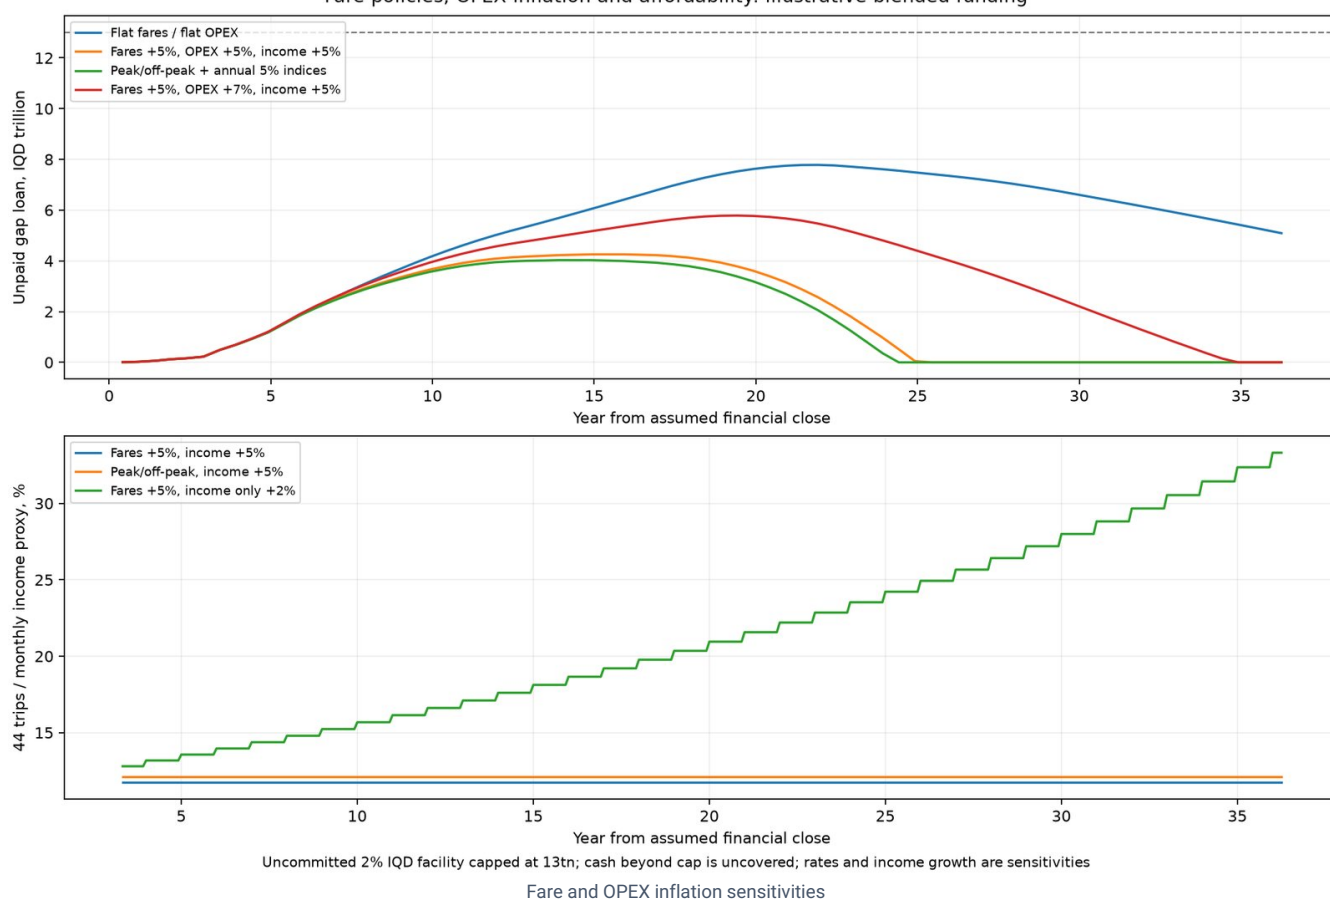

[Paired 5% six-month funding requirements](#) · [paired monthly prices and affordability](#) · [variable-ticket funding requirements](#) · [variable monthly tickets](#)

The initial real-fare multiplier required to remove both terminal debt and uncovered cash under paired 5% indices and the other blended assumptions is approximately 1.000 times the existing baseline. This is a conditional break-even sensitivity, not a tariff recommendation; it does not guarantee the facility can be placed or that households' incomes will grow.

Surplus cash and early repayment

These cases use identical paired 5% fare/OPEX/income assumptions and the same conditional blended capital sources. Each pays OPEX, scheduled principal, interest and fees, then funds the debt-service reserve and a three-month current-OPEX buffer before voluntary repayment. Borrowed gap proceeds and uncovered external cash cannot fund early payments. The extra buffer remains cash held at the terminal horizon and earns no interest.

Compare strategies against buffered gap-only, rather than attributing the buffer change to repayment savings. Loans-first pays bank credit, Chinese credit and gap credit before bonds. Cost priority pays bank (9%), ordinary bonds (8%), Chinese credit (5%), green bonds (4% plus 0.5% annual guarantee), then gap credit (2%). It is an interest-rate heuristic, not a proof of the globally best strategy.

Surplus strategy	All debt cleared, month from close	Finance cost saving vs buffered gap-only, USD equivalent m	Early-payment premiums, USD equivalent m	Peak gap debt, IQD tn	Terminal unrestricted cash, IQD tn
gap only buffered	365	0.000	0.000	4.418	14.870
gap then core	306	9.839	1.572	4.418	14.883
loans then bonds	305	81.916	6.310	4.372	14.976
cost priority	303	168.132	21.169	4.371	15.088
cost priority zero premium	303	195.771	0.000	4.368	15.124
cost priority noncallable bonds	365	71.442	4.683	4.372	14.963


Cost priority clears all debt in month 303, compared with 365 for buffered gap-only. Net nominal financing savings are USD 168.132m equivalent, after USD 21.169m assumed early-payment premiums. Savings include core interest, annual green guarantee charges and supplemental interest/draw fees; they exclude principal, which is returned once. All cases retain IQD 0.362tn operating buffer separately from unrestricted cash. There is no additional government contribution above 25% of CAPEX in these cases.

Assumed premiums are 1% of bank/Chinese/green principal and 2% of ordinary bond principal. A minimum draw age of 6 months (bank), 12 (Chinese) and 24 (both bonds) prevents immediate issue-and-redemption. Eligible vintages are repaid oldest first; contractual instalments are kept and maturity shortens. Notice, issuer call rights, investor consent, buyback price, remaining-maturity compensation, tax and FX require actual agreements. Noncallable-bond sensitivity makes no voluntary bond payments; zero-premium sensitivity removes only the assumed premium, retaining minimum ages.

Facility	Buffered gap-only final principal payment month	Cost-priority final principal payment month	Early principal, native currency	Premium, native currency
bank credit	161	161	IQD 179.993bn	IQD 1.800bn
domestic bonds	281	230	IQD 853.131bn	IQD 17.063bn
chinese export credit	305	235	USD 239.631m	USD 2.396m
green bonds	365	244	IQD 554.236bn	IQD 5.542bn

The gap facility's final principal payment is in month 303. Later surplus remains unrestricted cash after debt retirement. Each month's native debt balance equals prior balance plus draws minus scheduled and early principal. Each six-month closing balance is its final month's balance; payments, premiums, interest and reserve movements are period sums. Contractual repayment windows in tranche files describe the original draw terms; the actual final-payment months above incorporate early repayment.


Monthly cost-priority repayments · six-month repayment tranches · loans-first tranches · all six complete calculations

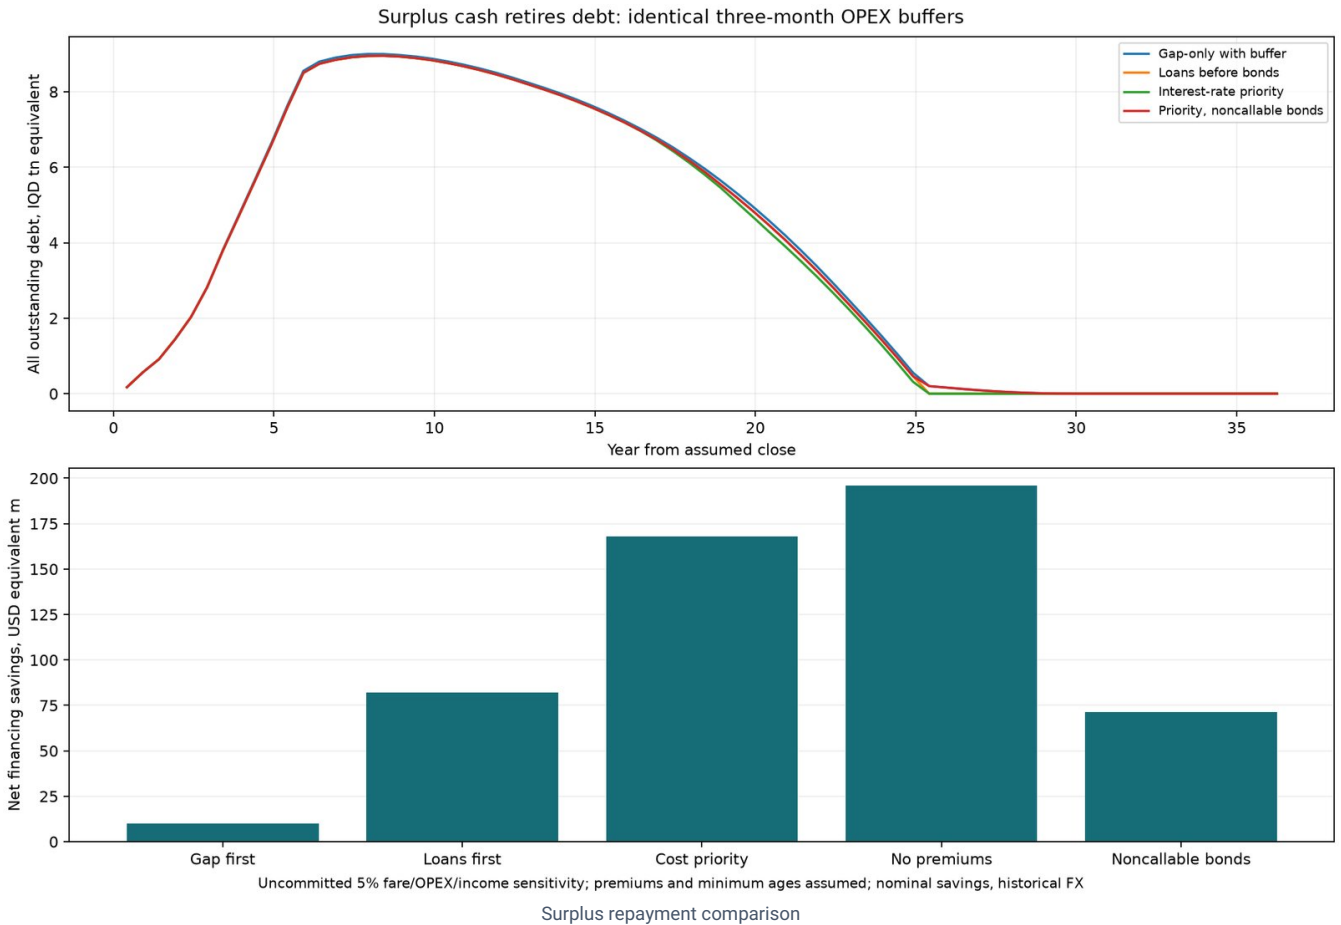

Loan prepayment can carry redeployment/unwind charges: the [World Bank Treasury FAQ](#) illustrates the concept, without establishing Chinese or Iraqi loan terms. The [US Treasury buyback FAQ](#) and [published purchase results](#) illustrate issuer authority and priced buybacks rather than automatic par redemption; they do not supply an Iraqi legal mandate.

This repayment allocation does not change the unlevered project NPV or validate demand. Nominal savings over several decades are not present-value gains. CAPEX escalation, FX, lifecycle replacement, floating-rate risk and the uncommitted early funding still require appraisal.

Six-month bond sales and capital loan requirements

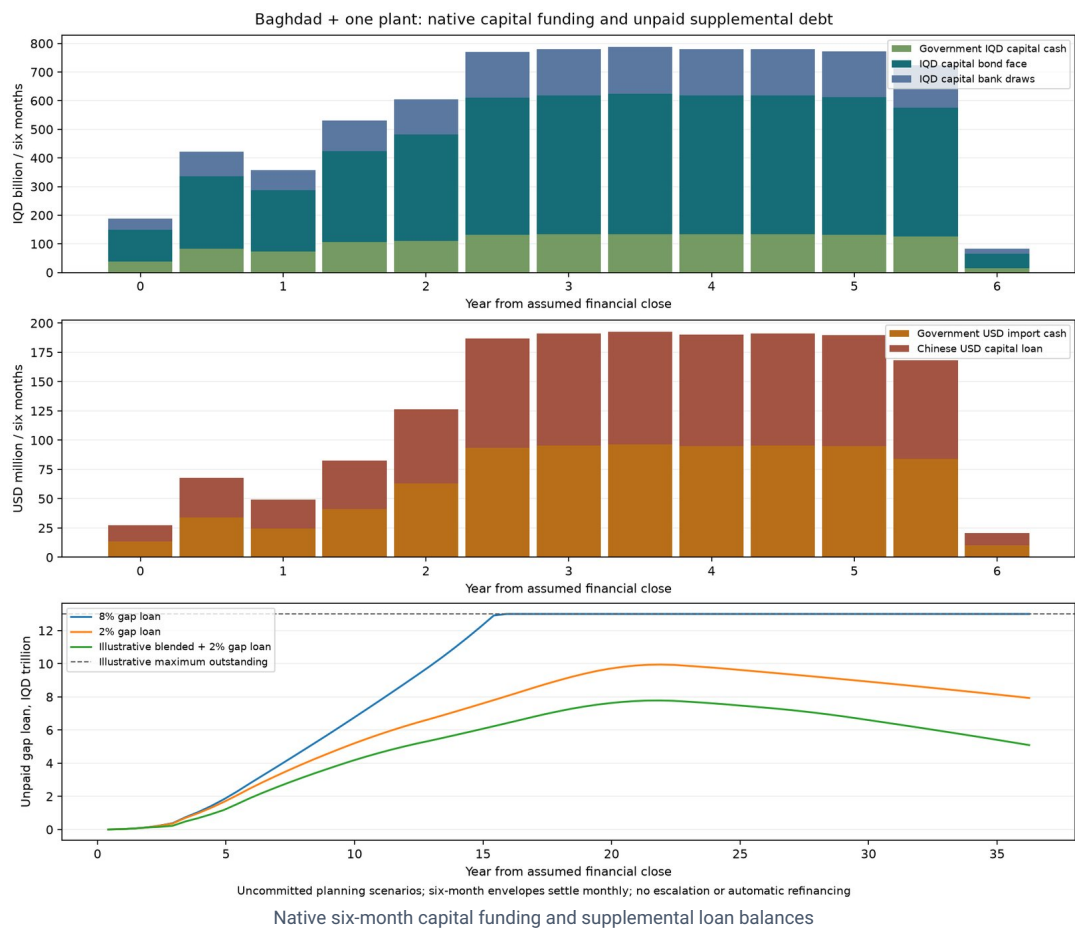

Each half-year is a placement/draw envelope, with monthly settlement against capital milestones. Bonds assume par proceeds and an illustrative IQD 1,000,000 denomination. Face-value requirements below use unrounded values; unit counts in CSV round upwards and separately disclose the resulting indicative face amount. Sale discounts, issuance fees and investor capacity need actual bookbuilding. Selling every half-year amount upfront changes interest/carry and grace clocks and is not simulated here.

The government USD cash and Chinese USD loan are separate; government local cash, bonds, bank draws and uncovered liquidity are native IQD. Chinese facility commitment fees retain the existing annual procurement-cohort assumption; six-month envelopes do not assert a new signing schedule. Grace starts on each actual monthly settlement. First/last repayments for a half-year series therefore differ by draw date.

Tranche	Months from close	Government USD m	Government IQD bn	Chinese loan USD m	Bond face IQD bn	Bank loan IQD bn	Additional cash need IQD bn
BGD-H001	0–5	13.66	37.91	13.66	111.93	37.31	5.20
BGD-H002	6–11	33.85	83.24	33.85	253.29	84.43	18.17
BGD-H003	12–17	24.72	73.41	24.72	213.37	71.12	36.96
BGD-H004	18–23	41.27	105.74	41.27	318.38	106.13	60.14
BGD-H005	24–29	63.11	110.25	63.11	371.12	123.71	104.09
BGD-H006	30–35	93.45	131.93	93.45	479.07	159.69	126.01
BGD-H007	36–41	95.67	132.94	95.67	485.69	161.90	334.76
BGD-H008	42–47	96.39	134.48	96.39	490.54	163.51	275.72
BGD-H009	48–53	95.10	132.99	95.10	484.68	161.56	310.25
BGD-H010	54–59	95.57	133.12	95.57	485.88	161.96	341.65
BGD-H011	60–65	94.87	131.37	94.87	480.60	160.20	368.52
BGD-H012	66–71	84.17	126.31	84.17	448.33	149.44	383.60
BGD-H013	72–77	10.35	13.88	10.35	51.41	17.14	353.06
Total capital envelopes	—	842.17	1347.58	842.17	4674.29	1558.10	—

Displayed two-decimal values can differ from full-precision totals by rounding. The six-month CSVs continue through the entire operating/repayment horizon, including periods with no new capital but interest, principal, liquidity draws, reserve movements and cash sweeps. Every tranche independently reconciles its capital sources and uses.

Financing routes to investigate in Iraq

Route	What it can finance	Cashflow treatment and next requirement
IQD green bonds / green sukuk	Qualified electric transport, solar and charging capital	Replace conventional debt. Define eligible use, segregate proceeds, obtain independent review and report allocation/impact. Sukuk requires an approved asset/usufruct, legal and Sharia structure; the model does not assume a qualified sukuk issue.
GCF / GEF preparation and climate capital support	Climate studies, proven incremental mitigation/adaptation expenditure and eligible capital	Grants reduce debt only when approved; concessional debt still repays. Seek an accredited entity and Iraq NDA support with an emissions/resilience baseline. No grant is booked in the reference.
CBI renewable-energy initiative	Qualifying solar installations under the latest participating-bank rules	Obtain bank confirmation of borrower/project eligibility, current caps and terms. This existing Iraqi route is not assumed available for the whole metro or booked as a new capital source.
MDB / IFC credit enhancement and IQD syndication	Mobilising Iraqi banks and institutional bond investors	Guarantees improve placement or terms, supply no standalone cash, cost fees and may create sovereign contingent liabilities. Confirm IQD availability, hedge pricing and lender limits.
Station-area joint development and development rights	A contracted contribution towards stations/access or unrestricted net proceeds	Independently value parcels and rights, confirm title and revenue powers, tender transparently, deduct costs and future rent foregone. Early rights proceeds can reduce peak liquidity more than late rents.
Parking/congestion proceeds, employer transport subscriptions and business improvement charges	Incremental local recurring cash after authorised net collection costs	Separate each revenue stream from existing fare/nonfare receipts; validate legal powers, demand, affordability, exemptions and enforcement. No unverified tax power is assumed.
Solar/BESS project company, energy-service or availability contracts	Private financing of an accepted energy package	Remove transferred CAPEX and related city debt once; add the PPA/lease/service payments and guarantees. Compare their NPV with existing electricity/OPEX to avoid a free-CAPEX saving. No assumed saving is booked here.
Manufacturer / tooling leases and supplier finance	Qualified equipment and assembly capacity	Deferred invoices or leases are debt-like obligations with priced future payments. Do not duplicate Chinese invoice credit. Factory customer receipts and actual margins need a consolidated business case.
Diaspora and institutional IQD issues	Local capital subscription within the bond programme	These are purchaser channels for existing bond face, not another capital source. Disclose investor FX risk, maturity and redemption; no automatic rollover or compulsory pension purchase.
Carbon / results-based climate receipts	Verified additional emission reductions after delivery	Treat as contingent upside until methodology, monitoring, ownership and an offtake are contracted; no carbon revenue in the reference or blended case.

Priority: first align civil spending and production with accepted openings, then seek eligible cheaper/longer capital financing and contractual early rights proceeds. Obtain a funded recurring-revenue plan before borrowing a multi-trillion-dinar gap facility. Green finance and creative structures do not cure an unfunded timing mismatch or unsupported demand on their own.

Primary evidence checked 3 October 2026

The [GCF Iraq country profile](#) lists two projects with USD 49.5m total GCF finance and USD 5.2m approved readiness support when checked; these are existing country programmes, not Baghdad rail allocations. The [Iraq country programme](#) provides national priorities. An additional USD 25m application target is therefore a sensitivity requiring a new proposal, not money already available.

[GCF investment framework](#) and [financial instruments](#) support the grant/concessional/guarantee concepts and require viable revenue-generating activities for loans. [ICMA Green Bond Principles](#) require a transparent use-of-proceeds process, allocation controls and impact reporting; they do not promise a reduced coupon.

The [CBI renewable-energy amendment of April 2025](#) establishes a local financing route to investigate for eligible energy packages. Its limits and bank eligibility cannot be extrapolated into a multi-trillion-dinar metro facility. [IsDB green/sustainability sukuk guidance](#) supplies a structuring reference, not a Baghdad issuance mandate.

[World Bank guarantee programme](#) supports foreign/local-currency obligations subject to project and sovereign approvals. [IFC local-currency syndications](#) explains domestic parallel loans and hedge structures; it does not establish an IQD loan offer for OSR. [IFC Iraq investment activity](#) establishes an existing country presence, not project eligibility or earmarked money.

[World Bank land-value-capture guidance](#) and [innovative revenues](#) provide structuring examples, not Iraq borrowing/tax authority or a Baghdad parcel valuation.

[World Bank integrated-fare guidance](#) supports examining peak/off-peak, transfer and integrated ticket structures. Its [Bogotá affordability study](#) illustrates the need for household-specific demand evidence; neither calibrates the -0.30 sensitivity for Baghdad or endorses a 5% annual increase.

Remaining modelling and term-sheet limits

- Six-month bond placement envelopes settle monthly at par; they are not advance-funded bond sales. Advance issuance changes carry, reserve and interest costs and needs a separate cash forecast.
- Full unrounded placement values reconcile; illustrative IQD 1 million unit counts round upwards and are not executable orders. No auction price, investor demand or mandate is established.
- A green label alone uses unchanged domestic pricing. The lower coupon/longer tenor and 0.5% annual guarantee fee are explicit sensitivities, not donor or lender terms.
- Climate capital grants replace domestic capital borrowing only, against candidate local expenditure. They do not pay old debt interest, imported invoices already funded 50:50, or increase government cash above 25%.
- Incremental land/rights/local receipts are zero in the reference and must be genuinely additional to existing fare, retail, rent and advertising forecasts. Net proceeds after costs, title, statutory powers and independent valuation require qualification.
- The supplemental IQD facility pays its own interest and origination fees. Surplus is swept to repayment; terminal balances are exposed rather than assumed refinanced or forgiven.
- The illustrative IQD facility has a 13 trillion maximum outstanding commitment; residual cash requirements beyond that cap remain explicitly uncovered. No committed lender or future market capacity is assumed.
- Supplemental facilities have no extra DSRA or undrawn commitment fee and no fixed amortisation before the terminal maturity; term sheets can materially increase costs. Long draw availability and the terminal balloon are uncommitted assumptions.
- City/plant cash is pooled subject to legally permitted transfers and creditor consent. Factory income/OPEX remain outside the capital-only plant appraisal; no free factory profit is credited.
- All non-Chinese debt is modelled in IQD. Foreign-funded concessional programmes need confirmed IQD on-lending or a priced hedge; an unhedged USD development loan would change the currency strategy.
- The reference has constant nominal fares, OPEX and FX. Dedicated pricing cases explicitly index fares, OPEX and income independently from financial close. Capital escalation, FX inflation pass-through and separate lifecycle replacement inflation remain outside this sensitivity; full nominal appraisal must include them.
- Pricing cases retain fixed nominal core and gap debt terms; supplier terms, floating rates and imported OPEX exposure need qualification. New net revenue targets are held nominal rather than assumed inflation-protected.
- Price elasticity is an uncalibrated response to fare relative to indexed income; no transfer, peak switching or low-income household demand survey is modelled. Off-peak trip increases are bounded by the same practical capacity, not new physical capacity.
- Early repayment is a contractual sensitivity, not an exercised call right. Bank/Chinese loan eligibility, bond call or voluntary buyback rights, notice, price and premiums require actual terms. The noncallable case forbids all early bond principal. Illustrative minimum draw ages are 6 months for bank credit, 12 for Chinese credit and 24 for bonds; these are not actual covenants.
- Cost priority is a coupon/guarantee-fee heuristic, not a globally optimal treasury strategy. Premiums, tax, remaining maturities, future draws and FX can change the best order; no refinancing or capital-issue cancellation is modelled.
- A three-month OPEX buffer is funded before discretionary repayment in every early-policy comparison. It is retained at the terminal horizon and earns no income. Original baseline cases have no such additional buffer; savings are compared with a buffered gap-only case as well as the original.

[Editable options](#) · [existing capital assumptions](#) · [original city appraisal](#) · [Baghdad-only programme](#)

Baghdad financing redesign – 2026-10-04

Source: cities/catalogue/west-asia/Iraq/Baghdad/engineering/financing-redesign/README.md

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

Twelve executable alternatives use 9 lines, 474.1797 km, 164 stations and 762 six-car trains. Financial close, title, investor equity, insurance eligibility and physical acceptance remain unestablished. The [existing baseline](#) remains the planning reference. Conditional full-line openings are 40, 45, 50, 55, 59, 65, 69, 74, 76 months; the [independently operable first section](#) is a separately costed sensitivity, not silently added to these full-network cases.

Results and what they mean

Case	Peak aggregate IQD liquidity tn	Cumulative missing IQD funding tn	Terminal IQD gap debt tn	Lifetime interest/fees USD bn eq	Consolidated resource NPV USD bn eq
reference	4.371	0.000	0.000	4.906	n/a
opening_linked_debt	3.863	0.000	0.000	6.421	n/a
development_rights_1bn	2.352	0.000	0.000	4.947	n/a
insured_15year_debt	4.809	0.000	0.000	6.690	n/a
integrated	7.929	0.000	2.518	7.281	-2.906
integrated_low_ppa	4.997	0.000	0.075	6.065	-2.906
integrated_high_ppa	8.509	2.550	7.436	8.004	-2.906
integrated_public_availability	3.315	0.000	0.075	5.376	-2.906
integrated_joint_downside	3.400	46.788	3.400	17.621	-6.127
integrated_rental_small	7.929	0.059	2.518	7.297	-2.911
integrated_rental_medium	7.929	0.034	2.518	7.305	-2.886
integrated_rental_medium_downside	7.929	0.297	2.518	7.344	-2.944

Next financing priority: obtain opening-linked IQD terms and independently valued station proceeds, then compare quoted PPA prices against continued ownership. The integrated high-PPA structure shifts substantial cash to the energy company while rail remains short; private equity needs an acceptable return as well as debt repayment. The tested property margin improves resource NPV before land cost, but the assumed in-kind land cost more than offsets that improvement. None of these scenarios establishes financial feasibility.

[Summary with exact figures and appraisal definitions](#); every case has a complete JSON model, monthly native-currency CSVs, six-month placements and contractual loan-vintage dates. Missing funding must be filled before any reported conditional repayment date is credible. Independently funded entities cannot use another company's cash without a separately approved agreement. Liquidity caps are allocated once: 65% rail, 10% energy, 5% factory and 20% development. The sum is IQD 13.0tn reference; the downside divides the existing IQD 4tn cap in the same proportions.

Integrated borrower	Capital uses USD m eq	Private equity IQD bn	Peak gap IQD tn	Missing funding IQD tn	Terminal gap IQD tn
rail	6421.167	0.000	7.870	0.000	2.443
energy	747.367	194.315	0.017	0.000	0.000
factory	346.545	90.102	0.302	0.000	0.075
development	3400.000	1105.000	0.368	0.000	0.000

These are pre-tax sensitivities. Corporate tax, duties, VAT, sponsor equity hurdle rates, dividend restrictions, lender DSCR and termination liabilities need quoted/legal terms. Surplus is swept after monthly OPEX, scheduled debt service, reserve funding and the existing lock-ins/premiums. A positive cash balance or an annuity model does not establish bankability. The factory has no assumed national orders or residual asset sale.

Opening-linked credit and insured green instruments

Bank amortisation becomes 240 months and ordinary bonds 216 months at the unchanged 9%/8% reference rates. Monthly draw cohorts use the latest opening of the assets included in that cohort; shared contracts use full opening. This conservative aggregation needs actual line-linked facility documents. Interest is paid throughout grace, funded by the separate IQD liquidity account if cash is insufficient; no interest is silently forgiven or capitalised. Arrangement/commitment charges, buffer and surplus rights remain priced. Chinese USD loan terms remain unchanged.

Loan-vintage and six-month CSVs show actual draw, first principal and final contractual principal dates. Cheaper/longer debt changes liquidity and finance cost, while core unlevered NPV stays USD -3.262bn. Core excludes grant, development rights

and new net receipt targets.

[ICIEC's official product](#) describes sovereign/sub-sovereign sukuk with coverage up to 15 years. The tested insured instrument has grace plus amortisation capped at 180 months from each draw, replacing the previous 48+240-month assumption in that sensitivity. A 6% coupon, 0.75% annual insurance and 1% annual IQD conversion/on-lending cost are assumptions, not insurer pricing or proof that an IQD issue is eligible. No climate grant is booked in insured/integrated cases. Obtain written eligibility, binding terms and a priced local-currency route before using an institution's name in funding commitments.

Station-area partnership and public land

[15 station candidates](#) are selected only by network archetypes, with actual station IDs/coordinates. Parcel title, legal ownership, survey area, encumbrances, independent values, displacement and developer interest are null/unverified. No selection is a claimed commercial valuation. First investigate 10–20 sites through independent market/title/safeguards work and competitive long leases or voluntary pooling.

USD 1bn total net development-rights replaces USD 300m; the increase is USD 700m. Six equal tranches begin month 24, every six months. Receipts are IQD using the model's 1,300 IQD/USD reference; they are not USD debt or dollar-indexed obligations. In the integrated sensitivity developers finance both rights and buildings. The hypothesis is 1.2m m² land, FAR 2.5, 3m m² buildings at USD 800/m², USD 4.2bn sales in months 60–96 and 5% sales costs. There is no rent revenue additionally booked against sold floor space. Public land's assumed USD 600m opportunity cost is an in-kind exposure, never spendable cash. All prices are unverified and require an Iraqi valuation/tax review. The downside halves rights, reduces sales 30%, delays both 24 months and escalates construction.

Rights payments are a developer use and a rail receipt. They cancel in consolidated appraisal; they cannot also be counted as programme profit. Developer equity is 25% of its rights/build uses, and its borrowing is IQD bank credit. Property debt/transaction costs and missing funding are included in its own ledger. [World Bank land-value guidance](#) and [MTR's model](#) provide precedents, not Baghdad valuations.

Energy and manufacturing contracts

Dedicated solar capital is transferred once, without inventing an additional EPC removal. Charging/microgrid equipment and its existing EPC remain rail assets. The railway pays a PPA of IQD 104/kWh, indexed 5% annually; the annual planning purchase is 1.779bn kWh, USD 142.325m equivalent at reference prices. Dispatch/load follows open-line weights, not fare demand. Energy receives exactly what rail pays. Existing solar maintenance transfers once; a further 0.5% of solar capital/year is an explicit renewal-spending sensitivity. Timetable-derived annual generation is not 8760-hour dispatch proof: grid backup, curtailment, storage adequacy and metered purchases require qualification. Export sales are zero, with no signed buyer. Low/high PPA cases redistribute company cash and leave the consolidated resource NPV unchanged. [World Bank PPA guidance](#) explains the contractual financing route.

Energy and factory each test 20% private IQD equity. Government remains 25% of original physical rail/energy/factory capital. The factory receives Baghdad's existing train invoices and pays the same resource budgets one month earlier, exposing working capital. Original train prices already include manufacturing labour, QA, ordinary overhead and warranty; 1,044 production staff wages are not added again. An additional USD 250,000-equivalent capacity fee per train, annually indexed and paid in IQD, is a separately visible investor-return sensitivity. It cancels on consolidation but increases rail's operating obligations. Warranty cash is locked at 5% of cumulative train payments until 12 months after the final invoice, then released; it is cash restriction, not a duplicate warranty expense. Fifteen caretaker staff and 0.25% plant carrying cost are added during that tail. Plant costs, working-capital funding, interest and outstanding debt at backlog close remain visible in [integrated.json](#). New orders and salvage are zero until contractual.

At the illustrative capacity fee, factory cash remaining at contract/warranty close is USD 0.000m against USD 69.309m invested equity. The 15% equity-hurdle NPV is USD -60.176m. Debt repayment therefore does not establish an investable factory partnership. Developer equity-hurdle NPV is USD -194.940m. These close-date distribution diagnostics deduct any remaining debt and disclose missing funding; no dividend or sponsor return is assumed to be committed. Competitive pricing, equity terms and a bankable capacity contract require further work.

Appraisal and public exposure

Three retained under-viaduct rental variants add a fifth independently financed entity to the integrated case: small, medium and lower-rent/prolonged-vacancy medium. The [civil-linked register](#), [pilot unit](#), [costs](#), [leases](#) and [hazards](#) have no accepted site/demand evidence. External rent adds revenue; actual collection follows fit-outs, physical line availability, initial rent-free periods, occupancy ramp, arrears/recovery, tenant turnover and lease-end refunds. Fit-out capital, occupied/vacant maintenance/insurance, 12-year refurbishment and a standalone 15% cash-tax proxy are included. No station sale parcel also earns rent; no existing kiosk income is duplicated. Tenant deposits are restricted cash and matching liabilities, never construction finance or revenue.

The rental partner supplies 25% fit-out capital as private IQD equity and the residual is IQD bank capital, with opening-linked principal and 240-month amortisation. It has zero new operating-gap capacity: missing construction interest, fees or reserves remains an explicit funding requirement. The original four borrowers keep their existing allocated caps; combined cap remains 13tn. Rental transfers to rail are zero until an approved agreement exists, so rail cannot silently use the new company's cash. Each borrower exports monthly native ledgers, six-month placements and loan vintages. These ring-fenced structures are alternative to the wholly owned holding rental cases, whose subscriptions replace rather than add partner equity.

Consolidated resource NPV adds collected rent less its OPEX and physical fit-out capital, before financing/tax, to the original resource case. A separately labelled after-rental-tax diagnostic deducts rental tax once; the original four businesses retain their existing before-tax basis. Additional rental-site rights/land opportunity cost is unknown, so the existing station-land subtraction is not a complete new-site appraisal. The 200,000 m² area illustration is blocked as unmapped and supplies no integrated cash.

Core rail/energy/factory unlevered NPV: USD -3.262bn. Rail entity NPV including its PPA, capacity fees and internal rights: USD -3.020bn. Consolidated resource NPV including property sales/building costs and additional renewals/caretaking: USD -2.906bn; including land opportunity cost: USD -3.372bn. Debt/equity/grants are financing transfers and excluded from resource NPV; intercompany transfers cancel to the cent. Nominal discount is 13.4%, combining 8% real and 5% general inflation.

Government original-capital cash is USD 1.879bn equivalent (25%). Its USD import cash is USD 842.170m and Chinese USD credit is USD 842.170m, splitting imports 50:50. All other debt, private equity, property payments, fares and subsidy payments are IQD. Original programme USD capital intensity therefore remains 22.41%; SPV transfers do not remove those USD import requirements. Property construction is assumed contracted in IQD; actual imported content/FX exposure needs quotes.

Public cash capital PV is USD 1.234bn; in-kind land PV USD 0.467bn. The optional availability case pays USD 100m equivalent/year at full opening, indexed 5% and phased by available lines; its PV is USD 0.804bn. It sits outside the 25% capital limit and needs appropriation, service performance terms and affordability review. Recipient NPV adds public cash explicitly; the public-plus-private resource appraisal cancels that transfer. Contingent bond/guarantee/termination exposures remain unquantified rather than assumed zero. [World Bank public-support guidance](#) describes these obligations.

Existing fares and kiosk/advertising receipts are retained with their original demand/price/OPEX indices. Integrated cases omit the old USD 25m grant and USD 25m/year new-net-income targets. Fibre, naming rights, parking and employer contracts require incremental net quotes; prepaid fares change timing of existing receipts and do not create revenue twice. At 13.4%, USD 50m/year for 20 end-of-year payments has PV USD 342.962m at the beginning of the payment period, lower when discounted back to close.

Iraqi financing routes and 90-day evidence programme

The [World Bank's USD 930m national railway project](#) is a separate Umm Qasr–Mosul programme through Baghdad, not metro money. IFC's [September 2025 Iraqi announcement](#) combines investments and engagements across industrial/property/financial partnerships, not an available USD 1bn fund for this proposal. ICIEC's [2025 impact report](#) records reinsurance for Iraqi substations; it does not commit rail credit. Sources checked 3 October 2026. [GCF's published Iraq country programme](#) and [transport programme](#) establish potential application routes, not an award. Climate funding requires emissions baselines, eligibility, accredited-entity engagement and actual terms; no grant is presumed.

[Six workstreams](#) cover lender terms, land/valuation, PPA, standalone factory, existing independently operable phase, and independent model/public-affordability review. Due days are relative to an actual approved start. Named people, legal opinions, quotes and accepted evidence remain pending. [ERPNext Task JSON](#) is a draft native-import package with stable evidence subjects, not live IDs or accepted evidence. Local deployments record actual IDs privately and preserve assignments/status when refreshing descriptions. No external lender/developer contact, issuance or expenditure is authorised by these model files.

Later construction commitments require executable native-currency funding, separately accepted physical evidence and a conservative demand case. Integrated joint downside retains the existing 55/106-month physical stress and adds weaker property conditions: missing funding is IQD 46.788tn, terminal gap debt IQD 3.400tn. The proposed structure is a market-test programme, not a claim that the financing gap is solved.

Regenerate with `.venv/bin/python tools/automation/baghdad_financing_redesign.py`; validate exact inputs/outputs with `--check`. No new financial commitments or physical release are implied.

Baghdad programme recalculation

Source: cities/catalogue/west-asia/iraq/baghdad/engineering/programme-recalculation/README.md

Controlled planning basis, 2026-10-04; unquoted and uncommitted. This is the latest staffing/depot/local-production review. Existing cost and financing cases remain historical comparators; no survey, manufacturing qualification or lender commitment is created.

Operating people and wages

The 164 stations require two concurrent staff during two normal eight-hour shifts: 656 daily shift assignments, not a headcount of people working every day. Retaining 20.5 service hours also requires 4.5 hours of separately funded late cover per station. Weekly cover, leave, training, sickness and handovers give 1620 station-cover FTE, within 3430 permanent operating FTE. Full-operation loaded payroll is IQD 80.292bn/year (USD 61.763m equivalent), indexed thereafter with OPEX.

The employee median is IQD 614,000 from the 2021 Labour Force Survey, cited in the [IMF 2023 report](#). Applying an assumed 5% annual index to 2026 gives IQD 783,637; the general-worker floor is IQD 1,175,455/month, 50% higher. Technical, supervisor, senior and director roles use 2.25/3/4/5 times that indexed proxy. This is a historical observation plus an editable index, not a measured current national median. Employer costs and overtime are priced separately. [Roles](#) and [recruitment/cohorts](#) retain appointment and competence gates.

[ERP planning drafts](#) map the revised Staffing Plan, depot Project/Asset budgets and factory Workstations to native business records; they create no Employee, appointment, transaction or approval.

Construction workers, factory production/support workers and permanent operators are separate populations. [Construction](#) applies explicit trade-crew allowances to actual work-package resource lanes/dates, counting overlapping use of the same lane once; its peak is 445 FTE. It is not a measured complete contractor crew schedule; revised depot and upstream factory construction crews still require their own work-package schedules. Construction labour is already inside contract rates; its unknown payroll-content overlap remains unpriced, preventing a duplicate charge. A separate wage-content stress increases assumed labour content (20% of affected contracts) by 50%, with incremental EPC once; it is an overlap sensitivity, not proof of contractor wage contents. Existing assembly wages are replaced using an explicitly assumed embedded payroll credit; component process labour is inside component unit prices. Paid production capacity above those productive hours is added separately, never charged twice.

The final-assembly establishment is 1273 production FTE plus 191 support FTE. The scheduled order requires 55 paid months from month 18 through month 72; payroll follows this calendar, rather than dividing the order by a theoretical steady-state rate and losing ramp-up/idle months. Each upstream plant also funds its whole production establishment for that period, with the productive labour already in unit prices deducted once. These jobs are additional to permanent railway operations; no national order or permanent post-order subsidy is assumed.

One depot per line, full-size trains and fleet

There are 9 line-local depots, providing 762 storage slots for all six-car revenue/spare/reserve trains. Slots use the actual 111 m train plus 10 m clearance. Workshop bays follow annual bay-hour demand and usable bay capacity; parking slots are not maintenance bays. Station storage is an option without any capacity credit in this case. Full overnight-to-morning launch and throat conflicts remain unvalidated.

Line	Trainsets/storage slots	Tracks	Workshop bays	Land envelope ha	Reference USD m
line-1	86	29	12	11.50	27.045
line-2	101	34	14	13.37	37.338
line-3	97	33	14	13.05	30.553
line-4	80	27	11	10.72	25.276
line-5	86	29	12	11.50	27.045
line-6	100	34	14	13.37	30.808
line-7	79	27	11	10.72	25.246
line-8	90	30	13	11.94	28.589
line-9	43	15	6	6.20	15.891

Total depot reference: USD 247.790m, replacing the original USD 8m exactly once. Storage, workshop and access tracks, points, drainage/access, workshop shell/equipment/services, yard lighting/fire services, wash plant, wheel lathe, offices/stores and rescue/quarantine are visible. Access-track length is an editable allowance, not a connected site alignment. Existing depot PV/BESS is retained once. Land/title, utility relocation, actual soil/foundations, installed charger/grid upgrades and tax/duties remain unpriced. [Item register](#).

Core elevated stations

The reworked core has 95 station platforms with raised-structure/access scope. The register replaces their catalogue allowance with a separately stated elevated reference, adding USD 241.910m direct, with incremental EPC and operating maintenance once. Elevated interchange allowances are already present where catalogued; they receive no duplicate uplift. Other core stations use a 30% structure allowance plus USD 1m for vertical access. These are unquoted allowances, not released multi-level junction or station designs. [Core station register](#).

Iraqi component manufacture

Product	Network quantity	Required units/year	Cells	Production/support FTE	Factory capital USD m	Unit make/buy USD	Whole-order margin USD m
bogie	9144	2690	31	145/22	43.487	15156/25000	35.296
motor-inverter-set	9144	2690	21	74/12	29.965	11078/15000	-0.911
battery-225kwh-pack	4572	1345	8	38/6	25.577	29828/45000	39.071
door-cassette	18288	5379	13	46/7	15.964	2023/3333	3.996
window-cassette	27432	8069	10	35/6	23.658	687/1111	-16.477

[Make/buy inputs](#) price imported process machinery, Iraqi buildings/site work, qualification, residual imported inputs, local materials, graded labour, process overhead, fixed support and plant maintenance. Cells are sized to the existing train factory's required production rate, not a small demonstration line. The order is 1.029 GWh of gross onboard packs. Battery pack assembly is evaluated; imported cells/BMS remain. Bogie wheels/axles/bearings, motor inverters/magnets, door safety electronics and glazing feedstock also retain imports. Local manufacture does not mean zero USD input.

The buy case itemises these five imported completed products; the old blanket vehicle import percentage is retained only for other parent scope. This prevents replacing already-local scope with a second import credit. The all-product and positive-margin selections are separate unquoted cases. Whole-order margins are before finance/tax/risk; vendor prices, license, QA, process yield, supply commitments and first articles must validate them. No future national order pays Baghdad debt or makes an uneconomic line look profitable. Serial component qualification is assumed within the 18-month readiness target, not proven. A six-month supplier delay shifts rolling-stock invoices and opening/service cash, extends the full operating horizon and prices idle production payroll. A 25% raw-input price stress preserves the same selected facilities. Rejected/reworked product still needs a measured production replay. Existing final assembly tooling remains priced; upstream machinery is added without an unproven overlap credit.

More elevation and fewer bends

The current main design adopts the straight central elevated alignment. The screening policy allows up to 65% elevated and at least 25% at grade, subject to site/design acceptance. Baghdad currently has 54.86% elevated. Investigation windows around all 16 exceptional segments add 7.015 km of candidate at-grade conversion, reaching 56.34%; overlapping intervals are merged and existing viaduct/bridge lengths excluded. Approach length is at least 300.0 m from assumed height/gradient.

Elevation alone removes no horizontal bend. Wider-radius geometry, station moves, ROW, vertical alignment, ramps, egress, ground/utility evidence, crossings and whole-life costs must be designed together. The finance cases separately test no routing-penalty removal and hypothetical 25%/50% removal; these percentages are unverified counterfactuals, not achieved savings. The added standard civil allowance uses the conservative simple-span bearing index. [Candidate intervals](#).

Funding and mezzanine comparison

Government capital remains exactly 25% of the scenario total. Imported invoices receive 50% government USD cash / 50% Chinese USD credit. Remaining government cash, bonds, senior bank/gap credit and mezzanine are IQD. Government USD payment dates follow machinery/input invoices; the remaining appropriation is allocated proportionally to local invoices, so a machinery-heavy month need not be falsely limited to 25% government cash. Chinese supplier origin and export-credit eligibility are assumptions requiring vendor/lender confirmation. China Exim describes buyer credit for Chinese products, technologies and services; machinery eligibility is not a loan commitment ([official product description](#)).

The positive-margin local-production senior case's capital-only sources are shown below. They sum to its capital uses; gap credit, interest/fees, reserve funding and operating receipts are additional cashflows in its [monthly ledger](#) and [six-month placement schedule](#). Ordinary and green bonds are separate placements, never added again to a combined bond figure. Bond face units are IQD 1m; rounded placement envelopes are not additional cash raised.

Capital source	Currency	Native amount	USD equivalent m
Government import cash	USD	970,909,383	970.909
Government local cash	IQD	1,384,956,400,257	1065.351
Chinese capital credit	USD	970,909,383	970.909

Capital source	Currency	Native amount	USD equivalent m
Ordinary capital bonds	IQD	3,944,816,429,415	3034.474
Green capital bonds	IQD	1,040,233,767,709	800.180
Senior bank capital credit	IQD	1,661,683,399,041	1278.218
Conditional climate capital grant	IQD	32,500,000,000	25.000

Mezzanine replaces 10% of domestic residual capital borrowing; it is not extra capital on top of the uses. The IQD case has 6% cash coupon, 4% PIK, 2% arrangement fee and a 15-year balloon from each draw. Deferred cash coupon and PIK increase outstanding debt until maturity. Thereafter the overdue principal is retained with separately disclosed simple 10% contractual-interest sensitivity; arrears are not compounded and the balloon is not silently extended. Cash junior payments require senior DSCR of 1.20, funded reserves and actual residual cash; new gap draws/unfunded support cannot pay junior debt. No conversion, fresh equity or automatic refinancing is invented. Unpaid maturity balances/defaults remain visible. Mezzanine is structurally junior to senior debt and senior to equity, as described by [UNCITRAL](#); the rates here are project sensitivities.

Matched case / six-month placement schedule	CAPEX USD bn	USD capital intensity	Peak IQD gap tn	Terminal all debt IQD tn	Unfunded IQD tn	Junior defaulted vintages
revised_scope_buy	8.250	26.71%	12.614	10.200	0.000	0
local_all	8.152	23.05%	12.424	10.018	0.000	0
local_positive	8.145	23.84%	12.399	9.966	0.000	0
local_positive_mezzanine	8.145	23.84%	11.758	15.906	0.000	79
local_positive_commercial_gap	8.145	23.84%	13.000	13.000	19.487	0
local_positive_mezzanine_stress	8.145	23.84%	13.000	40.960	17.741	79
grade-separation-penalty-0pct	8.202	23.77%	12.525	10.131	0.000	0
grade-separation-penalty-25pct	8.087	23.91%	12.270	9.799	0.000	0
grade-separation-penalty-50pct	7.972	24.05%	12.016	9.467	0.000	0
local_positive_raw_price_stress	8.218	24.19%	12.537	10.157	0.000	0
local_positive_supplier_delay	8.145	23.84%	12.527	9.942	0.000	0
construction_wage_content_stress	8.702	23.30%	13.000	10.744	0.603	0

The 3 positive-margin process options reduce capital from USD 8.250bn to USD 8.145bn, and imported invoice exposure from USD 2.204bn to USD 1.942bn. Half of that exposure is government USD cash and half Chinese USD credit; all other capital funding is IQD. The historical 148 km / USD 18bn third-party benchmark has a different scope and assumed full foreign-currency financing; this is a planning comparison, not a like-for-like tender saving. The reworked 474.2 km network's 38.9% population-access proxy is not surveyed pedestrian coverage.

Current financial conclusion: the positive-margin senior case records IQD 0.000tn of residual unsourced support after assumed facilities and retains IQD 9.966tn of debt at the horizon. Its company NPV before finance is USD -4.678bn at the assumed nominal discount rate. Adding mezzanine does not change the underlying operating return: it leaves IQD 15.906tn of total debt and 79 unpaid junior vintages. It is not recommended as a cure for the funding deficit. Fare and OPEX indexation, kiosks/advertising and inherited additional receipts are already included; new verified capital, affordable revenue or accepted scope savings are still needed.

All cases use the same revised staff, depot and indexed fare/OPEX assumptions. Six months of scheduled senior service are reserved from the first draw; three months of OPEX plus explicit industrial working capital are restricted. This revised reserve policy differs from older reference cases, so compare matched cases in this table when judging mezzanine. Concessional 2% gap funding, grants/rights/additional income and enhanced green coupons are uncommitted; the 8% gap and high mezzanine-rate case expose that dependence. There are zero dividends. Cash/principal/PIK identities, maturity risk, monthly draws and six-month bond denominations are retained for every case.

Regenerate with `.venv/bin/python tools/automation/baghdad_programme_recalculation.py`; verify with `--check`. Complete installed scope, construction wage-content adjustment, local-pay survey, validated demand/timetable and supplier/lender agreements remain open.

Baghdad qualification, funding gates and first operating section

Source: cities/catalogue/west-asia/Iraq/Baghdad/engineering/qualification/README.md

This package turns the review findings into executable draft work. It supplies no physical acceptance, supplier quotation, named owner assignment or financing commitment. The full 762-train Baghdad baseline uses the current generated route and opening schedule.

Temporary first-article industrial package

[Site block layout](#), [quantities and reconciliation](#), and [RFQ schedule](#) specify six prototype cells, 4,960.0 m² process floor, 6,696.0 m² total covered floor and 16,740.0 m² fenced-site allowance. The metric 180 x 93 m envelope is a reference arrangement, not a selected or surveyed site. Access/fire widths, hazardous materials, drainage, foundations, heavy-haul route, crane coverage and utilities require detailed vendor/civil drawings. No production acceptance paths are counted at this temporary site.

The quantity-based direct subtotal is USD 19.873m; contingency USD 3.975m; allocated total USD 23.848m. USD 11.152m remains unallocated within the existing USD 35m allowance. EPC remains USD 2.45m. Nothing in this package is added a second time to the USD 37.45m recovery case. Rates are editable assumptions, not received quotations or realised savings.

Vendor interfaces: bogie/body datum and lifting reactions; composite mould temperature/cure traceability and ventilation; door/window fit and tolerance stack; battery transport SOC/fire segregation and HV isolation; electrical test connectors and calibrated instruments; ERP lot/serial traveller and revision interfaces. RFQ returns must identify imported tooling versus Iraqi buildings/labour, actual origin, tax, delivery slots and financed invoice eligibility; the recovery model's 20% tooling/import fraction remains unqualified until these are reconciled.

Transfer sequence: permanently identify TFA-C01 through C06 tooling in the asset register; release the prototype traveller and first-article configuration; move the complete six-car train on certified frames/haulage with clearance and escort approval to permanent acceptance at day 390; retain all temporary tools until prototype acceptance and production continuity are secured; lock out, pack, transfer, reinstall and recalibrate each cell into its named permanent work centre; validate first-off dimensions/HV tests before release. Permanent plant tooling is already fully budgeted: temporary equipment is incremental and any reuse credit needs an approved asset/cost change, never an automatic reduction.

Readiness gates: survey/land and supplier interfaces before procurement; civil/fire/utility/lifting acceptance and calibrated equipment before day-260 assembly; permanent segregated test paths and bays before day-390 dynamic tests; the additional 60 working-day first-article qualification remains fixed; no series release before signed acceptance. Day 260/390 and month-36 first service are conditional dates, with independent ERP evidence tasks below.

Executable evidence work and ERPNext

[Ten source-bound work packages](#) map every delivery qualification row to an accountable role, measurement fields, units, numeric criteria, source content revision, ERPNext Task subject and result template. A named accountable person is deliberately pending rather than fabricated. [Task import JSON](#) and [CSV](#) are drafts; they are not live ERP records or accepted evidence. Reconcile them with the ERP app's `qualification.import_tasks` method; preview is the default. Assign actual users/owners through ERP and preserve assignment when refreshing descriptions.

Populate each BAG-EVID result template using real measurements and raw evidence file checksums. Use `.venv/bin/python tools/automation/baghdad_qualification.py --verify-result RESULT --envelope ENVELOPE --signature SIGNATURE --policy TRUSTED_POLICY`. The verifier rejects null/wrong-unit/out-of-threshold measurements, missing raw files, source changes, absent or unauthorized review and self-review. It reuses the subsystem qualification's externally controlled Ed25519 reviewer policy and envelope (`osr-subsystem-review/1`), with evidence fingerprint = SHA256 of the exact result bytes, configuration fingerprint = package source revision, required role = assessor, acceptance reference and expiry. Trusted reviewer identities/keys must be supplied independently; the generator provides no signing key and no acceptance. An accepted evidence package still does not authorize public operation.

Coverage ratios require item/lot/phase-level underlying files and independent scope review, not an unsupported declaration of 1. Production records must separate elapsed cure clocks and inspection holds from staffed hours. Baseline throughput and the shifted recoveries remain unmeasured. Funding evidence needs the appropriation, actual native-currency term sheets, investor/underwriter placement mandates, collateral/guarantees, maturity/fees, and every six-month sources-and-uses gate, including reserves and interest. Demand work must include a surveyed OD matrix, affordable fare/elasticity tests and net kiosk/advertising concessions after vacancy, collection and management costs.

Denied and interrupted funding

[Funding gate cases](#) and each placement-monthly/six-month CSV distinguish requested source face, available fraction, refused amount, invoices held and undrawn capital capacity reserved for deferred invoices. Recovered domestic placement assumes half the ordinary IQD bond placement fails for months 29–34; all unfinished procurement, civil work, production and running tests pause at working day 600 for 130 working days. Recovered export credit pauses the programme at NTP for 130 working days and requires the refused initial USD credit to be placed before imported procurement restarts. The costed schedules and financing are in the delivery-risk cases `domestic_placement_interrupted_recovered` and `export_credit_delayed_recovered`. A USD 10m equivalent IQD local remobilisation assumption plus 7% EPC is added once, with staff/site carrying costs charged in the six suspension months for the already-mobilised domestic case. An export refusal at proposed NTP shifts the entire unstarted programme without buying another construction/production staffed span; only the quoted-later remobilisation/reservation allowance is added. Cure/inspection restart requirements could cost more and need vendor evidence. Longer delay, storage damage, cancellation penalties, FX changes and lender acceleration/default are outside these recovery prices.

The placement files diagnose the original invoice request. Recovered cashflow files retime actual invoice milestones using the held schedule; they must not be added together. The available-capital column is an undrawn capacity requirement, not received or free operating cash. Recovered cases retain uncommitted liquidity for interest and hold costs; it never replaces the refused core capital. Investor commitment/carry fees on undrawn domestic placement are unquoted and excluded. Partial grants/green placements already in the baseline remain assumed; refusing ordinary bonds does not prove green placements will succeed. Bank refusal can be run with the same gate mechanism. Recovered dates and repayment require renewed placement and restart appropriations, which remain uncommitted. Permanent domestic/export refusal has no operating opening or debt-clearance date. Existing debt is not forgiven; cancellation, default/workout, liquidation proceeds and prior-creditor claims require a separate resolution model and are not represented by zero balances. Government is not automatically increased beyond 25%; the original import split stays 50% government USD / 50% Chinese USD loan; only actual import invoices can qualify. Domestic cash, bonds, bank/green/gap credit remain IQD, while foreign donor receipts would have separately identified FX conversion requirements.

Gate	Currency	Refused amount	Recovery assumed
<code>domestic_half_placement_recovered</code>	IQD	165,159,676,655.48	True
<code>domestic_half_placement_permanent</code>	IQD	1,196,998,024,536.58	False
<code>export_unavailable_recovered</code>	USD	13,655,333.57	True
<code>export_denied_permanent</code>	USD	842,170,426.59	False

Separate independently operable first-section option

[First-section duty, assets and finance](#) takes the actual first five line-1 stations, from the Mahmudiya terminal to line-1-1848-0797-s014034, spanning 14.034 km. This outer corridor is a demonstrator candidate, not a proven best catchment. It needs its own OD/accessibility study and comparison against better central corridors. Existing station/track/wayside tasks alone are pulled forward within the frozen lane/predecessor graph; their already-budgeted capital is retimed, not purchased again. Other route quantities and the 762-train city fleet remain unchanged.

At the reference six-minute headway and 40 km/h average running speed, the round trip is 74.10 minutes including intermediate dwells and ten-minute charging/turnaround at each end. It requires 13 peak + 2 spare + 1 cold reserve = 16 existing six-car trains. Allocated train IDs are in the data file and must all pass acceptance before section operation. A six-minute section service is an explicit early-phase option rather than the ultimate line's three-minute design demand.

Each end needs 2 independent 121 m clear berths for the 111 m train, No.9 crossover/points, a safeguarded 185 m terminal arrangement, 2 x 2,000 kW chargers and 4,000 kW feeder capacity. Dwell plus clearance occupies each berth for 11 minutes against a 12-minute two-berth arrival cycle. These are geometry/utility requirements pending surveyed access, swept path, braking, interlocking and electrical studies; a generic standard station cannot silently serve as the new terminal.

Round-trip traction plus the conservative auxiliary proxy is 587.9 kWh, compared with 600.0 kWh delivered terminal charge at 90% efficiency. Battery definitions are 1,350 kWh nameplate / 1,080 kWh usable from the controlled six-car profile. The conservative section-specific 40% floor is applied to usable energy, leaving 648 kWh; one-leg duty fits that window. Normal charging margin is only 2.05%. A 10% reduction in delivered charging gives -8.15% balance and is not qualified. Roof PV and intermediate charging are excluded. The battery acceptance power, HVAC electrical demand, gradients, ambient heat, degraded charging and rescue case require measured qualification; the small energy margin is not operational robustness.

The [section RFQs](#) provide four incremental packages excluding already-budgeted route, station and fleet equipment. Reuse one original charger per end and add two berth chargers in total, upgrading each end to 4 MW. Independent maintenance/stabling, battery quarantine, lifting, rescue and road access avoid reliance on the distant line-6 depot. The provisional 3.5 ha maintenance site has eight stabling roads of 250 m usable length (two 111 m trains per road plus 28 m clearance) and two 135 x 6.5 m maintenance bays; site rights, turnout ladders, fire/access geometry and measured depot duty

remain open. Turnback/platform adaptation USD 5m, charging/grid USD 8m, maintenance/access USD 12m and controls/acceptance USD 3m give USD 29.96m including EPC, assuming 20% imported direct scope pending RFQs. The section has its own reference 200 operating FTE and USD 10.486m/year OPEX before indexation, replacing the whole-network fixed OPEX before month 41. It covers 16 hours/day over 330 days/year, USD 0.10/kWh grid electricity with no PV generation credit, Iraqi wage proxies, proportional existing civil/solar/signalling maintenance and train maintenance including the existing battery reserve, plus 2% maintenance on additional support assets. These cost/demand/utility assumptions need quotations and surveys. Separately, sixty temporary construction/qualification support FTE are indexed and charged from support readiness until the full line opens, then integrated into the baseline allowance; they are not counted as section operating staff. Civil/support acceptance at day 560 is an additional unqualified support-package assumption, not an existing accepted site.

The first 16 accepted trains finish at day 676; selected civil at day 652; independent support at day 560. The resulting conditional section opening is month 36, including the same three-month commissioning allowance; complete line opening stays month 40. No passengers or fares occur before that opening. Section paid demand is only half the smaller of fleet-capacity and route-length allocation proxies, weight 0.010499, deducted from later full-line demand to avoid double counting. This is a scenario, not population coverage evidence. Opening acceptance must cover section-specific turnbacks/chargers/depot, full allocated section fleet, isolation from works, evacuation/rescue, software configuration, hazards and independently signed operator/authority release; the full-line BAG-EVID-009 remains separate.

[Monthly finance](#), [six-month tranches](#) and [incremental cost ledger](#) include early baseline invoice timing, new support capital, indexed support payroll, fares/nonfare ramp, fixed/variable OPEX, reserves, native debt and prepayments. Peak gap debt is IQD 4.460tn; clearance month 304. Its unlevered NPV is USD -3.305bn. Compare against the current baseline IQD 4.371tn peak / month 303 clearance / USD -3.262bn NPV. At the conservative demand proxy, mature section receipts are only USD 4.658m/year versus its USD 10.486m OPEX before indexing/ramp: it is not independently self-financing. Earlier service requires an explicit operating bridge; the extra facilities and advanced invoices must be justified by measured access benefits, demand or lower costs.

Financial feasibility and funding evidence

The baseline remains conditionally financeable under uncommitted cheap IQD gap credit and green/rights/receipt assumptions. Its unlevered financial NPV is USD -3.262bn at 13.4% nominal (8% real plus 5% inflation), before additional grant/rights/receipt targets. Clearing debt through later nominal fare growth is not the same as positive discounted investment value. [Feasibility data](#) supplies an illustrative annual external-benefit threshold of USD 405.9m in reference prices, phased with baseline openings and indexed 5%, whose discounted value would offset that financial deficit. This is not a completed economic appraisal: economic CBA must remove fares/taxes/financing transfers, use shadow resource costs, count time/safety/emissions benefits without double counting, and assess displacement/opportunity cost of labour rather than call every wage a net benefit.

Additional funding routes to investigate are competitively leased station land/development rights, employer travel contracts, advertising/kiosk concessions, utility/telecom corridor leases, climate grant/guarantee applications, and Iraqi institutional or retail IQD placements. Their net contract proceeds, authority, collection costs, timing and senior-creditor covenants are required before cash enters the ledger; a loan/guarantee is financing, not new operating revenue. The existing USD 300m net rights and USD 25m/year additional net receipts are targets, not a valuation or signed concession, and must not be added again as these same mechanisms. Replicable land value capture depends on land rights, planning powers and market demand ([World Bank financing guidance](#)). Iraq's [GCF country programme](#) establishes a project-development framework, not a Baghdad rail award or a 2% IQD facility. No fund application, lender term sheet or placement was obtained in this work.

Compare liquidity, repayment and discounted value separately

[Financial comparison data](#) uses each case's actual capital and indexed operating ledger, excluding debt and new grant/rights/receipt targets from unlevered NPV. All dates require physical acceptance and financing availability.

Case	First/full month	Capital USD bn	NPV USD bn	Peak IQD gap tn	Debt cleared month
calendar_baseline	40/76	7.515	-3.262	4.371	303
temporary_first_article	36/76	7.553	-3.287	4.323	302
availability_75pct_costed	42/83	7.515	-3.291	4.587	306
availability_75pct_all_stage_shifts	40/76	7.531	-3.310	4.495	305
domestic_placement_interrupted_recovered	46/82	7.526	-3.148	4.417	306
export_credit_delayed_recovered	46/82	7.526	-3.036	4.250	305
independent_first_section	36/76	7.545	-3.305	4.460	304

Temporary first-article production opens the complete first line earlier and lowers peak gap/repayment time, yet worsens discounted reference investment value after its additional capital/early operating costs. The independent shorter section also

adds capital and runs a conservative standalone operating deficit. Neither is adopted merely because fares arrive sooner. Coordinated shifts should be compared with the matching 75% availability case, not assumed to save money against the stronger baseline. Funding-delay NPV can look less negative because nominal un-escalated purchases are deferred; this discounting effect is not a benefit of denied credit. Real delay appraisal needs contract escalation, FX, cancellation/default costs and lost passenger benefits. Existing escalation/downside scenarios demonstrate their materiality.

Rebuild after delivery stresses with `.venv/bin/python tools/automation/baghdad_qualification.py`; validate with `--check`. Physical evidence and finance gates remain open.

Baghdad operations cross-check

Source: cities/catalogue/west-asia/Iraq/Baghdad/engineering/simulation/operations-crosscheck.md

- Status: running-time-screen-passed-awaiting-junction-evidence
- Automatic running-time cross-check: passed
- Retained full-service replay matches current inputs/tools: yes
- Service execution basis: source-bound-CI-executable
- Junction occupancy evidence: pending
- Authority accepted: no

Line	OSR reference	SUMO mean	Difference	Tolerance	Result
line-1	4350.0 s	4010.0 s	-340.0 s	652.5 s	pass
line-2	5051.9 s	4685.0 s	-366.9 s	757.8 s	pass
line-3	4889.5 s	4566.0 s	-323.5 s	733.4 s	pass
line-4	3961.9 s	3672.0 s	-289.9 s	594.3 s	pass
line-5	4280.6 s	3947.5 s	-333.1 s	642.1 s	pass
line-6	4926.2 s	4553.0 s	-373.2 s	738.9 s	pass
line-7	3866.0 s	3594.0 s	-272.0 s	579.9 s	pass
line-8	4394.7 s	4058.0 s	-336.7 s	659.2 s	pass
line-9	8989.8 s	8364.5 s	-625.3 s	1348.5 s	pass

The automatic result is a deterministic planning-model timing comparison, not proof of safe headways, signalling performance or junction capacity.

Junction occupancy must be checked in an independently reviewed conflict-capable model and the operator or authority must sign the bound evidence before operational release.

Remaining junction gate

- independently reviewed junction-occupancy evidence not received

Remaining acceptance gate

- signed operational acceptance record not received

Baghdad civil soil screening

Source: cities/catalogue/west-asia/Iraq/Baghdad/engineering/soil/README.md

3,458 route/station sample locations; 3,395 complete profiles; 63 profiles with missing data.

Published soilDB 2020–2022 predictions, 120 m pixels, 0–30 / 30–60 / 60–100 cm depths. Mean and p16–p84 are retained for clay, sand, silt, bulk density, organic carbon and pH.

The [samples](#), [source receipt](#), [map](#) and [civil investigation plan](#) are reproducible planning inputs. Each station and civil segment has an investigation scope. These records do not close the surveyed ground-model or foundation-design gates.

Investigation trigger	Sample locations
coverage-gap	63
fine-soil-plasticity-and-shrink-swell-tests	3228
granular-density-and-groundwater-tests	1828
silt-moisture-frost-and-erosion-review	2005

- No bearing capacity, CBR, friction angle, cohesion, groundwater, contamination, sulfate/chloride or deep stratigraphy is inferred from these maps.
- Desert, water, urban fill and other nodata remain unknown; no nearest-pixel or climate-based substitution.
- Texture fractions are independent predictions; they are not renormalised or converted to a geotechnical soil class.
- Prioritisation thresholds are editable OSR screening rules, not statutory limits or evidence of a hazard.
- No excavation depths, foundation dimensions, treatment quantities or civil costs are changed from pedological predictions.

Source: [OpenLandMap soilDB](#), Hengl et al., DOI 10.5194/essd-2025-336, CC BY 4.0. Exact source revision, URLs and raster metadata are retained in the receipt.

Sampled property ranges

Ranges below span the sampled locations; they are not a city-wide characteristic soil value. The uncertainty envelope spans the lowest p16 to highest p84.

Depth	Property	Unit	Mean range	Uncertainty envelope	Available locations
0..30cm	clay	%	16–32	2–42	3395
0..30cm	sand	%	25–58	6–86	3395
0..30cm	silt	%	26–45	8–59	3395
0..30cm	bd.core	kg/m3	1410–1510	1210–1720	3395
0..30cm	soc	g/kg	2.1–6.2	0.5–14.8	3395
0..30cm	ph.h2o	pH	7.6–8.4	6.5–9.2	3395
30..60cm	clay	%	17–33	1–42	3395
30..60cm	sand	%	26–57	5–92	3395
30..60cm	silt	%	23–42	4–60	3395
30..60cm	bd.core	kg/m3	1410–1560	1170–1770	3395
30..60cm	soc	g/kg	1.6–4.2	0–13.7	3395
30..60cm	ph.h2o	pH	7.6–8.7	6.3–10.2	3395
60..100cm	clay	%	17–34	2–43	3395
60..100cm	sand	%	27–59	5–92	3395
60..100cm	silt	%	22–41	1–58	3395
60..100cm	bd.core	kg/m3	1400–1630	1200–1940	3395
60..100cm	soc	g/kg	1.6–3.2	0–9.1	3395
60..100cm	ph.h2o	pH	7.5–8.8	6–10.3	3395

Station and depot overnight allocation

Source: [cities/catalogue/west-asia/Iraq/Baghdad/engineering/stabling/README.md](#)

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

The hybrid allocation below remains a planning candidate; physical release is open.

Plan: 265 trainsets at stations + 497 at depots = 762 total. Two revenue trainsets per selected station support coordinated morning starts; the remaining revenue trains and reserves stay at storage on their own line.

Allocation check: FAIL. Depot stabling positions are planning requirements, separate from workshop bays. Physical release remains open.

Depot/storage station	Line	Site basis	Stabling positions required	Usable slot length m	Workshop bays
line-1-0166-0866-s049067	line-1	storage-at-existing-powered-service-point	52	6,292.0	0
line-2-0595-0296-s052851	line-2	declared-depot	67	8,107.0	115
line-3-0151-1637-s049496	line-3	storage-at-existing-powered-service-point	65	7,865.0	0
line-4-1246-1628-s042068	line-4	storage-at-existing-powered-service-point	54	6,534.0	0
line-5-0677-2304-s047321	line-5	storage-at-existing-powered-service-point	60	7,260.0	0
line-6-0495-1669-s052503	line-6	storage-at-existing-powered-service-point	74	8,954.0	0
line-7-1531-0418-s039957	line-7	storage-at-existing-powered-service-point	53	6,413.0	0
line-8-0785-0290-s047849	line-8	storage-at-existing-powered-service-point	68	8,228.0	0
line-9-0819-0573-s090161	line-9	storage-at-existing-powered-service-point	4	484.0	0

Line	Location	Type	Direction	Role	Trainsets
line-1	line-1-0166-0866-s049067	station	reverse	revenue	2
line-1	line-1-0260-0833-s046583	station	forward	revenue	1
line-1	line-1-0260-0833-s046583	station	reverse	revenue	1
line-1	line-1-0382-0837-s044110	station	forward	revenue	1
line-1	line-1-0382-0837-s044110	station	reverse	revenue	1
line-1	line-1-0528-0840-s041099	station	forward	revenue	1
line-1	line-1-0528-0840-s041099	station	reverse	revenue	1
line-1	line-1-0677-0837-s038094	station	forward	revenue	1
line-1	line-1-0677-0837-s038094	station	reverse	revenue	1
line-1	line-1-0826-0834-s035089	station	forward	revenue	1
line-1	line-1-0826-0834-s035089	station	reverse	revenue	1
line-1	line-1-0975-0831-s032084	station	forward	revenue	1
line-1	line-1-0975-0831-s032084	station	reverse	revenue	1
line-1	line-1-1124-0828-s029068	station	forward	revenue	1
line-1	line-1-1124-0828-s029068	station	reverse	revenue	1
line-1	line-1-1273-0825-s026063	station	forward	revenue	1
line-1	line-1-1273-0825-s026063	station	reverse	revenue	1
line-1	line-1-1422-0822-s023058	station	forward	revenue	1
line-1	line-1-1422-0822-s023058	station	reverse	revenue	1
line-1	line-1-1553-0819-s020413	station	forward	revenue	1
line-1	line-1-1553-0819-s020413	station	reverse	revenue	1
line-1	line-1-1702-0808-s017045	station	forward	revenue	1
line-1	line-1-1702-0808-s017045	station	reverse	revenue	1
line-1	line-1-1848-0797-s014034	station	forward	revenue	1
line-1	line-1-1848-0797-s014034	station	reverse	revenue	1
line-1	line-1-2017-0784-s010529	station	forward	revenue	1
line-1	line-1-2017-0784-s010529	station	reverse	revenue	1
line-1	line-1-2180-0774-s007014	station	forward	revenue	1
line-1	line-1-2180-0774-s007014	station	reverse	revenue	1
line-1	line-1-2343-0771-s003515	station	forward	revenue	1
line-1	line-1-2343-0771-s003515	station	reverse	revenue	1
line-1	line-1-2500-0775-s000000	station	forward	revenue	2

Line	Location	Type	Direction	Role	Trainsets
line-2	line-2-0595-0296-s052851	station	reverse	revenue	2
line-2	line-2-0670-0367-s050001	station	forward	revenue	1
line-2	line-2-0670-0367-s050001	station	reverse	revenue	1
line-2	line-2-0741-0469-s047164	station	forward	revenue	1
line-2	line-2-0741-0469-s047164	station	reverse	revenue	1
line-2	line-2-0819-0573-s044239	station	forward	revenue	1
line-2	line-2-0819-0573-s044239	station	reverse	revenue	1
line-2	line-2-0903-0683-s041132	station	forward	revenue	1
line-2	line-2-0903-0683-s041132	station	reverse	revenue	1
line-2	line-2-0985-0791-s038129	station	forward	revenue	1
line-2	line-2-0985-0791-s038129	station	reverse	revenue	1
line-2	line-2-1065-0897-s035123	station	forward	revenue	1
line-2	line-2-1065-0897-s035123	station	reverse	revenue	1
line-2	line-2-1147-1006-s032100	station	forward	revenue	1
line-2	line-2-1147-1006-s032100	station	reverse	revenue	1
line-2	line-2-1228-1112-s029098	station	forward	revenue	1
line-2	line-2-1228-1112-s029098	station	reverse	revenue	1
line-2	line-2-1310-1220-s026095	station	forward	revenue	1
line-2	line-2-1310-1220-s026095	station	reverse	revenue	1
line-2	line-2-1390-1326-s023089	station	forward	revenue	1
line-2	line-2-1390-1326-s023089	station	reverse	revenue	1
line-2	line-2-1471-1434-s020071	station	forward	revenue	1
line-2	line-2-1471-1434-s020071	station	reverse	revenue	1
line-2	line-2-1504-1477-s018832	station	forward	revenue	1
line-2	line-2-1504-1477-s018832	station	reverse	revenue	1
line-2	line-2-1550-1543-s017049	station	forward	revenue	1
line-2	line-2-1550-1543-s017049	station	reverse	revenue	1
line-2	line-2-1648-1703-s012612	station	forward	revenue	1
line-2	line-2-1648-1703-s012612	station	reverse	revenue	1
line-2	line-2-1895-2056-s003494	station	forward	revenue	1
line-2	line-2-1895-2056-s003494	station	reverse	revenue	1
line-2	line-2-1987-2192-s000000	station	forward	revenue	2
line-3	line-3-0151-1637-s049496	station	reverse	revenue	2
line-3	line-3-0288-1607-s046283	station	forward	revenue	1
line-3	line-3-0288-1607-s046283	station	reverse	revenue	1
line-3	line-3-0378-1545-s043281	station	forward	revenue	1
line-3	line-3-0378-1545-s043281	station	reverse	revenue	1
line-3	line-3-0465-1526-s041263	station	forward	revenue	1
line-3	line-3-0465-1526-s041263	station	reverse	revenue	1
line-3	line-3-0556-1502-s039233	station	forward	revenue	1
line-3	line-3-0556-1502-s039233	station	reverse	revenue	1
line-3	line-3-0628-1483-s037624	station	forward	revenue	1
line-3	line-3-0628-1483-s037624	station	reverse	revenue	1
line-3	line-3-0691-1466-s036223	station	forward	revenue	1
line-3	line-3-0691-1466-s036223	station	reverse	revenue	1
line-3	line-3-0827-1430-s033205	station	forward	revenue	1
line-3	line-3-0827-1430-s033205	station	reverse	revenue	1
line-3	line-3-0962-1395-s030191	station	forward	revenue	1
line-3	line-3-0962-1395-s030191	station	reverse	revenue	1
line-3	line-3-1096-1359-s027190	station	forward	revenue	1
line-3	line-3-1096-1359-s027190	station	reverse	revenue	1
line-3	line-3-1231-1323-s024180	station	forward	revenue	1
line-3	line-3-1231-1323-s024180	station	reverse	revenue	1
line-3	line-3-1367-1288-s021170	station	forward	revenue	1
line-3	line-3-1367-1288-s021170	station	reverse	revenue	1
line-3	line-3-1502-1252-s018148	station	forward	revenue	1
line-3	line-3-1502-1252-s018148	station	reverse	revenue	1
line-3	line-3-1613-1236-s015796	station	forward	revenue	1
line-3	line-3-1613-1236-s015796	station	reverse	revenue	1
line-3	line-3-1702-1235-s014007	station	forward	revenue	1
line-3	line-3-1702-1235-s014007	station	reverse	revenue	1
line-3	line-3-2271-1120-s000000	station	forward	revenue	2
line-4	line-4-0146-0199-s000000	station	forward	revenue	2

Line	Location	Type	Direction	Role	Trainsets
line-4	line-4-0298-0305-s004261	station	forward	revenue	1
line-4	line-4-0298-0305-s004261	station	reverse	revenue	1
line-4	line-4-0491-0706-s015030	station	forward	revenue	1
line-4	line-4-0491-0706-s015030	station	reverse	revenue	1
line-4	line-4-0569-0798-s017763	station	forward	revenue	1
line-4	line-4-0569-0798-s017763	station	reverse	revenue	1
line-4	line-4-0644-0884-s020327	station	forward	revenue	1
line-4	line-4-0644-0884-s020327	station	reverse	revenue	1
line-4	line-4-0731-0987-s023342	station	forward	revenue	1
line-4	line-4-0731-0987-s023342	station	reverse	revenue	1
line-4	line-4-0818-1088-s026352	station	forward	revenue	1
line-4	line-4-0818-1088-s026352	station	reverse	revenue	1
line-4	line-4-0906-1190-s029379	station	forward	revenue	1
line-4	line-4-0906-1190-s029379	station	reverse	revenue	1
line-4	line-4-0993-1292-s032385	station	forward	revenue	1
line-4	line-4-0993-1292-s032385	station	reverse	revenue	1
line-4	line-4-1080-1393-s035395	station	forward	revenue	1
line-4	line-4-1080-1393-s035395	station	reverse	revenue	1
line-4	line-4-1144-1468-s037613	station	forward	revenue	1
line-4	line-4-1144-1468-s037613	station	reverse	revenue	1
line-4	line-4-1210-1544-s039856	station	forward	revenue	1
line-4	line-4-1210-1544-s039856	station	reverse	revenue	1
line-4	line-4-1246-1628-s042068	station	reverse	revenue	2
line-5	line-5-0677-2304-s047321	station	reverse	revenue	2
line-5	line-5-0853-1593-s029915	station	forward	revenue	1
line-5	line-5-0853-1593-s029915	station	reverse	revenue	1
line-5	line-5-0863-1462-s027063	station	forward	revenue	1
line-5	line-5-0863-1462-s027063	station	reverse	revenue	1
line-5	line-5-0897-1326-s024049	station	forward	revenue	1
line-5	line-5-0897-1326-s024049	station	reverse	revenue	1
line-5	line-5-0932-1191-s021036	station	forward	revenue	1
line-5	line-5-0932-1191-s021036	station	reverse	revenue	1
line-5	line-5-0967-1056-s018034	station	forward	revenue	1
line-5	line-5-0967-1056-s018034	station	reverse	revenue	1
line-5	line-5-1001-0920-s015033	station	forward	revenue	1
line-5	line-5-1001-0920-s015033	station	reverse	revenue	1
line-5	line-5-1036-0785-s012031	station	forward	revenue	1
line-5	line-5-1036-0785-s012031	station	reverse	revenue	1
line-5	line-5-1070-0649-s009029	station	forward	revenue	1
line-5	line-5-1070-0649-s009029	station	reverse	revenue	1
line-5	line-5-1105-0514-s006016	station	forward	revenue	1
line-5	line-5-1105-0514-s006016	station	reverse	revenue	1
line-5	line-5-1128-0422-s003974	station	forward	revenue	1
line-5	line-5-1128-0422-s003974	station	reverse	revenue	1
line-5	line-5-1170-0351-s002077	station	forward	revenue	1
line-5	line-5-1170-0351-s002077	station	reverse	revenue	1
line-5	line-5-1199-0260-s000000	station	forward	revenue	2
line-6	line-6-0495-1669-s052503	station	reverse	revenue	2
line-6	line-6-0647-1587-s047165	station	forward	revenue	1
line-6	line-6-0647-1587-s047165	station	reverse	revenue	1
line-6	line-6-0713-1485-s044164	station	forward	revenue	1
line-6	line-6-0713-1485-s044164	station	reverse	revenue	1
line-6	line-6-0817-1407-s041145	station	forward	revenue	1
line-6	line-6-0817-1407-s041145	station	reverse	revenue	1
line-6	line-6-0932-1321-s038132	station	forward	revenue	1
line-6	line-6-0932-1321-s038132	station	reverse	revenue	1
line-6	line-6-1047-1235-s035108	station	forward	revenue	1
line-6	line-6-1047-1235-s035108	station	reverse	revenue	1
line-6	line-6-1150-1158-s032106	station	forward	revenue	1
line-6	line-6-1150-1158-s032106	station	reverse	revenue	1
line-6	line-6-1264-1073-s029098	station	forward	revenue	1
line-6	line-6-1264-1073-s029098	station	reverse	revenue	1
line-6	line-6-1379-0987-s026086	station	forward	revenue	1

Line	Location	Type	Direction	Role	Trainsets
line-6	line-6-1379-0987-s026086	station	reverse	revenue	1
line-6	line-6-1483-0909-s023078	station	forward	revenue	1
line-6	line-6-1483-0909-s023078	station	reverse	revenue	1
line-6	line-6-1580-0848-s020342	station	forward	revenue	1
line-6	line-6-1580-0848-s020342	station	reverse	revenue	1
line-6	line-6-1694-0774-s017029	station	forward	revenue	1
line-6	line-6-1694-0774-s017029	station	reverse	revenue	1
line-6	line-6-2322-0251-s000000	station	forward	revenue	2
line-7	line-7-1069-2206-s000000	station	forward	revenue	2
line-7	line-7-1185-1622-s012693	station	forward	revenue	1
line-7	line-7-1185-1622-s012693	station	reverse	revenue	1
line-7	line-7-1206-1546-s014599	station	forward	revenue	1
line-7	line-7-1206-1546-s014599	station	reverse	revenue	1
line-7	line-7-1238-1464-s016516	station	forward	revenue	1
line-7	line-7-1238-1464-s016516	station	reverse	revenue	1
line-7	line-7-1276-1329-s019531	station	forward	revenue	1
line-7	line-7-1276-1329-s019531	station	reverse	revenue	1
line-7	line-7-1313-1195-s022541	station	forward	revenue	1
line-7	line-7-1313-1195-s022541	station	reverse	revenue	1
line-7	line-7-1351-1061-s025559	station	forward	revenue	1
line-7	line-7-1351-1061-s025559	station	reverse	revenue	1
line-7	line-7-1389-0926-s028574	station	forward	revenue	1
line-7	line-7-1389-0926-s028574	station	reverse	revenue	1
line-7	line-7-1426-0792-s031584	station	forward	revenue	1
line-7	line-7-1426-0792-s031584	station	reverse	revenue	1
line-7	line-7-1444-0727-s033033	station	forward	revenue	1
line-7	line-7-1444-0727-s033033	station	reverse	revenue	1
line-7	line-7-1464-0658-s034590	station	forward	revenue	1
line-7	line-7-1464-0658-s034590	station	reverse	revenue	1
line-7	line-7-1497-0538-s037275	station	forward	revenue	1
line-7	line-7-1497-0538-s037275	station	reverse	revenue	1
line-7	line-7-1531-0418-s039957	station	reverse	revenue	2
line-8	line-8-0785-0290-s047849	station	reverse	revenue	2
line-8	line-8-0851-0373-s045009	station	forward	revenue	1
line-8	line-8-0851-0373-s045009	station	reverse	revenue	1
line-8	line-8-0948-0460-s042156	station	forward	revenue	1
line-8	line-8-0948-0460-s042156	station	reverse	revenue	1
line-8	line-8-1026-0532-s039824	station	forward	revenue	1
line-8	line-8-1026-0532-s039824	station	reverse	revenue	1
line-8	line-8-1125-0623-s036821	station	forward	revenue	1
line-8	line-8-1125-0623-s036821	station	reverse	revenue	1
line-8	line-8-1224-0715-s033798	station	forward	revenue	1
line-8	line-8-1224-0715-s033798	station	reverse	revenue	1
line-8	line-8-1323-0806-s030783	station	forward	revenue	1
line-8	line-8-1323-0806-s030783	station	reverse	revenue	1
line-8	line-8-1423-0898-s027774	station	forward	revenue	1
line-8	line-8-1423-0898-s027774	station	reverse	revenue	1
line-8	line-8-1525-0991-s024765	station	forward	revenue	1
line-8	line-8-1525-0991-s024765	station	reverse	revenue	1
line-8	line-8-1645-1094-s021347	station	forward	revenue	1
line-8	line-8-1645-1094-s021347	station	reverse	revenue	1
line-8	line-8-2231-1783-s000000	station	forward	revenue	2
line-9	line-9-0492-0740-s006009	station	reverse	revenue	1
line-9	line-9-0552-0632-s003005	station	forward	revenue	1
line-9	line-9-0552-0632-s003005	station	reverse	revenue	1
line-9	line-9-0558-0854-s009023	station	forward	revenue	1
line-9	line-9-0558-0854-s009023	station	reverse	revenue	1
line-9	line-9-0566-0985-s012040	station	forward	revenue	1
line-9	line-9-0619-1393-s022049	station	forward	revenue	1
line-9	line-9-0619-1393-s022049	station	reverse	revenue	1
line-9	line-9-0628-1483-s024068	station	forward	revenue	1
line-9	line-9-0628-1483-s024068	station	reverse	revenue	1
line-9	line-9-0647-1607-s027110	station	reverse	revenue	1

Line	Location	Type	Direction	Role	Trainsets
line-9	line-9-0678-0582-s000000	station	forward	revenue	1
line-9	line-9-0678-0582-s000000	station	reverse	revenue	1
line-9	line-9-0875-1578-s032071	station	forward	revenue	1
line-9	line-9-0875-1578-s032071	station	reverse	revenue	1
line-9	line-9-1032-0449-s084241	station	forward	revenue	1
line-9	line-9-1032-0449-s084241	station	reverse	revenue	1
line-9	line-9-1128-0422-s081781	station	reverse	revenue	1
line-9	line-9-1185-1622-s039062	station	forward	revenue	1
line-9	line-9-1190-0372-s079883	station	forward	revenue	1
line-9	line-9-1190-0372-s079883	station	reverse	revenue	1
line-9	line-9-1217-0443-s078216	station	forward	revenue	1
line-9	line-9-1217-0443-s078216	station	reverse	revenue	1
line-9	line-9-1246-1628-s040331	station	forward	revenue	1
line-9	line-9-1246-1628-s040331	station	reverse	revenue	1
line-9	line-9-1322-0517-s075210	station	forward	revenue	1
line-9	line-9-1363-0647-s072200	station	forward	revenue	1
line-9	line-9-1363-0647-s072200	station	reverse	revenue	1
line-9	line-9-1427-1526-s046095	station	forward	revenue	1
line-9	line-9-1427-1526-s046095	station	reverse	revenue	1
line-9	line-9-1444-0727-s069624	station	reverse	revenue	1
line-9	line-9-1503-1477-s048127	station	reverse	revenue	1
line-9	line-9-1512-0785-s067632	station	forward	revenue	1
line-9	line-9-1512-0785-s067632	station	reverse	revenue	1
line-9	line-9-1580-0848-s065621	station	forward	revenue	1
line-9	line-9-1580-0848-s065621	station	reverse	revenue	1
line-9	line-9-1613-1218-s056128	station	forward	revenue	1
line-9	line-9-1613-1218-s056128	station	reverse	revenue	1
line-9	line-9-1645-1094-s058873	station	forward	revenue	1
line-1	line-1-0166-0866-s049067	depot	—	revenue	44
line-1	line-1-0166-0866-s049067	depot	—	spare	7
line-1	line-1-0166-0866-s049067	depot	—	cold_reserve	1
line-2	line-2-0595-0296-s052851	depot	—	revenue	57
line-2	line-2-0595-0296-s052851	depot	—	spare	9
line-2	line-2-0595-0296-s052851	depot	—	cold_reserve	1
line-3	line-3-0151-1637-s049496	depot	—	revenue	56
line-3	line-3-0151-1637-s049496	depot	—	spare	8
line-3	line-3-0151-1637-s049496	depot	—	cold_reserve	1
line-4	line-4-1246-1628-s042068	depot	—	revenue	46
line-4	line-4-1246-1628-s042068	depot	—	spare	7
line-4	line-4-1246-1628-s042068	depot	—	cold_reserve	1
line-5	line-5-0677-2304-s047321	depot	—	revenue	52
line-5	line-5-0677-2304-s047321	depot	—	spare	7
line-5	line-5-0677-2304-s047321	depot	—	cold_reserve	1
line-6	line-6-0495-1669-s052503	depot	—	revenue	64
line-6	line-6-0495-1669-s052503	depot	—	spare	9
line-6	line-6-0495-1669-s052503	depot	—	cold_reserve	1
line-7	line-7-1531-0418-s039957	depot	—	revenue	45
line-7	line-7-1531-0418-s039957	depot	—	spare	7
line-7	line-7-1531-0418-s039957	depot	—	cold_reserve	1
line-8	line-8-0785-0290-s047849	depot	—	revenue	59
line-8	line-8-0785-0290-s047849	depot	—	spare	8
line-8	line-8-0785-0290-s047849	depot	—	cold_reserve	1
line-9	line-9-0819-0573-s090161	depot	—	spare	3
line-9	line-9-0819-0573-s090161	depot	—	cold_reserve	1

Native hybrid candidate unavailable: morning station allocation is incomplete.

Station-only native benchmark

The runnable scenario below tests station holding and restart behaviour. It does not yet execute the station/depot allocation above or depot yard movements. Its station overflow is a diagnostic result, not the overnight design allocation.

Operating allocation: 762 trainsets at 140 stations; largest initial station queue 10. Physical release: open.

This candidate preserves all non-fleet scenario inputs and the existing fleet counts/service windows. It enables station holding and 150 kW top-up to 95% SoC, subject to shared site limits. Existing canonical simulation evidence still describes the retained endpoint-dispatch scenario.

Fleet roles: 688 revenue, 65 spare, 9 cold reserve. Reserves are held out of routine dispatch.

Two-train station-capacity check: FAIL. Selected stations provide 280 positions; 482 fleet positions exceed station-only provision. The initial allocation exceeds the limit at 112 stations. Four-berth reference platforms do not override the two-train provision.

Line	Station	Direction	Role	Initial trainsets	Verified track slots
line-1	line-1-2500-0775-s000000	forward	revenue	3	pending
line-1	line-1-2343-0771-s003515	forward	revenue	3	pending
line-1	line-1-2343-0771-s003515	reverse	revenue	3	pending
line-1	line-1-2180-0774-s007014	forward	revenue	3	pending
line-1	line-1-2180-0774-s007014	reverse	revenue	3	pending
line-1	line-1-2017-0784-s010529	forward	revenue	3	pending
line-1	line-1-2017-0784-s010529	reverse	revenue	3	pending
line-1	line-1-1848-0797-s014034	forward	revenue	3	pending
line-1	line-1-1848-0797-s014034	reverse	revenue	3	pending
line-1	line-1-1702-0808-s017045	forward	revenue	3	pending
line-1	line-1-1702-0808-s017045	reverse	revenue	3	pending
line-1	line-1-1553-0819-s020413	forward	revenue	3	pending
line-1	line-1-1553-0819-s020413	reverse	revenue	3	pending
line-1	line-1-1422-0822-s023058	forward	revenue	3	pending
line-1	line-1-1422-0822-s023058	reverse	revenue	2	pending
line-1	line-1-1273-0825-s026063	forward	revenue	2	pending
line-1	line-1-1273-0825-s026063	reverse	revenue	2	pending
line-1	line-1-1124-0828-s029068	forward	revenue	2	pending
line-1	line-1-1124-0828-s029068	reverse	revenue	2	pending
line-1	line-1-0975-0831-s032084	forward	revenue	2	pending
line-1	line-1-0975-0831-s032084	reverse	revenue	2	pending
line-1	line-1-0826-0834-s035089	forward	revenue	2	pending
line-1	line-1-0826-0834-s035089	reverse	revenue	2	pending
line-1	line-1-0677-0837-s038094	forward	revenue	2	pending
line-1	line-1-0677-0837-s038094	reverse	revenue	2	pending
line-1	line-1-0528-0840-s041099	forward	revenue	2	pending
line-1	line-1-0528-0840-s041099	reverse	revenue	2	pending
line-1	line-1-0382-0837-s044110	forward	revenue	2	pending
line-1	line-1-0382-0837-s044110	reverse	revenue	2	pending
line-1	line-1-0260-0833-s046583	forward	revenue	2	pending
line-1	line-1-0260-0833-s046583	reverse	revenue	2	pending
line-1	line-1-0166-0866-s049067	reverse	revenue	2	pending
line-1	line-1-1422-0822-s023058	reverse	spare	1	pending
line-1	line-1-1273-0825-s026063	forward	spare	1	pending
line-1	line-1-1273-0825-s026063	reverse	spare	1	pending
line-1	line-1-1124-0828-s029068	forward	spare	1	pending
line-1	line-1-1124-0828-s029068	reverse	spare	1	pending
line-1	line-1-0975-0831-s032084	forward	spare	1	pending
line-1	line-1-0975-0831-s032084	reverse	spare	1	pending
line-1	line-1-0826-0834-s035089	forward	cold_reserve	1	pending
line-2	line-2-1987-2192-s000000	forward	revenue	3	pending
line-2	line-2-1895-2056-s003494	forward	revenue	3	pending
line-2	line-2-1895-2056-s003494	reverse	revenue	3	pending
line-2	line-2-1648-1703-s012612	forward	revenue	3	pending
line-2	line-2-1648-1703-s012612	reverse	revenue	3	pending
line-2	line-2-1550-1543-s017049	forward	revenue	3	pending
line-2	line-2-1550-1543-s017049	reverse	revenue	3	pending
line-2	line-2-1504-1477-s018832	forward	revenue	3	pending
line-2	line-2-1504-1477-s018832	reverse	revenue	3	pending
line-2	line-2-1471-1434-s020071	forward	revenue	3	pending
line-2	line-2-1471-1434-s020071	reverse	revenue	3	pending
line-2	line-2-1390-1326-s023089	forward	revenue	3	pending
line-2	line-2-1390-1326-s023089	reverse	revenue	3	pending
line-2	line-2-1310-1220-s026095	forward	revenue	3	pending

Line	Station	Direction	Role	Initial trainsets	Verified track slots
line-2	line-2-1310-1220-s026095	reverse	revenue	3	pending
line-2	line-2-1228-1112-s029098	forward	revenue	3	pending
line-2	line-2-1228-1112-s029098	reverse	revenue	3	pending
line-2	line-2-1147-1006-s032100	forward	revenue	3	pending
line-2	line-2-1147-1006-s032100	reverse	revenue	3	pending
line-2	line-2-1065-0897-s035123	forward	revenue	3	pending
line-2	line-2-1065-0897-s035123	reverse	revenue	3	pending
line-2	line-2-0985-0791-s038129	forward	revenue	3	pending
line-2	line-2-0985-0791-s038129	reverse	revenue	3	pending
line-2	line-2-0903-0683-s041132	forward	revenue	3	pending
line-2	line-2-0903-0683-s041132	reverse	revenue	3	pending
line-2	line-2-0819-0573-s044239	forward	revenue	3	pending
line-2	line-2-0819-0573-s044239	reverse	revenue	3	pending
line-2	line-2-0741-0469-s047164	forward	revenue	2	pending
line-2	line-2-0741-0469-s047164	reverse	revenue	2	pending
line-2	line-2-0670-0367-s050001	forward	revenue	2	pending
line-2	line-2-0670-0367-s050001	reverse	revenue	2	pending
line-2	line-2-0595-0296-s052851	reverse	revenue	2	pending
line-2	line-2-0741-0469-s047164	forward	spare	1	pending
line-2	line-2-0741-0469-s047164	reverse	spare	1	pending
line-2	line-2-0670-0367-s050001	forward	spare	1	pending
line-2	line-2-0670-0367-s050001	reverse	spare	1	pending
line-2	line-2-0595-0296-s052851	reverse	spare	1	pending
line-2	line-2-1987-2192-s000000	forward	spare	1	pending
line-2	line-2-1895-2056-s003494	forward	spare	1	pending
line-2	line-2-1895-2056-s003494	reverse	spare	1	pending
line-2	line-2-1648-1703-s012612	forward	spare	1	pending
line-2	line-2-1648-1703-s012612	reverse	cold_reserve	1	pending
line-3	line-3-2271-1120-s000000	forward	revenue	3	pending
line-3	line-3-1702-1235-s014007	forward	revenue	3	pending
line-3	line-3-1702-1235-s014007	reverse	revenue	3	pending
line-3	line-3-1613-1236-s015796	forward	revenue	3	pending
line-3	line-3-1613-1236-s015796	reverse	revenue	3	pending
line-3	line-3-1502-1252-s018148	forward	revenue	3	pending
line-3	line-3-1502-1252-s018148	reverse	revenue	3	pending
line-3	line-3-1367-1288-s021170	forward	revenue	3	pending
line-3	line-3-1367-1288-s021170	reverse	revenue	3	pending
line-3	line-3-1231-1323-s024180	forward	revenue	3	pending
line-3	line-3-1231-1323-s024180	reverse	revenue	3	pending
line-3	line-3-1096-1359-s027190	forward	revenue	3	pending
line-3	line-3-1096-1359-s027190	reverse	revenue	3	pending
line-3	line-3-0962-1395-s030191	forward	revenue	3	pending
line-3	line-3-0962-1395-s030191	reverse	revenue	3	pending
line-3	line-3-0827-1430-s033205	forward	revenue	3	pending
line-3	line-3-0827-1430-s033205	reverse	revenue	3	pending
line-3	line-3-0691-1466-s036223	forward	revenue	3	pending
line-3	line-3-0691-1466-s036223	reverse	revenue	3	pending
line-3	line-3-0628-1483-s037624	forward	revenue	3	pending
line-3	line-3-0628-1483-s037624	reverse	revenue	3	pending
line-3	line-3-0556-1502-s039233	forward	revenue	3	pending
line-3	line-3-0556-1502-s039233	reverse	revenue	3	pending
line-3	line-3-0465-1526-s041263	forward	revenue	3	pending
line-3	line-3-0465-1526-s041263	reverse	revenue	3	pending
line-3	line-3-0378-1545-s043281	forward	revenue	3	pending
line-3	line-3-0378-1545-s043281	reverse	revenue	3	pending
line-3	line-3-0288-1607-s046283	forward	revenue	3	pending
line-3	line-3-0288-1607-s046283	reverse	revenue	2	pending
line-3	line-3-0151-1637-s049496	reverse	revenue	2	pending
line-3	line-3-0288-1607-s046283	reverse	spare	1	pending
line-3	line-3-0151-1637-s049496	reverse	spare	1	pending
line-3	line-3-2271-1120-s000000	forward	spare	1	pending
line-3	line-3-1702-1235-s014007	forward	spare	1	pending
line-3	line-3-1702-1235-s014007	reverse	spare	1	pending

Line	Station	Direction	Role	Initial trainsets	Verified track slots
line-3	line-3-1613-1236-s015796	forward	spare	1	pending
line-3	line-3-1613-1236-s015796	reverse	spare	1	pending
line-3	line-3-1502-1252-s018148	forward	spare	1	pending
line-3	line-3-1502-1252-s018148	reverse	cold_reserve	1	pending
line-4	line-4-0146-0199-s000000	forward	revenue	3	pending
line-4	line-4-0298-0305-s004261	forward	revenue	3	pending
line-4	line-4-0298-0305-s004261	reverse	revenue	3	pending
line-4	line-4-0491-0706-s015030	forward	revenue	3	pending
line-4	line-4-0491-0706-s015030	reverse	revenue	3	pending
line-4	line-4-0569-0798-s017763	forward	revenue	3	pending
line-4	line-4-0569-0798-s017763	reverse	revenue	3	pending
line-4	line-4-0644-0884-s020327	forward	revenue	3	pending
line-4	line-4-0644-0884-s020327	reverse	revenue	3	pending
line-4	line-4-0731-0987-s023342	forward	revenue	3	pending
line-4	line-4-0731-0987-s023342	reverse	revenue	3	pending
line-4	line-4-0818-1088-s026352	forward	revenue	3	pending
line-4	line-4-0818-1088-s026352	reverse	revenue	3	pending
line-4	line-4-0906-1190-s029379	forward	revenue	3	pending
line-4	line-4-0906-1190-s029379	reverse	revenue	3	pending
line-4	line-4-0993-1292-s032385	forward	revenue	3	pending
line-4	line-4-0993-1292-s032385	reverse	revenue	3	pending
line-4	line-4-1080-1393-s035395	forward	revenue	3	pending
line-4	line-4-1080-1393-s035395	reverse	revenue	3	pending
line-4	line-4-1144-1468-s037613	forward	revenue	3	pending
line-4	line-4-1144-1468-s037613	reverse	revenue	3	pending
line-4	line-4-1210-1544-s039856	forward	revenue	3	pending
line-4	line-4-1210-1544-s039856	reverse	revenue	3	pending
line-4	line-4-1246-1628-s042068	reverse	revenue	3	pending
line-4	line-4-0146-0199-s000000	forward	spare	1	pending
line-4	line-4-0298-0305-s004261	forward	spare	1	pending
line-4	line-4-0298-0305-s004261	reverse	spare	1	pending
line-4	line-4-0491-0706-s015030	forward	spare	1	pending
line-4	line-4-0491-0706-s015030	reverse	spare	1	pending
line-4	line-4-0569-0798-s017763	forward	spare	1	pending
line-4	line-4-0569-0798-s017763	reverse	spare	1	pending
line-4	line-4-0644-0884-s020327	forward	cold_reserve	1	pending
line-5	line-5-1199-0260-s000000	forward	revenue	4	pending
line-5	line-5-1170-0351-s002077	forward	revenue	4	pending
line-5	line-5-1170-0351-s002077	reverse	revenue	4	pending
line-5	line-5-1128-0422-s003974	forward	revenue	4	pending
line-5	line-5-1128-0422-s003974	reverse	revenue	4	pending
line-5	line-5-1105-0514-s006016	forward	revenue	4	pending
line-5	line-5-1105-0514-s006016	reverse	revenue	3	pending
line-5	line-5-1070-0649-s009029	forward	revenue	3	pending
line-5	line-5-1070-0649-s009029	reverse	revenue	3	pending
line-5	line-5-1036-0785-s012031	forward	revenue	3	pending
line-5	line-5-1036-0785-s012031	reverse	revenue	3	pending
line-5	line-5-1001-0920-s015033	forward	revenue	3	pending
line-5	line-5-1001-0920-s015033	reverse	revenue	3	pending
line-5	line-5-0967-1056-s018034	forward	revenue	3	pending
line-5	line-5-0967-1056-s018034	reverse	revenue	3	pending
line-5	line-5-0932-1191-s021036	forward	revenue	3	pending
line-5	line-5-0932-1191-s021036	reverse	revenue	3	pending
line-5	line-5-0897-1326-s024049	forward	revenue	3	pending
line-5	line-5-0897-1326-s024049	reverse	revenue	3	pending
line-5	line-5-0863-1462-s027063	forward	revenue	3	pending
line-5	line-5-0863-1462-s027063	reverse	revenue	3	pending
line-5	line-5-0853-1593-s029915	forward	revenue	3	pending
line-5	line-5-0853-1593-s029915	reverse	revenue	3	pending
line-5	line-5-0677-2304-s047321	reverse	revenue	3	pending
line-5	line-5-1105-0514-s006016	reverse	spare	1	pending
line-5	line-5-1070-0649-s009029	forward	spare	1	pending
line-5	line-5-1070-0649-s009029	reverse	spare	1	pending

Line	Station	Direction	Role	Initial trainsets	Verified track slots
line-5	line-5-1036-0785-s012031	forward	spare	1	pending
line-5	line-5-1036-0785-s012031	reverse	spare	1	pending
line-5	line-5-1001-0920-s015033	forward	spare	1	pending
line-5	line-5-1001-0920-s015033	reverse	spare	1	pending
line-5	line-5-0967-1056-s018034	forward	cold_reserve	1	pending
line-6	line-6-2322-0251-s000000	forward	revenue	4	pending
line-6	line-6-1694-0774-s017029	forward	revenue	4	pending
line-6	line-6-1694-0774-s017029	reverse	revenue	4	pending
line-6	line-6-1580-0848-s020342	forward	revenue	4	pending
line-6	line-6-1580-0848-s020342	reverse	revenue	4	pending
line-6	line-6-1483-0909-s023078	forward	revenue	4	pending
line-6	line-6-1483-0909-s023078	reverse	revenue	4	pending
line-6	line-6-1379-0987-s026086	forward	revenue	4	pending
line-6	line-6-1379-0987-s026086	reverse	revenue	4	pending
line-6	line-6-1264-1073-s029098	forward	revenue	4	pending
line-6	line-6-1264-1073-s029098	reverse	revenue	4	pending
line-6	line-6-1150-1158-s032106	forward	revenue	4	pending
line-6	line-6-1150-1158-s032106	reverse	revenue	4	pending
line-6	line-6-1047-1235-s035108	forward	revenue	4	pending
line-6	line-6-1047-1235-s035108	reverse	revenue	4	pending
line-6	line-6-0932-1321-s038132	forward	revenue	4	pending
line-6	line-6-0932-1321-s038132	reverse	revenue	4	pending
line-6	line-6-0817-1407-s041145	forward	revenue	4	pending
line-6	line-6-0817-1407-s041145	reverse	revenue	3	pending
line-6	line-6-0713-1485-s044164	forward	revenue	3	pending
line-6	line-6-0713-1485-s044164	reverse	revenue	3	pending
line-6	line-6-0647-1587-s047165	forward	revenue	3	pending
line-6	line-6-0647-1587-s047165	reverse	revenue	3	pending
line-6	line-6-0495-1669-s052503	reverse	revenue	3	pending
line-6	line-6-0817-1407-s041145	reverse	spare	1	pending
line-6	line-6-0713-1485-s044164	forward	spare	1	pending
line-6	line-6-0713-1485-s044164	reverse	spare	1	pending
line-6	line-6-0647-1587-s047165	forward	spare	1	pending
line-6	line-6-0647-1587-s047165	reverse	spare	1	pending
line-6	line-6-0495-1669-s052503	reverse	spare	1	pending
line-6	line-6-2322-0251-s000000	forward	spare	1	pending
line-6	line-6-1694-0774-s017029	forward	spare	1	pending
line-6	line-6-1694-0774-s017029	reverse	spare	1	pending
line-6	line-6-1580-0848-s020342	forward	cold_reserve	1	pending
line-7	line-7-1069-2206-s000000	forward	revenue	3	pending
line-7	line-7-1185-1622-s012693	forward	revenue	3	pending
line-7	line-7-1185-1622-s012693	reverse	revenue	3	pending
line-7	line-7-1206-1546-s014599	forward	revenue	3	pending
line-7	line-7-1206-1546-s014599	reverse	revenue	3	pending
line-7	line-7-1238-1464-s016516	forward	revenue	3	pending
line-7	line-7-1238-1464-s016516	reverse	revenue	3	pending
line-7	line-7-1276-1329-s019531	forward	revenue	3	pending
line-7	line-7-1276-1329-s019531	reverse	revenue	3	pending
line-7	line-7-1313-1195-s022541	forward	revenue	3	pending
line-7	line-7-1313-1195-s022541	reverse	revenue	3	pending
line-7	line-7-1351-1061-s025559	forward	revenue	3	pending
line-7	line-7-1351-1061-s025559	reverse	revenue	3	pending
line-7	line-7-1389-0926-s028574	forward	revenue	3	pending
line-7	line-7-1389-0926-s028574	reverse	revenue	3	pending
line-7	line-7-1426-0792-s031584	forward	revenue	3	pending
line-7	line-7-1426-0792-s031584	reverse	revenue	3	pending
line-7	line-7-1444-0727-s033033	forward	revenue	3	pending
line-7	line-7-1444-0727-s033033	reverse	revenue	3	pending
line-7	line-7-1464-0658-s034590	forward	revenue	3	pending
line-7	line-7-1464-0658-s034590	reverse	revenue	3	pending
line-7	line-7-1497-0538-s037275	forward	revenue	3	pending
line-7	line-7-1497-0538-s037275	reverse	revenue	3	pending
line-7	line-7-1531-0418-s039957	reverse	revenue	2	pending

Line	Station	Direction	Role	Initial trainsets	Verified track slots
line-7	line-7-1531-0418-s039957	reverse	spare	1	pending
line-7	line-7-1069-2206-s000000	forward	spare	1	pending
line-7	line-7-1185-1622-s012693	forward	spare	1	pending
line-7	line-7-1185-1622-s012693	reverse	spare	1	pending
line-7	line-7-1206-1546-s014599	forward	spare	1	pending
line-7	line-7-1206-1546-s014599	reverse	spare	1	pending
line-7	line-7-1238-1464-s016516	forward	spare	1	pending
line-7	line-7-1238-1464-s016516	reverse	cold_reserve	1	pending
line-8	line-8-2231-1783-s000000	forward	revenue	5	pending
line-8	line-8-1645-1094-s021347	forward	revenue	4	pending
line-8	line-8-1645-1094-s021347	reverse	revenue	4	pending
line-8	line-8-1525-0991-s024765	forward	revenue	4	pending
line-8	line-8-1525-0991-s024765	reverse	revenue	4	pending
line-8	line-8-1423-0898-s027774	forward	revenue	4	pending
line-8	line-8-1423-0898-s027774	reverse	revenue	4	pending
line-8	line-8-1323-0806-s030783	forward	revenue	4	pending
line-8	line-8-1323-0806-s030783	reverse	revenue	4	pending
line-8	line-8-1224-0715-s033798	forward	revenue	4	pending
line-8	line-8-1224-0715-s033798	reverse	revenue	4	pending
line-8	line-8-1125-0623-s036821	forward	revenue	4	pending
line-8	line-8-1125-0623-s036821	reverse	revenue	4	pending
line-8	line-8-1026-0532-s039824	forward	revenue	4	pending
line-8	line-8-1026-0532-s039824	reverse	revenue	4	pending
line-8	line-8-0948-0460-s042156	forward	revenue	4	pending
line-8	line-8-0948-0460-s042156	reverse	revenue	4	pending
line-8	line-8-0851-0373-s045009	forward	revenue	4	pending
line-8	line-8-0851-0373-s045009	reverse	revenue	4	pending
line-8	line-8-0785-0290-s047849	reverse	revenue	4	pending
line-8	line-8-1645-1094-s021347	forward	spare	1	pending
line-8	line-8-1645-1094-s021347	reverse	spare	1	pending
line-8	line-8-1525-0991-s024765	forward	spare	1	pending
line-8	line-8-1525-0991-s024765	reverse	spare	1	pending
line-8	line-8-1423-0898-s027774	forward	spare	1	pending
line-8	line-8-1423-0898-s027774	reverse	spare	1	pending
line-8	line-8-1323-0806-s030783	forward	spare	1	pending
line-8	line-8-1323-0806-s030783	reverse	spare	1	pending
line-8	line-8-1224-0715-s033798	forward	cold_reserve	1	pending
line-9	line-9-0678-0582-s000000	forward	revenue	1	pending
line-9	line-9-0678-0582-s000000	reverse	revenue	1	pending
line-9	line-9-0552-0632-s003005	forward	revenue	1	pending
line-9	line-9-0552-0632-s003005	reverse	revenue	1	pending
line-9	line-9-0492-0740-s006009	reverse	revenue	1	pending
line-9	line-9-0558-0854-s009023	forward	revenue	1	pending
line-9	line-9-0558-0854-s009023	reverse	revenue	1	pending
line-9	line-9-0566-0985-s012040	forward	revenue	1	pending
line-9	line-9-0619-1393-s022049	forward	revenue	1	pending
line-9	line-9-0619-1393-s022049	reverse	revenue	1	pending
line-9	line-9-0628-1483-s024068	forward	revenue	1	pending
line-9	line-9-0628-1483-s024068	reverse	revenue	1	pending
line-9	line-9-0647-1607-s027110	reverse	revenue	1	pending
line-9	line-9-0875-1578-s032071	forward	revenue	1	pending
line-9	line-9-0875-1578-s032071	reverse	revenue	1	pending
line-9	line-9-1185-1622-s039062	forward	revenue	1	pending
line-9	line-9-1246-1628-s040331	forward	revenue	1	pending
line-9	line-9-1246-1628-s040331	reverse	revenue	1	pending
line-9	line-9-1427-1526-s046095	forward	revenue	1	pending
line-9	line-9-1427-1526-s046095	reverse	revenue	1	pending
line-9	line-9-1503-1477-s048127	reverse	revenue	1	pending
line-9	line-9-1613-1218-s056128	forward	revenue	1	pending
line-9	line-9-1613-1218-s056128	reverse	revenue	1	pending
line-9	line-9-1645-1094-s058873	forward	revenue	1	pending
line-9	line-9-1580-0848-s065621	forward	revenue	1	pending
line-9	line-9-1580-0848-s065621	reverse	revenue	1	pending

Line	Station	Direction	Role	Initial trainsets	Verified track slots
line-9	line-9-1512-0785-s067632	forward	revenue	1	pending
line-9	line-9-1512-0785-s067632	reverse	revenue	1	pending
line-9	line-9-1444-0727-s069624	reverse	revenue	1	pending
line-9	line-9-1363-0647-s072200	forward	revenue	1	pending
line-9	line-9-1363-0647-s072200	reverse	revenue	1	pending
line-9	line-9-1322-0517-s075210	forward	revenue	1	pending
line-9	line-9-1217-0443-s078216	forward	revenue	1	pending
line-9	line-9-1217-0443-s078216	reverse	revenue	1	pending
line-9	line-9-1190-0372-s079883	forward	revenue	1	pending
line-9	line-9-1190-0372-s079883	reverse	revenue	1	pending
line-9	line-9-1128-0422-s081781	reverse	revenue	1	pending
line-9	line-9-1032-0449-s084241	forward	revenue	1	pending
line-9	line-9-1032-0449-s084241	reverse	revenue	1	pending
line-9	line-9-0948-0460-s086012	forward	spare	1	pending
line-9	line-9-0889-0468-s087258	forward	spare	1	pending
line-9	line-9-0889-0468-s087258	reverse	spare	1	pending
line-9	line-9-0819-0573-s090161	forward	cold_reserve	1	pending

Reference platform capacity comparison

433 trainsets exceed the reference platform envelope, requiring 52,393.0 m of additional usable slots under this initial allocation. This does not establish the location or need for new infrastructure; existing sidings require evidence before crediting them.

Station	Trainsets	Reference platform berths	Beyond envelope	Additional usable slot length m
line-1-0166-0866-s049067	2	2	0	0.0
line-1-0260-0833-s046583	4	2	2	242.0
line-1-0382-0837-s044110	4	2	2	242.0
line-1-0528-0840-s041099	4	4	0	0.0
line-1-0677-0837-s038094	4	2	2	242.0
line-1-0826-0834-s035089	5	2	3	363.0
line-1-0975-0831-s032084	6	2	4	484.0
line-1-1124-0828-s029068	6	2	4	484.0
line-1-1273-0825-s026063	6	2	4	484.0
line-1-1422-0822-s023058	6	4	2	242.0
line-1-1553-0819-s020413	6	4	2	242.0
line-1-1702-0808-s017045	6	4	2	242.0
line-1-1848-0797-s014034	6	2	4	484.0
line-1-2017-0784-s010529	6	2	4	484.0
line-1-2180-0774-s007014	6	2	4	484.0
line-1-2343-0771-s003515	6	2	4	484.0
line-1-2500-0775-s000000	3	2	1	121.0
line-2-0595-0296-s052851	3	2	1	121.0
line-2-0670-0367-s050001	6	2	4	484.0
line-2-0741-0469-s047164	6	2	4	484.0
line-2-0819-0573-s044239	6	4	2	242.0
line-2-0903-0683-s041132	6	2	4	484.0
line-2-0985-0791-s038129	6	2	4	484.0
line-2-1065-0897-s035123	6	2	4	484.0
line-2-1147-1006-s032100	6	2	4	484.0
line-2-1228-1112-s029098	6	2	4	484.0
line-2-1310-1220-s026095	6	4	2	242.0
line-2-1390-1326-s023089	6	2	4	484.0
line-2-1471-1434-s020071	6	2	4	484.0
line-2-1504-1477-s018832	6	4	2	242.0
line-2-1550-1543-s017049	6	2	4	484.0
line-2-1648-1703-s012612	8	2	6	726.0
line-2-1895-2056-s003494	8	2	6	726.0
line-2-1987-2192-s000000	4	2	2	242.0
line-3-0151-1637-s049496	3	2	1	121.0
line-3-0288-1607-s046283	6	2	4	484.0
line-3-0378-1545-s043281	6	2	4	484.0
line-3-0465-1526-s041263	6	2	4	484.0

Station	Trainsets	Reference platform berths	Beyond envelope	Additional usable slot length m
line-3-0556-1502-s039233	6	2	4	484.0
line-3-0628-1483-s037624	6	4	2	242.0
line-3-0691-1466-s036223	6	4	2	242.0
line-3-0827-1430-s033205	6	4	2	242.0
line-3-0962-1395-s030191	6	2	4	484.0
line-3-1096-1359-s027190	6	2	4	484.0
line-3-1231-1323-s024180	6	2	4	484.0
line-3-1367-1288-s021170	6	2	4	484.0
line-3-1502-1252-s018148	8	2	6	726.0
line-3-1613-1236-s015796	8	4	4	484.0
line-3-1702-1235-s014007	8	2	6	726.0
line-3-2271-1120-s000000	4	2	2	242.0
line-4-0146-0199-s000000	4	2	2	242.0
line-4-0298-0305-s004261	8	2	6	726.0
line-4-0491-0706-s015030	8	4	4	484.0
line-4-0569-0798-s017763	8	2	6	726.0
line-4-0644-0884-s020327	7	2	5	605.0
line-4-0731-0987-s023342	6	2	4	484.0
line-4-0818-1088-s026352	6	2	4	484.0
line-4-0906-1190-s029379	6	4	2	242.0
line-4-0993-1292-s032385	6	2	4	484.0
line-4-1080-1393-s035395	6	2	4	484.0
line-4-1144-1468-s037613	6	2	4	484.0
line-4-1210-1544-s039856	6	4	2	242.0
line-4-1246-1628-s042068	3	2	1	121.0
line-5-0677-2304-s047321	3	2	1	121.0
line-5-0853-1593-s029915	6	4	2	242.0
line-5-0863-1462-s027063	6	2	4	484.0
line-5-0897-1326-s024049	6	2	4	484.0
line-5-0932-1191-s021036	6	4	2	242.0
line-5-0967-1056-s018034	7	2	5	605.0
line-5-1001-0920-s015033	8	2	6	726.0
line-5-1036-0785-s012031	8	2	6	726.0
line-5-1070-0649-s009029	8	2	6	726.0
line-5-1105-0514-s006016	8	2	6	726.0
line-5-1128-0422-s003974	8	4	4	484.0
line-5-1170-0351-s002077	8	4	4	484.0
line-5-1199-0260-s000000	4	2	2	242.0
line-6-0495-1669-s052503	4	2	2	242.0
line-6-0647-1587-s047165	8	4	4	484.0
line-6-0713-1485-s044164	8	4	4	484.0
line-6-0817-1407-s041145	8	4	4	484.0
line-6-0932-1321-s038132	8	2	6	726.0
line-6-1047-1235-s035108	8	2	6	726.0
line-6-1150-1158-s032106	8	2	6	726.0
line-6-1264-1073-s029098	8	2	6	726.0
line-6-1379-0987-s026086	8	2	6	726.0
line-6-1483-0909-s023078	8	2	6	726.0
line-6-1580-0848-s020342	9	4	5	605.0
line-6-1694-0774-s017029	10	4	6	726.0
line-6-2322-0251-s000000	5	2	3	363.0
line-7-1069-2206-s000000	4	2	2	242.0
line-7-1185-1622-s012693	8	4	4	484.0
line-7-1206-1546-s014599	8	4	4	484.0
line-7-1238-1464-s016516	8	2	6	726.0
line-7-1276-1329-s019531	6	2	4	484.0
line-7-1313-1195-s022541	6	4	2	242.0
line-7-1351-1061-s025559	6	2	4	484.0
line-7-1389-0926-s028574	6	2	4	484.0
line-7-1426-0792-s031584	6	4	2	242.0
line-7-1444-0727-s033033	6	4	2	242.0
line-7-1464-0658-s034590	6	2	4	484.0
line-7-1497-0538-s037275	6	2	4	484.0

Station	Trainsets	Reference platform berths	Beyond envelope	Additional usable slot length m
line-7-1531-0418-s039957	3	2	1	121.0
line-8-0785-0290-s047849	4	2	2	242.0
line-8-0851-0373-s045009	8	2	6	726.0
line-8-0948-0460-s042156	8	4	4	484.0
line-8-1026-0532-s039824	8	2	6	726.0
line-8-1125-0623-s036821	8	2	6	726.0
line-8-1224-0715-s033798	9	2	7	847.0
line-8-1323-0806-s030783	10	2	8	968.0
line-8-1423-0898-s027774	10	2	8	968.0
line-8-1525-0991-s024765	10	2	8	968.0
line-8-1645-1094-s021347	10	4	6	726.0
line-8-2231-1783-s000000	5	2	3	363.0
line-9-0492-0740-s006009	1	4	0	0.0
line-9-0552-0632-s003005	2	2	0	0.0
line-9-0558-0854-s009023	2	4	0	0.0
line-9-0566-0985-s012040	1	2	0	0.0
line-9-0619-1393-s022049	2	2	0	0.0
line-9-0628-1483-s024068	2	4	0	0.0
line-9-0647-1607-s027110	1	4	0	0.0
line-9-0678-0582-s000000	2	2	0	0.0
line-9-0819-0573-s090161	1	4	0	0.0
line-9-0875-1578-s032071	2	4	0	0.0
line-9-0889-0468-s087258	2	2	0	0.0
line-9-0948-0460-s086012	1	4	0	0.0
line-9-1032-0449-s084241	2	2	0	0.0
line-9-1128-0422-s081781	1	4	0	0.0
line-9-1185-1622-s039062	1	4	0	0.0
line-9-1190-0372-s079883	2	4	0	0.0
line-9-1217-0443-s078216	2	2	0	0.0
line-9-1246-1628-s040331	2	4	0	0.0
line-9-1322-0517-s075210	1	2	0	0.0
line-9-1363-0647-s072200	2	2	0	0.0
line-9-1427-1526-s046095	2	2	0	0.0
line-9-1444-0727-s069624	1	4	0	0.0
line-9-1503-1477-s048127	1	4	0	0.0
line-9-1512-0785-s067632	2	2	0	0.0
line-9-1580-0848-s065621	2	4	0	0.0
line-9-1613-1218-s056128	2	4	0	0.0
line-9-1645-1094-s058873	1	4	0	0.0

- Initial queues are balanced across powered station/direction choices; this is not a surveyed parking layout.
- Declared spares and cold reserves remain parked and charge; automatic substitution, defect routing and maintenance release are not modelled.
- Returning trains hold at selected powered stations after service ends; no train is teleported back to its initial placement.
- Reference platform berths are an optimistic length/count comparison, not verified parking capacity; dedicated sidings and workshop bays receive no automatic credit.
- Station berths, crossovers and shared junction conflicts are outside the simplified interstation movement-authority graph.
- Existing depot/station energy quantities and service schedules are preserved, not accepted as correctly sized.

Regenerate this report and its local runnable scenario with:

```
.venv/bin/python tools/automation/generate-stabling-plan.py --design 'cities/catalogue/west-asia/Iraq/Baghdad/design.toml'
```

The scenario is generated under `build/engineering/stabling/`; its hash is recorded in `summary.json`. Source-linked operating replay evidence, where available, is in `operating-screen.json` beside this report.

Baghdad survey-control processing

Source: cities/catalogue/west-asia/iraq/baghdad/engineering/survey/control-processing-readiness.md

- Status: awaiting-field-data
- RTKLIB runtime: not probed
- Processing completed: no
- Technical screen passed: no
- Survey authority accepted: no

The automated result is a reproducibility and solution-quality screen. It is not a network adjustment, survey certification or permission to use the control for design or construction.

Only the appointed deployment survey authority can accept the control network after redundant occupations, independent checks, network adjustment, datum/geoid review and monument documentation.

Current gates

- Missing processing roles: rover_observation, base_observation, navigation, rtklib_configuration
- Duplicate processing roles: none
- Processing-configuration findings: 0
- Missing authority-review roles: rover_observation, base_observation, navigation, rtklib_configuration, field_log, monument_schedule, network_adjustment_report, authority_acceptance_record

Controlled-storage workflow

RINEX observations and navigation data remain in access-controlled project storage. Git records only the receipt manifest, file hashes, requirements and non-sensitive processing/acceptance summaries.

- 1 Put received files in access-controlled project storage.
- 2 Add one SUR-CTRL manifest row per file, including file_role, metadata and SHA-256.
- 3 Freeze the required RTKLIB settings, then run this processor; the four processing roles must occur exactly once.
- 4 Review RTKLIB outputs, complete independent checks and network adjustment, then add the controlled acceptance record.
- 5 Re-run; only the appointed survey authority's explicit record can close the authority gate.

Baghdad drainage and ground-design gate

Source: cities/catalogue/west-asia/iraq/baghdad/engineering/survey/drainage-ground-readiness.md

- Status: awaiting-drainage-ground-evidence
- Lines/stations: 9 / 164
- SWMM/ground technical screen passed: no
- OpenGeoSys required by received decision: no
- Authority accepted: no

The automated gate reruns the received SWMM model, checks continuity and hydraulic performance for normal/blockage/backwater scenarios, reconciles exact reviewed assets/supports, and checks numerical site comparisons for catalogue foundation/ground-treatment selections. It does not validate rainfall, flood levels, soil parameters, hydraulic boundaries, structural capacity, settlement predictions or construction suitability.

The drainage and geotechnical engineers of record, asset owner, relevant authority and information manager must accept the project inputs, calculations, selected variants, residual risks and immutable evidence record.

Current gates

- Missing technical roles: ground_model_readiness, route_station_fit_readiness, accepted_hydrology_basis, swmm_model, swmm_processing_report, geotechnical_ground_model, foundation_ground_schedule, ground_design_verification_report, groundwater_coupling_decision, civil_asset_register
- Duplicate roles: none
- Authority findings:
 - drainage/ground acceptance record not received

[Desktop soil inputs and route/station investigation priorities](#) are available. These do not replace the received geotechnical ground model.

Controlled workflow

Keep borehole logs, laboratory results, sensitive asset data, native calculations and large model results in controlled project storage. Git carries requirements, receipts, hashes, reproducible exchange inputs and non-sensitive summaries.

- 1 Accept the ground model, route fit, hydrology basis and geotechnical model.
- 2 Run the project SWMM model; retain its input, report, source hashes and continuity results.
- 3 Size a checked catalogue foundation or ground-treatment system for every line and station scope.
- 4 Record whether groundwater/coupled analysis is warranted; require OpenGeoSys evidence only when the reviewed triggers say yes.
- 5 Close residual risks and obtain the signed drainage/geotechnical acceptance record.

Baghdad field-evidence brief

Source: <cities/catalogue/west-asia/iraq/baghdad/engineering/survey/field-evidence-brief.md>

Deterministic pre-mobilisation requirements generated from the shared field-evidence template. It issues the information request; it does not claim that field data or approvals exist.

- Brief status: brief-issued-awaiting-signatures
- Mobilisation authorized: no
- Field evidence accepted: no
- Horizontal CRS: EPSG:32638 candidate UTM zone 38N; survey authority to confirm or replace
- Vertical datum: authority-to-confirm-before-mobilisation
- Canonical requirements: lib/templates/field-evidence.toml

The appointed survey authority, architect/engineer of record, operator and information manager approve this brief, responsibility matrix, CRS, vertical datum, accuracy schedule, access plan and data rights before field capture.

Required packages

ID	Dataset	Owner role	Delivery
SUR-CTRL	Primary and secondary survey control	appointed survey authority	RINEX plus field logs, adjustment report, coordinate schedule and signed control report
SUR-TOPO	Corridor and site topographic survey	survey delivery lead	GeoPackage 3D points/lines/polygons plus LandXML terrain and accepted PDF plans
SUR-UTIL	Above- and below-ground utilities	utility survey lead	GeoPackage 3D utility features, investigation records, photographs and confidence/quality attributes
SUR-LAND	Property, right-of-way and access constraints	client land and legal lead	GeoPackage boundaries/rights plus controlled title, consent and access register
SUR-FLOOD	Hydrology, flood and drainage evidence	drainage and flood lead	GeoPackage water/flood/outfall layers plus rainfall, level, model and authority records
GEO-GI	Ground investigation and laboratory testing	geotechnical engineer of record	AGS or equivalent structured logs, coordinates, samples/tests, factual report and interpretive design report
OPS-WORKSHOP	Existing workshop and depot capability audit	operator engineering lead	asset/capability register, measured layouts, utilities, photographs and gap assessment
OPS-FLEET	Existing fleet and operating interface audit	operator rolling-stock lead	fleet register, measured interface sheets, duty/condition records and migration constraints
SUR-IMAGE	Georeferenced photography and photogrammetry	reality-capture lead	source-image manifest and hashes, camera logs, GCP/check points, orthophoto/DSM and processing report
SUR-SCAN	Point-cloud and dimensional interface capture	reality-capture lead	E57/LAS/LAZ plus station setup, targets/control, registration and CloudCompare QA report
INF-GOV	Information ownership, security and acceptance	client information manager	responsibility matrix, naming/revision rules, common-data-environment plan, licence/consent register and acceptance record

Scope and acceptance

SUR-CTRL — Primary and secondary survey control

Stable primary/secondary monuments covering every corridor, station, depot, bridge, energy site and construction compound.

Provisional accuracy/quality requirement: Primary control ≤ 10 mm horizontal and ≤ 15 mm vertical expanded uncertainty; interface control ≤ 5 mm relative to accepted project control. Survey authority must approve or replace these project targets.

Acceptance evidence:

- approved projected CRS, epoch, units, geoid model and vertical datum
- instrument/antenna serials and calibration status
- redundant occupations and independent checks

- least-squares residuals, covariance/uncertainty and rejected-observation record
- signed monument descriptions and protection/inspection plan

SUR - TOP0 — Corridor and site topographic survey

Full corridor, station, depot, access, watercourse, road, structure, compound and lifting-route coverage with breaklines and feature coding.

Provisional accuracy/quality requirement: Hard-surface/detail points ≤ 25 mm horizontal and ≤ 20 mm vertical; general ground ≤ 50 mm. Survey authority must approve class-by-feature targets and check density.

Acceptance evidence:

- feature code and layer dictionary
- check-point residual report
- coverage/void map and inaccessible-area register
- capture date/epoch and change notes
- signed completeness review against route limits

SUR - UTIL — Above- and below-ground utilities

Electricity, telecoms, water, sewer, drainage, fuel, irrigation and unknown services within the works influence zone.

Provisional accuracy/quality requirement: Every feature carries horizontal/vertical uncertainty and detection/verification method; trial holes or records alone must not be silently treated as surveyed truth.

Acceptance evidence:

- records search and authority contacts
- detection method, equipment and calibration
- surface-feature correlation
- verification exposure/trial-hole schedule where design risk warrants
- unresolved and abandoned-service issue register

SUR - LAND — Property, right-of-way and access constraints

Ownership, occupation, easements, road reserve, temporary access, compounds, lifting routes and acquisition constraints.

Provisional accuracy/quality requirement: Boundary geometry remains indicative until reconciled to authoritative records and verified by the competent land authority.

Acceptance evidence:

- authoritative source and retrieval date
- boundary/status confidence
- owner/occupier and consent state
- temporary/permanent requirement
- dispute and encroachment register

SUR - FLOOD — Hydrology, flood and drainage evidence

Catchments, channels, historical levels, culverts, outfalls, tailwater, groundwater indicators and exceedance routes affecting the works.

Provisional accuracy/quality requirement: Levels use the accepted vertical datum; rainfall return periods and climate allowances require local authority confirmation.

Acceptance evidence:

- source dates and return periods
- surveyed channel/outfall/culvert levels
- historical event and community evidence

- blockage/tailwater assumptions
- authority-approved design storm and discharge constraints

GEO - GI — Ground investigation and laboratory testing

Boreholes, CPTu, test pits, groundwater monitoring and laboratory programme zoned for at-grade, elevated, station, depot and energy works.

Provisional accuracy/quality requirement: Investigation spacing/depth and tests are risk-based and approved by the geotechnical engineer after desk study and walkover.

Acceptance evidence:

- desk study, walkover and conceptual ground model
- location/elevation tied to accepted control
- factual logs and chain of custody
- strength, settlement, corrosivity and groundwater parameters with uncertainty
- signed geotechnical design recommendations and residual risks

OPS - WORKSHOP — Existing workshop and depot capability audit

Buildings, pits, cranes, lifting, machine tools, power, compressed air, fire systems, stores, access and workforce capability.

Provisional accuracy/quality requirement: Critical lifting, clearance and interface dimensions are measured to the tolerance required by the selected equipment supplier.

Acceptance evidence:

- asset identity, condition and certification
- measured capacity/clearance and utility availability
- repair/reuse/replace decision
- production and maintenance throughput
- operator-approved upgrade work packages

OPS - FLEET — Existing fleet and operating interface audit

Existing vehicles, gauges, couplers, wheel/rail, depot interfaces, rescue, operating rules and reusable components relevant to the pilot.

Provisional accuracy/quality requirement: Safety and physical interfaces use independently checked measurements and controlled vehicle/configuration identity.

Acceptance evidence:

- vehicle/configuration and maintenance history
- measured gauge/coupler/wheel/depot interfaces
- operating duty and failure records
- rescue/recovery constraints
- signed compatibility and migration decisions

SUR - IMAGE — Georeferenced photography and photogrammetry

Continuous corridor and detailed station/depot/structure/utility-context coverage, subject to permissions and privacy controls.

Provisional accuracy/quality requirement: Ground sampling distance and independent check-point limits are agreed by use case; neither EXIF position nor self-reported processing precision is acceptance evidence.

Acceptance evidence:

- capture plan, permissions and privacy controls
- camera/lens identity and calibration

- GCP versus independent check-point separation
- processing software/version/settings
- check-point residuals, voids, artefacts and obscuration map

SUR - SCAN — Point-cloud and dimensional interface capture

Complex structures, station/depot interfaces, constrained utilities and clearance-critical areas selected by the design team.

Provisional accuracy/quality requirement: Registration RMS is reported but not used alone; independent control/check residuals and local interface comparisons govern acceptance.

Acceptance evidence:

- scanner identity/calibration and setup log
- target/control schedule
- registration method and residuals
- independent check points and cloud-to-cloud sections
- density, range, noise, void and movement/change register

INF - GOV — Information ownership, security and acceptance

All raw and derived field information, personal/sensitive content, third-party records and authoritative project derivatives.

Provisional accuracy/quality requirement: Not applicable; this package governs provenance, access, revision, retention and authorized use.

Acceptance evidence:

- owner, producer, checker and accepting authority per dataset
- licence, reuse, publication and personal-data constraints
- file naming, metadata, revision and immutable hash rules
- backup, retention and access-control plan
- signed receipt/rejection/reissue workflow

Data handling and handoff

Keep raw survey, imagery, scan, utility and personal data in access-controlled project storage; Git contains requirements, manifests, hashes, accepted summaries and non-sensitive derivatives only.

Complete [survey-input-manifest.csv](#) for every delivery. Each accepted row must name the producer/checker, CRS and vertical datum, capture date, controlled project-storage path, SHA-256 digest and acceptance state. RTKLIB processing configurations/status/residual outputs, QGIS/CloudCompare/ODM settings and signed review records accompany their respective source data.

Baghdad surveyed-ground-model gate

Source: cities/catalogue/west-asia/Iraq/Baghdad/engineering/survey/ground-model-readiness.md

- Status: awaiting-ground-model-data
- Technical inspection completed: no
- Technical screen passed: no
- Survey authority accepted: no

Automated inspection checks file integrity, GeoPackage structure, independent-check residuals and processing-report completeness. It does not prove feature completeness, datum correctness or fitness for design.

Only the appointed survey authority and information manager can accept the master ground model after control, coverage, void, epoch, uncertainty, CRS and vertical-datum review.

Current gates

- Missing technical roles: control_acceptance_report, topographic_features, terrain_dtm, checkpoint_residuals, odm_processing_report, orthophoto, registered_point_cloud, cloudcompare_qa_report, void_register, master_ground_model
- Duplicate roles: none
- Missing authority-review roles: control_acceptance_report, topographic_features, terrain_dtm, checkpoint_residuals, odm_processing_report, orthophoto, registered_point_cloud, cloudcompare_qa_report, void_register, master_ground_model, ground_model_acceptance_record
- Authority-record findings:
 - ground-model acceptance record not received

Controlled workflow

Keep source imagery, raw scans and intermediate dense clouds in access-controlled project storage. Git records requirements, file hashes, non-sensitive QA summaries and accepted derivatives only.

- 1 Complete accepted survey control before registering terrain or clouds.
- 2 Process imagery in OpenDroneMap and registration/comparison in CloudCompare; preserve settings, source/output hashes and QA reports.
- 3 Build the federated master GeoPackage in the approved horizontal CRS and vertical datum.
- 4 Add every derivative to the shared receipt with its immutable hash and independent checker.
- 5 Run inspection, resolve residual/coverage findings, and obtain the controlled authority acceptance record.

Baghdad route and station fit gate

Source: cities/catalogue/west-asia/iraq/baghdad/engineering/survey/route-station-fit-readiness.md

- Status: awaiting-route-fit-evidence
- Lines: 9
- Stations: 164
- Technical screen passed: no
- Coordinated authority acceptance: no

The automated gate proves that every current line and station is covered by hash-locked, internally consistent route-fit evidence and that no unresolved critical/high issue is hidden. It does not determine land rights, utility position, flood risk, accessibility, traffic safety, lifting feasibility or possession sufficiency.

Only the relevant utility, land, drainage, highway, operations and design authorities can accept their evidence, followed by the engineer of record, operator and information manager accepting the coordinated route-fit record.

Current gates

- Missing technical roles: ground_model_readiness, surveyed_alignment_readiness, utility_coordination, land_access, flood_drainage, station_access, intercity_yard_integration, road_traffic_management, construction_logistics, possession_staging, route_fit_verification_report, route_fit_issue_register
- Duplicate roles: none
- Authority findings:
 - route-fit acceptance record not received

Controlled workflow

Store titles, personal data, utility-sensitive records, permits and native studies in the controlled project environment. Git carries requirements, empty receipts, immutable hashes and non-sensitive acceptance summaries.

- 1 Accept survey control, the ground model and every surveyed alignment.
- 2 Register checked utility, land, flood, station-access, yard/intercity, road, logistics and possession evidence.
- 3 Reconcile exactly one resolved result for every current line and station, with source hashes.
- 4 Close or formally transfer all high/critical issues in the controlled issue register.
- 5 Obtain the coordinated authority acceptance record against the immutable evidence hashes.

Baghdad structural-release gate

Source: cities/catalogue/west-asia/Iraq/Baghdad/engineering/survey/structural-release-readiness.md

- Status: awaiting-structural-evidence
- Lines: 9
- Technical screen passed: no
- Authority accepted: no

The automated gate checks actual solver output files and numerical limits, reviewed asset/support coverage, load-case/result reconciliation and independent-check completeness. It does not validate modelling assumptions, codes, loads, mesh quality, reinforcement, prestress, soil springs, fatigue detail, seismic response or structural safety.

Only the structural and geotechnical engineers of record, independent checker, asset owner and approving authority can release the project structures in a signed controlled record.

Current gates

- Missing technical roles: drainage_ground_readiness, structural_design_basis, structural_asset_schedule, load_case_register, opensees_model, opensees_report, calculix_input, calculix_report, structural_verification_report, independent_check_record, civil_asset_register
- Duplicate roles: none
- Authority findings:
 - structural acceptance record not received

Controlled workflow

- 1 Accept drainage/ground design and freeze the project structural basis and load combinations.
- 2 Schedule every span, pier, abutment, foundation and special structure against line chainage.
- 3 Preserve OpenSees global/seismic/soil-spring and CalculiX component input/output hashes and convergence evidence.
- 4 Reconcile foundation, wind, seismic, fatigue and bearing/movement results per scheduled asset.
- 5 Close independent-check comments and obtain the signed structural release.

Baghdad surveyed-alignment gate

Source: cities/catalogue/west-asia/iraq/baghdad/engineering/survey/surveyed-alignment-readiness.md

- Status: awaiting-surveyed-alignments
- Lines expected: line-1, line-2, line-3, line-4, line-5, line-6, line-7, line-8, line-9
- Technical screen passed: no
- Authority accepted: no

The automated gate proves receipt integrity, OSR-ALN hard-gate compliance, explicit horizontal/vertical/cant content, line and station reconciliation, deterministic LandXML re-import, and recorded interface tolerances. It does not establish that the survey, fit, clearances, possessions or construction design are correct.

Only the appointed alignment designer, survey authority, track engineer and information manager can accept an alignment for design use in a controlled signed record.

Current gates

- Missing technical roles: *:ground_model_readiness, *:interface_verification_report, line-1:surveyed_osr_aln, line-1:landxml_export, line-1:landxml_roundtrip_report, line-2:surveyed_osr_aln, line-2:landxml_export, line-2:landxml_roundtrip_report, line-3:surveyed_osr_aln, line-3:landxml_export, line-3:landxml_roundtrip_report, line-4:surveyed_osr_aln, line-4:landxml_export, line-4:landxml_roundtrip_report, line-5:surveyed_osr_aln, line-5:landxml_export, line-5:landxml_roundtrip_report, line-6:surveyed_osr_aln, line-6:landxml_export, line-6:landxml_roundtrip_report, line-7:surveyed_osr_aln, line-7:landxml_export, line-7:landxml_roundtrip_report, line-8:surveyed_osr_aln, line-8:landxml_export, line-8:landxml_roundtrip_report, line-9:surveyed_osr_aln, line-9:landxml_export, line-9:landxml_roundtrip_report
- Duplicate roles: none
- Authority findings:
 - alignment acceptance record not received

Controlled workflow

Keep signed source surveys, native authoring files and large point clouds in controlled project storage. Git carries the empty receipt, requirements, reproducible checks and non-sensitive accepted exchange derivatives.

- 1 Accept survey control and the surveyed ground model.
- 2 Fit each line in the confirmed CRS/datum; explicitly issue horizontal, vertical and cant schedules.
- 3 Export one OSR-ALN and LandXML file per line and record the deterministic re-import hash and comparison tolerances.
- 4 Reconcile every platform and record yard, turnout and clearance dispositions per line.
- 5 Run this inspection and obtain the controlled multi-discipline acceptance record.

Baghdad manufactured-viaduct comparison

Source: cities/catalogue/west-asia/iraq/baghdad/engineering/viaduct-comparison/README.md

Status: controlled planning package; no construction design, quotations or selected corridor.

Compare Pi20, Pi25 and constrained-access OSR-US for the same complete double-track scope. Supplier bids must include fabrication, transport, erection, temporary works, foundations, traffic management, connections, track/egress, checking and maintenance. No 30 m product is introduced.

The investigation candidate is line-9 chainage 66367.9–93067.1 m (26699.2 m), the longest current Pi25 run. It is not a surveyed or selected alignment. The separate 1,000 m comparison below includes both end supports; support ground zones and deep-element lengths are unknown.

Package	Bays	Supports	Bearings	Beam/segment lifts	Bare member kg	Installed USD/double-track m
Pi20-simple-span-link-slab	50	51	400	100	59950.0	Unpriced
Pi20-structural-continuity	50	51	252	100	59950.0	Unpriced
Pi25-simple-span-link-slab	40	41	320	80	74937.5	Unpriced
Pi25-structural-continuity	40	41	200	80	74937.5	Unpriced
US25-segmental	40	41	None	800	None	Unpriced

Pi25 has only 62.5 kg bare margin beneath 75 t; Pi20 has 50 kg beneath its 60 t product target. Complete member and hook masses remain unknown. Segmental concrete and support/bearing geometry require their own supplier design; Pi quantities are not transferred. The current OSR-US coordination envelope is 5.12 m wide, exceeding the primary 3 m shipping target. Shorter/lighter segments do not solve a width restriction without redesign or a reviewed oversize route.

Connections and quantities

A link slab can remove an expansion joint while simply supported girders retain their bearings. The shared-bearing scheme needs a structural connection and checked staged load path. A finite 40-span Pi25 corridor has 320 simple-span bearings versus 200 in the structural alternative. The periodic planning index also uses 320 versus 200, but its ten expansion gaps differ from the nine gaps between finite units. Both schemes need CWR/thermal/braking/seismic/foundation interaction, fatigue, replacement access and connection prices.

Under the existing index only, restoring simple-span bearings changes USD 9.748m/km to USD 10.198m/km: USD 117.066m as a uniform-rate illustration over all current elevation. This is an unadopted counterfactual before connection/end-effect/EPC costs, not a priced scope or a transfer of Pi bearings to segmental/special designs.

The [financed bearing sensitivity](#) applies only to 249.785 km of existing standard Pi25: USD 112.403m direct plus the existing incremental EPC rate once. Its capital is USD 7.799bn and terminal gap debt IQD 3.602tn. Monthly/six-month cash, debt/reserves/early repayment are recalculated under unchanged government and currency rules. Original civil invoice timing and origin shares are inherited assumptions, not supplier evidence; all consequential costs remain open.

Alignment and budget boundary

The register covers all 497 elevated segments, including 16 individual special reviews. It separates USD 2.536bn standard-rate allowance from USD 0.431bn routing penalty. Their sum reproduces the original model. A routing deterrent is not a priced structure; removing it is not a saving. Each special segment has wider-curve, station-move, right-of-way, segmental, land/utility, traffic and whole-life comparison fields. No alternative is accepted and original capital/debt figures are preserved.

The individual special reviews are ranked by existing penalty exposure to direct investigation effort, not by achieved savings. Approximate radius is recovered from the rounded routing multiplier; it is not a fitted/surveyed radius. The Pi20 chord screen shows where shortening alone still fails the existing catalogue allowance. Nearby station IDs support bounded station/right-of-way studies.

Special priority	Line/chainage m	Length m	Routing penalty USD m	Radius proxy m	Pi20 chord screen
1	line-9 26335.5–27430.0	1094.5	101.197	92.6	False
2	line-9 50996.0–51282.3	286.3	64.695	61.0	False
3	line-9 50811.2–50947.8	136.6	33.917	58.3	False
4	line-6 0.0–173.1	173.1	18.708	86.3	False
5	line-1 20148.4–20225.0	76.6	7.524	90.1	False
6	line-4 220.0–296.6	76.6	6.703	95.0	False
7	line-5 48.3–156.6	108.3	6.253	114.0	False

Special priority	Line/chainage m	Length m	Routing penalty USD m	Radius proxy m	P120 chord screen
8	line-1 10276.2–10364.5	88.3	6.032	106.0	False
9	line-1 3602.8–3651.1	48.3	4.745	90.1	False
10	line-2 12924.9–12973.2	48.3	4.393	93.3	False

A further 20% reduction in beam concrete changes the existing index by only USD 0.450m/km before any offsetting prestress, reinforcement or fabrication changes. No literature percentage is applied again.

Production, procurement and first article

[comparison.json](#) contains per-support foundation records, five complete-package quantity/rate forms, equipment-release fields, all eight production fronts and first-article hold points. [installed-cost-rfq.csv](#) retains invoice currency, origin, quote date and exclusions. Unknown costs remain null, not zero; partial totals cannot produce an installed price. IQD quotes stay IQD, with historical FX used only for reporting. Loan eligibility requires actual invoices and lender terms.

Measure casting, strength release, column/cap connections, transport, erection, closure curing, survey/tolerance correction, track/egress and acceptance in crew-hours per complete double-track bay. The rate is the slowest front, not the beam lift count. Parallel moulds and fronts, shifts, closures, 10–15-bay foundation/accepted-stock buffers and deck-supply loads require a resource-loaded programme and trials. The existing 48-hour casting planning cycle remains until the 24-hour target is physically qualified.

Issue competing ground-crane/portal and overhead-launcher bids for the same route. Include configured charts, pads/ground improvement, mobilisation, closures, launch/deck reactions and recovery. Use conventional prestressed concrete first; compare UHPC connections and special steel/composite crossings where measured whole-life resources justify them. Carbon percentages are not cost savings.

Build and measure the first beam and representative pier/cap/connection only after design release. Record accepted complete bays/week, labour, rejected/reworked pieces and installed cost. Supplier bids, boreholes, utilities, demand counts, actual production trials, signed checks and funding remain external work.

Review scope and evidence

The older review of 135e249e predates the integrated USD 7.679bn full-fleet sensitivity and its IQD 3.253tn terminal gap debt. Depot/workforce/site-energy reconciliation, supplier RFQ forms, opening-fleet replay, rental alternatives and clean-checkout bootstrap already exist in [delivery closure](#). This package closes repository comparison gaps; it does not replace supplier offers, measured demand or a complete delivery budget.

- [FHWA field-cast UHPC connections](#): Link slabs can join simple-span decks while independent bearings remain; highway precedent only (checked 2026-10-04).
- [FHWA prefabricated bridge selection framework](#): Compare access, supplier capability, connections and the complete installation system (checked 2026-10-04).
- [Chennai Metro construction methods](#): Precast substructure and advance investigation are precedents, not Iraqi production rates or quotations (checked 2026-10-04).

Baghdad retained under-viaduct rental portfolio — 2026-10-04

Source: cities/catalogue/west-asia/Iraq/Baghdad/engineering/viaduct-rentals/README.md

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

Rental income is a conditional addition to the existing station-development sale case, with different assets and external tenants. No site is commercially accepted, surveyed, leased or funded. [Network Rail's arch portfolio](#) provides a precedent for railway SME premises. [Places for London's guidance](#) emphasises access, services, insulation, fit-out responsibilities and permitted uses. These UK precedents do not establish Iraqi demand, prices or building permissions. Sources checked 4 October 2026.

Geometry, eligibility and pilot

The controlled design has 497 elevated civil segments totalling 260.1474 km, with median length 48 m. Each [register entry](#) carries its civil index, line/chainage, planning coordinates, existing parent track assets and nearest station. 0 segments lack a materialised parent track link and need asset-register reconciliation; no ID is invented. Coordinates interpolate the corridor and are not surveyed footprints. Clear height, frontage, ownership, title, utilities, permitted use and street/rail access remain null or unaccepted.

The reference screen excludes segments shorter than 75 m, reserves 10 m at each approach and counts complete 25 m planning bays. Each bay tests three independent 30 m² internal units, with 2 m protected support-end inspection zones and 1.2 m independent access. It suggests 873,810 m², before unknown road crossings, utility space, pier positions, access, ownership, flooding, station-sale overlap and fire exclusions. Confirmed eligible area is zero. Elevation alone never grants eligibility. Pier height is not usable clear height beneath a cap/deck.

The 200,000 m² illustration exceeds this screen by 0 m² and is unmapped-area-blocked, with no lease receipts in executable integrated cases. It requires a different surveyed footprint/reference layout; there is no automatic widening of a viaduct. Small/medium models allocate assumed area against identified civil segments and phase construction by their infrastructure dates. These are conditional surveys-to-test, not valuations. [Thirty draft pilot units](#) use one long candidate selected by station-chainage proximity and bay count, without a claim of commercial desirability. Market-test 20–50 units through comparable IQD rents, tenant interest, permissions and costed fit-outs before expansion. No external contact has been made.

Open reference unit and costs

[Unit plan](#) gives a 6 × 5 m internal module in a 6.4 × 5.4 m independent shell, requiring 3.2 m measured clear height. [Parts and allowances](#) total USD 21,000 equivalent per 30 m² unit: USD 18,000 direct, USD 2,000 design/shared services and USD 1,000 contingency, contracted in IQD. These are planning allowances, not quotes. Walls/roof, thermal/acoustic insulation, drainage, slab, independent foundations, doors/windows, separate metered/isolation services, fire/egress equipment, vehicle protection and removable inspection panels are included. Actual soil, materials, fire protection and service capacity may change cost materially. No structure is dimensioned from rental value alone; compare net value against costs before modifying supports or spans. Open licences remain intact.

The shell is independent of railway piers/caps/deck: no drilling, welding or load attachment. Preserve bearing/jacking, drainage and electrical access, surveyed support clearances and maintenance easements. Independent utility meters are paid directly by tenants in the model; no utility reimbursement is booked as extra profit. Retail, services and studios are candidate uses only; workshops, cooking, hot works, fuel/solvent storage and battery activities require specific assessments. There is no generic permission for a use because it fits the floor area.

Illustrations versus priced cash-flow scenarios

Area illustration	Lettable m²	Monthly rent USD eq/m²	Occupancy	Annual landlord NOI USD m eq
small	40,000	10	70%	2.52
medium	100,000	15	80%	10.80
large	200,000	20	85%	30.60

These illustrations deduct 25% of occupied receipts and exclude capital, financing and tax. For the medium illustration, 30 annual receipts, first at month 48, rising 5% each year, discounted at 13.4%, have PV USD 79.405m. Explicit payment dates matter: this is receipts-only PV, not project NPV or the phased portfolio forecast.

Executable rental scenario	Status	Fit-out capital USD m eq	First conditional cash month	Resource NPV before tax USD m eq	Standalone after-tax NPV USD m eq
small	conditional-unverified-retained-portfolio	33.646	43	-5.624	-6.989
medium	conditional-unverified-retained-portfolio	87.523	43	19.166	11.924
large	conditional-unverified-retained-portfolio	180.062	43	98.180	75.736
medium_downside	conditional-unverified-retained-portfolio	87.523	55	-38.539	-39.058

Monthly ledgers phase fit-outs after the corresponding infrastructure-completion month and delay tenant handover until railway opening or fit-out completion, whichever is later. Six-month enclosures, three initial rent-free months and an 18-month occupancy ramp precede steady receipts. The last fractional module is constructed in full; spare floor area receives no rent. Rent and OPEX escalate 5% from financial close, and unquoted capital escalates 5% to each invoice. The downside uses rent USD 9/m², 55% target occupancy, 12 extra months of vacancy, a 36-month ramp, 8% arrears and 7% OPEX inflation.

Market vacancy is separate from modeled tenant turnover (10%/year, three-month re-letting vacancy and one-month free concession). Three-percent arrears have 50% recovery after six months; unrecovered debt is written off, and final unresolved receivables have zero recoverable value. Revenue is cash collected in these pro-forma sensitivity accounts; statutory accrual/tax treatment needs advice. Occupied maintenance/insurance uses 25% of reference occupied face rent with its own OPEX index, including during rent-free concessions, plus USD 10/m²/year for vacant-unit maintenance/insurance. Costs persist through concessions or defaults. Major refurbishment is additional cash expense at 20% of reference fit-out every 12 years, with OPEX inflation; it is not also capitalised. Existing station kiosk receipts are unchanged.

Security deposits of two months' indexed face rent are assumed topped up/refunded with occupancy. They are separately restricted cash and tenant liabilities, with zero revenue, zero construction funding and no shareholder distribution. Ending leases refund all deposits. No upfront lease premium or sold rental parcel is booked. Parcel overlap with the existing 15 station sale candidates is unknown and must be accepted as disjoint before either case can become executable. Current site-right cash is explicitly assumed zero, with additional land opportunity cost unknown: full site economics cannot be concluded from the reported before-land NPV. No USD credit or additional government cash is assumed for fit-outs.

Assets depreciate over 20 years from each cohort handover. Standalone tax applies the illustrative 15% positive annual cash-profit-after-depreciation proxy, with no loss relief or interest deductions, paid the next month; it is not an Iraqi tax ruling. The holding model instead includes the same portfolio inside its separate-business tax stress, so standalone tax is not deducted twice. The project horizon caps late cohorts' rental years and leaves no unsupported terminal sale/rent beyond the railway forecast. These cases improve only to the extent that collected rent exceeds all additional resources and costs.

Financing, dividends and terminal cash

[Financing redesign](#) adds a separately financed retained-property entity with 25% private partner fit-out equity and IQD construction bank debt. Its operating-gap capacity is zero; missing carry/fees/reserves are exposed rather than adding an uncommitted facility to the existing 13tn cap. Internal distributions are zero pending lender consent. External tenant cash adds group revenue; future property-to-rail transfers would cancel exactly. The [holding-equity study](#) uses the same resources with a 100%-owned business, replacing partner equity with the parent subscription case and borrowing the residual in IQD. These are alternative ownership/funding structures, not cumulative sources.

The holding study separately compares all-debt-repaid dividends with an unapproved coverage/reserve/profit-based policy, and reports a diagnostic of proportional final unrestricted cash net of liabilities. Cash at the horizon is not a guaranteed redemption, quoted share price or assumed sale of railway/property assets. Do not confuse that diagnostic with actual company distributions or count cash twice. Company accounts remain separately reconciled.

Digital twin, common hazards and evidence

Every draft pilot unit links its civil segment/parent track, proposed enclosure design, unknown lease and tenant IDs, meters, isolation, inspection rights, permitted use and [hazard records](#). The [native ERP mapping](#) uses existing Asset/Contract/Customer/Sales Invoice/Payment Entry/Asset Maintenance/Issue types when actual records and permissions exist; null IDs are not live leases, meters or safety records. No fake tenant, permit, contract or asset is created from an unverified footprint.

Tenant fire, flooding/drainage, delivery impact, blocked inspection access and utility/attachment faults propagate from enclosure to pier/foundation, bearings and shared spans and can affect railway operations. Redundant onboard controllers provide no mitigation for these common physical hazards. Proposed inspections include pre-lease engineering acceptance, monthly access/drain/isolation checks, post-incident checks, annual structure-linked inspection and controlled jacking/maintenance closures; durations and legal/fire requirements need actual assessment. Native maintenance/Issue records must trace the landlord obligation to the railway asset and escalation owner. Occupancy and any railway restriction

require the authorised engineer's decision, not automatic evidence acceptance by this model.

[Six 90-day evidence packages](#) require surveyed eligibility and rights/no-overlap, independent civil/fire/utility access acceptance, market-tested pilot leases, supplier fit-out/refurbishment quotes, native lease/meter/maintenance controls, and independent cash/tax/funding/distribution review. Named people, surveys, quotes and leases remain pending. Native ERP Task imports are open drafts; no evidence or operating release is granted.

Regenerate `.venv/bin/python tools/automation/baghdad_viaduct_rentals.py`, then financing redesign, equity and proposal; validate source/output hashes with `--check`.

Baghdad Acceptance And Accreditation Evidence Basis

Source: <cities/catalogue/west-asia/Iraq/Baghdad/operations/acceptance-evidence-report.md>

This report is the generated evidence basis for acceptance, trial-running readiness, and accreditation review. It is not itself an approval or certificate; it is the traceability index that shows which assets, manufacturing packages, BOM/material refs, QA hold points, evidence records, release authorities, and predecessor controls must be closed.

Summary

Item	Count / Status
Assets in register	1,680
Manufacturing schedule rows	7,311
Manufacturing material/BOM rows	14,323
Manufacturing QA verification rows	7,311
Construction QA action rows	6,098
Maintenance handover schedule rows	9,804
Manufacturing rows with material refs	7,311 / 7,311
Manufacturing rows with verification refs	7,311 / 7,311
Manufacturing rows linked to QA actions	7,311 / 7,311
Unresolved external predecessors	0

Material / BOM Basis

Source	Rows
project_kit	14,323

Rolling-stock rows link to the generated rolling-stock BOM and COTS fit-out BOM. Infrastructure rows use controlled `project_kit : *` refs until detailed civil/station/energy BOMs are added.

QA Gate Coverage

QA gate	Verification rows
qa-00-design-freeze	1
qa-10-carbody-structure	2,286
qa-11-bogie-wheelset	762
qa-12-traction-brake-battery	762
qa-13-passenger-systems	762
qa-15-first-article-trainset	762
qa-20-survey-geotech	155
qa-21-earthworks-drainage	155
qa-22-trackform-rail	417
qa-24-stations-depots-plant	330
qa-25-power-energy	281
qa-26-wayside-comms-safety	638

Acceptance Control Logic

- Every manufacturing package has a controlled material/BOM row set.
- Every manufacturing package has a QA verification row.
- Every verification row links to a generated QA action by `qa_uid`.
- Resolved predecessor ids are generated for schedule blocking.
- The portal blocks successor manufacturing work until predecessor work orders are closed with pass evidence.
- The portal blocks manufacturing closeout until the selected work order has pass evidence.
- Failed evidence creates a defect/NCR and puts the work order on hold.
- SQLite-backed Ops Core stores work orders, inspections, defects/NCR, and audit records for handover.

Remaining External Release Gates

This generated evidence basis organizes acceptance work, but it does not close release gates that require independent review, field data, hardware bring-up, supplier freeze, first-article tests, or authority acceptance. The open gates remain:

Gate family	Still required before accreditation / revenue release
Independent safety assessment and residual risk	Named ISA/assessor review, action log, residual-risk acceptance, and deployment-specific ALARP/tolerability decision.
Formal safety integration	Consensus refinement proof from TLA+ to implementation behavior, plus signed safety-log integration tests for forged, replayed, stale, and unknown-issuer entries.
Pilot hardware evidence	Exact COTS BOM freeze, wiring/harness maps, enclosure/mounting, power/thermal margins, SD image checksums, self-test logs, bench/safety evidence, and commissioning records for T-ECU/S, T-ECU/A, T-OBS, W-SBC, and S-SBC.
Rolling-stock production release	Supplier envelope freeze, EN structural/FEA reports, weld/WPS/NDT packages, manufacturing drawings, flat patterns/NC output, harness routing, weight/balance, first-car build hold point, and first-article inspection.
Field validation	Obstacle/intrusion sensor calibration and representative hot-weather, dust/soiling, night, and rain datasets with false-positive/false-negative analysis.
Charging and site energy	Site-specific solar yield, grid interconnect, charger thermal study, protection settings, utility approval, and train charging interface tests.
Operations validation	Operator workshops, translated/deployment rulebook where needed, competence records, emergency exercises, maintenance access trials, and trial-running records.

Those items are tracked in the [certification release gap register](#), [control-electronics release checklist](#), and [rolling-stock v2 release checklist](#). The acceptance matrix should be treated as the evidence index that collects those closures, not as the closure itself.

Review Artifacts

- Tracked compact asset register: [baghdad-assets.csv](#)
- Tracked operations manifest: [baghdad-operations-manifest.json](#)

The following high-volume files are regenerated in the local city package and intentionally excluded from Git. Their names are recorded for handover without presenting unavailable GitHub links:

- [baghdad-operations.json.gz](#)
- [baghdad-acceptance-evidence-matrix.csv](#)
- [baghdad-manufacturing-schedule.csv](#)
- [baghdad-manufacturing-materials.csv](#)
- [baghdad-manufacturing-verification.csv](#)
- [baghdad-qa-register.csv](#)
- [baghdad-maintenance-schedule.csv](#)

Accreditation Use

The evidence matrix can be filtered by asset, package, QA gate, release authority, or material source. During acceptance, each row should be matched to completed Ops Core evidence, defects/NCR status, and the release authority signoff before the related asset is accepted into trial running or passenger operation.

Baghdad-only funding programme

Source: <cities/catalogue/west-asia/Iraq/IRAQ-FUNDING-PROGRAMME.md>

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

Scope: [Baghdad](#) and one manufacturing plant sized for Baghdad. Samawah, Mosul and every other city are excluded. All funding is proposed and uncommitted.

Independent reconciliation, priced gap finance and six-month tranches

Capital sources still total USD 7,515.079m. The independent pooled-cash reconstruction requires USD 5,962.665m of gross extra cash and retains USD 3,662.282m later, leaving a USD 2,300.383m nominal net deficit before pricing additional gap finance. These three amounts answer different questions. The original capital principal is repaid in the lifetime cash ledger, not added to CAPEX a second time. City EPC is now spread over direct works; the initial baseline-freeze task no longer receives the full programme overhead allowance.

[Detailed arithmetic and Iraqi financing routes](#) · [six-month reference bond/loan requirements](#) · [six-month blended candidate independent calculation](#).

Green debt replaces qualified conventional borrowing; grants replace domestic capital debt; guarantees supply credit enhancement rather than cash. The new sensitivity charges supplemental IQD funding for interest and fees, sweeps later surplus to repayment, and exposes cash beyond its illustrative IQD 13tn cap and any unpaid terminal loan. The earlier gross cash-support figures below assume external contributions; they are not a priced bridge-loan requirement.

Priced gap-finance sensitivity	Gross gap draws, IQD tn	Uncovered cash, IQD tn	Unpaid terminal loan, IQD tn
unfunded reference	0.000	7.751	0.000
green label only	0.000	7.751	0.000
zero cost liquidity bound	7.751	0.000	2.990
commercial gap credit	13.000	17.914	13.000
concessional gap credit	9.950	0.000	7.934
blended candidate	7.959	0.000	5.091
green concessional only	9.085	0.000	7.363
fare 5pct flat costs fixed demand	3.357	0.000	0.000
fare 5pct flat costs elastic	4.017	0.000	0.000
fixed fare 5pct opex	13.170	9.741	13.000
fare 5pct opex 5pct	4.430	0.000	0.000
fare 5pct opex 7pct	5.957	0.000	0.000
fare 5pct opex 5pct income 2pct	5.613	0.000	0.000
variable fare 5pct opex 5pct	4.202	0.000	0.000
fare 5pct opex 5pct rents indexed	4.245	0.000	0.000

The candidate mix is uncommitted: eligible IQD green bonds at an assumed 4% plus enhancement fees; USD 25m equivalent climate capital grant; USD 300m equivalent net development-rights proceeds; and USD 25m equivalent annual new net local receipts at full opening. The grant, valuation, legal powers and IQD concessional facility need evidence. Existing rents/fare receipts cannot be counted again. With constant nominal fares and OPEX, a terminal unpaid loan means that sensitivity has not achieved self-financing.

Additional pricing and OPEX inflation sensitivities

The requested paired sensitivity increases fares and OPEX 5% annually from financial close, while testing income growth separately. At 5% income growth and assumed -0.30 real-price elasticity, the illustrative blended case peaks at IQD 4.256tn supplemental debt and ends with IQD 0.000tn unpaid. This can repay the priced facility under the assumptions, but still requires placed early financing, the candidate grant/rights receipts, fixed nominal debt terms and income growth. It is not a committed funding outcome.

Average nominal tickets move from IQD 1,525 at first opening to IQD 1,765 at full opening; 44 trips remain 11.7% of the indexed income proxy when incomes grow 5%. Separate cases test 2% income growth, 7% OPEX inflation, peak/off-peak tiers, fixed demand, and rental indexation. Capital escalation and future FX changes remain outside these sensitivities.

[Paired 5% six-month financing](#) · [monthly tickets and affordability](#) · [variable-ticket six-month financing](#). The detailed report contains the NPV, all assumptions and downside cases.

Surplus cash and early repayment

These cases use identical paired 5% fare/OPEX/income assumptions and the same conditional blended capital sources. Each pays OPEX, scheduled principal, interest and fees, then funds the debt-service reserve and a three-month current-OPEX buffer before voluntary repayment. Borrowed gap proceeds and uncovered external cash cannot fund early payments. The extra buffer remains cash held at the terminal horizon and earns no interest.

Compare strategies against buffered gap-only, rather than attributing the buffer change to repayment savings. Loans-first pays bank credit, Chinese credit and gap credit before bonds. Cost priority pays bank (9%), ordinary bonds (8%), Chinese credit (5%), green bonds (4% plus 0.5% annual guarantee), then gap credit (2%). It is an interest-rate heuristic, not a proof of the globally best strategy.

Surplus strategy	All debt cleared, month from close	Finance cost saving vs buffered gap-only, USD equivalent m	Early-payment premiums, USD equivalent m	Peak gap debt, IQD tn	Terminal unrestricted cash, IQD tn
gap only buffered	365	0.000	0.000	4.418	14.870
gap then core	306	9.839	1.572	4.418	14.883
loans then bonds	305	81.916	6.310	4.372	14.976
cost priority	303	168.132	21.169	4.371	15.088
cost priority zero premium	303	195.771	0.000	4.368	15.124
cost priority noncallable bonds	365	71.442	4.683	4.372	14.963


Cost priority clears all debt in month 303, compared with 365 for buffered gap-only. Net nominal financing savings are USD 168.132m equivalent, after USD 21.169m assumed early-payment premiums. Savings include core interest, annual green guarantee charges and supplemental interest/draw fees; they exclude principal, which is returned once. All cases retain IQD 0.362tn operating buffer separately from unrestricted cash. There is no additional government contribution above 25% of CAPEX in these cases.

Assumed premiums are 1% of bank/Chinese/green principal and 2% of ordinary bond principal. A minimum draw age of 6 months (bank), 12 (Chinese) and 24 (both bonds) prevents immediate issue-and-redemption. Eligible vintages are repaid oldest first; contractual instalments are kept and maturity shortens. Notice, issuer call rights, investor consent, buyback price, remaining-maturity compensation, tax and FX require actual agreements. Noncallable-bond sensitivity makes no voluntary bond payments; zero-premium sensitivity removes only the assumed premium, retaining minimum ages.

Facility	Buffered gap-only final principal payment month	Cost-priority final principal payment month	Early principal, native currency	Premium, native currency
bank credit	161	161	IQD 179.993bn	IQD 1.800bn
domestic bonds	281	230	IQD 853.131bn	IQD 17.063bn
chinese export credit	305	235	USD 239.631m	USD 2.396m
green bonds	365	244	IQD 554.236bn	IQD 5.542bn

The gap facility's final principal payment is in month 303. Later surplus remains unrestricted cash after debt retirement. Each month's native debt balance equals prior balance plus draws minus scheduled and early principal. Each six-month closing balance is its final month's balance; payments, premiums, interest and reserve movements are period sums. Contractual repayment windows in tranche files describe the original draw terms; the actual final-payment months above incorporate early repayment.

[Monthly cost-priority repayments](#) · [six-month repayment tranches](#) · [loans-first tranches](#) · [all six complete calculations](#)

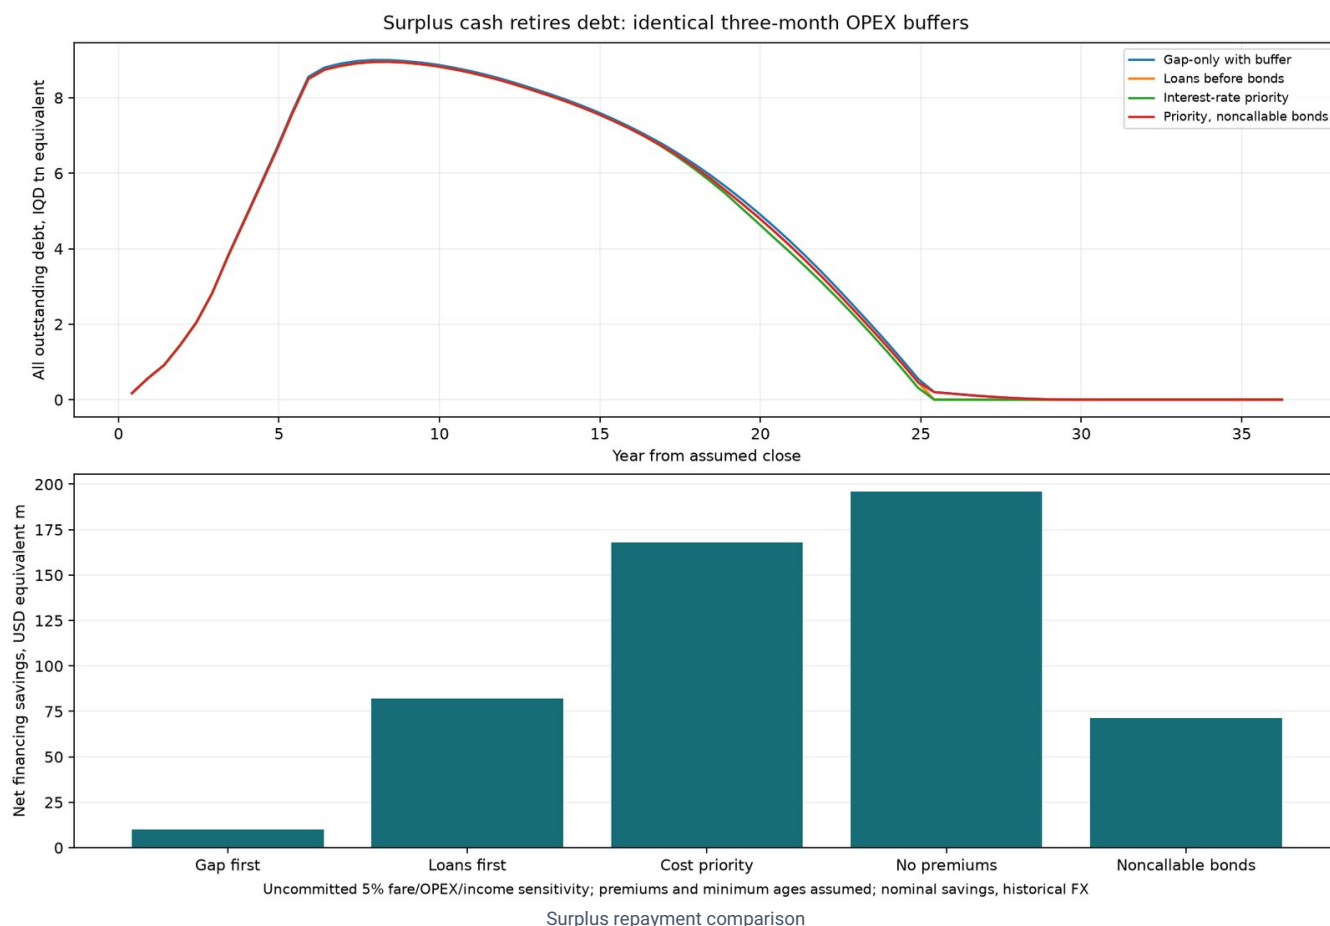

Loan prepayment can carry redeployment/unwind charges: the [World Bank Treasury FAQ](#) illustrates the concept, without establishing Chinese or Iraqi loan terms. The [US Treasury buyback FAQ](#) and [published purchase results](#) illustrate issuer authority and priced buybacks rather than automatic par redemption; they do not supply an Iraqi legal mandate.

This repayment allocation does not change the unlevered project NPV or validate demand. Nominal savings over several decades are not present-value gains. CAPEX escalation, FX, lifecycle replacement, floating-rate risk and the uncommitted early funding still require appraisal.


Consolidated sources and uses

Government contributes 25% of total capital uses, including the plant and EPC. Imported purchases are split 50% government USD cash and 50% proposed Chinese USD credit, assuming the full imported basket can qualify. That USD government cash is inside the 25% total contribution; the rest of the government contribution is IQD. The remaining balance after those two sources is split 75% domestic IQD bonds and 25% IQD bank term credit.

Proposed capital source	Currency	Native amount, billions	USD equivalent, million	Share of total capital
chinese export credit	USD	0.842	842.17	11.21%
government import cash	USD	0.842	842.17	11.21%
government local cash	IQD	1,347.579	1,036.60	13.79%
domestic bonds	IQD	4,674.285	3,595.60	47.85%
bank credit	IQD	1,558.095	1,198.53	15.95%
Total capital uses	Mixed	—	7,515.08	100%

Baghdad city CAPEX is USD 7,168.53 million. The plant is counted once at USD 323.87 million plus USD 22.67 million EPC. Its sizing basis is 4,572 vehicle/car modules from Baghdad's controlled fleet and car count. Imported tooling receives proposed Chinese credit within that plant budget. The physical cell/floor/tooling envelope replaces the smaller module allowance where necessary; both remain unquoted engineering assumptions.

Currency and USD capital intensity

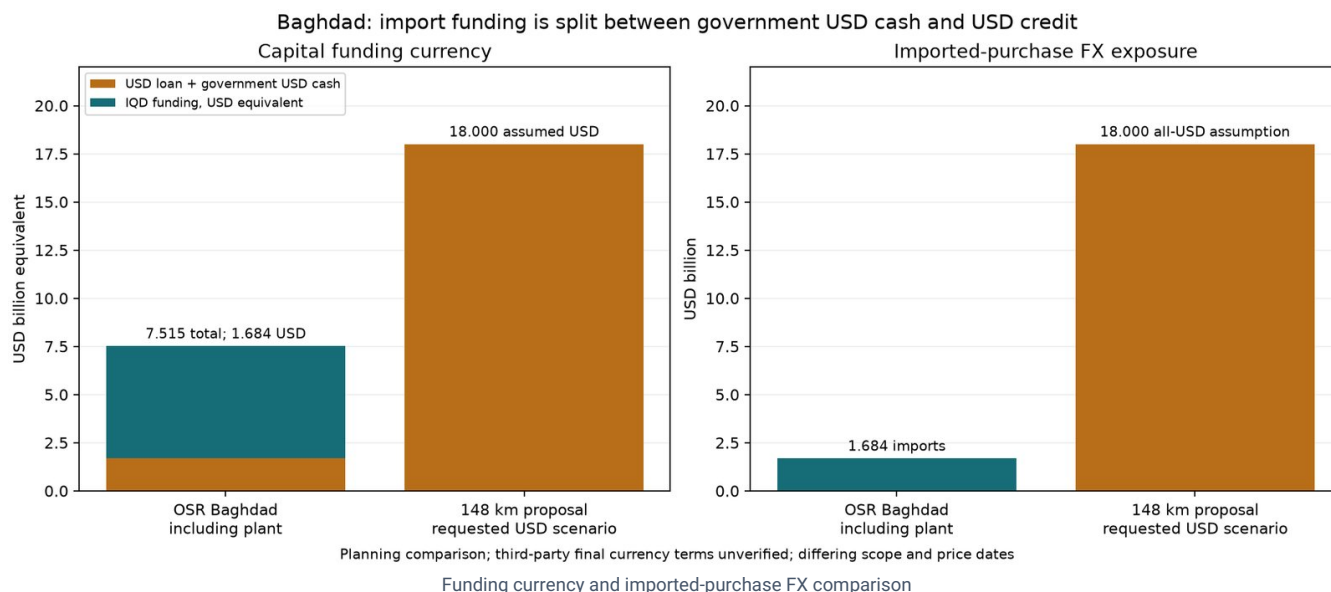

Only Chinese credit is USD-denominated debt: USD 842.17 million. Government additionally provides USD 842.17 million cash for imports. Combined USD capital funding is 22.41% of uses; the remaining 77.59% is IQD government cash, IQD bonds and IQD bank credit. Revenue and local OPEX are also budgeted in IQD. At the historical planning conversion of 1,300 IQD/USD, the local government cash allowance is IQD 1.348 trillion, alongside its separate USD import cash. Together they equal 25% of total capital. USD columns are comparison equivalents, not a requirement to borrow or appropriate those domestic amounts in dollars.

Funding currency and procurement currency differ. Estimated imported purchases total USD 1,684.34 million (22.41% of capital), including plant imports. The government supplies half directly in USD cash; proposed Chinese credit supplies half as USD debt. The full import pool, including categories beyond the initially selected solar, bogies, batteries, windows, doors and tooling, is assumed lender-eligible pending origin qualification. If that expanded basket cannot qualify, its loan funding is uncovered; it is not automatically replaced by IQD bank credit or another grant. IQD borrowing reduces the revenue/debt currency mismatch; it does not remove Chinese debt-service FX risk, imported maintenance costs, domestic interest, inflation or placement constraints.

Eligibility sensitivity: the original named-component categories cover USD 799.28 million of invoices. At a 50% advance, they alone support USD 399.64 million of proposed credit. If the additional imported categories cannot qualify, USD 442.53 million of planned capital loan proceeds remains uncovered, in addition to the base support requirement below. Even the original categories remain unqualified; this screen is not a lender approval. No extra government contribution is assumed to replace that missing loan.

What the 25% government limit leaves unfunded

The 25% capital contribution is USD 1,878.77 million. If that is also the limit on all public cash, the model leaves USD 6,309.57 million of additional funding requirements across the full construction, operating and debt horizon. These are interest, fees, reserve and operating/debt cash needs after modelled revenue; they are not additional approved government contributions.

Peak annual capital contribution is USD 397.77 million. Peak annual additional funding requirement is USD 956.55 million. If all additional support were provided publicly, conditional lifetime public cash would be USD 8,188.34 million, with a combined annual peak of USD 977.58 million. This exceeds the requested contribution and is shown only to expose the funding gap.

Across the 36.5-year nominal model horizon, additional requirements divide into USD 1,697.19 million before Baghdad's full-network opening, USD 4,159.06 million during Baghdad operations/debt tail, and USD 453.31 million for plant capital financing. Principal repayment before opening is part of the pre-opening requirement. This base withholds all fares until full-network completion; the separate phased sensitivity below tests earlier revenue. Gross additional support is a liquidity requirement over time, not net lifetime loss: later retained cash cannot repay earlier obligations without an approved bridge.

The programme CSVs distinguish the capped capital contribution, additional funding requirement and conditional payment requirements. Underlying city and factory ledgers calculate the support needed to pay scheduled obligations; their positive reserve balances and completed repayments are conditional on that support being raised. They are not a cash-solvent forecast under the public cash cap. No bridge, equity investor, rollover or extra appropriation is invented to close the gap.

Cash and contractual structure

- 1 An Iraqi public sponsor seeks MoF authority for proposed sovereign IQD bonds through the established MoF/CBI issuance route, subject to legal review and placement. Municipal borrowing powers are not assumed. The 25% limit is the direct capital contribution, not a limit on sovereign bond liabilities, guarantees or lifetime public exposure.
- 2 Chinese export buyer credit is allocated to qualified Chinese invoices for solar equipment, bogies, batteries, windows, doors and Baghdad plant tooling. The requested 50% loan advance is matched by 50% government USD cash. All other imported categories also require Chinese supplier-origin and lender qualification before the full-basket financing assumption is valid. Noneligible imports still need foreign currency. Eligibility and origin require supplier evidence.
- 3 Government's 25% capital contribution covers the planned eligible downpayment; bonds and bank credit cover the remaining capital balance. Fees, construction interest and reserve funding are separate cash requirements, not silently capitalised or counted as capital-source proceeds.
- 4 Each draw starts its own grace and repayment clock. Planned receipts match procurement milestones; no actual payment or lender commitment is asserted. Chinese credit uses USD, bonds and bank credit IQD. Terms remain unconfirmed appraisal assumptions: 5%/48-month grace/180-month repayment, 8%/24/180, and 9%/0/84 respectively.
- 5 Revenue pays OPEX first and debt service next; subsidy is excluded from DSCR. Additional support shown by the city and plant models is an unfunded requirement under the cap. The factory model covers capital financing only; manufacturing income and factory OPEX need a separate business case.
- 6 Declined Chinese finance, delayed contributions, FX changes and bullet redemption are separately tested in the Baghdad appraisal. None creates an automatic facility or refinancing source.

Rollout and financial close

Baghdad's current capital milestones span 78 calendar months. Full-network fare revenue begins after all budget milestones. Lowering the capital grant increases borrowing and cash-service needs; it does not shorten this schedule. The city-sized Baghdad plant becomes available after 390 working days (18 months from NTP), followed by the separately scheduled first-article series-release gate. The separate phased sensitivity uses this integrated planning schedule; actual plant and line acceptance and a commissioned operating baseline remain pending.

Required before financial close: approved sponsor and borrowing powers; appropriation limited to the agreed government contribution; a funded solution for the additional cash gap; supplier quotations and origin evidence; signed term sheets, guarantees and insurance; IQD placement/redemption plan; lender draw windows and FX access; surveyed demand/fare policy; tax, duty, land and utility pricing; accepted resource calendar and reserve covenants.

Model and evidence

[Programme monthly cashflow](#) · [annual cashflow](#) · [machine-readable programme](#) · [Baghdad city appraisal](#) · [editable assumptions](#). Other Iraqi city appraisals remain standalone examples outside this programme.


[IMF 2025 Article IV](#) supplies the historical 2024 FX anchor, not a current dealing rate. [CBI fiscal-agent description](#) and [Injaz issue example](#) support sovereign-bond context. [China Exim export buyer credit](#) supports the instrument concept; numeric terms and eligibility are unconfirmed assumptions.

Recalculation: conditional phased opening

The earlier USD 9.890 billion result combined whole-fleet stage batching, no fares before the final capital payment and reserve deposits always funded with additional public cash. Ready-task dispatch now pipelines work within the same resource limits, gates train production on the new plant, and funds reserves from available project cash before seeking support. The full-network-only result above remains a conservative comparator.

With line openings tied to completed line and shared/depot work plus a 3-month commissioning allowance, first revenue begins in month 40, and all nine lines operate from month 76 after financial close. These dates are conditional planning milestones, not authorisation to run trains.

Each line's controlled trainset share allocates revenue and variable OPEX; its own 50% / 75% / 100% ramp applies. From first opening, 25% of full-network OPEX is fixed and 75% scales with opened fleet. This proxy can misstate early demand, central staffing and transfer benefits; a surveyed phase-specific operating plan is required. The same nominal fares, capital total, debt terms and 25% grant apply in every case.

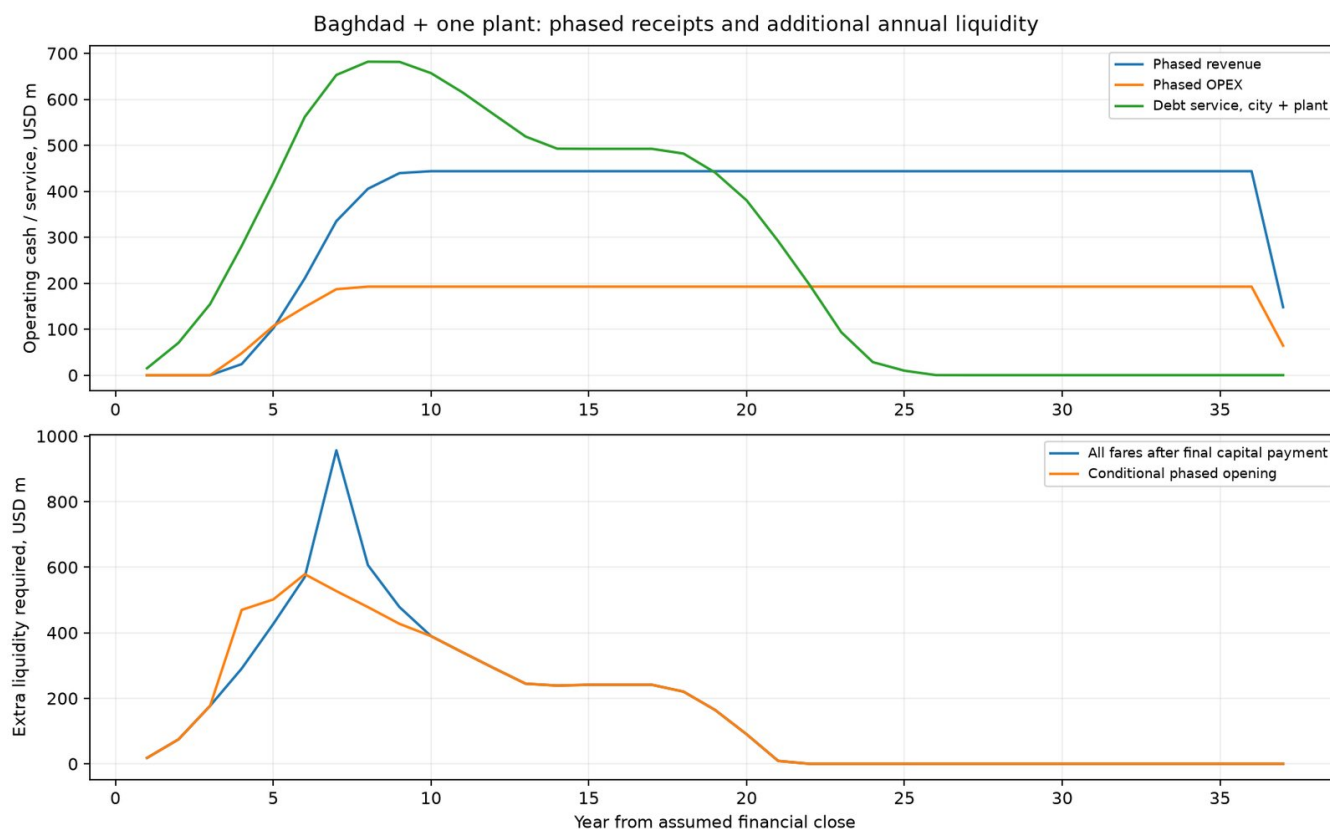

Conditional nominal planning flows; 25% capital grant excluded from extra liquidity; opening and funding uncommitted

Phased operating cash and additional liquidity

Opening / demand scenario	Additional funding beyond 25% capital, USD bn	Conditional lifetime public cash, USD bn
All fares after final capital payment	6.310	8.188
Phased: commissioning delay two years	6.465	8.344
Phased: demand minus 40 percent	8.759	10.638
Phased: low demand	5.963	7.842

Line	Planned opening month	Fleet / variable-cost share
line-1	40	11.29%
line-2	45	13.25%
line-3	50	12.73%
line-4	55	10.50%
line-5	59	11.29%
line-6	65	13.12%
line-7	69	10.37%
line-8	74	11.81%
line-9	76	5.64%

All these are gross nominal liquidity contributions, conditional on funding. Later operating surplus is retained and is not netted against earlier required injections. The phased city ledger ends with USD 3.662 billion of unrestricted cash; no distribution or return to the sponsor is assumed. The plant ledger has no manufacturing income/OPEX: it remains a capital-financing allowance. A 25% direct grant also does not cap sovereign IQD bond liabilities or guarantees.

[Phased programme monthly cashflow](#) · [phased programme annual cashflow](#)

Comparison with the historical 148 km third-party proposal

The [July 2024 report](#), citing the prime minister's adviser, gives USD 18 billion, 148 km, seven lines and 64 stations. The [NIC procurement notice](#) describes DBOMFT and requires bidders to submit a funding plan. Neither establishes a final all-USD financing contract. The 100% USD foreign-loan/government-cash comparator below is the user's requested scenario, not a verified split of debt and grants. The older USD estimate has not been restated to a common price date.

Measure	Current OpenSourceRail Baghdad plan	Historical proposal / requested USD scenario
Route km (not track km)	474.2	148
Lines / stations	9 / 164	7 / 64
Capital uses, USD equivalent bn	7.515, including one plant	18.000, reported estimate
Capital intensity, USD equivalent m / route km	15.85	121.62

Measure	Current OpenSourceRail Baghdad plan	Historical proposal / requested USD scenario
USD-denominated capital funding, USD bn	1.684, half loan / half government cash	18.000, assumed USD cash + loans
IQD-denominated capital funding, IQD tn	7.580	Zero in requested scenario
Imported-purchase FX exposure, USD bn	1.684	18.000 only under all-USD purchase assumption
USD purchase intensity, USD m / route km	3.55	121.62 under that assumption
Contracted fares / debt terms	Planning fare and uncommitted facilities	Not established by these sources

The OSR plan has 3.20 times the route length and 2.56 times the stations. Its planning capital estimate is 58.2% below USD 18 billion. Under the requested all-USD funding scenario, USD-denominated capital funding is 90.6% lower; under an all-USD purchase scenario, imported-purchase exposure is 90.6% lower. These measure different exposures and are not interchangeable debt-service savings.

The planning comparison is not a like-for-like qualified bid: route geometry, tunnelling/structures, land, utilities, taxes/duties, contingency, escalation, supplier qualification and acceptance maturity differ or remain unresolved. The older report's four-year completion expectation also differs substantially from OSR's current 78-month capital schedule. A lower capital estimate does not establish an earlier or more sustainable delivered service.

Fares, population access and financial sustainability

The modelled average paid-trip fare is IQD 1,317 (USD 1.01 comparison equivalent), denominated in IQD rather than automatically indexed to the USD loan. It derives from the retained USD 380/month income proxy, equivalent to IQD 494,000/month at the planning anchor. Thirty paid trips consume 8.0% of that proxy income; 44 commuter trips cost IQD 57,963, or 11.7%. This is an average-trip yield assumption, not an adopted tariff or unlimited monthly pass; concessions, transfers and family affordability need an explicit tariff and household survey.

Low/high capacity-use cases assume 1,138,320 / 1,821,312 paid trips/day, not unique people or surveyed demand. Low-case steady annual revenue is IQD 576.8 billion; OPEX is IQD 250.4 billion. At that trip volume, the OPEX-only neutral fare is IQD 532, with nonfare receipts held constant. It excludes capital, debt and reserve funding.

In the first complete operating year, the 50% revenue ramp produces 207.7 million paid trips. Holding those trips and nonfare receipts fixed, covering OPEX, scheduled debt service and fees requires approximately IQD 5,116 per paid trip, excluding reserve deposits and factory debt. This is a cash threshold, not a recommended tariff; higher fares can reduce demand. Minimum annual operating DSCR before support is 0.02. Higher utilisation improves later cashflow but cannot fund the long pre-opening debt-service period. Neither this fare nor IQD denomination closes the additional funding gap shown above.

The design retains a planning population of 9,780,429. Its 38.9% anchor-weighted coverage score gives an indicative proxy of 3,804,586 residents. That proxy is not measured population within a real 800 m walking network: survey, population grid, station access, river crossings and feeder coverage remain unvalidated. The older report's 80% city-coverage ambition uses no published comparable denominator or access method; it cannot establish that either plan reaches more residents. The 164 stations and 9 routes offer a larger network to test, not proof of superior population access.

Direct Iraqi labour and industrial benefits

Approximately USD 5.831 billion equivalent (77.6%) of programme procurement is assigned to local suppliers under the editable origin assumptions. This is potential local expenditure, not wages, GDP added or guaranteed Iraqi content. City civil works alone allocate USD 3.306 billion locally; rolling stock allocates USD 832.10 million locally, with plant local expenditure separately counted.

Local train assembly and fabrication create work in body modules, fit-out, wiring, coatings, systems integration, inspection and maintenance while bogies, batteries, windows and doors remain imported inputs requiring supplier and process qualification. Infrastructure work supports Iraqi concrete/precast production, civil erection, stations, utilities, solar installation and supervision. Tooling, training, process qualification and supplier access can leave reusable industrial capacity, shorter repair chains and retained skills after construction. Local employment and supplier income circulate in IQD and can generate Iraqi tax receipts; no multiplier or tax recovery is booked without evidence.

The operating allowance supports 3,217 indicative FTE with annual labour cost of IQD 47.04 billion. These are operating positions, not construction or manufacturing job counts. Construction employment requires validated work hours, productivity, wage rates, shift cover and local-content contracts; no fabricated job total is assigned. The third-party proposal may also use Iraqi civil labour, so its local share cannot be assumed zero.

A sustainable appraisal must demonstrate phased service before full-network completion, realistic paid demand and affordable tariffs, funded debt/interest/reserves within the public limit, placed IQD facilities, supplier and labour qualification, lifecycle replacement funding and an accepted environmental/physical design. Current software and ledger checks establish planning consistency, not those outcomes.

Iraq National OpenSourceRail Strategy

Source: [cities/catalogue/west-asia/Iraq/NATIONAL-BRIEF.md](#)

Original catalogue or earlier scope reference. The figures and policies below retain their original assumptions; they are not the latest Baghdad staffing, depot, procurement or funding basis. See the [current Baghdad recalculation](#) and [current city summary](#). National/portfolio totals have not been repriced with that conditional Baghdad option.

This page contains only Iraq-specific aggregation. Shared network, service, energy, civil, cost, finance, QA and validation methods are defined once in the [deployment planning reference](#).

Important
Foreign-capital advantage: against the default equivalent foreign-turnkey sensitivity, this national programme avoids \$54.49 B (88.6%) of external capital and \$66.99 B of external interest. Capital plus saved interest totals \$121.49 B.

The [Baghdad physical factory plan](#) sizes production cells and test paths for its current six-car trainset order to finish alongside the overall city infrastructure programme, with facility readiness at 18 months from NTP. The national aggregation uses the largest physical city-order capital envelope across Iraq or the original module allowance, counted once. Any allowance above the Baghdad plant belongs to future national scope. Future city loads are not concurrent factory commitments or part of Baghdad finance.

Iraq financing

The catalogue-wide figures below are generic capital/benchmark aggregations. They do not establish a five-year rollout or an Iraq lender commitment. The scheduled proposal covers Baghdad only, including one manufacturing plant. It uses government capital at 25% of total CAPEX, imports split 50% government USD cash / 50% proposed Chinese USD credit, with the remaining government capital, bonds and bank credit in IQD. Full-basket Chinese eligibility remains unqualified. Additional cash requirements beyond that public contribution remain visible in the [Baghdad funding programme](#). Samawah, Mosul and every other Iraqi city are excluded from its cashflows.

National Programme

Local measure	Planning value
Catalogue cities	18
Represented population	29,491,199
Trainsets / vehicle modules	3,652 / 15,530
City infrastructure and fleet CAPEX	\$33.36 B
Shared national factory	\$769.6 M
Factory sizing basis	4,572 modules for Baghdad, then reused nationally
Total national programme	\$34.19 B

Capital And Funding

Local funding measure	Planning value
Imported / external capital	\$7.05 B (20.6%)
Domestic / local capital	\$27.14 B (79.4%)
Default foreign-turnkey external capital	\$61.54 B
External capital saved	\$54.49 B
Capital + lifetime external interest saved	\$121.49 B

Procurement-Origin Composition

CAPEX bucket	Total	Imported	Local value
Civil works	\$20.16 B	\$3.02 B	\$17.14 B
Stations	\$3.02 B	\$603.6 M	\$2.41 B
Depots	\$1.33 B	\$332.1 M	\$996.3 M
Rolling stock	\$4.43 B	\$1.55 B	\$2.88 B
Dedicated solar plants	\$2.09 B	\$941.1 M	\$1.15 B
Residual train control	\$101.2 M	\$50.6 M	\$50.6 M
Charging microgrids	\$184.8 M	\$73.9 M	\$110.9 M
EPC / project services	\$2.10 B	\$315.0 M	\$1.78 B
Shared national trainset factory	\$769.6 M	\$153.9 M	\$615.7 M
Total	\$34.19 B	\$7.05 B	\$27.14 B

City Programme

City	Population	Fleet	City CAPEX	External capital	Local capital
Baghdad	9,780,429	762	\$7.17 B	\$1.62 B	\$5.55 B
Basra	3,955,000	396	\$4.73 B	\$1.00 B	\$3.73 B
Sulaymaniyah	2,150,000	121	\$1.63 B	\$325.7 M	\$1.31 B
Erbil	1,952,000	198	\$1.66 B	\$350.0 M	\$1.31 B
Mosul	1,940,000	246	\$3.11 B	\$602.7 M	\$2.50 B
Kirkuk	1,780,000	151	\$1.97 B	\$380.7 M	\$1.59 B
Najaf	1,540,000	196	\$2.17 B	\$433.3 M	\$1.74 B
Karbala	1,390,000	188	\$3.31 B	\$602.1 M	\$2.71 B
Nasiriyah	705,000	136	\$830.4 M	\$165.1 M	\$665.3 M
Hillah	700,000	161	\$809.3 M	\$170.7 M	\$638.6 M
Amarah	660,000	130	\$817.3 M	\$162.1 M	\$655.2 M
Ramadi	525,000	118	\$683.4 M	\$139.2 M	\$544.2 M
Baqubah	470,000	164	\$850.7 M	\$176.5 M	\$674.2 M
Diwaniyah	440,000	120	\$653.2 M	\$134.1 M	\$519.1 M
Kut	410,000	131	\$793.0 M	\$158.1 M	\$634.9 M
Samawah	373,770	133	\$690.6 M	\$144.5 M	\$546.1 M
Duhok	360,000	162	\$789.0 M	\$174.0 M	\$615.1 M
Fallujah	360,000	139	\$697.3 M	\$146.0 M	\$551.3 M

Local Basis And Regeneration

Country finance parameters use IQ in `lib/templates/country-finance.toml`. The factory is counted once nationally and excluded from city CAPEX. City values come from each `local design.toml` and expanded scenario; common limitations and interpretation are not repeated here.

```
python3 tools/automation/generate-national-briefs.py
```

RFC 0033 – TACS runtime and committed resource control

Source: docs/rfcs/0033-tacs-runtime-and-resource-control.md

Status: proposed development target; software evidence generated/unreviewed. Supersedes: RFC 0032's separate authority/protection implementation. Deployment: synthetic reference only; sectional-authority pilot retained.

Responsibility and interface map

Function	Decision owner	Physical or deployment boundary
Shared railway identities/configuration	osr-core::deployment	Exact model-byte hash; frozen startup parameters; designed revision distinct from installed and approved records
Authoritative resource lifecycle	osr-interlocking::resources, resource_log, DerivedState	Only verified committed ResourceControl entries mutate ownership
Ordered authoritative decisions	Existing osr-consensus::step	Three static voters; independent power/network placement must be designed and assessed
Physical proving	Identified point/station I/O hosts	Asset-scoped occupancy, integrity, points, restrictions and qualified no-reentry proof; synthetic ports in the reference
Onboard movement authority	Existing compute_self_ma_from_state	Validated committed view, exact frozen model, bounded full train footprint and evidence age
Speed and emergency protection	Existing osr-atp::atp_evaluate	Grade-adjusted illustrative braking profile; measured braking/adhesion/latency remains open
Mission and station requests	Existing osr-ato::ato_evaluate, station_step	Doors, charger isolation, connector clearance and energy independently gate departure
Final brake request	Existing osr-brake::brake_evaluate	Application request to separately qualified safety-output channel; software host is not qualified output hardware
Authentication and message contracts	osr-proto, osr-crypto, osr-secbus, consensus proposal verifier	Registered issuer, asset permissions, configuration/session/sequence/time checks before state effects
Process execution and persistence	Thin osr-runtime hosts	Framed local ports, event scheduling, disk writes before outbound effects, conservative cold start
OCC	Service intentions and observations	No authority, ownership release or latch-clear bypass
ERPNext/FUXA	Existing observation/maintenance integrations	Observation only; no new railway command interface

There is one MA implementation and one ATP implementation, executed in each logical protection channel. Resource contracts from the earlier prototype move into existing crates; osr-tacs and its parallel MA/protection algorithms are retired. osr-runtime contains orchestration and adapters. Route selection remains intent, per osr-onboard-routing; agreement cannot supersede missing permission or physical proving. Logical peer observations may traverse common infrastructure; no direct radio or osr-t2t crate is added.

Configuration and communications

railway-model.json schema osr-tacs-railway/2 supplies resource IDs, existing section IDs, conflicts, extents, asset identities, train/session/formation parameters, station locations, static voters and role-scoped public keys. deployment.json is an exact-byte-hash-bound generated startup export. FrozenRailway rejects unsupported versions, invalid topology/identities, changed startup parameters and operational activation. This source is a designed synthetic configuration; installed_state=not-installed and approved_operating_profile=prototype-unapproved are separate explicit facts. Changes require a new bundle and restart, never live digital-twin mutation.

The reference transport uses signed osr-runtime/1 packets, postcard encoding, existing signed consensus proposals and explicit internal interlocking entries. Legacy protobuf/postcard osr-proto::Entry remains a separate versioned format; it must not be deserialised directly into internal entries. Float-based legacy position inputs require checked unit conversion at an explicitly selected adapter. The runtime path publishes integer measured speed and bounded, non-zero uncertainty. Unsupported/malformed packets fail closed.

The envelope binds configuration hash, registered session, monotonic sequence, original observation time and message kind. Limits: 512 KiB application payload, 768 KiB signed payload, 4 MiB framed command, 16 publications per batch, 12,000 log entries and a 256-message reference queue. One-second input freshness and 100 ms maximum configured clock error are prototype assumptions; PTP and hardware timing must establish their operational applicability. Future-dated packets are rejected. Send/receive counters persist across restart. Asset permissions are separate from signature validity. All load-bearing events, including positions, use Safety. The legacy simulator consensus publisher also classifies occupancy-changing position reports as Safety and retains its last committed view when quorum confirmation is unavailable. No advisory route/position can unlock track.

The published deterministic reference keys are test fixtures. Operational provisioning, protected key storage, rotation, revocation distribution, offline replacement and recommissioning require a controlled maintenance pack. Changing keys or sessions changes the configuration hash; interoperability stops until the complete bundle is reconciled. Revoked participants

are rejected. Crash-fault Raft is assumed: a signed member's committed-prefix assertion is not a Byzantine quorum certificate. Authenticated erroneous sensors and common software, configuration, power and clock causes remain FMEA concerns.

Ownership and evidence freshness

Unknown qualified clear available reserve/prove/lock occupy explicit withdrawal qualified no-reentry/clearance available. Identified occupied startup admission can bind the proved train/session when no conflicting owner exists; it cannot transfer another owner's lock. Leases time out to ReleasePending, retaining their owner. Restart increments the committed controller epoch, retains owners as unknown and quarantines empty clearance for the maximum prior permission plus clock error. Identified retained owners can be reconciled without transferring protection. Blocked possessions cannot be cleared by these recovery APIs.

An empty detector does not prove cancellation safe. Qualified release requires bounded full rear clearance with integrity, or committed withdrawal and a proved stop/protected approach that prevents old-permission re-entry. These are physical interface assumptions to validate. Platform resources remain owned at arrival. Depot/work resource is explicitly protected; rescue, coupled formations, turnbacks, arbitrary topology and large fleets remain separate packages.

MA expiry is the minimum of the new MA window and the original position, local proof and held permission deadlines. Recalculation cannot refresh evidence. Every traversed section must have the correct active owner/configuration/epoch, current point proof and integrity. Local full-footprint uncertainty checking adds a restrictive gate before ATP. Recovery requires stopped, valid local facts and a privileged local procedure, never a dashboard acknowledgement. Civil conditions enter through asset-scoped signed restrictions/closures; urgent protection must have an engineered path independent of alarm viewing. Removal requires qualified inspection/handback, not an ERP status change.

Persistence and process reference

osr-consensus::disk::DiskJournal has one OS-locked writer. Frames carry node, configuration, term, vote, complete log deltas, commit index, application state and replay fences, with length and CRC bounds. Every host persists and fsyncs file and directory before exposing messages or actuator requests. Torn/corrupt journals inhibit startup; repair never silently discards an accepted lock. Storage compaction atomically replaces a full-log checkpoint after fsync. Logical Raft snapshotting/log truncation is not implemented. Capacity exhaustion inhibits further publication; offline servicing requires retained-protection and configuration reconciliation. A power interruption during rename/fsync requires storage/hardware qualification; SIGKILL tests are software evidence.

The default Raft batch remains one entry. The reference host uses bounded contiguous batches of twelve; Rust handles each entry under the same checked prefix semantics. This is outside the one-entry formal refinement and needs independent refinement review. Quorum confirmation records fresh per-peer responses in the current term, including empty-log heartbeats; stale historical replication indices cannot refresh a quorum. Durable reboot restores no leader role, quorum confirmation or volatile acknowledgements.

Run `python3 tools/automation/tacs_reference.py --output /tmp/reference.json`. The coordinator spawns four osr-train-agent processes (A/B for each train) and six osr-wayside-agent processes: three voters, point I/O and west/east station I/O. Charger requests and local proving pass through the station process ports; their asset-scoped interlocks can inhibit power and cannot grant movement. The depot/work resource is committed blocked and remains blocked across expiry and controller restart. Two further osr-safety-output processes each host the paired osr-brake::dual::DualGuard comparator. Both channels must agree to permit; either emergency, missing/stale/replayed request, disagreement or unhealthy feedback latches an emergency output with zero torque. The reference feeds at 50 ms, before the 100 ms output deadline. A late feed cannot replace an overdue request to hide a missed interval; only stopped, privileged, fresh recovery can clear the latch. These ports block on coordinator commands and use virtual time. They do not establish autonomous real-clock execution, independent physical timers or de-energised hardware outputs. Processes exchange signatures through asynchronous bounded queues; publication does not wait for commitment. Simulation truth enters only own-train sensors and local infrastructure proving ports, never the MA state. Real journals and process kill/restart are used. The same frozen bundle feeds every process. The physics fixture checks its supported extents, conflict identities, formation/braking and berth/energy parameters before startup; unsupported bundles require a new calibrated fixture. osr-sim's legacy synchronous cluster publisher remains isolated from this reference; it is not claimed as the deployed asynchronous path. Full integration of its scenarios/physics, shared clocks, radio/T2G/TCN failover and direct-peer performance is future work.

Station sequence is stop/secure exchange/charge isolate physical departure proof ready. The reference measures synthetic energy and closed-loop speed; per-car BMS/thermal/door/PSD/traction integrations remain pending HIL. Failed charging can hold service without erasing track ownership. Emergency departure cannot bypass a connected charger or unlocked door. Missing application output must trip a separately qualified deadline/output channel; the isolated reference output ports model deadlines and latches but do not qualify that hardware function.

Default redundant protection and platform review follow-up

The [executable policy](#) sets two logical channels, two-out-of-two permission and either-channel trip as the development default for train protection, point proving/locking, crossings, doors/platforms, charging isolation and obstacle protection. Loss of either channel stops the affected function. Automatic single-channel operation or takeover is excluded. Availability after a channel failure requires a separately assessed architecture. Three Raft voters replicate authoritative state; they are not protection outputs. The conservative deployable pilot profile and its release gates remain in force.

Each train A/B host uses a separate OS process, journal and restored committed view. The binary requires `--safety-channel A|B`; a persisted journal cannot change channel on restart. A publishes the train's network proposals; B evaluates the same committed domain inputs without publishing duplicate proposals. Loss of A does not authorise B takeover. Pair comparison uses exact synthetic cycle sequence/time, brake and torque agreement. It has no end-to-end source-issued output identity yet. Shared software, sensor fixture, host, test keys, coordinator clock and comparator are explicit common causes. Physical power/output separation, channel-local clocks and independent feedback must be engineered and qualified. Only train protection's logical pair is executed; the policy explicitly keeps all five other local pairs open. Two processes are not installed board quantities.

The 2 October 2026 review of 17b31f055c9e16b5439c18b4a4d83f004890bcad identified a stale FMEA applicability check and a concealed deadline gap. This change rejects stale failure subjects as well as stale configuration baselines, retains the late-feed regression and adds missing-A, missing-B, disagreement, replay and feedback-failure process cases. Each new case must first permit motion, actually inject its fault, trip within one 50 ms reference step, stop with retained protection and remain latched. These are virtual-time software criteria, not measured hardware response times. The existing TLC abstraction covers resource ownership only; it does not prove the new paired output function.

Next work closes named integration gaps in this order. Owners and reviewers are roles to appoint; acceptance is still open.

Work	Owner / independent reviewer	Required exit evidence
Autonomous watchdog and output paths	Embedded/electronics / safety-I/O reviewer	Coordinator/application/comparator freeze and kill, delayed scheduling, clock rollback/skew, power loss and stuck feedback; measured traction inhibition and effective braking without a new application command
Sensors and emergency union	Train integration / protection reviewer	Typed adapters to existing localisation, fire, derailment, obstacle and BMS/thermal evaluators; wheel slip/bias and simultaneous resource faults independently reach the final output; shared bad sensors do not establish independence
Repeated station missions	ATO/station integration / operations reviewer	Explicit mission/stop identity and arrival/departure transitions; at least three stops, short charge, delayed doors, turnback/resume, per-car charging and no moving door release
Remaining local protection pairs	Wayside/station / safety-I/O reviewer	Point/crossing proving, door/PSD, charger isolation and obstacle channels; independent release and inspected handback
Calibrated plant and city conversion	Simulation/configuration / braking and site reviewers	Sealed city revision converted to supported resources and shared osr - sim plant with mass/load, adhesion, gradients, build-up/delay, thermal/energy limits; full LM3 stopping envelope under uncertainty sweeps
Duty, recovery and storage	Simulation/runtime / operations and storage reviewers	Representative city's station capacity, overnight storage, morning dispatch, charging outage/recovery; separate rescue/tow/split/reverse/handover missions and sustained duty without capacity exhaustion or unbounded restart; safe snapshots/replay fences retain locks
Formal and scenario evidence	Assurance / independent formal reviewer	Property-to-code/test mapping, overlapping multi-resource routes, sequences/epochs/crash points, counterexample replay and specific hazard activation/deadline/excursion/queue/CPU/storage/recovery metrics
Integration and lifecycle quantities	Platform/hardware / configuration and cost reviewers	Observation-only A/B health/discrepancy/feedback/age/degraded/revision data through supervision gateway to FUXA/ERP; no acknowledgement resets; actual serial/power/firmware/calibration/replacement records and matched-service redundancy/spares/training/assessment costs
Physical release	Hardware/operations / independent assessor	HIL, measured braking/integrity/radio, power interruption, closed-track recovery and maintenance drills before profile approval

`station_step(Ready, fresh berthed/secured arrival)` currently remains Ready; the host targets the final stop. Nominal arrival therefore does not demonstrate another passenger exchange or a multi-station mission. The bounded two-train fixture retains geometry checks; expanding it cannot substitute for calibrated city conversion. Civil closures must bind precise operational resources and inspected handback separately from ERP repair completion. No duplicated ERP/GUI or comfort software is implied by protection redundancy. Commodity hosts, the existing small Rust evaluators, reusable local controllers and open replacement/ calibration procedures remain the implementation approach. Hardware quantities and hot-standby/two-MCU mappings must be reconciled at the hardware freeze.

Evidence and staged delivery

The shared connected-engineering compiler carries part subassembly controller function train/infrastructure hazard control evidence operating response. Source changes stale execution hashes and propagate through configuration-bound claims and blocked release decisions. TLC checks a bounded resource abstraction with qualified physical proving assumptions; it is neither a Rust refinement proof nor an unbounded liveness result. G0–G4 decisions remain blocked pending review and measurements.

Owners/reviewers below are accountable roles to appoint, not fabricated named approvals. No package is accepted merely because a generated checkbox is true.

Package	Technical owner	Independent reviewer	Exit evidence / dependency
1 Architecture	Control architect	Independent railway safety engineer	Reviewed responsibility map; current baseline
2 Shared configuration	Configuration/lifecycle engineer	Independent configuration auditor	Identity/schema/mixed-version tests; 1
3 Resource/durability	Interlocking/consensus engineer	Independent formal/storage reviewer	Lifecycle, crash and restart evidence; 2
4 Authority/protection	ATP/localisation engineer	Independent braking engineer	Freshness/uncertainty/integrity properties; 2–3
5 Communications	Communications/security engineer	Independent security/timing reviewer	Replay/loss/restart/vendor-neutral transport tests; 2
6 Runtime	Embedded runtime engineer	Independent safety-I/O reviewer	Multi-process reference and physical power-loss tests; 3–5
7 Station	Station/energy integration engineer	Independent doors/charging reviewer	Complete station-cycle and per-car tests; 4–6
8 Twin/campaign	Simulation engineer	Independent test engineer	Reproducible raw results; starts after 2
9 FMEA/GSN	Assurance engineer	Independent hazard reviewer	Connected change impact and applicability; continuous from 1
10 HIL/hardware	Electronics integration engineer	Independent hardware assessor	Measured output/timing/fault records; 6–9
11 Closed track	Test/operations engineer	Independent field safety reviewer	Braking, integrity, recovery drills; 10
12 Profile release	Railway release authority	Independent assessor	Named gates, rollback and approved installed bundle; 9–11

Hardware preparation proceeds with software and assurance using existing t-ecu-s, t-ecu-a, t-obs, w-sbc, s-sbc families. Each pack needs exact module/SKU/substitutes, wiring/connectors/enclosure, power/thermal/environmental budgets, fail-safe outputs/watchdogs, calibration, controlled firmware, fixtures, bench records, and complete-unit replacement/recommissioning instructions. Existing COTS and custom-board release tracks both remain valid; safety-channel selection follows control-electronics/safety-controller-selection.md. This change supplies no invented SKUs, installed serials or physical test records.

Cost comparison uses equivalent service and availability, separately counting train controllers, static voters, non-voting sites, radios/antennas/power, retained detection, installation, spares/calibration/maintenance, integration, assessment, recovery/disruption and local/import content. No equipment removal or city-model savings is authorised without replacement function and evidence. The reference's ten processes are software roles, not a bill of materials. Cost quantities/prices remain deployment-specific inputs; an unknown input must keep the comparison incomplete. Track duplicate safety implementations, configuration variants, core dependencies and physical interfaces alongside money.

Distributed Onboard Control Profile

Source: <docs/certification/distributed-onboard-control-profile.md>

Status: development target; not the deployable pilot baseline.

This profile reduces dependence on centralised wayside computation and permits continued route selection during a communications outage. It does not remove the safety functions commonly implemented by interlocking, ATS or ATP. Those functions may move between onboard and distributed equipment only after a hazard analysis, independent assessment and deployment approval demonstrate equivalent or better safety.

The deployable reference remains the conservative sectional-authority profile in [pilot-signalling-profile.md](#).

Executable train-centred milestone

[RFC 0033](#) and the [TACS assurance package](#) use the existing committed interlocking MA and ATP/ATO/brake components through thin, authenticated process hosts. The reference includes A/B agents for each of two trains, three static voters, point I/O and two station/charging interfaces. The [development default](#) requires both protection channels to permit and either to trip; loss stops the affected function. Train logical pairs are executed; point/crossing/door/charger/obstacle pairs and physical independence remain open. Raft replication cannot substitute for safety outputs. Generated software evidence remains unreviewed. HIL, measured braking/integrity, field recovery, independent assessment and a named approved installed bundle are required to change the deployable profile. The conservative pilot remains the default.

Three independent route inputs

The onboard selector compares:

- 1 a signed, versioned plan stored onboard;
- 2 route and position inferred from onboard sensors against immutable topology;
- 3 an authenticated network command from operations control.

An input is eligible only while trusted, fresh and internally valid. Exactly matching route, next-section and plan-epoch values from two eligible sources are required. If all three disagree, only one source is eligible, or the two available sources disagree, the result is Ho l d. A network outage can produce OnboardAutonomous only when the onboard plan and sensor-derived input agree.

Route selection is not permission to move. Every accepted selection carries an explicit `movement_authority_required` condition and is passed through the independent authority, localisation, speed-envelope and emergency-brake path.

Functions that must remain

Any implementation must retain, even if equipment placement changes:

- movement-authority generation and expiry;
- train separation and opposing-move exclusion;
- route locking and detected/locked point position;
- occupancy or safety-integrity localisation;
- overspeed supervision and emergency braking;
- intrusion/obstacle gates required by the operating envelope;
- degraded-mode supervision, event recording and accountable override.

“Eliminating interlocking/ATS/ATP” is therefore interpreted as reducing duplicated central equipment, not deleting their safety outcomes. A model, sensor fusion algorithm or radio link cannot independently claim equivalence.

Narrow single-track operation

Short single-track sections are permitted only on exclusive guideway and with passing loops at passenger stops or protected portals. Entry requires locked route exclusivity, detected points, clear occupancy, a valid authority and a proved timetable/degraded-mode strategy. Loss of required state prevents entry; it does not rely on two trains negotiating informally over the radio.

Recovery sites and shunt robots

The reference planner reserves a recovery siding at or immediately beyond every third passenger station. Each site has a protected mainline interface, independent stop detection and remote isolation. Its small shunt robot is remote-controlled, has local emergency stop and fail-held braking, and cannot autonomously enter the main line. Radio loss inhibits traction. Mainline entry, towing and return to service remain controlled recovery operations.

Evidence gates

Before this profile can replace any pilot equipment, the project must freeze the safety allocation and demonstrate source independence/common-cause analysis, target-hardware timing, localisation accuracy, radio-loss behaviour, point and occupancy interfaces, cybersecurity, HIL fault injection, shadow running, representative field trials, recovery drills and independent safety assessment. The deterministic report records design coherence; it does not close these physical or regulatory gates.

Rolling-stock top-down / bottom-up design system

Source: [docs/rolling-stock/design-system.md](https://docs.rolling-stock/design-system.md)

This is the design authority layer above the parametric CAD. It gives the project a systemic way to move from whole-train intent down to bought-in parts, fabricated parts, subassemblies, final assemblies, and then back up through scoring and evidence.

The rule of thumb is simple:

- 1 Start top-down with requirements: platform fit, axle load, range, traction margin, thermal margin, cost, mass, manufacturability, and safety evidence.
- 2 Decompose into the owned design hierarchy: external components, fabricated parts, subassemblies, final assemblies.
- 3 Iterate candidate definitions automatically inside an explicit design space.
- 4 Promote only feasible candidates into FreeCAD/FEM regeneration.
- 5 Freeze only when the requirements scorecard, supplier evidence, CAD, FEM, BOM, and manufacturing plan agree.

Hierarchy

Layer	Meaning	Examples	Source of truth
Top-level requirements	What the train must achieve	platform margin, range, axle load, cost, mass, traction/HVAC margin	<code>osr_mech.design_definition.REQUIREMENTS</code>
External components	Bought-in or BID/SOURCE modules	traction motors, HVAC, batteries, doors, glazing, sensors, couplers	ExternalComponent records plus supplier evidence
Fabricated parts	Parts OSR owns and regional workshops make	shell, bogie frame, motor cradle, cowl rings, articulation adapters	FabricatedPart records plus CAD templates
Subassemblies	Integration units that can be inspected	car module, powered bogie, trailer bogie, cowl, articulation, roof services	Subassembly records plus FreeCAD review groups
Final assemblies	Released trainset configurations	promoted light-metro 3-car trainset	FinalAssembly records plus generated CAD/FEM/BOM

Automated iteration

The first implementation is deterministic and dependency-free:

```
tools/automation/design-iterate.sh
```

It exhausts the declared discrete design space for the default light-metro-3car family, evaluates every candidate, and writes:

- `design/component-catalogue/catalog/design-system/design-iteration.json`
- `design/component-catalogue/catalog/design-system/design-iteration-summary.md`

To turn the winning candidate into a buildable product tree and review the current CAD/BOM baseline against it:

```
tools/automation/buildable-trainset.sh
```

That writes the buildable manifest and buildability review under `design/component-catalogue/catalog/buildable-trainset/`.

To run a bounded exploratory pass:

```
tools/automation/design-iterate.sh --family metro-4car --max-iterations 250
```

The current scorecard is intentionally planning-grade. It is good enough to rank candidate architecture choices before spending FreeCAD/FEM time, but it is not a certification result. As the project matures, replace or augment the simple metrics with:

- FreeCAD-derived mass properties and package clearances;
- CalculiX margins from `tools/automation/freecad-generate.sh --fem`;
- supplier quotations and evidence status;
- lifecycle energy and maintenance models;
- risk penalties from the hazard log and compliance matrix.

Promotion loop

Use the generated best candidate as a design review input, then run:

```
tools/automation/freecad-generate.sh --models --assemblies --fem  
tools/automation/freecad-generate.sh --screenshots --station-scenes
```

If CAD/FEM/supplier evidence rejects the candidate, update the component catalogue or constraints in `osr_mech.design_definition`, rerun `tools/automation/design-iterate.sh`, and promote the next best feasible candidate. That is the closed loop: requirements drive definitions, definitions drive CAD/FEM, evidence updates definitions.

RFC 0011 – Civil Infrastructure Design Standard

Source: docs/rfcs/0011-civil-infrastructure-design-standard.md

Status: Draft – planning only, no structural drawings ship with this RFC Date: 2026-04-22 Updated: 2026-08-17 – OSR Rapid Viaduct Kit correction Depends on: [RFC 0008 Rolling-Stock Reference Design](#), [RFC 0009 Track Design Standard](#), [RFC 0010 Station Design Standard](#)

1. Summary

OpenSourceRail commits to two civil classes only – at-grade and elevated – with bridges for water crossings as a narrow third class. No tunnels. Every corridor the auto-gen pipeline produces, and every hand-authored corridor the operator commits, will sit on one of:

Class	Share (target)	Description
at-grade	≥ 70 %	Track sits on prepared subgrade at natural ground level (possibly with minor cut/fill ≤ 3 m). The cheapest and fastest class by 1–2 orders of magnitude.
elevated	≤ 25 %	Track sits on a viaduct structure 5–12 m above ground (precast OSR-Pi20/Pi25 decked beams, standardised span).
bridge	≤ 5 %	Over a water crossing or deep gap. Separately engineered special span with site-specific substructure.

The fourth class the first-pass auto-gen inference used – tunnel (cut-and-cover and bored) – is removed from the catalogue. Where an alignment previously would have gone underground, it now goes elevated over the same footprint, or deviates around the constrained zone on at-grade. Operators who deliberately want a tunnel are forking the project; OpenSourceRail upstream does not carry tunnel designs, tunnel cost models, or tunnel-specific signalling / ventilation / evacuation engineering.

2. Non-goals

- Not a tunnel standard. By construction. The project's cost model, the simulator's energy budget, the sensor-tuning for GNSS + balise, and the operations rulebook (RFC 0013) are all calibrated against above-ground operation. Going underground reopens every one of those calibrations.
- Not a geotechnical rulebook. Soil survey, pile type, foundation depth, seismic detailing – owned by the deploying operator's civil team. This RFC fixes the functional envelope (span range, clearance, load class) not the method.
- Not a bridge design manual. Spans above 30 m, water crossings, turnouts, and exceptional crossings use a separately engineered segmental, I-girder, or steel-composite product. They are not a stretched version of the standard full-span trough.
- Not a land-acquisition policy. How a deployment acquires right-of-way (ROW) – expropriation, purchase, existing-rail corridor reuse, new-build – is municipal work.
- Not a standards body. We reference EN 1990 (Eurocode basis), EN 1991-2 (traffic loads on bridges / viaducts), EN 1998 (seismic), UIC 777-2 (infrastructure gauge), local building codes where deployed. We do not publish new ones.

3. Why no tunnels

A planning-grade cost comparison for a 1 km segment in typical dense-urban conditions across the target regions:

Class	OSR target / retained benchmark (USD/km)	Build time	Post-build maintenance
At-grade dedicated ROW	2.584 M / 3.0 M	6–12 months	Low – ballastless slab/embedded trackform
Elevated viaduct	9.748 M / 12.0 M	12–18 months	Medium – bearing + expansion-joint inspection
Bridge over water	18.0 M / 18.0 M	18–24 months	Medium – same as viaduct + scour inspection
Cut-and-cover tunnel	60–120 M conventional	30–48 months	High – ventilation + pumping + egress drills
Bored tunnel	90–200 M conventional	48–72 months	High – same as above, plus tunnel-boring-machine commissioning

Numbers are planning-grade, calibrated against generated deployment instances including Samawah context ([RFC 0003 §2.3](#)).

A tunnel segment is 10–40× the CAPEX and 4–8× the build-time of an equivalent at-grade segment. It also brings a permanent operational overhead: mechanical ventilation, flood pumping, fire suppression, emergency evacuation plans, and radio-coverage retrofit. Every one of those is an additional subsystem the deploying operator must staff and maintain.

The mission is "urban rail affordable enough that a developing nation can finance it domestically." A corridor with any tunnelling in it is outside that envelope. The design decision is: if the alignment can't go at-grade or elevated, the alignment should deviate around the constraint. Even at a 20 % longer corridor, the detour is cheaper than the tunnel it avoids.

4. At-grade – the 70 % case

4.1 Envelope

- Subgrade: compacted fill or in-situ soil graded to +/-25 mm of design. Capping layer of 150 mm crushed stone, then ballastless reinforced slab / embedded direct-fixation plinths for the running rails. The default urban trackform avoids ballast migration, tamping cycles, and loose aggregate at crossings.
- Earthworks: cut / fill up to 3 m depth only. Beyond 3 m the segment is either:
 - Re-classified to elevated (bridge over the gap / viaduct over the hill), or
 - Deviated around the constraint.
- Drainage: transverse slope $\geq 2\%$ either side; longitudinal channels every 50 m; culverts at every flow-path crossing. Drainage is not optional: a flooded slab undermines fastener integrity, corrodes embedded hardware, and damages the subgrade.
- Fencing: dedicated ROW is fenced the full length on both sides. No uncontrolled pedestrian crossings. Level crossings only where a city street intersects and an underpass / overpass is prohibitively expensive. See [RFC 0012](#) for the level-crossing equipment standard.
- ROW width: minimum 10.5 m for double-track at-grade (two tracks $\times$ 3.5 m wide plus 1 m each side clearance plus fencing allowance); 7 m for single-track.

4.1.1 Narrow old-town single-track option

Some historic cores and market streets cannot fit a 10.5 m dedicated double-track reservation without demolition, but also do not justify viaduct intrusion. OpenSourceRail therefore permits a constrained single-track at-grade segment as an at-grade variant, not a fourth civil class.

Rules:

- Use only for short constrained sections where double track would require demolition or permanent removal of the street's essential pedestrian/service function.
- Fit the running way inside the 7 m single-track envelope, with protected pedestrian edges and no mixed running with road traffic.
- Provide double-track passing loops only at stations, portals, or immediately outside the constrained street.
- Interlocking treats the whole single-track section as one opposing-move exclusion zone unless a deployment-specific signalling design divides it into shorter protected blocks.
- Timetables must prove the desired headway through the single-track section before the option is accepted. At 3-minute peak headway, a single-track section longer than roughly 800-1,000 m will usually force either lower frequency, directional tidal operation, or a bypass.
- Emergency walkways, evacuation gates, drainage, charging isolation, and intrusion detection remain mandatory; the narrow option saves width, not safety systems.

The auto-generation pipeline should prefer this option before elevated only when a tagged old-town / constrained-street corridor is short, station-loop spacing is feasible, and the resulting timetable still meets the line's published service class. Otherwise it should stay double-track or go elevated/deviate.

4.2 When at-grade is inappropriate

Even with the default bias to at-grade, certain conditions push toward elevated:

- The alignment crosses a river wider than 30 m bridge.
- The alignment crosses a highway or mainline rail at grade that cannot be broken by a level crossing (too many crossings per hour would make the crossing barrier close more than open) elevated.

- The alignment runs through a dense built-up core where ROW acquisition would require demolition of more than 3 buildings per 100 m of corridor elevated or deviate.
- The alignment runs along a street where at-grade light-rail running would conflict with road vehicles at every junction elevated or route to a parallel street.

The auto-gen pipeline's civil inference (§6) now maps these conditions to Elevated where it previously would have emitted BoredTunnel.

5. Elevated – the 25 % case

5.1 Envelope

- Structure: paired single-track prestressed decked pi-beams. OSR-Pi25 is the primary product and OSR-Pi20 is the closure/utility- avoidance product. Each beam is 2.9 m wide with stems beneath the rail lines; independent outer walkway/barrier cassettes produce an 8.5–9.0 m controlled twin-track envelope. The catalogue contains no 30 m Pi beam.
- Piers: single-column reinforced concrete, 1.5 m × 2.0 m rectangular, heights 5–12 m, with a 6.5–7.5 m hollow/precast-shell cap. Foundation type comes from the soil/access catalogue and actual deep-element lengths.
- Deck clearance: 5.0 m vertical under the girder soffit over any road; 5.5 m over a truck route; 7.5 m over a rail corridor (UIC 777-2 minimum).
- Pier spacing: 25 m nominal, using 20 m closure bays where constrained. Spans above 30 m use OSR-SP or another separately engineered structure.
- Bearings: scheduled fixed/guided/free bearings. A semi-continuous internal pier has four bearings in one longitudinal line; an expansion-unit boundary has eight in two independent lines; an end support has four. Permanent checked jacking interfaces permit replacement.
- Movement: four normal spans form a short semi-continuous unit using a released reinforced diaphragm or link slab. Expansion gaps occur every 80–125 m, never as one kilometre-long continuous structure. The project issues a bearing/movement schedule and continuous-welded-rail interaction, braking, temperature, seismic and foundation-flexibility analyses.
- Parapets: 1.4 m solid concrete panel, continuous, with a handrail on the inspection walkway.
- Walkway: separate outer inspection/escape cassette, 1.0 m clear, escape ramps every 250 m down to at-grade.
- Acoustic screens: fit only where the project noise model demonstrates a requirement; use replaceable secondary panels rather than widening the primary member by default.
- PV integration: concentrate PV at stations, depots and canopies. Normal viaduct spans do not carry a default PV attachment.

5.2 Rationale for one reference girder

- One long-line mould family across the whole project. The precast yard casts one Pi-beam section with movable Pi20/Pi25 stop ends; every normal span of an OpenSourceRail deployment uses that shape. This is the biggest single CAPEX / schedule lever in elevated construction and matches the "one spares pool, one CAD reuse" principle from RFC 0008 / 0009 / 0010.
- Double-track substructure, repeated single-track beams. One shared hollow/precast-shell cap carries two identical Pi-beams at 3.5 m centres. A single-track initial line still builds the shared substructure and may defer the second girder until capacity demands it.
- Short semi-continuity, not kilometre-long continuity. Transport and erect ordinary individual beams, then connect four spans with a released link slab or diaphragm. This removes most deck gaps and one bearing line at ordinary internal supports while retaining manageable thermal units.

6. Bridge – the 5 % case

- Reference class: separately engineered OSR-SP segmental, I-girder, or steel-composite span. The standard full-span U catalogue ends at 30 m.
- Pier: when a pier has to sit in the water, foundation is a reinforced-concrete caisson or a pile group with a protection cutwater. Scour assessment per EN 1991-2 §13 with a 100-year design flood.

- Navigation clearance: per the navigable waterway's published class. The operator commissions the bridge design and the standard OSR-U catalogue ends at the approach where the site demands a non-catalogue structure.
- Thermal: project-specific bearing, joint, and rail/bridge interaction design for the complete temperature, creep, shrinkage, and seismic range.

7. Stations-as-structures

Station archetypes from [RFC 0010](#) map to civil class as follows:

Archetype	Typical civil class	Notes
halt	at-grade	No canopy PV. Single side platform on direct-ground footing.
standard	at-grade	Solar canopy + side platforms.
major	at-grade	Island platform, larger canopy.
interchange	elevated + at-grade	One line is on the viaduct, the other at-grade. The two platforms stack vertically at the junction. Never two elevated lines stacked – the second level's wind and seismic loads rule that out of the upstream catalogue.
terminal	at-grade	End-of-line; turnback tracks sit at grade.
depot-terminal	at-grade	Yard footprint is large; elevating it is prohibitively expensive.

Underground stations are not in the catalogue. The previous draft of RFC 0010 used the word "stacked" to describe interchange layouts; this RFC clarifies that stacked means vertical separation between at-grade and elevated levels at the junction, not between two underground levels.

8. Auto-gen pipeline – the civil inference, revised

The civil-class inference in [crates/osr-routing/src/civil.rs](#) currently classifies a cell based on the underlying cost surface. Under the no-tunnel invariant:

- Cells with cost ≤ 40 at-grade (unchanged).
- Cells with cost 40..100 at-grade (was already; unchanged).
- Cells with cost 100..400 (water) bridge (unchanged).
- Cells with cost ≥ 400 (building / dense built-up) elevated (was BoredTunnel now elevated).

This aligns with the rule: "if the corridor can't be at-grade, it goes above, not below."

Two downstream consequences, surfaced in `design-quality.yaml`:

- 1 Elevated fraction as a soft gate. If the share of elevated structure for a line exceeds 30 %, the quality file raises a warning. Designs with > 50 % elevated either need deviation or are inherently expensive and should prompt review.
- 2 No tunnel class. Quality output reports only at-grade, elevated, and bridge fractions.

9. Cost-anchor lookup

Total CAPEX drives the national-treasury conversation. The auto-gen pipeline emits a full `[costs]` block per city in `design.toml`, broken down by bucket below.

The source currency is USD because the marketplace and country-finance templates quote in USD. Generated `*_eur` fields are converted reporting views at 0.92 USD->EUR. Non-civil units and retained civil benchmarks live in [capex-costs.toml](#). The active civil rates are generated from [civil-cost-calibration.toml](#) and CAD quantities into [civil-cost-model.toml](#); this RFC keeps the narrative summary.

9.1 Civil works (USD/km × civil mix)

Class	Active USD planning target	Retained benchmark
at-grade	2 584 000 / route-km	3 000 000 / route-km
elevated	9 748 000 / route-km	12 000 000 / route-km
bridge	18 000 000 / route-km	18 000 000 / route-km
elevated-interchange premium	4 500 000 / site	—

9.2 Stations (RFC 0010 archetype catalogue)

Archetype	USD planning-grade
halt	600 000
standard	2 500 000
major	4 500 000
terminal	4 500 000
depot-terminal	5 000 000
interchange	8 000 000
interchange-elevated	12 000 000

The elevated-junction premium in §9.1 covers the viaduct + upper deck at interchanges; the table above covers the at-grade lower platform, ground-level pedestrian access, and protected crossing equipment where needed. Overbridges, lifts, and stairs are not the standard station assumption; they are carried only by elevated/stacked sites or local road-barrier overrides.

9.3 Depots (RFC 0014 archetype catalogue)

Archetype	USD planning-grade
main-heavy	8 000 000
secondary-medium	3 000 000
layup-minimal	400 000

These rates assume RFC 0014 distributed overnight stabling: healthy trainsets may sleep at powered passenger stations and layups, so the main-heavy no longer carries parking capacity for every train every night and layup-minimal is a powered-station stabling/isolation kit rather than a small standalone yard.

9.4 Rolling stock (RFC 0008 local-owner production × fleet count)

Rolling-stock city CAPEX uses a local-owner trainset-family planning unit, not an inflated per-car multiplier and not the raw marketplace BOM floor. The unit includes direct material, local assembly/labour, nominal per-train QA/acceptance evidence, and modest local handover logistics. Fixtures/tooling live in the railway production plant line; warranty, spares, and routine commissioning support are OPEX.

Family	USD / trainset local-owner unit
urban-shuttle-1car	280 000
tram-2car	560 000
light-metro-3car	900 000
metro-4car	1 120 000
metro-6car	1 680 000

Fleet count = peak-revenue + spare + cold-reserve per RFC 0014 §4.

9.5 Railway production plant

Each country carries one lean shared railway production-plant setup allowance for all city fleets it will build or assemble locally. Cities do not duplicate this asset in city CAPEX. The national factory is sized to the largest single-city fleet programme, costed per supported vehicle/car module, reused through a phased rollout, and kept separate from rolling-stock procurement.

Item	Planning-grade basis
Base local plant setup	60 000 USD / vehicle-car module
High sensitivity check	120 000 USD / vehicle-car module

The allowance covers reusable 1 m fiberglass panel moulds, clip/drill gauges, basic steel fixtures, plant services, commissioning bay setup, material handling, and production-readiness work. It excludes a full-length body mould and production adhesive cure hall. Six parallel two-person crews can install and release a three-car exterior body in one eight-hour shift after painted-frame dimensional release; doors, glazing, equipment, bogies, commissioning, homologation, and first-article testing remain separate work. Distributed overnight stabling reduces the number of depot-centred commissioning and parking bays needed in the production/depot complex. A three-module increment of supported factory capacity therefore carries 180 000 USD of base plant allowance, while the high sensitivity is 360 000 USD.

9.6 Systems

Item	Planning-grade basis
Residual train-control wayside (RFC 0015 GoA 4)	50 000 USD / route-km
Station/depot charging microgrid interfaces	120 000–1 000 000 USD / stop, by station archetype

RFC 0015 mandates battery-electric operation with station charging: there is no overhead catenary, third rail, feeder substation, or route traction-power budget. The energy infrastructure bucket covers the conductive chargers, local switchgear, inverter interface, and station/depot microgrid tie-in. PV/storage quantities are sized in the energy-site catalogue rather than as a continuous per-km rail-power system.

9.7 EPC overhead

Integration + project management is 7 % of the subtotal across §9.1 – §9.6.

Rates are deployment-localised via the [country-costs.toml](#) template (labour, materials, finance cost adjustments). The base rates above are what the upstream catalogue quotes; actual numbers in any given deployment can be $\pm 40\%$.

`total_usd` is the procurement-basis headline per city. `total_eur` is also emitted for compatibility with earlier generated schemas.

10. Constructability constraints

- Concrete supply. Precast concrete yards exist in every target region; the Pi section needs a supplier-designed railway prototype and a reusable long-line mould fabricated from established formwork systems (PERI, Meva, Doka). Operators without a nearby precast yard bootstrap one — a 5 km² yard with 20 formworks produces enough girders for 50 km of viaduct in 18 months.
- Steel reinforcement. All target regions have domestic rebar mills in the 12–40 mm range we use.
- Post-tensioning tendons. Commodity; local supply exists in every target region.
- Lifting and transport. Pi25 is 2.9 m wide and targets 65–75 t. The project must release the route, transporter, lifting points, portal/launcher or actual crane load chart, synchronized lift controls, ground pressure, wind limits and contingency landing method.
- Launching. Where full-span access is constrained, OSR-US uses match-cast 2.5–3.0 m segments, post-tensioning, and an overhead launcher with specialist geometry, epoxy-joint, tendon-grouting, and staged-load QA.

No restricted-export equipment. No bespoke machinery. The construction envelope matches what a mid-size regional civil contractor can mobilise.

11. Pitfalls and decisions

- No tunnels is the non-negotiable decision. An operator who believes their corridor absolutely requires a 3 km tunnel under a city centre has exactly two options: (a) deviate the alignment; (b) fork the project. Upstream stays on the at-grade / elevated / bridge envelope.
- Choose the civil mix from the actual corridor. Use at grade where land, access and geometry permit. Controlled central viaduct concepts trade higher civil costs for more direct routes and fewer street conflicts. Report the resulting quantities, property needs and whole-scope costs; the earlier 70% at-grade aspiration is retained as a comparison assumption.
- Use the controlled viaduct families. OSR-Pi20/Pi25 decked beams are the primary products; OSR-US match-cast segments and OSR-SP special crossings address project constraints. Product geometry, complete lift masses, load combinations and independent checking remain release gates.
- Special crossings are separate products. OSR-Pi25 is not stretched to 40 m. OSR hands off to OSR-SP or a local engineering tender at the approach.
- Noise mitigation is structural, not operational. Acoustic screens on viaducts > operational speed restrictions. A 2 m concrete panel costs almost nothing and avoids a permanent speed-limit loss. Operators sometimes skip this; upstream builds it in.
- Seismic detailing is per deployment. The reference viaduct envelope handles $PGA \leq 0.3$ g; above that, the deployment's structural team ups the rebar + bearing spec per EN 1998. The shape stays the same.

12. Rollout

Phase	Deliverable	Dependencies
v0	This RFC ratified	—
v1	<code>osr-routing::civil</code> updated to drop tunnel classes (in this RFC's commit)	v0
v2	Emit <code>[costs]</code> block (<code>at_grade / elevated / bridge / total_eur</code>) per city in the auto-gen output, using the §9 rate table (done 2026-04-22)	v1
v2.1	Extend <code>[costs]</code> to the full CAPEX stack – stations (RFC 0010 archetypes), depots (RFC 0014 archetypes), rolling stock (RFC 0008 families), GoA 4 onboard autonomy/residual wayside train control, station/depot charging microgrids, and EPC overhead. USD is the procurement basis and EUR values are explicit converted views.	v2
v2.2	Move the source cost basis to USD direct-procurement planning rates, add <code>*_usd</code> fields, keep <code>*_eur</code> mirrors, and drop EPC overhead to 7 % (done 2026-06-04).	v2.1
v2.3	Add the railway production-plant setup bucket, now 60 000 USD per vehicle/car module with 120 000 USD retained as a high sensitivity check after 1 m clip-on fiberglass body and distributed-stabling scope reductions (updated 2026-08-15).	v2.2
v2.4	Replace duplicated city production plants with one shared national factory sized to the largest city fleet programme; city CAPEX is zero for this bucket and national briefs carry the asset once. Add imported-value and local-capital financing boundaries.	v2.3
v3	Parametric OSR-Pi20/Pi25 decked beams, transportable OSR-ST6 panels, 3.5 m elevated track centres, 6.5–7.5 m hollow caps, soil/access foundation catalogue, geometry-derived quantities and resource-driven production equations are controlled under design/component-catalogue/src/osr_mech/civil/ . Legacy U-troughs remain special products; OSR-US and OSR-SP cover exceptional geometry. The controlled design-basis, load, egress, movement, erection, first-article, foundation, production and quantity packages live under docs/civil/ .	v0
v4	Surveyed civil design package for the first pilot line, generated from the current city model	v3, RFC 0003
v5	First-article viaduct erected for a deployment instance	v3

13. Relationship to existing work

- [lib/templates/structures.toml](#) – the Lego-block schema. v1 of this RFC removes the `cut-and-cover-tunnel` and `bored-tunnel` entries.
- [crates/osr-routing/src/civil.rs](#) – the inference function. v1 of this RFC collapses the top threshold to `Elevated` (was `BoredTunnel`) and removes the `CutAndCoverTunnel` and `BoredTunnel` variants from `CivilClass`.
- [crates/osr-design/src/emit.rs](#) – the quality YAML emitter. v1 stops counting tunnel length (always zero now) and adds the `elevated-fraction` soft gate.
- RFC 0009 §5 and RFC 0010 §13 reference tunnel alignment / stacked-underground interchange respectively – both amended in this commit to match the no-tunnel invariant.
- [lib/templates/platform-doors.toml](#) references "tunnel stations"; that line is updated to describe full-height PSDs as an optional upgrade for climate-sealed stations regardless of civil class.

14. Open questions

- 1 Grade-separated level crossings – a road underpass below an at-grade rail corridor counts as a structure; does it get its own civil class? v1 folds it into the road authority's scope, not rail's.
- 2 Cut-and-fill extent limits. 3 m is arbitrary. Real deployments in hilly terrain may need 5 m cuts. Revisit with a hilly-pilot case study.
- 3 Acoustic screen effectiveness in hot climates. Concrete screens expand/contract; joints need seasonal inspection. How does that feed the CBM schedule? Candidate `osr-cbm-*` extension.
- 4 Wooden / bamboo viaduct for ultra-low-cost deployments? Real regional-rail projects in parts of South and Southeast Asia have used timber structures historically. Out of scope upstream; a local fork can layer that on.
- 5 Green-roof viaducts – planting integrated into the deck for heat-island mitigation. Candidate v4 addendum.

15. Done criteria

- [x] Two classes only — at-grade + elevated — with bridges narrow (§1)
- [x] No-tunnel rationale explicit with cost comparison (§3)
- [x] At-grade envelope specified (§4)
- [x] Elevated envelope specified, one reference girder (§5)
- [x] Bridge class as a viaduct variant (§6)
- [x] Stations-as-structures mapping (§7)
- [x] Civil inference updated (§8)
- [x] Cost anchors named (§9)
- [x] Constructability constraints stated (§10)
- [x] Pitfalls + alternatives (§11)
- [x] Rollout ordered (§12)
- [x] Relationship to existing code + templates (§13)

The next session picks up at v2 — cost estimates in auto-gen output (a short follow-on to the v1 tunnel-removal already landed in this commit).

RFC 0014 — Depot Design Standard

Source: docs/rfcs/0014-depot-design-standard.md

Status: Draft — planning only, no site drawings ship with this RFC Date: 2026-04-22 Depends on: RFC 0008 Rolling-Stock Reference Design, RFC 0010 Station Design Standard, RFC 0011 Civil Infrastructure Design Standard, RFC 0013 Operations Rulebook

1. Summary

The current city catalogue adopts one full-fleet planning depot per line, sized to that line's complete stock and actual train length. Storage tracks and workload-sized maintenance bays are separate quantities. Depot PV/storage is priced once; property, access alignment, yard topology, installed quotations and morning launch capacity remain releases. The controlled generic quantities are in `city-operating-scope.toml` and each city's `engineering/line-depots/summary.json`. Baghdad retains its dedicated revised scope and financing ledger.

The distributed-stabling pattern below is retained as the earlier reference and simulation comparison. Its passenger-platform parking assumptions do not reduce the current full-fleet depot capital requirement.

1.1 Retained distributed-stabling reference

OpenSourceRail commits to three depot archetypes covering the full range of deployment sizes. Every deployment has exactly one main depot plus optional secondaries and layups. The main depot co-locates with a depot-terminal station (RFC 0010 §1).

The default operating pattern is distributed overnight stabling: clean, telemetry-healthy trainsets may finish service at powered passenger stations or layups near their first morning trip instead of all running empty to a terminal depot. This reduces depot stall requirements, avoids wasteful dead mileage, and lets first departures begin across the line at the same time. The main-heavy remains the maintenance authority. Defective trains are held and recovered to a service point on their own line; maintenance planning must not assume an interline rail connection. Two revenue trains per selected station form the morning launch stock; remaining revenue trains and reserves stable at a powered service point on their own line. Storage tracks are sized separately from workshop bays, using reusable depot/layup blocks.

Archetype	Catalogue max stalls	Heavy maintenance	Overhaul throughput	Notes
main-heavy	20	Yes — overhaul bay, wheelset lathe	≤ 40 trainsets	Larger workshops require a controlled site-specific extension
secondary-medium	12	Light only — brake disc, door actuator, HVAC modules	—	Second depot on a long line
layup-minimal	6	None — overnight stabling only	—	Remote-terminal layup

The catalogue max is the reference layout envelope. The per-deployment workshop requirement comes from §4 ($\max(4, \text{ceil}(\text{fleet} \times 0.15))$). It is not an overnight parking allowance. Requirements beyond that envelope need an explicit site design; a template ceiling must not silently truncate them.

Plus one optional type for edge cases:

Archetype	Purpose
training-wing	Co-located operations-training facility — OCC dispatcher-console simulators, maintenance-technician workshop mock-ups, and recovery-mode-crew briefing rooms. OSR is GoA 4 driverless (RFC 0015), so there are no revenue-service drivers to train — the wing exists for dispatchers, maintainers, station staff, and the recovery-mode crew who operate the manual-fallback joystick (RFC 0015 §8.2). Opt-in on main-heavy; not a standalone depot.

All depots are at-grade. Per RFC 0011 §1 depots are never elevated — the footprint is too large to economically put on viaduct. A deployment that can't site its depot at-grade has an alignment problem, not a depot problem.

2. Non-goals

- Not a workshop management system. How the depot schedules its work — CMMS, parts management, labour planning — is owned by the operator and overlays with the `osr-cbm-backend` output.
- Not an off-line overhaul facility. Major overhauls (wheel reprofiling at 150 000 km, bogie overhaul at 600 000 km, body overhaul at 10 years) happen in the main-heavy depot's overhaul bay. Deployments without a main-heavy either contract overhaul out or depot-trip their fleet to a sister network.
- Not a yard-design manual. Track yard geometry within the depot boundary uses RFC 0009's standard-urban or (for large shunting yards) a depot-specific geometry variant. Detailed yard layout per facility.

- Not an HR / workforce document. Shift patterns and headcount from the ops rulebook (RFC 0013) and the workforce template.
- Not a brownfield-rehabilitation scope. Where a deployment inherits an existing rail workshop (Samawah, Khartoum-Atbara, Karachi Cantt, Maputo Machava, etc.), [RFC 0027](#) governs the conversion of the existing site into an OSR depot. This RFC's archetypes are the greenfield envelope; the brownfield path swaps greenfield depot CAPEX (use the current [cost template](#) and reconcile energy inclusions) for workshop rehabilitation (~\$0.5–2 M building + \$1–3 M new OSR-specific tooling) – an order-of-magnitude saving that the per-deployment plan should commit to whenever assets are real.

3. Why three archetypes

Depots are where the simplicity bet pays off most. The three- archetype set covers:

- main-heavy – the one non-negotiable facility per deployment, where heavy maintenance happens.
- secondary-medium – for deployments whose geography makes defect and light-maintenance access to the main depot impractical.
- layup-minimal – storage at a line's powered service location for stock beyond the two-train station provision; no separate heavy workshop or interline connection is implied.

The catalogue provides reference envelopes. A workshop exceeding the reference bay count needs a controlled extension at the deployment main depot, including access, equipment and staffing capacity.

4. Fleet-sizing formula

Historical distributed-stabling comparison. The workshop and overnight allocation formulas below belong to the earlier reference. Current full-fleet line depots use the workload, storage and price controls linked in §1; the current Samawah quantities are generated in [RFC 0003](#).

Workshop bays are sized for concurrent maintenance and inspection. Two revenue sets stable at each selected powered passenger station where fleet permits; remaining revenue trains and reserves use separate depot stabling tracks:

```
main_depot_workshop_bays = max(4, ceil(total_fleet * 0.15))
secondary_depot_bays = site-specific exception
service_rotation = 0 # depot service is prohibited in peak windows
total_fleet = peak_revenue_trainsets + service_rotation + spare + cold_reserve
station_overnight_positions = 2 * unique_selected_station_count
depot_overnight_trainsets = total_fleet - station_overnight_trainsets
```

The two-train station provision is an overnight allocation constraint. Allocate remaining revenue trains and all reserves to same-line storage, preserving total fleet inventory. Depot storage positions and usable track lengths are sized separately from workshop bays. The earlier Samawah comparison allocated 40 trains to stations and 68 to storage on their own lines: 37 on Line 1, 16 on Line 2 and 15 on Line 3. These comprise 57 revenue, eight spare and three cold reserve trains. The storage requirement totals 4,046 m of usable slots at 59.5 m per train, separately from the existing 17 main-depot workshop bays. Lines 2 and 3 reuse their powered service terminals. Local storage layouts need detailed design; interline depot connections are not part of the operating requirement.

- peak_revenue_trainsets = what the schedule requires at peak. Sized from the physical round-trip cycle vs. the peak headway:

```
traversal_energy_kwh = line_length_km * cars * 2.4 * 1.25 * 1.25
charging_dwell_s = ceil_30s(3600 * traversal_energy_kwh / sum(charger_kw))
charging_dwell_s = clamp(charging_dwell_s, 120, 600)
added_dwell_min = charging_stops * max(charging_dwell_s / 60 - 1, 0)
stop_count = station_count - 2 # radial; station_count for a ring
one_way_min = (line_length_km / cruise_speed_kmh) * 60
               + stop_count * stop_penalty_min
radial_cycle_min = 2 * one_way_min + 2 * 3 + 2 * added_dwell_min
ring_cycle_min = one_way_min + added_dwell_min
peak_revenue_trainsets = max(2, ceil(cycle_min * recovery_factor / headway_min))
```

Current [native emitter](#) parameters:

Family	Cruise km/h	Stop penalty min	Recovery factor	500 kW cabinets per powered station
tram-2car	48	1.45	1.10	1
light-metro-3car	62	1.35	1.62	1
metro-4car	72	1.30	1.30	3
metro-6car	72	1.30	1.45	4

Radials use a three-minute peak headway and a three-minute turnback at each end; rings use a six-minute peak headway. The stop penalty includes the one-minute reference dwell, and only charging dwell above that reference is added. The energy balance uses a 25% climate uplift and a separate 25% charging margin. The larger recovery factors include the emitter's retained onboard-energy resilience allowance; they are planning assumptions requiring city-specific service and energy evidence, not a uniform 10% timetable margin.

These parameters replace the former written 35 km/h proxy and uniform 1.10 recovery factor. Existing city fleet inventories remain declared inputs; reconcile regeneration changes with timetable, energy, cost and physical stabling evidence before adopting a different count. This formula does not enforce two trainsets per station. Station capacity must be checked separately.

- $\text{spare} = \max(1, \text{floor}(\text{peak_revenue_trainsets} / 10))$, for planned maintenance rotation.
- $\text{cold_reserve} = 1$ per line, for unplanned incidents per [RFC 0013 §7](#).
- $\text{service_rotation} = \text{zero}$ dedicated sets. Depot service is prohibited in the 3-minute peak windows and uses surplus peak-fleet capacity when the timetable relaxes to 6 or 12 minutes.

The 12-minute service happens at one designated service depot per line only in lower-frequency windows. During 07:00–09:00 and 15:00–17:00, trains make the normal quick terminal turnback, can use the platform connector, and may deplete the battery further while the 20% section-entry reserve remains mandatory. Interior cleaning, exterior/running-gear walk-around, door, coupler and emergency-equipment release checks, fault-log download, and a 150 kW low-C recharge run concurrently. A red defect removes the set from rotation and uses a planned spare; a clear inspection releases it straight back to revenue service. The opposite terminal may still top up or stable a train, but does not repeat the full inspection on the same round trip.

The 15% workshop concurrency allowance covers overhaul, defect repair, incoming inspection, and planned maintenance. Growth beyond the 20-bay catalogue envelope requires a controlled workshop extension; it does not restore fleet-wide depot parking.

Distributed overnight stabling does not increase the service-rotation fleet. End-of-service dispatch assigns healthy trainsets to powered stations with CCTV monitoring, remote isolation, and at least low-C charging access capped by installed equipment. The 150 kW rate is a top-up target, not a minimum station rating. Morning dispatch releases those sets from their stabled stations so outer stops do not wait for trains to run out from the terminal depot. The main-heavy stall formula remains sized for maintenance, inspection, overhaul, spares, and growth rather than for parking every healthy set every night.

Historical Samawah comparison (September 2026, 3-min peak headway):

- The earlier figures are retained in the [historical Samawah reference](#). The [current city summary](#) adopts the full-fleet line-depot requirement.
- The September 2026 design has fleets of 53, 28 and 27 trainsets: 108 total. The [depot reconciliation](#) derives initial placements and slot-length requirements from the stored scenario. Physical overnight allocation remains unverified.
- `design.toml` emits the depot archetype, terminal assignment, and `fleet_stalls` as workshop/inspection bays from the same run. Older 1.25× fleet-parking examples and hand-calculated 6/4/8 trainset examples were removed from the docs and must not be copied into current deployment documents.

The emitter (RFC 0014 v2) computes this from the `design.toml`'s `fleet_sizing` block.

5. main-heavy envelope

5.1 Functions

- Workshop holding for inspection, scheduled work and defective trainsets (bay count per §4); overnight fleet allocation requires a separate plan.
- Daily inspection of every incoming trainset.
- Weekly inspection (7-day service).
- 30-day inspection (A-class service per EN 50126).
- Light repair (door actuator, HVAC module, brake-disc replacement, battery module swap).
- Heavy overhaul: bogie swap, wheel reprofiling on depot lathe, body-work repaint.
- Wash: automated two-pass wash track.
- Battery-module inspection, coolant service, and sealed-module exchange.

5.2 Physical layout

Area	Target footprint (per consist bay)
Stabling track	1× consist length + 5 m clearance at each end
Daily-inspection bay	Roofed, pit-equipped, overhead power, compressed air, data sync drop (TCN-E monitoring)
Weekly bay	Pit + roof walkway for upper-body access
Overhaul bay	Pit + overhead crane (40 t) + wheel-lathe trench
Wash track	Two-pass automatic with water recycling
PV canopy	4 000 m ² reference allowance; full operating PV inventory needs additional located area (§5.3)
Classroom + office	≥ 200 m ² for operators + trainers
Stores	≥ 600 m ² with rack storage for spare modules

Total main-heavy footprint: ~5 000 m² gross for a 10-stall facility, ~8 000 m² for a 20-stall. These historical workshop envelopes do not include the complete operating PV/storage inventory and cannot be used as total deployment land requirements.

5.3 Energy

- [depots.toml](#) selects the canonical [energy-sites.toml](#) tier. main-heavy uses depot-main: 5,000 kWp PV and 40,000 kWh storage, comprising 80 × 500 kWh stationary modules. Scenario, BOM and layout requirements resolve the same inventory; explicit site overrides must remain traceable. These are retained operating assumptions, not validated depot sizing. Reassess energy duties with distributed overnight station charging before freezing procurement or depot land requirements.
- The old 4,000 m² / 600 kWp / 2,000 kWh scope is a reference allowance. At the catalogue density of 0.15 kWp/m², 5,000 kWp requires 33,333 m² of modules, before access, setbacks and packing. Additional land/canopy and the battery compound are not yet located by the reference CAD.
- Annual PV generation must come from the city energy study with declared weather and loss assumptions. A nameplate rating alone is not annual yield.
- Stationary storage feeds the RFC 0021 DC charging system. Supplier dimensions, conversion/protection equipment, fire separation and installed cost require explicit reconciliation with the fixed depot allowance.
- Grid import/export must satisfy the declared connection limits and utility study. Per [RFC 0002](#), every depot is one physical osr-energy-site, including when co-located with a passenger station.

5.4 Signalling

- A single W-SBC plus an interlocking zone boundary at the depot entry.
- Inside the depot, speed limit 15 km/h, manual operation under mode M3 ([RFC 0013 §5](#)).
- Shunting signals at each stall entry — mechanical dwarf signals driven by osr-wayside-points extensions.
- No ATP envelope inside the depot; osr-atp disables below 15 km/h in depot-tagged geofence, per a safety-bounded configuration. The operational safety envelope inside the depot is line-of-sight + hand-signal coordination.

5.5 Access

- Personnel access: turnstile-gated with ID-card entry, separate from the fleet access.
- Fleet access: one track connection to the line, TPS-style merge per [RFC 0012 §4.3](#) (trains go in — it's a trailing move).
- Road access: for parts delivery, emergency services, depot staff parking. Minimum one 4 m-wide road connection.
- Rail access for deliveries of new trainsets is via the same line connection (new rolling stock rolls in on its own wheels).

6. secondary-medium envelope

- Functions: overnight stabling for ≤ 16 trainsets, daily inspection, weekly inspection, light module swap.
- No overhaul bay. No wheel lathe. No bogie-lift. Anything heavier is trips back to the main-heavy.
- Footprint: ~2 500 m² for 8 stalls.
- Reference PV canopy: 1,500 m² / 225 kWp, with 500 kWh baseline storage.

- Operating depot - secondary tier: 1,500 kWp PV and 5,000 kWh storage (10 × 500 kWh modules); additional placement and installed cost remain open.
- Signalling: same as main-heavy but smaller zone.
- Classroom: none. Reuse the nearest major station's community room if needed.

7. layup-minimal envelope

- Functions: overnight stabling, low-C top-up, cleaning, and a ground-level safety-release walk-around. Trainsets drive in at end of service, can pass through the same 12-minute turnaround service if the site is designated for its line, sit overnight, and drive out at morning service start. There is no pit inspection, repair work, or heavy maintenance.
- Footprint: ~1 000 m² for 4 stalls.
- PV canopy: 600 m² 90 kWp.
- Operating depot - layup tier: one 150 kWh stationary package for opportunity charging during dwell; the main-heavy is primary.
- Train top-up: 150 kW low-C per occupied stabling road, used while a set is held between duties and overnight; passenger-platform fast charging remains a separate terminal function.
- Signalling: single W-SBC at the layup entry; rest is manual line-of-sight.
- No personnel on-site overnight; the OCC monitors via CCTV.

8. Integration with the auto-gen pipeline

Today's emitter picks one depot - terminal archetype ([crates/osr-design/src/emit.rs](https://github.com/osr-design/src/emit.rs), `compute_archetypes`, `priority` rule). That choice is where the main-heavy sits. v2 of the emitter extends this:

- 1 Main depot: co-located with the longest radial line's far terminal. The station archetype is `depot-terminal`; the depot archetype is `main-heavy`.
- 2 Powered station stabling: every other terminal and selected intermediate powered stations receive healthy sets overnight; they do not emit depots.
- 3 Secondary/layup exception: emit only after a site-specific security, utility, access, or defect-recovery study shows station stabling is not viable.

Every depot writes a record into `design.toml`:

```
[[depots]]
station      = "line-a-east"
archetype    = "main-heavy"
fleet_stalls = 4 # illustrative workshop bays; calculate per $4
energy_site_tier = "depot-main" # optional: selected by the archetype
```

The scenario generator resolves depot energy tiers into `[[sites]]` and operating service settings into the simulator input. The simulator ([osr-sim](https://github.com/osr-sim)) models service countdowns and energy flows. A future physical distributed-stabling model must satisfy these requirements:

- Charges each trainset at depot pad power while held and overnight.
- Treat powered passenger stations and layups as valid overnight stabling points when the distributed-stabling policy is enabled in [lib/templates/depots.toml](https://github.com/osr-sim/blob/main/lib/templates/depots.toml).
- Holds a returning train for the configured clean/inspect/recharge slot at one designated depot per line and emits service-start/service-complete evidence.
- Preserves the zero dedicated service-rotation policy and distinguishes planned spares and cold reserve from revenue fleet requirements.
- Feeds the depot battery bank into the network-wide energy balance.

8.1 Executable station-stabling candidate

The simulator supports `station_stabling = true` in scenario `[[fleets]]`, with selected powered-station `dispatch_points`. Stations may use solar/storage without grid import. Waiting trains use up to 150 kW, capped by installed station and shared cabinet/source limits, for low-C top-up to 95% SoC; after closing, returning trains hold at selected stations and resume under schedule, energy and movement-authority gates. This does not require returning healthy trains to the main depot. Before departure, a distributed train must retain the 20% reserve over the route to the next selected charging station, including unpowered stops and terminal reversals. A failed pad or unavailable energy source excludes a destination. A grid outage alone does not disable a battery-backed charger. The gate checks current source availability; it does not reserve future energy against other arrivals. Actual charging debits shared storage, and each next departure rechecks the onboard reserve. Continuous replay verifies the duty. Optional `spare_count` and `cold_reserve_count` are included in each fleet's total inventory and default to zero. Candidates use the city's declared counts; these trains remain parked and can charge without routine dispatch.

The [distributed-stabling workflow](#) generates separate candidates for all catalogue cities and records the Samawah overnight comparison, checking each planned line/station/direction at opening. Plans compare allocated train lengths with the reference platform envelope. The planning/replay acceptance gate also limits overnight allocation to two trainsets per selected station, including reserves. Shared station IDs count once; a four-berth reference platform does not override this provision. The simulator exposes over-capacity queues for diagnosis, and the combined replay fails even when holding, charging and morning departures otherwise pass. Verified physical slots, security, inspection release, reserve activation, defective-train routing, full-day energy duty and deployment acceptance remain open.

9. Pitfalls and decisions

- At-grade only, per RFC 0011. Depots are large; elevating the footprint is prohibitively expensive. The auto-gen emitter rejects depot siting on an elevated section.
- One reference `main-heavy` everywhere. Operators with unique geography (coastal, mountainside) will push for bespoke depots. The upstream catalogue stays at one shape; the deployment's civil team handles the site-specific adaptation.
- Wheel lathe at the `main-heavy` only. Decentralising lathes is tempting (saves depot-trip time) but the operator depth for wheel-reprofiling is thin in target regions; centralising at one site lets that thin team do all the work.
- No pit at `layup-minimal`. A pit adds cost, safety maintenance, and lighting — just for overnight parking. Skip.
- Depot simulation in `osr-sim`. The sim models depot top-up while held plus an explicit service countdown at the designated depot. Cleaning, release inspection, diagnostics, and recharge are concurrent; deeper maintenance remains a separate availability/CMMS model.
- Distributed stabling is not distributed maintenance. Overnight passenger-station stabling is allowed only for healthy sets with remote isolation and CCTV. Any trainset needing inspection beyond the daily release walk-around, fault rectification, wheel work, or battery-module exchange goes to the `main-heavy`.

10. Rollout

Phase	Deliverable	Dependencies
v0	This RFC ratified	—
v1	Shared energy tier, BOM quantities and layout requirements reconciled (2026-09-09); full equipment placement and installed cost remain open	v0
v2	Retained Rust seed and distributed-stabling studies; catalogue post-processing now prices one full-fleet depot per line	v0, RFC 0010 v2
v3	<code>osr-sim</code> turnaround-service state (clean / inspect / diagnostics / recharge), service countdown and event evidence (done 2026-08-12)	v2
v4	Accepted site/access/topology plans for all current Samawah line depots, with separately verified launch and maintenance capacity	Current full-fleet scope, v3
v5	Reference depot CAD under CERN-OHL-S v2	v4

11. Relationship to existing work

- [lib/templates/depots.toml](#) — schema this RFC ratifies.
- [crates/osr-design/src/emit.rs](#) — auto-gen emitter. `depot-terminal` detection today; the `[[depots]]` block emission is v2.
- [crates/osr-energy-site](#) — every depot is one `osr-energy-site` instance; existing integration holds.

- [crates/osr-sim](#) — modest extension for v3; charging semantics already work.
- [RFC 0010](#) depot-terminal archetype pairs 1:1 with this RFC's main-heavy or a mix of main-heavy + layup.

12. Open questions

- 1 Co-located vs detached training wing. Some operators prefer the training simulator in a quiet city building (closer to drivers' homes). The catalogue default is co-located with the main depot; per-deployment override.
- 2 Decentralised battery swapping. A future opt-in where trainsets exchange their battery pack at depot instead of recharging — halves the charging-pad occupancy. Out of scope upstream until battery-swap mechanical designs mature.
- 3 Night-shift head count. Ops rulebook §4.5 (RFC 0013) fixes the shift structure; what's the minimum overnight staff headcount at a layup-minimal? Currently zero (CCTV-monitored); confirm when the first layup-minimal deploys.
- 4 Depot expansion path. A secondary-medium that outgrows its 8 stalls — does it upgrade to main-heavy in place, or is a second-depot-nearby preferred? Likely the latter given construction-on-live-facility complexity.

13. Done criteria

- [x] Three archetypes committed (§1)
- [x] Fleet-sizing formula (§4)
- [x] Main-heavy envelope (§5) + secondary-medium (§6) + layup-minimal (§7)
- [x] Auto-gen pipeline integration (§8)
- [x] Pitfalls (§9)
- [x] Rollout ordered (§10)
- [x] Relationship to existing software + templates (§11)

Next: locate the full PV/storage inventory, reconcile installed cost, and provide track-by-track overnight allocation and conflict-aware run-in/run-out evidence. The quantity contract alone does not satisfy those release gates.

RFC 0013 – Operations Rulebook

Source: <docs/rfcs/0013-operations-rulebook.md>

Status: Draft — planning only Date: 2026-04-22 Depends on: [RFC 0008 Rolling-Stock Reference Design](#), [RFC 0009 Track Design Standard](#), [RFC 0010 Station Design Standard](#), [RFC 0011 Civil Infrastructure Design Standard](#), [RFC 0012 Switches & Crossings](#)

1. Summary

Every OpenSourceRail deployment inherits one baseline operations rulebook — the standing rules for drivers, dispatchers, station staff, and maintenance workers. The rulebook is deliberately short (target ≤ 60 pages in the rendered PDF) and shared across deployments. Operators adapt it for national regulatory overlays but do not re-invent it.

This RFC fixes the rulebook's table of contents and the governing rule-granularity principle. The rule text itself lives in markdown under `docs/operations/` and is owned by a standing committee once the project has one; until then, the project maintainer ratifies additions.

2. Non-goals

- Not a national regulatory document. Every country that adopts OSR has a national rail safety authority (NRSA or equivalent) that must accept the rulebook. This RFC produces a baseline that a deployment's local legal counsel adapts.
- Not a driver training manual. Training content comes from the rulebook, but the pedagogy (lesson plans, sim scenarios, exam questions) is a per-deployment deliverable handled by workforce materials ([lib/templates/workforce.toml](#)).
- Not a safety-case evidence file. The rulebook is an operational artefact; the safety case ([docs/safety-case/](#)) references rules as supporting evidence, not the other way around.
- Not an incident-response playbook. Playbooks are scenario- specific and owned per-deployment (fires, passenger illness, derailment, signal failure); this RFC specifies the categories each playbook must exist for, not the specific response.

3. The simplicity principle

Every rule in the rulebook must pass this test:

A new driver who has never seen this system before can read the whole rulebook in one morning and have an accurate enough mental model to operate safely under supervision by the end of the day.

This means:

- Every rule is one sentence, one decision. No compound rules.
- Every rule has exactly one author (the project maintainer until the standing committee exists).
- Every rule is numbered; operators cite rules by number in incident reports.
- Every rule has a why: a short justification paragraph. No rule is an unexplained ritual.

The target is a ≤ 60 -page PDF. Rail industry rulebooks that hit 200 + pages are artefacts of 150 years of accretion — we're not accruing that.

4. Table of contents — one section per role

The rulebook is organised by role, not by scenario. A driver reads one section; a dispatcher reads another; the sections overlap only where the roles interact.

4.1 Dispatcher rulebook (target ≤ 15 pages)

Section	Scope
S1	Shift start — OCC login, fleet inventory check, schedule ready
S2	Routine dispatching — route grants, timetable adherence, headway maintenance
S3	Incident handling — single-train fault, section unavailable, mass-casualty
S4	Weather and environmental — dust storms, heatwave, flood warning
S5	Maintenance interlock — work-on-track grants, blocking a section from revenue
S6	Shift end — handover, outstanding-event log, system state summary
S7	Intrusion response (RFC 0016) — track-patrol dispatch, return-to-service gating, sustained-Unknown escalation

4.2 Station staff rulebook (target ≤ 10 pages)

Section	Scope
T1	Station opening — power up, PIS check, fare-gate test
T2	Passenger boarding — platform supervision, PSD status, wheelchair assist
T3	Passenger incidents — medical, fare dispute, unattended item
T4	Fare enforcement — inspector on-board, non-payment, appeal
T5	Station closure — evacuation, power down

4.3 Maintenance worker rulebook (target ≤ 10 pages)

Section	Scope
M1	Depot safety — hazard awareness, PPE, lone-worker protocol
M2	Work-on-track authorisation — formal blocks, protection signals, access to active ROW
M3	Routine track inspection — walking the line, visual checks, GPM/RECD recording-car cadence (per RFC 0009 §9)
M4	Switch maintenance — blade lubrication, detection-sensor cleaning, 30-day check
M5	Fleet maintenance at depot — inspection intervals (daily / 7-day / 30-day / overhaul)
M6	Incident site access — derailment response, fire site, crane operations
M7	Wayside sensor maintenance (RFC 0016) — 30-day walkthrough, post-weather inspection, sensor replacement + calibration

4.4 Control-centre rulebook (target ≤ 5 pages)

Section	Scope
C1	OCC watch roles — dispatcher, supervisor, engineer-on-call
C2	Communications — radio discipline, PA authority, external-party notifications
C3	Shift handover — written log, outstanding items, emergency-on-call list

Total target: 40 pages across four sections.

5. Degraded-mode operations — the important part

Modern CBTC metros routinely run in "normal mode" (full ATO under a fresh MA) and have short, mission-critical manual-restoration procedures when the signalling degrades. OpenSourceRail keeps exactly three degraded modes:

Mode	Trigger	Operator action
M1 — Automated restricted MA	ATO is healthy and ATP can enforce a shortened MA	OCC authorises reduced-speed automatic movement; ATP remains fully active and speed is capped at 80 % of normal.
M2 — Controlled stop	Consensus cannot issue a trustworthy MA	Every affected train remains stopped while OCC establishes a work block and restores the signalling quorum. No written order may bypass ATP.
M3 — Protected depot shunt	Movement is required inside an isolated depot worksite	An authenticated local maintenance pendant requests automatic movement at ≤ 15 km/h under ATP, direct CCTV observation, and a locked work zone.

No intermediate modes. No "sort-of-ATP" states. Either the safety envelope holds (modes M1 / M3) or the train remains stopped (mode M2). This is a forcing decision: ambiguous degraded modes are the dominant cause of metro-world incidents.

6. Weather-dependent rules

Target regions routinely experience weather conditions that challenge legacy rolling stock:

- Dust storm (haboob): visibility < 100 m automatic speed cap at 50 % (osr - ato enforces). Dispatcher issues a network-wide speed restriction at the OCC. Passenger announcements via osr - pis - onboard. See also [lib/templates/climate-adapters.toml](#).
- Heatwave (> 45 °C sustained): rail-expansion risk triggers a pre-emptive 15 % speed cap on mainline-mixed and standard-metro presets with continuous-welded-rail. Switch detection sensors recalibrate at dawn.
- Flooding: any rainfall > 50 mm / h triggers immediate inspection of at-grade segments; the dispatcher can preventively block sections via osr - interlocking's maintenance-override. Elevated segments per RFC 0011 §5 are unaffected by surface flooding — deliberate design bet.
- Lightning: nearest-strike distance < 2 km Cat.22 5G backhaul and LoRa backhaul are both watched for outage; if both fail for > 10 s the operator notifies the OCC and cooperates with osr - atp's default fail-restrictive MA.

7. Incident categorisation

Every incident fits one of six categories. This drives the notification chain and the regulatory report:

Category	Example	Dispatcher action
I1 – fleet self-recovery	Door interlock fault on a single train, resolved at next terminal	Log in event recorder; notify depot; no regulatory report.
I2 – service disruption	Single-train immobile; next train coupled to rescue it	Passenger PA, timetable recovery plan; 24h incident report.
I3 – short safety event	Emergency brake triggered by spurious trip; no injury	Log, investigate root cause, 72h report.
I4 – passenger injury	Slip, fall, medical emergency on board	Medical call, depot handover; formal incident report to NRSA within 7 days.
I5 – collision / derailment	Train-to-train, train-to-obstacle, train off-rail	Full network shutdown of affected line; NRSA notification within 2 hours; incident-site preservation.
I6 – mass-casualty / fire	Onboard fire not extinguished, large-scale passenger injury	Immediate evacuation protocol; emergency services; NRSA + national media escalation.

The categories map directly to `osr - event - recorder` tags, so the post-incident analysis starts from the same data the categories describe.

8. Training and recurrent qualification

- Initial driver qualification: 4 weeks classroom + 2 weeks simulator + 4 weeks supervised revenue service. Final qualification exam in written + simulator + on-road segments.
- Recurrent: 2 days refresher every 12 months + 1 simulator session per quarter.
- Degraded-mode drills: every driver runs modes M1 / M2 / M3 in the simulator every quarter. The `osr - sim` is the primary training platform.
- Dispatcher qualification: 8 weeks OCC-side classroom + simulator + supervised desk time.
- Maintenance: role-specific certification per EN 50126 / per national NRSA rules.

Training content is a deployment deliverable; this RFC fixes the minimum hours + structure.

9. Auto-gen implications

The rulebook does not directly feed the corridor-generation pipeline — but it does feed two outputs:

- 1 Depot capacity: `osr - sim`'s fleet-sizing needs to include enough spare trains for the rulebook's degraded-mode operations. A deployment with 10 trainsets on rostered revenue needs ≥ 1 spare in depot for maintenance (M5) and ≥ 1 cold- reserve for I-category incidents. See RFC 0014 §4 for the formula.
- 2 Workforce sizing: the driverless financial model supplies group FTE; [lib/templates/workforce.toml](#) allocates those totals into city roles, skills and tasks. The [city delivery generator](#) writes the organisation and spreadsheet. Named duty/leave cover must still be checked against the rulebook's shift structure (§4.5).

Changing this prose does not change software parameters automatically. Update the controlled model/template inputs, regenerate and check fleet and workforce evidence when operating rules change.

10. Pitfalls and decisions

- One rulebook across deployments is a big bet. Legacy metros each have their own 200-page rulebook; consolidating to one is the simplicity gain. National NRSA's will initially resist. The counter: the process of NRSA approval works on a per-document basis, not per-system basis — a shorter document approves faster. The operator carries the regulatory overlay in a thin appendix.
- Six incident categories, not more. Operators unused to this regime sometimes want a I7 or I8 for niche scenarios. We absorb niche scenarios into the existing six rather than proliferate.
- Paper written orders are allowed in mode M2. This is not anti-digital — paper is explicitly the fallback when the digital system degrades. Written orders remove ambiguity about authority when the digital system can't issue it. Rare enough that the paperwork tax is tiny.
- No "caution mode" between M1 and M2. Legacy metros have a smorgasbord of half-ATP-half-manual modes; every one is a source of operator confusion. We commit to the hard boundary.
- ≤ 60 pages is a hard target. The rulebook is reviewed on every minor-version bump; if it exceeds 60 pages, something gets cut. Adding text is easier than subtracting.

11. Rollout

Phase	Deliverable	Dependencies
v0	This RFC ratified	—
v1	docs/operations/ scaffold with per-role stub files for dispatcher, station staff, maintenance, and control-centre roles, each with scope + cross-refs + proposed rule outline (done 2026-04-22)	v0
v2	Full unattended-operations rulebook drafted across all four role families. Every rule is one sentence + a why : paragraph, cross-referenced to the relevant crate and safety-case solution. Practising-operator review is v2.1 per-deployment work.	v1
v3	NRSA submission pack for Samawah (rulebook + safety case cross-reference)	RFC 0003 §5, v2
v4	osr - sim scenario library covering every degraded-mode scenario for operator refresher training	v2

12. Relationship to existing work

- [lib/templates/workforce.toml](#) — shift-structure + headcount inputs. v3 of this RFC aligns the two documents.
- [lib/templates/service-hours.toml](#) — service hours drive the rosterable workforce; the rulebook sets the rostering envelope.
- [docs/safety-case/](#) — references specific rulebook rules as "solution" evidence for goals around fail- restrictive operation, evacuation readiness, and training competence. GSN goals for "operational fail-restrictive behaviour" land in v4.
- [crates/osr - occ](#) — the dispatcher's OCC UI embeds the dispatcher rulebook's decision-support prompts. Software change in v3.

13. Open questions

- 1 Bilingual rulebooks. Every target-region deployment operates in at least one local language plus English. Do we maintain both upstream? v2 commits on this: likely yes, with English as the canonical and translations as separate branches in docs/operations/<lang>/.
- 2 Printable-PDF vs living-document. Rail NRSA's typically want a static PDF they can archive. The project wants a live document. Compromise: every minor-version bump produces a sealed PDF, and the commit hash is the canonical reference.
- 3 Simulator-based competence testing. osr - sim can evaluate driver actions against MA envelope in software. Can NRSA's accept simulator certification in lieu of on-road supervised hours? Per-country, probably not at v1.

14. Done criteria

- [x] Table of contents per role (§4)
- [x] Degraded-mode operations (§5)
- [x] Weather rules (§6)
- [x] Incident categorisation (§7)
- [x] Training envelope (§8)
- [x] Auto-gen implications (§9)
- [x] Pitfalls (§10)
- [x] Rollout ordered (§11)
- [x] Relationship to existing work (§12)

The next session picks up at v1 — docs/operations/ scaffold, short editorial PR that seeds the per-role files. Actual rule text lands in v2.

Reproducible city operating twins

Source: <docs/operating/city-platform.md>

Each city has a reproducible business operating baseline alongside its railway engineering baseline. ERPNext provides the native operating records. The OSR integration compiles planning inputs and returns permission-filtered execution snapshots; it never issues railway release authority.

Configuration layers

Layer	Location	Purpose
Shared configuration	generic.toml	Departments, warehouses, task categories, programme tasks and planning calendar defaults
City overrides	<code>cities/catalogue/<region>/<country>/<city>/operations/erpnext.toml</code>	Identity, local calendar, organisation, operating release and additional city tasks
Compiled package	<code>build/erpnext/cities/<slug>/</code>	Effective configuration, complete task plan, dependency graph and checksummed summary
ERP execution	Native Project, Task, Department, Warehouse, Cost Center	Actual work, assignments, dates, timesheets, costing and business document workflows
Twin feedback	Private <code>var/erpnext/operating-twins.json</code>	Observed task/category/asset status, recorded hours, task costs and project-linked business document counts

All 266 catalogue cities have specific override files. The compiler derives their actual task and asset scope from their own generated operations bundle; it does not reuse Samawah's tasks for another city. See the [Samawah profile](#) and [Mosul profile](#) for local timezones, illustrative six-day construction calendars and distinct city work packages. Other profiles inherit the shared planning assumptions until a city operator supplies overrides.

The [catalogue readiness gate](#) validates all 266 configurations against their own tracked asset, manifest and project-twin evidence. Supervision can compile directly from those reviewable assets for every city. Full ERP task plans additionally need the deterministic compressed operations payload: Samawah and Mosul keep it locally in Git, while the other 264 materialise it with `./osr city <slug>` before import. A manifest is not treated as a substitute for the task records it hashes.

Tables merge recursively. Lists explicitly replace the shared list. Unknown keys fail validation. `city_programme` adds city tasks to the shared programme; each task needs a unique ID. Removing a department requires updating every task category/programme reference that used it.

The generic company, calendar start date and timezone are unset. The shared Monday–Saturday calendar and the Iraq examples are planning assumptions, not claims about an operator's actual roster or approved public holidays. No employee, supplier, bank, payroll, tax or commissioned asset data is invented.

Repeatable deployment

```
# Creates missing profiles; existing overrides are preserved.
./osr erp city init-configs
./osr erp city validate
./osr readiness --check

# The target company must already exist in ERPNext.
./osr erp city prepare samawah --company 'OpenSourceRail Evaluation'
./osr erp import build/erpnext/cities/samawah/plan.json \
  --company 'OpenSourceRail Evaluation'

./osr erp city prepare mosul --company 'OpenSourceRail Evaluation'
./osr erp import build/erpnext/cities/mosul/plan.json \
  --company 'OpenSourceRail Evaluation'
./osr erp snapshot
```

Replace either slug with any catalogue city. If its generated operations bundle is missing, run `./osr city <slug>` first, or supply a generated bundle with `prepare --bundle <path>`. Generation and preparation do not contact ERP. Review `effective-config.json`, `summary.json` and `plan.json` before import.

To make company binding permanent, add `[organisation] company = "..."` to the city profile. CLI `--company`, `--start-date` and `--release` overrides are captured in the effective configuration and its checksum. No credentials belong in tracked city profiles; use separate private site configuration.

When updating the integration code on an existing site:

```
./osr erp backup
./osr erp build
./osr erp up
./osr erp bench migrate
```

Functions supplied by the city package

- Manufacturing delivery: native Tasks with OSR manufacturing identity, task types, baseline day offsets and native predecessor relationships.
- Maintenance planning: fleet work maps to Fleet Maintenance; other assets map to Infrastructure Maintenance. Source cadences, triggers and evidence remain attached. Operators turn approved schedules and actual commissioned assets into native Asset Maintenance/Repair workflows.
- Assurance coordination: native Tasks for QA actions retain the railway hold point, asset, evidence and release-authority references. Completing them in ERPNext does not close OSR NCRs or approve railway handback.
- Procurement packages: requirements are grouped by sourcing route, with their earliest order-by and latest required-by day. All original BOM and sourcing requirements remain in the source record. Use native Material Request/Quotation/Purchase Order forms after resolving real items, quantities, suppliers, currency and approvals. The [procurement automation](#) also converts a selected requirement into a native draft Material Request once the operator provides its Item, verified stock-unit quantity, date and city warehouse.
- Programme and people: tasks for governance, business masters, workforce planning, maintenance readiness, assurance responsibilities and recovery, plus the city's own additional tasks.
- Organisation: stable native departments, warehouse locations and a city cost centre, scoped by company and city. Task Types are shared. No existing roles or user permissions are expanded by the configuration process.
- Digital-twin feedback: native Project forms gain an OpenSourceRail Operating twin action. Workbench displays matching ERP execution in the Project Twin view, and the operating page compares city baselines and asset workload. Hours/costs come from native Task costing; these are not the full general ledger or the city's generated CAPEX estimate.

Project and Task forms keep their source evidence, checksums and configuration under an OpenSourceRail reference tab, alongside the native business tabs.

Relative working days map to dates only when `calendar.start_date` is set. Weekends and explicit holidays are skipped, including negative mobilisation offsets. A non-working anchor rolls forward to the next working day. The compiler rejects missing dependencies, cycles, duplicate IDs, invalid calendars, mixed-city records and checksum mismatches. Native ERP dependencies retain ERPNext's business semantics, including its treatment of cancelled tasks.

Baselines, upgrades and operator edits

The first operating release (`release = "1"`) upgrades the earlier Project/Task import in place when source identity and hashes match. It fills empty type, department and date fields, adds dependencies only when none exist, and preserves existing task IDs, status, progress, assignments, priorities and operator-entered planning fields. It also creates the new work categories. Subsequent identical imports skip configured tasks and reuse city masters.

A changed configuration or source package cannot silently replace an applied baseline. Increment the city's `release` and prepare again to create a separate reviewable project baseline. Existing records stay intact. There is no automatic transfer of actual costs or approval of a new release. Workbench's engineering view shows execution only when exactly one exported ERP project matches the city and engineering revision; multiple candidates require explicit review on the operating page. No release is silently selected as authoritative.

Imports use native document validation, one database transaction and a final project-total recalculation. A failure rolls back new masters/tasks and metadata. The importer preloads permitted task identities and uses ERPNext's native project bulk-update flag to avoid recalculating thousands of records repeatedly. Use the bench-backed CLI for large city packages; a synchronous HTTP import can exceed a deployment's request timeout. Native task-tree updates can hold database locks during large imports, so schedule them outside active task editing.

Refreshing the integrated twin

```
# One private, atomic export. Previous valid feedback survives export failures.
./osr erp snapshot

# Linux user timer: refresh every five minutes, using the local Docker/bench site.
./osr erp feedback start
./osr erp feedback status
./osr erp feedback stop
```

The timer and service are installed under `~/ .config/systemd/user/` as `osr-erp-feedback`. The user session and container runtime must be running. The snapshot file is mode 0600 in a private directory; OSR's static server does not expose it. Only the loopback Workbench exposes the aggregate snapshot endpoint. Shared/network deployments need an authenticated integration service and their own permissions; this local bridge is not a shared-host auth scheme. The bundled single-site proxy validates browser WebSocket origins and routes ERP notification authentication through the internal Compose network. Review that proxy configuration when adding a public domain or TLS termination.

ERP callers can GET `/api/method/osr_erpnext.city_runtime.city_status?project=...`. The method checks Project access and uses native permission-filtered lists for Tasks and business documents. Unavailable document categories are marked unavailable, not reported as zero. No employee personal details are exported. The local bench export runs with the site's administrative visibility.

Snapshots show their observation time; the UI labels snapshots older than one hour. Refresh view reads the latest exported file; it does not claim to query ERP directly. ERP unavailability leaves the previous snapshot available with its original timestamp and does not affect railway control.

Verification

```
tools/automation/osr-python -m pytest -q \
  tools/automation/tests/test_erpnext_city.py \
  tools/automation/tests/test_erpnext_planning.py
./osr_erp_city_validate
```

The tests cover configuration inheritance, every city's identity, working-day calendars, dependency rejection, deterministic packages, import fingerprints, legacy keys and company/release separation. Live validation should additionally exercise native imports, repeated imports, permission-filtered feedback and the Project/Workbench views against a private ERP site.

Upstream behaviour: [ERPNext Tasks](#), [Asset Maintenance](#).

Deployment Planning Reference

Source: [docs/deployment-planning-reference.md](https://docs.opensource-rail.org/deployment-planning-reference.md)

This page defines the common interpretation of every generated OpenSourceRail city README and national brief. Location folders contain only local inputs, calculated results, exceptions and evidence links. Shared assumptions belong here or in the linked machine-readable templates—not in hundreds of generated copies.

Generation And Review Boundary

The city catalogue is deterministic:

```
city catalogue + OSM/raster evidence + shared templates
- routed network + stations + service + fleet
- energy, civil, CAPEX and finance calculations
- engineering and simulation evidence
- concise city README and national aggregation
```

Generated READMEs are indexes and decision summaries. The authoritative local inputs and results remain `design.toml`, the expanded scenario TOML, and the JSON/GeoJSON evidence inside each city folder. Git records changes to inputs, generators and outputs together. Do not hand-edit a generated city or country README; change its source or a shared template and regenerate it.

Network And Station Planning

`osr_geo` rasterises source-locked OpenStreetMap roads, buildings, water, protected areas and demand anchors onto the planning grid. `osr - design` uses a demand-rewarded least-cost route, places stations against the demand surface, and classifies each segment as at-grade, elevated or bridge. Tunnels are not in the upstream catalogue.

The standard spacing policy is 1.6 km in central areas, 3 km in ordinary urban areas, and up to 7 km on low-demand outer approaches. Cross-line platforms inside the 600 m station-complex envelope are consolidated as one interchange. Coverage, transfer reachability, civil mix and source hits are reported in each city's `*.design-quality.yaml`; they are planning indicators rather than survey acceptance.

Service, Fleet And Capacity

The default service is GoA 4 battery-electric operation with line-specific time windows and headways. Fleet sizing covers peak revenue service, planned maintenance spares and cold reserve. Off-peak surplus performs terminal or depot inspections without creating a second service-rotation fleet unless a local schedule proves one is required.

Healthy trainsets may stable overnight at protected powered stations near their first departure. Red defects, overdue heavy maintenance, isolation failures or security failures return a set to the main depot. Station stabling requires charging, CCTV, remote traction isolation, emergency access and an OCC-assigned track slot.

Capacity uses the selected trainset family's AW2 planning capacity, the actual generated timetable and a controlled practical load factor. The annual paid-trip range is a capacity-use scenario, not a ridership forecast. Replace it with a surveyed demand model before an investment decision.

Energy Method

Each city calculation combines:

- trainset energy per car-km and the generated timetable;
- climate and non-revenue movement factors;
- opportunity charging at powered stations;
- station/depot PV and stationary LFP storage;
- a dedicated solar plant or equivalent PPA asset for the remaining annual traction-energy requirement; and
- residual grid import after those assets.

The generator checks every line's powered-stop gap, traversal energy, delivered charge, protected onboard reserve and operating margin. These are feasibility screens; grid connection, protection, harmonics, thermal, fire and local solar yield studies remain deployment work.

Civil And Cost Method

Civil geometry is generated from the parametric source and exported to IFC4.3 for Bonsai coordination. Checked quantities feed the generated [civil-cost-model.toml](#), which is then consumed by city CAPEX, finance, IFC properties and documentation. Current design targets are 2.584 M USD/route-km at-grade, 9.748 M USD/route-km elevated and 18 M USD/route-km for bridges. The retained 3/12/18 M benchmarks remain visible for audit.

These figures are unquoted planning targets. Land, utilities, tax and duty, site geotechnics, project risk, programme, independent checking and local supplier rates must be added or validated before procurement. The complete shared cost basis is in the [generated cost model](#).

Capital And Finance Method

City CAPEX includes civil works, stations, depots, rolling stock, residual train control, charging interfaces, timetable-sized dedicated solar and EPC/project services. The national trainset factory is excluded from cities and counted once in each national brief, sized to the largest single-city fleet programme.

The catalogue's controlled core concepts adopt elevated land sections and straight radial tangents where analytical geometry permits. Water crossings remain bridges; retained unsuitable fragments keep their geometry review gates. Core boundaries are design-centroid planning screens requiring survey, property and obstacle confirmation. Immutable seeds preserve the original line inventory, including rings.

The current line-depot scope stores the full fleet, including spares, in one planning depot per line. Train length sets storage track quantities; measured maintenance workload remains a release requirement for workshop bays. Depot PV/storage reference equipment is included once in depot capital. Land, utility upgrades, installation and site acceptance remain open.

Station staffing uses two posts, two normal eight-hour shifts and additional cover for the actual service window. Paid hours are reduced for leave, training, sickness and handover. Country income proxies are retained estimates: basic wages start at 150% of that proxy, technical grades at 225% and management at 300%, plus 25% employer and 10% overtime allowances. Baghdad's dedicated revised scope retains its separate indexed Iraqi wage evidence.

City-order factory requirements use the actual train family and consist. Facility readiness is 18 months; qualification and serial manufacture follow it. Short civil programmes explicitly wait for fleet readiness. The national factory allowance is the larger of the module-based allowance and independent city-order physical envelopes, counted once. Concurrent national loading and sequencing require a separate accepted programme.

The procurement-origin model separates imported value—the minimum foreign currency or international-capital requirement—from locally supplied labour, materials, fabrication and services that can use domestic funding. Country finance parameters define construction period, debt rates, tenor and the local bond/equity split.

For Iraq, the primary proposal is the [schedule-linked funding programme](#). It assigns proposed Chinese buyer credit only to assumed eligible imported component invoices, then splits the remainder among government appropriations, IQD bonds and IQD bank credit. The [controlled assumptions](#) remain uncommitted. Monthly native-currency debt schedules, interest on staged draws, fees, reserves, public support and downside cash gaps are explicit. Construction uses the actual resource-constrained procurement milestones under an assumed 260-working-day year; the generic five-year financing comparator does not define the Iraq construction schedule. Physical and operational release gates remain open even when all planning example artifacts are regenerated.

The foreign-turnkey comparison is an editable like-for-like sensitivity, not a vendor quotation. Both cases use the same network, fleet, service, energy scope and financing schedule. Replace the multiplier, external share and all funding terms with scope-normalised bids and signed lender terms before approval.

OPEX, revenue, NPV, IRR and DSCR outputs are planning screens. Capacity-use scenarios are not demand forecasts, and no grant, tax treatment, land-value capture or lender commitment exists unless explicit controlled evidence says otherwise.

QA, Maintenance And Assurance

Shared construction QA gates, manufacturing travellers and maintenance intervals are generated from the controlled templates. City-specific asset counts and schedules are materialised in the local operations bundle. The common system covers civil works, trackform, stations, rolling stock, passenger systems, energy, signalling/comms, depots and integrated trial running.

Generated evidence proves internal consistency and reproducibility—not railway certification. Survey, geotechnical release, structural design, fire/egress, product acceptance, calibrated operations modelling, independent safety assessment and authority approval remain deployment responsibilities.

Local Evidence Contract

Each city README links the current status of these local artifacts:

Artifact	Purpose
design.toml	Authoritative generated network, fleet and CAPEX design
<slug>.toml	Expanded simulator scenario
<slug>.design-quality.yaml	Coverage, routing and civil-quality gates
engineering/finance/summary.json	Reconciled CAPEX, OPEX and finance cases
engineering/simulation/validation-summary.json	Nominal and degraded simulation acceptance
engineering/gis/summary.json	GIS package provenance and layer counts
engineering/sumo/summary.json	Executed timetable screening
engineering/energy/summary.json	Grid, charging and solar screening
operations/	Asset, QA, manufacturing and maintenance evidence

The README generator verifies source hashes and passing status before publishing these evidence links. Repository health also regenerates city and country pages and rejects drift.

Regeneration

```
# One city
tools/automation/regenerate-city.sh samawah

# Complete catalogue, using current caches
tools/automation/regenerate-all.sh

# Documentation, links and generated drift
python3 tools/automation/check-readmes.py
python3 tools/automation/check-markdown-links.py
python3 tools/automation/repo-health.py --quiet
```

Changes to common assumptions should normally touch one template or this page, then regenerate affected outputs. Location folders should change only when their local input, calculated result, evidence or explicit exception changes.

Ballastless Slab Trackform Designs

Source: docs/civil/slab-trackforms.md

This note records the OSR planning-grade slab trackforms for urban at-grade and elevated sections. The parametric CAD source lives in [design/component-catalogue/src/osr_mech/civil/slab.py](#).

The designs are reference envelopes for cost, clash, fabrication, and constructability review. Deployment partners still need local structural checks for concrete grade, reinforcement, geotechnical support, drainage, stray-current control, thermal movement, seismic load, flood/scour, and product acceptance of the direct-fixation fasteners.

At-Grade Urban Slab

Long open, machine-accessible corridors use a continuously slipformed slab by default. The table below defines the six-metre single-track ST6 product kept for constrained streets, utility crossings, short possessions, flood-prone and replaceable zones. Both methods retain the same controlled track support section and concrete quantity basis; a project method-zone schedule determines panel counts.

Item	Reference value
Trackform	OSR-ST6 single-track transportable panel; two rows form double track
Panel length	6.0 m
Overall panel width	2.9 m
Track-centre spacing	3.5 m
Base slab thickness	250 mm
Rail plinth width	380 mm
Rail plinth height above base slab	160 mm
Direct-fixation pitch	Maximum 650 mm; centred 600 mm on the 6 m reference module
Rail seats per 6 m panel	20
Nominal concrete per 6 m panel	5.08 m ³
Planning bare panel mass	12.7 t

Use ST6 where the corridor is in a constrained street, utility or transition zone, short possession, flood-prone location, station interface, depot throat, or other place where ballast dust, tamping possessions, and loose aggregate are unwanted.

The slab uses two edge troughs for drainage, low-voltage/data routing, and maintainable cable access. The direct-fixation plinths are continuous so baseplates can recover small alignment tolerances without breaking out concrete.

Elevated Deck Slab

Item	Reference value
Trackform	Local direct-fixation plinths over thin non-structural alignment layer
Panel length	6.0 m
Overall alignment-layer width	2.7 m
Deck compatibility	Fits the 2.9 m OSR-Pi20/Pi25 flange
Alignment layer thickness	40 mm; may be omitted by project design
Rail plinth width	380 mm
Rail plinth height above base slab	160 mm
Direct-fixation pitch	Maximum 650 mm; centred 600 mm on the 6 m reference module
Rail seats per 6 m panel	20
Nominal concrete per 6 m panel	1.38 m ³

Use one elevated trackform run per single-track Pi-beam. A double-track elevated section therefore uses two parallel Pi-beam/trackform assemblies.

The Pi-beam upper flange is the structural deck. The alignment layer provides local tolerance recovery only and may be omitted where surveyed casting plus adjustable baseplates can recover rail geometry. A full-width reinforced or floating slab is reserved for locations where a vibration/noise and structural study justifies its dead weight.

The cable/drainage trough is installed on the inner/non-egress side. The separate outer 1.0 m walkway/barrier cassette remains clear of service covers, cabinets, screen posts and other permanent obstructions.


Iraqi manufacture and complete seat kits

The [Baghdad detailed engineering plan](#) adds the local slab production route, prototype inspection, lifting/bedding requirements and a complete fastener child schedule. The 6 m module has ten seats per rail centred at 300, 900, ..., 5700 mm, avoiding the former pad projection beyond the panel ends. Supplier anchor edge distances still require release. Continuous-run quantities retain the existing 650 mm planning basis; precast method zones use their own panel/seat installation schedule.

Concrete volume and bare mass cover base/plinths only. The CAD service troughs are allocation envelopes; covers, drainage sections, steel, inserts, bedding and rigging need separate schedules. Make panels, cages, moulds, ducts and suitable metalwork in Iraq; source qualified fastener/anchor systems initially and qualify any localisation through system fatigue, stiffness, insulation and process tests. The catalogue does not issue a rebar schedule, mix grade, lifting approval or supplier drill pattern.

FreeCAD Scene Renders

The slab trackforms are shown below in station context with driverless rolling stock and the station access elements that affect civil cost.

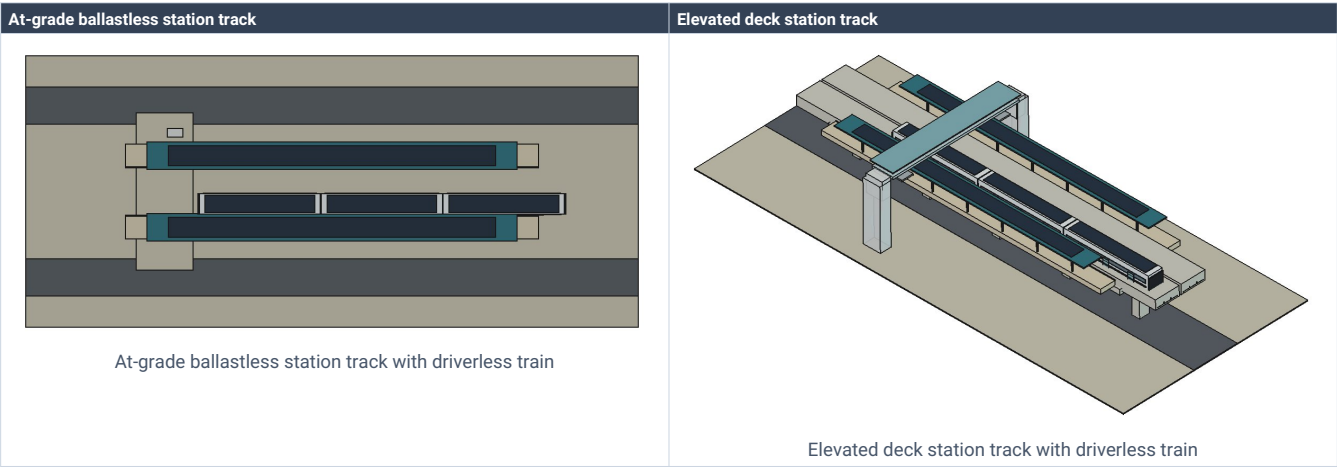

The source scene document is [design/component-catalogue/models/cad/station-scenes.FCStd](#) and is regenerated with [design/component-catalogue/scripts/freecad_station_scenes.sh](#).

Fabrication And Installation Rules

- Slipform long accessible runs over the released machine-controlled formation. Keep the 6 m ST6 module for constrained and replaceable zones; use closure pours only at turnouts, station ends, curves that require local survey correction, and transitions to bridge/special spans.
- Cast embedded inserts, earthing/bonding points, drainage scuppers, and lifting anchors in the precast yard.
- Require surveyed casting beds and a dimensional QA record for every batch.
- Use adjustable baseplates on all running rails.
- Keep prestressed elevated girders conservative; recycled aggregate and aggressive low-carbon mixes can be used first in non-prestressed slabs, piers, pile caps, and station modules.
- Treat direct-fixation pads, anchors, and baseplates as replaceable wear/interface parts, not as buried civil structure.

Cost Model Link

These slab designs feed the generated civil planning contract:

Civil class	Design-derived target	Retained benchmark
At-grade ballastless slab	2.584 M USD/route-km	3.0 M USD/route-km
Elevated guideway with local-plinth trackform	9.748 M USD/route-km	12.0 M USD/route-km
Bridge/water-crossing guideway	18.0 M USD/route-km	18.0 M USD/route-km

The active values come from [civil-cost-model.toml](#) and are planning targets, not tender or turnkey EPC estimates. Build the project estimate from [viaduct-quantity-cost-model.toml](#) plus site rates, utilities, access, risk, programme, independent checking, and contingency. Short elevated stubs, stations, soft ground, deep utilities, tight curves, or repeated

special spans carry project-specific premiums.

OSR Rapid Viaduct Kit – Design Basis

Source: <docs/civil/viaduct-design-basis.md>

Status: controlled planning basis; not a construction design
Primary products: OSR-Pi25 and OSR-Pi20 prestressed decked single-track beams
Special products: OSR-U25-SPECIAL acoustic/project-specific trough, OSR-US segmental U/box, and OSR-SP special crossing

Catalogue boundary

Two identical 2.9 m-wide decked pi-beams share a single-column pier at the same 3.5 m tangent track centres used at grade. Each beam has two stems beneath the rail lines and a full-depth upper flange forming the structural track deck. Separate 1 m outer walkway/barrier cassettes give a controlled 8.5–9.0 m twin-track envelope. Pi20 and Pi25 come from one long-line mould with movable stop ends. A 30 m beam is not in the catalogue.

Product	Controlled use
OSR - Pi25	Tangent and broad-curve normal span; target bare mass 65–75 t
OSR - Pi20	Closure bays, junctions and utility avoidance; target bare mass 50–60 t
OSR - U25 - SPECIAL	Project-specific acoustic/containment trough after transport, lift and structural release
OSR - US	2.5–3.0 m match-cast segments where access or curvature prevents full-span erection
OSR - SP	Separately engineered I-girder, steel-composite, or segmental crossing over 30 m; turnouts and exceptional crossings

The OSR-US review model places each 2.5–3.0 m chord on a surveyed circular arc, with rotated match-cast joint planes and chord-following tendon corridors; it is no longer represented by a straight full-span extrusion with markers.

The default Python geometry is `osr_mech.civil.decked_pi`; legacy troughs stay in `osr_mech.civil.ugirder` as special products. Flange/stem proportions, diaphragms, anchorages, tendons, lifting zones, reinforcement, fatigue, derailment, vibration and rail–structure interaction remain supplier design and independent-check releases.

Actions and design situations

Use the deployment country's adopted standards and combinations. The design must include the complete deployment train: the LM3 reference has 12 axles; Baghdad's six-car baseline has 24 axles. Its supplier axle positions and loaded axle distribution must be frozen before moving-load analysis. A 16 t infrastructure axle allowance does not replace the full consist loading pattern. Also include dynamic amplification, braking, traction, nosing, centrifugal force, wind on empty and loaded trains, derailment/containment, collision, maintenance and rescue vehicles, temperature, creep, shrinkage, fatigue, seismic/foundation interaction, and every lifting, transport, temporary-bracing, and erection stage. The machine-readable seed is [viaduct-load-model.toml](#).

Decked pi sections require three-dimensional analysis for torsion, transverse distribution, asymmetric loading, local flange/stem actions, end-zone bursting, camber, creep, shrinkage, fatigue and staged prestress. Final reinforcement, tendons, anchorages, bearings, foundations, rail/bridge interaction, and temporary works require independent checking by licensed bridge and geotechnical engineers.

Geometry and constructability gates

- A straight 25 m full-span unit is preferred at radii of about 300 m or more.
- Below about 300 m, use Pi20, OSR-US, a shorter verified product, an I-girder deck, or realign. A 90 m system curve is exceptional elevated geometry.
- Four normal spans may form a semi-continuous unit. Four bearings at internal piers require a checked structural continuity connection and its staged load path. A link slab joining simply supported decks retains eight bearings at internal piers; eliminating a deck joint does not eliminate bearing lines. Both configurations have four bearings at end supports. Price both using the [bearing schedule](#), including connection, CWR, temperature, braking, seismic and foundation effects.
- Parapet/containment height is measured above the finished escape walkway, not above the structural soffit or pre-track floor.
- The trackform is local direct-fixation plinths over the waterproofed structural floor. A full structural topping is a project-specific acoustic or vibration option, not the default.
- The shared hollow/precast-shell cap is 6.5–7.5 m wide and targets 25–35 t.

- Foundation selection uses `foundation-catalog.toml`. Deep-element geometry and cost require actual site length; no six-metre placeholder is permitted.
- Foundations and accepted beam stock are held 10–15 bays ahead of erection.

Automated catalogue checks live in `osr_mech.civil.viaduct`. Passing them is necessary but not sufficient for design release.

Minimum release evidence

The release package must close survey and utilities, ground model, design basis and combinations, global and local analysis, prestress/reinforcement, fatigue and durability, bearings and movement, rail/bridge interaction, drainage and egress, transport/erection, first-article testing, independent check, and deployment-authority approvals.

Viaduct Bearing And Movement Schedule

Source: <docs/civil/viaduct-bearing-and-movement-schedule.md>

Compare two twin-track schemes over the same four-span movement unit. Bearings remain replaceable in both. The reduced arrangement is an unaccepted structural alternative, not a saving established by a link slab.

Support	Tracks	Bearing lines	Bearings
Abutment/end support	2	1	4
Internal pier, structural continuity connection	2	1	4
Internal pier, simple spans with link slab	2	2	8
Expansion-unit boundary	2	2	8

Internal bearings are in one longitudinal row; adjacent unit ends retain two independent rows at an expansion boundary. The supplier schedule must assign fixed, guided, and free directions for every span end and show design reactions, translations, rotations, uplift restraint if required, replacement loads, installation temperature, and identification marks. Permanent jacking shelves and a checked load path are mandatory.

The 25 m reference places a deck gap every four spans, nominally 100 m; the permitted four/five-span family stays within 80–125 m. A structural connection must establish the shared support load path, including construction stages, prestress, reinforcement and fatigue. A link slab may remove a deck joint while each girder retains its independent end bearings and permitted rotation. For the periodic 25 m reference kilometre these alternatives require 200 and 320 bearings respectively. A finite 40-span structural layout also has 200 bearings: 30 internal supports, nine boundaries and two end supports. It has 41 supports and nine expansion gaps; the periodic index has 40 supports and ten gaps. Do not mix periodic and finite corridor quantities. The project schedule must close thermal, creep, shrinkage, seismic, braking, bearing-friction, connection fatigue and differential-settlement actions; provide covers over walkways and cable routes; and complete continuous-welded-rail/bridge interaction. Rail expansion devices are installed only where that analysis requires them.

The [FHWA UHPC connection guidance](#) describes a link slab over simple-span girders with rotating/moving bearings. It is a highway precedent, not a released rail design. Connection cost, foundation forces, maintenance access and bearing replacement must accompany both bids before whole-life selection.

Viaduct Transport And Erection Envelope

Source: docs/civil/viaduct-transport-and-erection-envelope.md

The bare OSR-Pi25 envelope is 74,937.5 kg, leaving only 62.5 kg below the 75 t product target before net details. Pi20 is 59,950 kg. Complete-member and hook masses remain unresolved. Use the [generated mass and equipment summary](#) and its controlled budget before selecting transport or erection plant. The 3.0 m shipping-width and 75 t member targets require product compliance or an independently reviewed deviation bound to the actual mass budget.

Compare the [Baghdad complete-package alternatives](#) before selecting plant. Pi20's bare mass is also only 50 kg below its 60 t product target; smaller is not automatically compliant. Price the extra supports, foundations and complete-bay cycles alongside lighter handling. Overhead delivery over completed spans adds construction loads and launch reactions requiring their own deck, pier and temporary-works analysis.

A portal, launching frame or certified strand-jack arrangement is an erection option awaiting selection and qualification. Its required capacity comes from complete member, rigging and dynamic demand at the reviewed configuration; an approximate 80 t label cannot establish suitability. The number and weight of lifts come from the actual asset layout.

Before release, record the casting-yard route, swept path, bridge and culvert capacities, overhead/side clearances, pavement and temporary works, transporter axle configuration, escort/closure plan, launcher reactions, strand-jack synchronization, wind limits, lifting points, temporary bracing, bearing survey, contingency landing position and rescue/recovery method.

For isolated packages a mobile or crawler crane may be used only against its actual configured load chart. The release records load, rigging, lift radius, wind limit, outrigger/crawler reactions and verified ground-bearing pressure; nominal crane tonnage is not accepted as proof.

Where the route or worksite cannot accept Pi20/Pi25, use OSR-US match-cast 2.5–3.0 m segments with an overhead launcher only after verifying every transport constraint. The current OSR-US coordination section exceeds the primary 3 m shipping-width target: shorter segments do not resolve restricted width. A supplier redesign or reviewed oversize route is required. Its release adds segment geometry control, match-cast records, epoxy joints, shear keys, post-tensioning, grouting, launcher stages and specialist QA. The legacy OSR-U25-SPECIAL trough is retained only where project acoustic/containment needs justify its wider and heavier transport envelope.

Viaduct First-Article Test Plan

Source: <docs/civil/viaduct-first-article-test-plan.md>

The first production mould, first Pi20/Pi25 unit, first selected foundation in each geotechnical zone, first cap shell, first erected bay, and first completed track/egress bay are hold points. Production may not free-run until the responsible engineer and independent checker accept the applicable evidence.

Hold point	Minimum evidence
Foundation zone	Utilities/CPTu/boreholes, selected catalogue type, actual pile/shaft count and length, installation time and cost, concrete/rebar quantity, representative load test and as-built survey
Mould and casting bed	Survey, stop-end settings, tendon/rebar/inserts, release agent, concrete process, calibration
First girder	Materials, cube/cylinder strength, maturity, prestress force/elongation, transfer sequence, dimensions, camber, cover, NDT, drainage test
Trial lift and transport	Certified portal/launcher or actual crane load chart, rigging, radius, wind and ground-pressure release, load test where required, strain/deflection observations, transporter trial and route clearance
Cap/column connection	Reinforcement and connection record, geometry, bearing-seat survey, grout/concrete acceptance, jacking interface
First erected bay	Bearing identity/orientation, role-selected one/two-row survey, reactions/level, girder geometry, gaps, stability, diaphragm/end-zone inspection
First selected connection unit	Four-span staged analysis correlation; distinguish structural continuity/shared bearings from simple spans/link slab; cage and closure record, maturity/grout release, waterproofing, fatigue detail, CWR/braking/temperature/seismic/foundation-flexibility closure
Track and egress	Waterproofing, local plinth geometry, fastener proof/torque, drainage flow, 1.0 m clear walkway, 1.4 m containment datum, gap covers, earthing
Structural acceptance	Correlated analysis; static/dynamic proof test if required by the design basis; residual deflection/cracking criteria; independent-check closure

Nonconformities require disposition, repaired-item acceptance, root-cause review, and demonstrated recurrence controls before the production hold point is released.

Record the complete double-track bay cycle: accepted foundations and caps, casting/strength release, transport, both track beams or all segments, closures, survey and tolerance corrections, waterproofing, track/egress and acceptance. Include crew/equipment hours, curing delays, rejects/rework, stock buffers and traffic possessions. Beam lifts per day alone cannot validate the programme.

Repository Artifact Policy

Source: [docs/repository-artifact-policy.md](https://docs.opensource-rail.org/repository-artifact-policy.md)

Git contains the useful source and review artifacts needed to understand, inspect, build, test and change OpenSourceRail without specialist regeneration. That includes CAD, IFC, PDFs, images and animations when they help a GitHub user inspect or build the system. Reproducible scratch output still belongs in `build/`; CI enforces a straightforward 50 MiB limit per tracked file.

Tracked

- Rust, Python, shell, HTML, CAD-generator, and configuration source.
- RFCs, engineering requirements, safety evidence authored by people, and stable schemas.
- Small test fixtures with a named consumer.
- The compact machine-readable city core for every entry in `lib/city-batches/world-sample.toml:design.toml`, simulator scenario, quality result, corridor GeoJSON, and station JSON. Routed designs are retained because regeneration can depend on changing external OSM and population data.
- Catalogue-wide ring/interchange and station-cluster validation reports. These reports are allowed to record inherited planning failures, but their source and validator hashes must remain current; reviewed references must pass both validators.
- Compact per-city soil/deployment and workforce/design review packages, including workforce CSVs and their input hashes. Large local operations bundles are bound through their tracked compressed-hash manifests; checking a compact report does not require downloading a complete operations bundle.
- One generated `NATIONAL-BRIEF.md` per country, aggregating city CAPEX, imported/external capital, local funding, and the single shared trainset factory.
- Two complete end-to-end acceptance references, Samawah (`light-metro-3car`) and Mosul (`metro-4car`), including map, README, alignment, simulation, energy, finance, QA, maintenance, manufacturing, acceptance evidence, and a fail-closed package manifest. Their simulation evidence includes nominal operation plus end-of-life battery, maximum planning-climate load, reduced charging-contact availability, all-site grid outage, and single-pad outage cases.
- One compact high-throughput architecture reference, Basra (`metro-6car`), adding a map and README without duplicating the complete acceptance bundles.
- Baghdad's complete planning proposal, supporting-data archive, source/output manifests and compact engineering/finance studies, including the manufactured viaduct comparison. Each tracked file remains below 50 MiB. The supporting archive preserves hash-bound ignored inputs for the clean-checkout bootstrap; it is not field acceptance or an independent source of revised assumptions. Current generated studies, explicitly superseded reviews and diagnostic sensitivities retain distinct labels; historical prices and returns do not describe a later scope.
- The Samawah OSR-ALN fixture used by converter tests.
- Compact FreeCAD and Blender review assemblies, including the LM3 selectable manufacturing-tool set; the named civil and LM3-manufacturing IFC4.3 review federations, native civil construction scene and complete sub-50-MiB review animations under `engineering/models/bim/reference/`; stable documentation images, and the root `OpenSourceRail-Book.pdf` reader edition. These are published review aids generated from authoritative sources, not parallel inputs.

Not tracked

- Rust/Python build products, logs, caches, temporary data, and screenshots that are not part of the stable documentation review set.
- High-volume generated city engineering and operations inputs except the named Mosul/Samawah acceptance payloads and Baghdad's hash-bound supporting archive. Baghdad's extracted ignored inputs remain local after bootstrap.
- Generated BOM exports, simulation traces, release-only brochures, unnamed or repeated videos, CAD/BIM job outputs, and other release binaries.
- Files that only preserve an obsolete schema, chemistry, voltage, or API name.

Output locations

Output	Location
Full city package	cities/catalogue/
Repeated simulation and engineering job output	build/engineering/
Public CAD review set	design/component-catalogue/models/cad/
Public BIM coordination review set	engineering/models/bim/reference/
BOM exports	build/bom/
Published reader book	OpenSourceRail-Book.pdf
Release-only media	build/releases/ before tagged release storage
Tagged deliverables	Release storage with version and checksum

Use `tools/automation/regenerate-city.sh <slug>` for a full city package in the canonical `cities/catalogue/` tree. Catalogue changes must include the corresponding current-generator scenario and pass the catalogue-completeness health check; generated engineering and operations directories remain tied to the city folder that produced them.

Rules

- 1 Change canonical source before regenerating output.
- 2 Do not hand-edit generated output.
- 3 Every retained fixture must name its generator and test consumer.
- 4 CI compares compact fixtures and regenerates larger evidence when required.
- 5 Never commit credentials, caches, absolute local paths, or live operational databases.
- 6 A complete generated city package is not release-ready merely because its manifest passes: survey, calibrated demand, local ground/fire/utility data, supplier freeze, and independent safety/construction release remain external project gates.
- 7 Tracked reports link only to tracked review artifacts; local high-volume outputs are named as code, not presented as GitHub links.
- 8 The root reader PDF is generated, never hand-edited. Its Markdown and city model sources remain authoritative and are printed in the book.
- 9 Keep useful CAD/BIM/media artifacts in Git when each file is at most 50 MiB. `tools/automation/check-tracked-file-sizes.py` enforces the ceiling. A future history optimisation must preserve access and requires an explicit maintainer decision; it is not part of routine cleanup.

Documentation ownership

- The root `README.md` is the only human-facing navigation page and owns the common setup instructions and source-of-truth map.
- A discipline or folder README contains only material local to that subject; it links to common guidance instead of copying it.
- City and country pages contain only local values and evidence. Shared planning interpretation lives in `docs/deployment-planning-reference.md`.
- `docs/INDEX.md` is a generated inventory for search and CI, not a competing guide or technical authority.
- When a claim can be derived, generate it from the authoritative source and test for drift rather than maintaining a second prose value.

Current Baghdad delivery review — 4 October 2026

Source: docs/baghdad-delivery-review-2026-10-04.md

Reviewed baseline: 135e249e20f0630f92f426764ea72d21e46c2a68. This source-bound reconciliation supersedes the current-state Baghdad figures in [the historical October 3 codebase review](#). It is a targeted delivery review, not a line-by-line audit or investment/construction release.

The controlled city remains 9 lines, 474.1797 km, 164 stations and 762 six-car trains. Published city capital is USD 7.168534bn, and one Baghdad factory including EPC brings the programme to USD 7.515079bn. Its monthly capital table has 78 periods and conditional full-line openings are 40, 45, 50, 55, 59, 65, 69, 74, 76 months; the facility's 18 months starts at proposed NTP. The older 347-month rollout and earlier funding totals are historical and superseded. Proposed government funding remains 25% of original capital, imports 50% government USD / 50% Chinese USD loan, with other funds in IQD. No wider national revenue is added.

The [delivery package](#) reconciles baseline WBS, exclusions, depot quantities, six-car product, chronological energy, demand/fleet phasing and workload/competence. None of its unquoted alternatives is adopted into debt, fares or official capital. Depot layouts, land/utility/title, local pay/workload, OD, equipment quotations and six-car first-article release remain open. Named owners cannot be manufactured by a role generator.

The current depot allowance is USD 8m, despite the full generated fleet, line-local storage/maintenance requirements and unresolved workshop sites and a failed morning-direction check. The new storage/workshop alternatives are quantity-based, with explicit baseline-overlap and unpriced-cost fields. The six-car allocation sums to USD 1.68m/train but does not imply qualified LM3 applicability or supplier quotations.

Hourly synthetic owned-solar reference purchases 860.2 GWh, costing USD 86.024m/year before separately identified wheeling/balancing/connection/O&M. These are sensitivity outputs from synthetic weather and aggregate pooling, not a Baghdad forecast. Unserved energy and per-site physical/contract constraints remain visible. Staffing uses explicit workload/shift cover rather than dividing the existing USD 15.002m labour budget; pay, productive hours and roster authorisations remain unaccepted.

Fresh checkout: run `.venv/bin/python tools/automation/bootstrap_baghdad_tests.py`, then `.venv/bin/python -m pytest tools/automation/tests design/component-catalogue/tests -q`. The bootstrap validates the tracked proposal archive and selectively restores the exact ignored operations payload. It preserves differing workspace data and does not resynthesise designs. Install the existing test/render dependencies, including `mistune` and `reportlab`, before publication tests. Validate the delivery package and proposal with their generators' `--check` modes.

Six local ERP evidence drafts carry estimator work budgets, accountable functions, source revisions and independent exit evidence. No appointment, quote, lease, lender commitment, physical permission or railway authority is granted. Existing observation-only integration remains intact. The full Rust/browser/hardware suites are outside this targeted calculation change; verification results are reported with its commit.

Baghdad continuation: physical packages and revised financial conclusion

Source: <docs/baghdad-continuation-review-2026-10-04.md>

The [delivery continuation](#) completes the repository calculations and reviewable work packages following the [first delivery reconciliation](#). Surveyed designs, quotations, actual demand, appointments, subscriptions and independent field acceptance remain open. The original 831-train, nine-line programme and factory opening dates are unchanged; new cases are explicit alternatives.

Financial finding

The full-fleet cost sensitivity replaces the USD 8m depot allowance with the USD 175.932m workload package and adds an explicit 7% incremental EPC allowance. Programme capital becomes USD 8.060bn, before still-unpriced scope. It replaces the original annual labour and solar allowances once, adds paid pre-opening mobilisation, and includes only replacement-reserve inflation shortfalls above contributions already in maintenance. Firm energy assumes physical upgrades whose capital is still unpriced.

Government covers 25%, USD 2.015bn equivalent. Its assumed imported-component downpayment is USD 913.123m; proposed Chinese credit is another USD 913.123m. Government's remaining cash, ordinary/green bonds, bank credit, supplemental credit, fares and commercial receipts are IQD. Total USD-denominated capital is USD 1.826bn, 22.7% of this scenario. At the historical model FX of IQD 1,300/USD this is about 89.9% below the requested USD 18bn all-foreign-currency comparator; distinct scope, price dates and unverified financing prohibit a like-for-like bid saving claim. Imported shares and Chinese eligibility require actual supplier/invoice evidence.

With existing variable pricing and annual 5% fare/OPEX/income growth, peak supplemental debt is IQD 11.360tn, and IQD 7.532tn remains outstanding at the 30-year full-network operating horizon. Before-finance company cash NPV is USD -4.692bn at the model's nominal discount rate. Surpluses repay USD 515.831m equivalent of eligible core principal early, after reserves/buffers and applicable call premiums, but do not eliminate the gap debt. Restricted maintenance cash cannot repay bonds or loans.

The [monthly and six-month ledgers](#) retain native currencies, bond-face/rounded-unit placement requirements, loan draws and principal/cash residuals. Conditional climate grants, rights proceeds, additional local income and cheap gap credit are uncommitted. A separate case fixes the original absolute government cash ceiling; another removes additional income and green pricing benefits. Opening-fleet and contracted-solar cases expose reduced receipts and transferred provider costs rather than treating them as free savings.

An initial IQD 1,750 base-fare sensitivity clears debt at month 378 after financial close, conditional on funding placement and the assumed demand elasticity. It still has negative company cash NPV, and 44 monthly trips consume 15.6% of the historical monthly income proxy before variable-price weighting. Higher-fare trials show repayment and affordability together; no tariff or commercial first-corridor selection is adopted. Actual OD, paid transfers, disposable-income distribution and concession funding remain required.

Prepared physical and operating packages

- Nine depot planning drawings label 533 storage positions, individual tracks/slots and 119 workload workshop bays. The yard-only slab production calculation meets cumulative installation deadlines using assumed mould cycles; its plant cost, curing qualification, reinforcement/foundations, turnouts, drainage, fire access and actual land remain open. Rectangular workshop packing is not an accepted accessible bay layout.
- Twenty-three six-car child-part/RFQ rows expand eight parent allocations within USD 1.68m/train. Unknown supplier quantities, prices, masses and drawings remain null. First article, LM3 applicability and qualification/design-training overlap remain unaccepted.
- Per-site chronological energy retains each installed storage/grid/charger limit. Reference imports are approximately 938.5GWh/year, with 6.6GWh unserved charging; firm energy services plus owned-solar maintenance cost USD 139.835m/year in the sensitivity. Synthetic allocation does not prove charger queues, charging events, outages or physical upgrade delivery.
- Task-based rolling maintenance and all 26 controlled intervals cover vehicles, stations, civil/track/structures, energy, wayside, tooling and finishes. Separate full/opening-fleet reserve ledgers show replacement dates, inflation top-ups and restricted cash without double-counting the replacement bill.
- Nine standalone opening-corridor cases compare operating break-even on a consistent basis; OD, actual catchments, shared dependencies and allocated debt remain unknown. Startup alternatives retain the frozen original dispatch points:

line 9 needs five extra revenue trains plus one spare, USD 10.08m vehicle reference before consequential costs, or an accepted smaller dispatch-point policy. Neither alternative closes the failed startup/access gate.

- Seven practical lesson cards and rest-limited anonymous pilot slots retain independent assessment and worker/task/location authorisation. No worker, assessor, permit or operational release is invented. Twelve scope-inclusion forms and supplier RFQs identify the remaining external inputs.

Native ERP and recovery evidence

The local ERP image was rebuilt with the workforce observer and bench-only administrative probes; the activated module hashes match repository files. Six existing DL90 Task descriptions were refreshed while preserving native Task identity, owner and operator-managed status. There are 34 Baghdad evidence Tasks in total; preparing or refreshing a Task accepts no evidence.

Five System Manager read probes each returned 54 permission-filtered rows from bounded native samples. The first took 0.455 seconds and subsequent samples approximately 0.008 seconds. This is a local read probe, not proof of complete-city throughput or the permissions of every production role. The workforce observer's permission and identity gates are separately tested.

Native Guest calls to the read probe, recovery fingerprint and workforce administration readiness were denied. These checks changed no worker, role, assignment or work-release record.

A native SQL backup was restored into a new MariaDB container with no network or published ports. Six data/schema/role/permission/File-inventory fingerprints matched; the temporary database was removed and the source database was never a restore destination. This verifies SQL recovery of the sampled inventories, not file decryption or production RTO/RPO. Private backups, import/deployment receipts, fingerprints and recovery receipts remain in ignored var/erpNext/; no native personal records or credentials enter the proposal archive.

Reproduction and acceptance

The checks below describe the preceding continuation. The [CI and controls follow-up](#) adds source-verified TLC, dependency, native-click and workforce fixes, earlier leadership/training cash and installed-throughput sensitivities.

Validation passed 1,747 Python tests and 12 subtests across city generation, components, engineering analysis, alignment/reference converters and automation. One Samawah planner test was skipped because its OSM cache is absent. Repository health, local Markdown links, source/output checks, proposal/archive checks and exact-input restoration in an empty temporary checkout passed. The full Rust, browser and target-hardware suites were not rerun for this continuation.

Run the [exact-input bootstrap](#), then the delivery baseline/continuation generators and proposal builder in the documented dependency order. Both delivery generators and the publication support - - check. The continuation binds source and output hashes; the proposal binds every packaged source and archive member. The complete proposal includes these packages and this review.

The [six work packages](#) remain field-open. Actual owners, surveyed parcels, supplier offers, OD/affordability evidence, Iraqi approvals, investor subscriptions and accepted engineering/operating evidence must replace the null fields. The delivered repository package is not a complete investment budget or railway release.

Baghdad review follow-up: controls, CI and deliverable-service sensitivity

Source: <docs/baghdad-ci-controls-review-2026-10-04.md>

Historical revision review. Its figures describe the revision reviewed below. The reworked central alignment, current staffing/depot scope and current cashflows are in the [Baghdad city summary](#) and [programme recalculation](#).

The attached review examined a f4fbc9; the subsequent continuation already integrated depot, energy, payroll and replacement-reserve cash. This follow-up strengthens that implementation and preserves the original financing case as a comparator. None of the engineering alternatives has field acceptance or committed finance.

Financing and service

The [integrated monthly and six-month ledgers](#) now include interim development leadership from NTP and separately purchased mentoring before opening. Existing contracted teaching/assessment is scheduled once. Added development/mentoring cash is IQD 2.582bn before inflation. The full-fleet sensitivity has USD 8.060bn capital, IQD 11.360tn peak gap debt, IQD 7.532tn terminal gap debt, and USD -4.692bn company cash NPV before finance. Approximately USD 515.831m equivalent of eligible core principal is prepaid after reserves, buffers and assumed call premiums; this does not clear gap debt.

Government remains 25% of scenario capital. Imports retain 50% government USD / 50% proposed Chinese USD credit. Remaining government cash, ordinary/green bonds, bank and gap credit, fares and commercial receipts remain IQD. There are no new commitments, subscriptions or guaranteed property proceeds. Existing variable fares and 5% annual fare/OPEX/income growth remain explicit assumptions. The IQD 1,750 sensitivity still clears debt in month 378, with negative company cash NPV and unverified demand/affordability.

The new installed-energy supply bound retains existing electrical capacity, removes purchases/connection charges for the unbuilt expansion, and reduces fares, station commercial receipts and additional commercial income. Synthetic installed charger/energy throughput is about 87.27% of allocated traction demand. Its terminal gap debt is approximately IQD 12.967tn, with IQD 2.787tn uncovered support. This is an energy-throughput upper bound; actual charging events, train circulation and a feasible timetable remain unaccepted. The firm-service case instead purchases shortage energy and requires unpriced physical upgrades. Neither may be described as a complete bankable budget or achieved service.

All integrated cases model zero dividends. Cash left after the debt/reserve/buffer waterfall stays in the company; audited after-tax distributable profit, covenant permission and shareholder approval remain unresolved. Earlier holding-company returns describe their original scope and must not be transferred to these higher-cost sensitivities.

Engineering and mobilisation

The [28 former pooled shortage hours](#) remain available as a comparator. [Site-hour diagnostics](#) trace grid/charger limits, opening/closing stored energy and generation paths. On-site PV receives no remote wheeling loss or charge. The reference has 2,194 distinct hours with at least one bus shortfall; the larger site-hour count also includes charger overload. Those counts measure different scopes.

[Retained workshop sites](#) explicitly require line-local covered lifting, bogie exchange, wheel servicing and body overhaul. Eight zero-bay sites still need additional facilities and quotes; mobile tools do not replace covered bays, and a disconnected central workshop provides no train-transfer route. Road transport covers removed components only. The integrated case uses workload bays at all nine sites. The five missing morning-direction requirements remain an open gate: frozen-start alternatives require either an accepted smaller start-point policy or five revenue trains plus one spare and consequential engineering/funding.

The [450-train factory replay](#) removes deferred orders and rebuilds factory resource queues, including the extra line-9 spare. Manufacturing selection, procurement cash, energy, operating payroll, maintenance and battery reserves follow the lower supply. Original expansion-capable factory/depot capital and civil opening dates remain funded; no earlier receipts or cheaper plant are invented. The case still has approximately IQD 6.525tn uncovered support, and deferred expansion remains unfunded.

[Development and training schedules](#) distinguish interim authorities, operating successors and signed handovers. Training leadership starts at month 18 and rigs must be ready by month 24, before the first operating cohorts join at month 34. Minimum purchased peak capacity is 19 teaching, 35 assessment and 90 mentoring posts, at different times. Operating recruits supply zero qualified training capacity. All 21 operating roles have lesson/coverage requirements; actual equipment, assessors, daily/rest rosters and named appointments remain absent. The anonymous OCC roster is only a pilot.

The editable metro-six-car price now feeds fleet procurement and the parent BOM allocation. Workforce conversion uses its configured FX reference; publication rejects inconsistent funding/workforce/corridor FX assumptions.

Workforce controls and CI corrections

The evaluator now checks task/location/asset/isolation scope, named authorised supervisors, qualified independent verifiers, correct calibrated tools and released part/revision/quantity. Duplicate stock records cannot count twice. Regression tests reject the review's combined wrong-line permit, missing supervisor and unqualified verifier example.

The [native workforce preview](#) validates a private attached snapshot. `snapshot_eligible` describes that snapshot; `eligible` and `live_start_check` remain false because current authoritative revocation is unresolved. Rechecking a timestamp detects expiry, not later revocation. Human task start still requires current authoritative evidence and work-release authority. No worker or assignment was created.

The six observed CI failures have corresponding changes:

- The Python test environment installs PyYAML. The hash-verified bootstrap restores declared energy/GIS/SUMO inputs and preserves differing workspace data.
- Portfolio browser expectations use the authoritative API and the UI's formatting rather than stale capital literals.
- Disabling unused postcard default features removes the heapless-CAS dependency path containing unmaintained `atomic-polyfill` and `yanked spin`; the wire fixture remains unchanged.
- TLC 1.8.0 is pinned to SHA256 `c2fe4e56e43bde19f213b4a7e441d037297fda733e503579623e859b79348239`, independently matched to upstream asset metadata and the [published SHA1](#). A changed artifact must fail verification rather than run unverified.
- Workbench uses a viewport-sized flex layout instead of an oversized minimum frame. The native test dismisses an asynchronous ERP update notice through its visible close button when present. Proposal, review and verification retain real clicks without forced clicks.

Local verification includes 124 focused tests, all 43 frontend acceptance tests, native disposition clicks with a deliberately obstructing Frappe notice, the source-bound TACS twin and bounded formal execution, and the Rust workspace/audit checks. The broad Python run passed 1,779 tests and twelve subtests, with one cache-dependent skip; its sole stale-offer failure was fixed and the four offer tests then passed. A further 124 publication/finance tests passed after regeneration. Source/output, archive, repository-health and link checks pass. Passing software checks provides no construction, railway-operation or investment release.

ERPNext now runs app 0.5.1 in the reproducible `osr14` image; deployed workforce/rules/probe hashes match repository files. Refreshing six packages updated 34 unique existing evidence Tasks, preserving native identity and operator-managed fields. A fresh SQL backup matched six inventory/schema/permission fingerprints in an isolated disposable database, which was removed. Private backups and receipts remain outside the publication.

For a source change, restore the exact ignored inputs first, then regenerate in this dependency order: Iraqi funding programme; delivery stress; viaduct rentals; qualification; financing redesign; equity; delivery baseline; delivery closure; reference offer; complete proposal; reader book. Source-bound checks reject stale intermediate packages. The proposal bootstrap also preserves differing local solver/GIS data rather than overwriting it.

Baghdad manufactured viaduct and cost review

Source: docs/baghdad-manufactured-viaduct-review-2026-10-04.md

The two supplied reviews cover a manufactured-viaduct proposal and the older 135e249e cost baseline. The latter predates the [integrated delivery and financing follow-up](#). Its USD 7.88bn is retained as a historical planning comparator; it is not a complete budget.

The [new comparison package](#) provides Pi20 and Pi25 with both structural-continuity and simple-span/link-slab schemes, plus an OSR-US constrained-access alternative. All use the same complete double-track comparison scope. The longest current Pi25 run is an investigation candidate; the separate 1 km study is not a surveyed alignment or selected project. No 30 m product or literature-based saving is introduced.

The civil load seed now distinguishes the 12-axle LM3 from Baghdad's six-car, 24-axle consist. Its 111 m length and tare/passenger masses reconcile with the controlled rolling-stock profile. Supplier axle positions and loaded axle distribution remain absent; repeating LM3 spacing would invent geometry. The 16 t infrastructure allowance must be applied with the complete loading pattern and adopted dynamic/combination rules.

The LM3 seed's passenger masses now use the same explicit 75 kg/person planning assumption: its previous AW2/AW3 masses silently used 60 kg. Reference axle geometry and both passenger-mass assumptions remain subject to deployment design acceptance; no physical load case is released by this correction.

Catalogue code now distinguishes a structural continuity connection from a link slab. A link slab retains eight bearings at internal twin-track piers; four shared bearings require the structural connection's staged load path. The finite support register includes both ends and reconciles with the shared catalogue function. Connections, CWR, thermal/braking/seismic/foundation forces, fatigue, replacement access and prices remain design/check releases. The existing lower civil rate is explicitly conditional on the unaccepted structural arrangement.

The comparison separates the standard allowance and routing penalty for every elevated segment, with an individual form for each exceptional alignment. Alternatives retain survey, wider curves, station movements, rights-of-way, segmental, utility/land, traffic and whole-life costs as unresolved fields. Removing a routing penalty is not an achieved saving. Existing capital and financing scenarios are preserved. A separate bearing-index cashflow sensitivity prices only existing standard Pi25 length, adds incremental EPC once and recalculates monthly/six-month funding, reserves and repayments. Government remains 25%; assumed imports retain 50% government USD / 50% Chinese USD credit, and other funding remains IQD. Invoice dates and origin shares are inherited assumptions; segmental/special designs receive no Pi25 bearing quantity or price credit. Connection and consequential costs remain unpriced.

Installed-price forms include quantities, invoice currency, price dates, origin, exclusions, supplier references and credit eligibility. Foundations need actual support ground zones and deep-element lengths. Unknown costs cannot produce a total. Ground cranes/portals and overhead launchers require configured proposals, complete member/rigging masses, route and support checks, temporary/deck loads and recovery plans. Pi25 and Pi20 have almost no bare-mass margin within their respective product targets.

The production model uses all eight fronts through survey/correction and final acceptance to calculate the slowest complete double-track bay rate. Missing cycles or resources keep that rate unknown. The existing casting cycle and 10–15-bay buffer remain planning assumptions pending measured trials. First article beam, pier/cap/connection, transport, erection and finished bay hold points provide the required measurement scope; no trial has been performed. UHPC connections and special composite crossings remain bounded alternatives, without carbon percentages being converted to cost savings.

The older review's depot/storage, hourly/site energy, six-car allocations, workforce, demand/fare sensitivities, rental alternatives and bootstrap work already have [controlled outputs](#). Supplier-backed prices, site design, demand counts and financing commitments remain open. The artifact policy now names Baghdad's proposal/archive and distinguishes current, historical and diagnostic evidence. The front-page README includes nobody should be priced out of dignity.

Regenerate the comparison with `.venv/bin/python tools/automation/baghdad_viaduct_comparison.py`; use `--check` to verify source/output hashes. The complete proposal includes this study and its machine-readable inputs. Automated checks verify arithmetic and data boundaries; physical trials and licensed independent checks remain necessary.

Baghdad scope and industrial review – 4 October 2026

Source: docs/baghdad-scope-and-industrial-review-2026-10-04.md

Historical review: numeric quantities and funding figures below describe the reviewed revision. Use the current city README, proposal and source-bound catalogue review for the regenerated planning basis.

Historical revision review. Its figures describe the revision reviewed below. The reworked central alignment, current staffing/depot scope and current cashflows are in the [Baghdad city summary](#) and [programme recalculation](#).

The [programme recalculation](#) is the latest Baghdad staffing, depot, procurement-origin and financing study. The [complete proposal](#) publishes it alongside its source files, twelve monthly cashflows, contract registers and six-month placement schedules. It supersedes the earlier staffing/depot assumptions for this study; the original catalogue design, generic city pages and financing cases remain separately identified comparators. No national borrowing or future factory sales are credited to Baghdad.

People and operating coverage

There are two concurrent station posts during two normal eight-hour shifts. That gives 728 daily shift assignments for 182 stations, rather than 728 employees covering every day. The retained 05:30–02:00 service requires an additional 4.5 hours of late cover. After weekly, leave, training, sickness and handover allowances, station cover requires 1,800 FTE within 3,762 permanent railway FTE. Role, line and recruitment-cohort registers reconcile payroll and pre-opening training. A shorter station opening day would require a separate service/revenue scenario.

The pay basis uses the employee median of IQD 614,000 in the 2021 Labour Force Survey, reported by the [IMF](#). An assumed 5% annual index gives the editable 2026 proxy; the general grade is 1.5 times that proxy, and technical, supervisor, senior and director grades are 2.25, 3, 4 and 5 times it. Employer costs and overtime are explicit. This is not a measured current median, and the old household-income proxy is not substituted for employee wages or altered to improve fare affordability.

Construction, train manufacture, upstream component manufacture and permanent operations are separate establishments. The construction register is a configured work-package crew screen; it is not a complete contractor payroll or a schedule for the new depot/factory sites. Contract rates already contain labour. A separate labour-content stress tests an assumed 20% content with 50% wage uplift and incremental EPC once, without inventing a measured overlap credit. Factory payroll funds the full establishment through the actual scheduled order; productive labour in unit costs is deducted before adding capacity payroll.

Depots and manufacture

Each of the nine lines receives one depot sized for its full six-car fleet, including spares and cold reserve. Storage totals 831 slots at 121 m per train position, using the actual 111 m train. Workshop bays follow annual bay-hour demand independently of storage tracks. The item register prices storage/workshop/access tracks, turnouts, drainage/access, workshop shells/equipment/services, lighting/fire services, offices/stores, wash plants, wheel lathes and isolation/rescue. Existing depot PV/BESS is counted once. Land, utilities, actual ground conditions, connected access alignments and installed charging/grid upgrades remain open; depot launch/throat conflicts still require a full-service replay.

The component study follows the actual six-car BOM quantities: 9,972 bogies and motor/inverter sets each, 4,986 battery packs, 19,944 door cassettes and 29,916 window cassettes. Process cells match the train factory's required rate and include Chinese process machinery, Iraqi facilities/materials, labour, support, maintenance, qualification and residual imported inputs. Bogie fabrication, motor assembly, battery-pack assembly and door manufacture show positive whole-order margins under the unquoted inputs. Window manufacture has a negative Baghdad-only margin; future national orders are not assumed to rescue it. Imported cells/BMS and other critical parts remain. Battery pack assembly does not imply local cell manufacture.

Serial qualification within the 18-month facility target remains an assumption. A six-month supplier-delay case shifts rolling-stock invoices, line openings and operating receipts, prices idle payroll and preserves the full operating horizon. A 25% raw-input price stress tests the same selected facilities. License, yield/rework, tooling overlap and actual vendor quotations require evidence before investment.

Alignment and finance

The study permits a 40% elevated ceiling and screens 29.148 km of candidate additional viaduct around exceptional segments, reaching 20.32% elevated. Intervals include approach allowances, merge overlap and exclude existing elevated/bridge lengths. Elevation alone removes no horizontal bend. Wider-radius geometry, station moves, land, gradients, egress, geotechnical and utility constraints need design work. The 0/25/50% routing-penalty-removal cases are counterfactuals; no penalty reduction is adopted as an achieved saving.

Government funds exactly 25% of each case's capital. Imported invoices are split 50% government USD cash and 50% proposed Chinese USD credit. The remaining government appropriation and all domestic bonds, bank/gap debt and mezzanine are IQD. Machinery-heavy months follow their invoice downpayments; the total government contribution, rather than each month's share, is constrained to 25%. Foreign procurement intensity, foreign debt and reporting equivalents are separate measures. The old 148 km / USD 18bn third-party example retains its distinct scope and assumed foreign-currency funding; it is not a matched tender comparison.

Mezzanine substitutes for 10% of domestic residual capital borrowing. The tested terms are project assumptions: 6% cash coupon, 4% PIK, 2% fee, 15-year balloon and senior DSCR 1.20 before junior cash payments. Deferred coupons and PIK increase debt until maturity; unpaid balloons become overdue balances, with simple-interest sensitivity and no automatic refinancing or conversion. Gap draws or unsourced support cannot fund junior distributions. Source/use, senior principal, junior principal/PIK and overdue-interest identities are checked independently. Semiannual schedules report flows separately from closing stocks and distinguish face-denomination rounding from actual cash raised.

The revised senior case still has unsourced support and unpaid debt at the horizon. Mezzanine reduces immediate funding pressure by deferring payments but increases terminal debt and leaves 85 junior draw vintages in default. It is not recommended as the solution to the operating deficit. Indexed fares, OPEX inflation, advertising/kiosks/rentals and inherited additional receipts are already included. Green terms, grants, rights income and 2% concessional gap credit remain uncommitted; the 8% gap-rate stress shows that financing dependence. There are no dividends. Verified capital, affordable revenue or accepted scope savings are still needed.

Reproduction and release limits

The [city landing page](#) is published from the current case rather than the earlier catalogue budget. The city regeneration, batch generation and controls-refresh commands use [publish-city-summary.py](#). Its [registry](#) identifies the current study and seventeen earlier reference documents. Original finance, depot, staffing, national and portfolio figures remain traceable with an explicit original-scope notice; document receipt updates do not change financial values or release flags. A stale study stops publication. CI checks the committed page before regeneration, then verifies the publisher after national-brief regeneration. The reader book includes the current city summary and current study before the original funding appendices.

- Assumptions: [baghdad-programme-recalculation.toml](#).
- Generate: `.venv/bin/python tools/automation/baghdad_programme_recalculation.py`; verify with `--check`.
- Cash engine: [baghdad_recalculation_finance.py](#).
- Tests: [test_baghdad_programme_recalculation.py](#).
- Earlier comparators: [delivery continuation](#) and [original funding programme](#).

The ERP payload contains planning drafts for staffing, depot projects/assets and factory workstations. It creates no actual employees, appointments, financing commitments, operational transactions or permissions. Survey, quotations, demand/timetable acceptance, wage data, manufacturing qualification, complete installed budgets and executed funding terms remain release gates.
